

कार्यालय
कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, बिक्रमगंज (रोहतास)।

पत्रांक...362 3150/बिक्रमगंज/दिनांक...09/03/2021

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, बिक्रमगंज।

सेवा में,

नोडल पदाधिकारी, (MR-3054)
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:- नई अनुरक्षण नीति 2018 (MR-3054) योजनान्तर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि नई अनुरक्षण नीति 2018 (MR-3054) योजनान्तर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अनुलग्नक:-यथोक्त।

विश्वासभाजन

09/03/2021
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, बिक्रमगंज।
बिनाई
09/03/2021
09/03/21

Requisition Format for Scheme Head- MR(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)
Name of Works Division:- BIKRAMGANJ

Sl. No.	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter no. & DT.	Administrative Approval		Agreement Amount (in Lakhs)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakhs)	Up-to-Date expenditure as per MIS (in Lakh)	Requisition against work done. (in Lakh)	Remarks
					Length	Amount of (in Lakhs)	Initial Rectification with Surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N 19-20 BIKRAMGANJ/06	Dumraon Distributory - Kheshandih Khurd	10301002082	MR 3054-04-139/2019-2065 DT.-04.07.2019	1.670	64.927	38.147	16.11654	52/MBD/2019-2028.01.20	29.09.2020	--	2263.7	25	5.01	22.88820	22.88820	15.25880	BT Completed
2	MR-N 19-20 BIKRAMGANJ/06	Gosuldihi Canal Bridge - Rutlanpatti	10301002087	MR 3054-04-139/2019-2065 DT.-04.07.2019	2.61	102.417	61.219	24.29527	52/MBD/2019-2028.01.20	29.09.2020	--	2364.07	25	5.01	36.73140	36.73140	24.48760	BT Completed
3	MR-N 19-20 BIKRAMGANJ/06	Surajpura to Agarar Kala via Dewaria Rampur (Phase-II)	10301002309	MR 3054-04-139/2019-2065 DT.-04.07.2019	2.00	78.4819	44.0279	16.534	52/MBD/2019-2028.01.20	29.09.2020	--	2551.7	25	5.01	26.41674	26.41674	17.61116	BT Completed
4	MR-N/19-20 BIKRAMGANJ/03	Construction of Road From Ara-Sasaram PWD Road Durgadih More to Tiliakpura	10301101005	MR 3054-04-139/2019-2065 DT.-04.07.2019	3.8	181.915	115.14979	36.12381	55 MBD/2019-2020 Date-13.02.2020	07.10.2020	-	2714.921	25	5.01	51.81705	51.81705	63.33195	BT Complete

- 1 Signed Hard Copy and Soft Copy (in excel) of Recorded IRI is enclosed.
2 UP-to date Physical Progress has been Uploaded in MIS.

Executive Engineer

PWD, Works Div. BIKRAMGANJ

09/03/2021
29/03/21

Name of Rod : Dumraon Distributri to Kasandih Khurd


Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IFRI mm/km	TEGORY ROAD	Latitude	ongitude	Event
18/12/20	9:8:17	90	0.1	130	12.3	1300	1609	G	25.28877	84.2696	Normal
18/12/20	9:8:52	90	0.1	260	10.1	2600	3086	G	25.28968	84.26948	Normal
18/12/20	9:9:0	90	0.1	190	20.2	1900	2290	G	25.29053	84.26933	Normal
18/12/20	9:9:0	90	0.1	230	20.2	2300	2745	G	25.29129	84.26884	Normal
18/12/20	9:9:0	90	0.1	230	20.2	2300	2745	G	25.29193	84.26813	Normal
18/12/20	9:9:28	90	0.1	230	20.2	2300	2745	G	25.29257	84.26741	Normal
18/12/20	9:9:28	90	0.1	230	20.2	2300	2745	G	25.29322	84.2667	Normal
18/12/20	9:10:3	90	0.1	130	20.2	1300	1609	G	25.29386	84.26599	Normal
18/12/20	9:10:3	90	0.1	280	20.2	2800	3313	G	25.29451	84.26527	Normal
18/12/20	9:10:3	90	0.1	150	20.2	1500	1836	G	25.2952	84.26455	Normal
18/12/20	9:10:38	90	0.1	140	20.2	1400	1722	G	25.2958	84.26386	Normal
18/12/20	9:11:0	90	0.1	240	20.2	2400	2858	G	25.29647	84.26313	Normal
18/12/20	9:11:13	90	0.1	110	10.1	1100	1382	G	25.29702	84.26236	Normal
18/12/20	9:11:13	90	0.1	190	20.2	1900	2290	G	25.29728	84.26141	Normal
18/12/20	9:11:49	90	0.1	160	20.2	1600	1950	G	25.29748	84.26044	Normal
18/12/20	9:12:0	90	0.1	140	20.2	1400	1722	G	25.29769	84.25943	Normal
18/12/20	9:12:24	90	0.1	270	10.1	2700	3199	G	25.29778	84.25864	Normal
18/12/20	9:13:0	90	0.1	110	10.1	1100	1382	G			
Total			1.7								

$Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$
 $X = 1100$
 $Y = 1382$
 (R) RURAL ROAD
 Good Average Poor
 < 4000 $4001-5000$ > 5001

22/12/20
 J.E

22/12/20
 J.E

after these

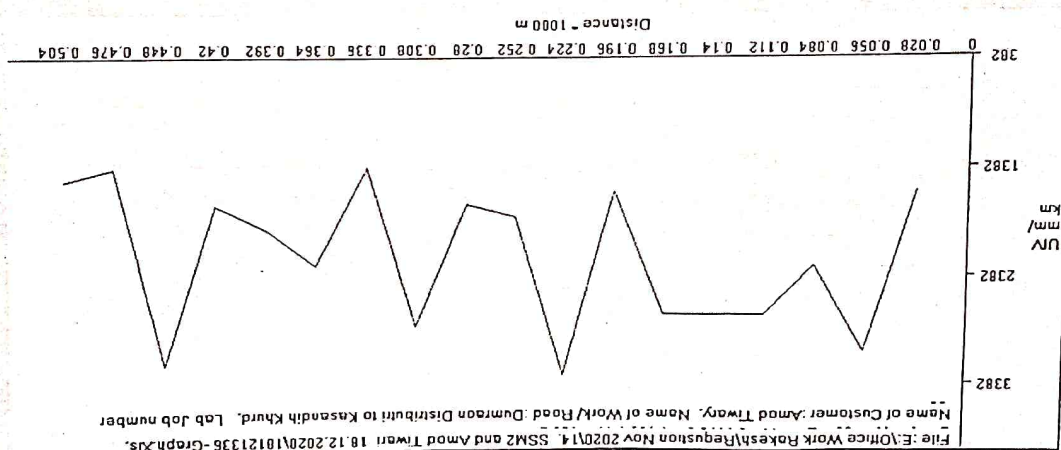

Test Date :	18/12/2020	Machine No :	331	Road Name :	Dumreeon Distributor to Kosandi
Start S No :	5873	Side :	Sunayapura	Road Type :	(R) RURAL ROAD
Start E No :	5880	Interval			
Weather :	Normal	UV Range :	362 To 4000	mm/km	
Start Location :	3528872 842	Dist Range :	0 To 0532	0028	1000 m
End Location :	3972 8425854	Equation :	$y = 0 \cdot x + 2 \cdot 2 + 1136 \cdot x - 1325$		

Print Generate Report and Graph	
Section No. 30	
Date: 18/2/2020	
Lab job number 30	
Name of Customer: Anand Tiwary	Name of Work/ Dumson Distribuit to Karsada
Road:	
