

कार्यालय
कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, बिक्रमगंज (रोहतास)।

पत्रांक...362 3750/बिक्रमगंज/दिनांक...09/03/2021

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, बिक्रमगंज।

सेवा में,

नोडल पदाधिकारी, (MR-3054)
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:- नई अनुरक्षण नीति 2018 (MR-3054) योजनान्तर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि नई अनुरक्षण नीति 2018 (MR-3054) योजनान्तर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अनुलग्नक:-यथोक्त।

विश्वासभाजन

09/03/2021
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, बिक्रमगंज।
बिनाई
09/03/2021
09/03/21

Requisition Format for Scheme Head- MR(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)
Name of Works Division:- BIKRAMGANJ

Sl. No.	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter no. & DT.	Administrative Approval		Agreement Amount (in Lakhs)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakhs)	Up-to-Date expenditure as per MIS (in Lakh)	Requisition against work done. (in Lakh)	Remarks
					Length	Amount of (in Lakhs)	Initial Rectification with Surface Renewal (in lakh)	5 Years Routine Maintenance (in lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N 19-20 BIKRAMGANJ/06	Dumraon Distributory - Kheshandih Khurd	10301002082	MR 3054-04-139/2019-2065 DT.-04.07.2019	1.670	64.927	38.147	16.11654	52/MBD/2019-2028.01.20	29.09.2020	--	2263.7	25	5.01	22.88820	22.88820	15.25880	BT Completed
2	MR-N 19-20 BIKRAMGANJ/06	Gosuldihi Canal Bridge - Rutlanpatti	10301002087	MR 3054-04-139/2019-2065 DT.-04.07.2019	2.61	102.417	61.219	24.29527	52/MBD/2019-2028.01.20	29.09.2020	--	2364.07	25	5.01	36.73140	36.73140	24.48760	BT Completed
3	MR-N 19-20 BIKRAMGANJ/06	Surajpura to Agarar Kala via Dewaria Rampur (Phase-II)	10301002309	MR 3054-04-139/2019-2065 DT.-04.07.2019	2.00	78.4819	44.0279	16.534	52/MBD/2019-2028.01.20	29.09.2020	--	2551.7	25	5.01	26.41674	26.41674	17.61116	BT Completed
4	MR-N/19-20 BIKRAMGANJ/03	Construction of Road From Ara-Sasaram PWD Road Durgadih More to Tiliakpura	10301101005	MR 3054-04-139/2019-2065 DT.-04.07.2019	3.8	181.915	115.14979	36.12381	55 MBD/2019-2020 13.02.2020	07.10.2020	-	2714.921	25	5.01	51.81705	51.81705	63.33195	BT Complete

- 1 Signed Hard Copy and Soft Copy (in excel) of Recorded IRI is enclosed.
2 UP-to date Physical Progress has been Uploaded in MIS.

Executive Engineer

PWD, Works Div. BIKRAMGANJ

09/03/2021
29/03/21

Name of Rod : Surajpura to Agrer kala via Dewariya Rampur

Date	Time	Section	Length	Bumps	Speed	OR	IRI	TEGORY	Latitude	ongtitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
18/12/20	10:18:0	92	0.1	290	26.3	2900	3426	G	25.25791	84.22537	Normal
18/12/20	10:19:0	92	0.1	210	10.1	2100	2518	G	25.2588	84.22544	Normal
18/12/20	10:19:8	92	0.1	250	10.1	2500	2972	G	25.25928	84.22461	Normal
18/12/20	10:20:18	92	0.1	150	21.4	1500	1836	G	25.25951	84.22365	Normal
18/12/20	10:21:29	92	0.1	250	26.7	2500	2972	G	25.25979	84.22278	Normal
18/12/20	10:22:4	92	0.1	250	10.1	2500	2972	G	25.26003	84.22184	Normal
18/12/20	10:22:39	92	0.1	200	21.3	2000	2404	G	25.26043	84.22098	Normal
18/12/20	10:23:0	92	0.1	200	23.1	2000	2404	G	25.26074	84.22003	Normal
18/12/20	10:23:15	92	0.1	220	20.2	2200	2631	G	25.26098	84.21912	Normal
18/12/20	10:23:15	92	0.1	200	30.3	2000	2404	G	25.26137	84.21823	Normal
18/12/20	10:23:15	92	0.1	270	30.3	2700	3199	G	25.26157	84.21722	Normal
18/12/20	10:23:50	92	0.1	230	30.3	2300	2745	G	25.2615	84.2163	Normal
18/12/20	10:24:0	92	0.1	280	30.3	2800	3313	G	25.26139	84.21529	Normal
18/12/20	10:24:0	92	0.1	230	30.3	2300	2745	G	25.26126	84.21429	Normal
18/12/20	10:24:25	92	0.1	170	30.3	1700	2063	G	25.26133	84.21332	Normal
18/12/20	10:24:25	92	0.1	150	30.3	1500	1836	G	25.26141	84.21227	Normal
18/12/20	10:24:25	92	0.1	160	30.3	1600	1950	G	25.26149	84.21135	Normal
18/12/20	10:25:0	92	0.1	190	30.3	1900	2290	G	25.26164	84.21034	Normal
18/12/20	10:25:0	92	0.1	210	30.3	2100	2518	G	25.26206	84.20944	Normal
18/12/20	10:25:0	92	0.1	150	20.2	1500	1836	G	25.26216	84.20916	Normal
Total			2								

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 1500$$

$$Y = 1836$$

(R) RURAL ROAD
 Good Average Poor
 <4000 4001-5000 >5001

File
 22/12/20
 J.S.

CS
 22/12/20


Name of Customer :	Amod Tiwari
Name of Work/Road :	Sursipura to Agrer Kala Via Dew
Lab Job number :	92
Date :	18/12/2020
Section No. :	92

Test Date :	18/12/2020	Road Name :	Sursipura to Agrer Kala Via De
Machine No :	391	Road Type :	(R) RURAL ROAD
Start S No :	5913	Side :	Sursipura
Start E No :	5932	Interval	
Weather :	Normal	UJV Range :	936 To 4000 mm/km
Start Location :	25 25791.842	Dist Range :	0 To 0.568 = 1000 m
End Location :	3216 8420316	Equation :	$Y = 0.00002 \cdot X^2 + 1.136 \cdot X + 132.5$

Print

Redraw Graph

Map View

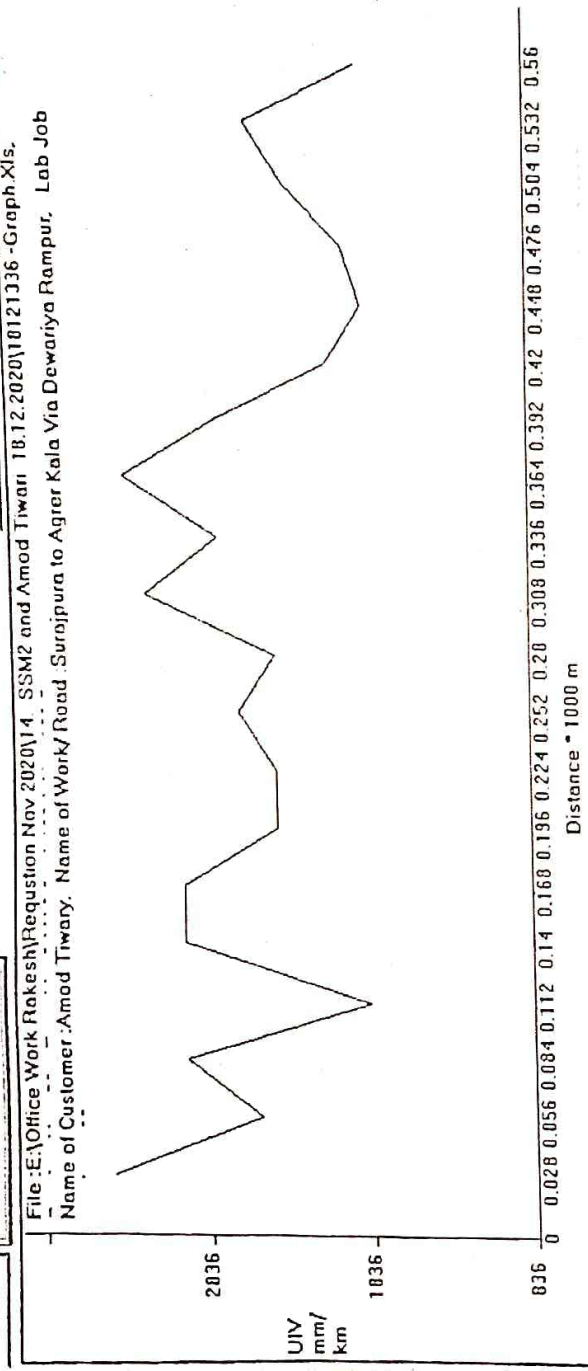

18/12/2020
J.E.

CP
Redraw Graph
J.E.
