

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, अरवल।

पत्रांक 320 अरवल/दिनांक 15-3-2017

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, अरवल

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :- नई अनुरक्षण नीति-2018MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अध्याचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :- यथोक्त।

विश्वासभाजन

15/3/21
कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, अरवल।
15/3/21

Requisition Format for Scheme Head- MR (3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Works Division- Arwal.

Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter no. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Date of Completion As per Agreement	Actual Date of Completion	Value of IRI (In MM/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content Percentage	Previous Total Allocated Amount (In Lakh)	Up to date expenditure as per MIS (in Lakh)	Requestion against work done (in Lakh)	Remarks	
					Length	Amount of (In Lakh)	Initial Rectification with surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/AR/AR W/20/0002	NIRANJANPUR TO KAMTA	16311032475	6287/02-12-2019	3	124.038	79.86300	28.10220	26/MBD/MR-NEW/2020-2021/29-08-2020	02-May-21	14.03.2021	3165	25 MM	5.00	0.00	79.86300	Complete	
	RM/AR/AR W/19/0006	Jamuhari to Trukkharsa	10603001025	3356/01-08-2019	2.5	74.05	48.95700	24.98451	96/MBD/MR/2019-2020/17-03-2020	16-Dec-20	28.01.2021	3312	25 MM	5.00	0.00	47.95700	Complete	
		Total			5.500	198.088	128.82000	53.08671								127.82000		

Divisional Accounts Officer
R.W.D (W) Division
Arwal.

Executive Engineer
R.W.D (W) Division
Arwal.

Road Name-NIRANJANPUR TO KAMTA

CONT.NAME:-Maa Kamakhya Construction And Company

Date	Time Section	Length	Bumps	Speed	OR	UUV	CATEGORY	Latitude	Longitude	Event
	No.	In km	In mm	Rate	mm/km		ROAD			
14/3/21	10:20:0	76	0.1	300	10.1	3000	3540 G	25.183237	84.530622	Speed Breaker
14/3/21	10:20:29	76	0.1	280	10.1	2800	3313 G	25.182952	84.531582	Normal
14/3/21	10:21:5	76	0.1	300	10.1	3000	3540 G	25.182102	84.531615	Normal
14/3/21	10:21:5	76	0.1	290	10.1	2900	3426 G	25.181228	84.53172	Normal
14/3/21	10:21:40	76	0.1	240	20.2	2400	2858 G	25.180273	84.5318	Normal
14/3/21	10:22:0	76	0.1	260	20.2	2600	3086 G	25.17942	84.531952	Normal
14/3/21	10:22:14	76	0.1	280	20.2	2800	3313 G	25.178498	84.532272	Normal
14/3/21	10:22:14	76	0.1	250	20.2	2500	2972 G	25.17763	84.532172	Normal
14/3/21	10:22:14	76	0.1	250	20.2	2500	2972 G	25.176675	84.532255	Normal
14/3/21	10:23:0	76	0.1	290	20.2	2900	3426 G	25.176345	84.533097	Normal
14/3/21	10:23:0	76	0.1	270	20.2	2700	3199 G	25.176275	84.53409	Normal
14/3/21	10:23:25	76	0.1	250	20.2	2500	2972 G	25.17631	84.5351	Normal
14/3/21	10:23:25	76	0.1	290	20.2	2900	3426 G	25.176207	84.536127	Normal
14/3/21	10:24:0	76	0.1	250	20.2	2500	2972 G	25.176148	84.537137	Normal
14/3/21	10:24:0	76	0.1	270	20.2	2700	3199 G	25.17612	84.53813	Normal
14/3/21	10:24:35	76	0.1	280	20.2	2800	3313 G	25.176122	84.539192	Normal
14/3/21	10:25:0	76	0.1	330	10.1	3300	3881 G	25.176097	84.540202	Normal
14/3/21	10:25:10	76	0.1	310	20.2	3100	3654 G	25.175558	84.540638	Normal
14/3/21	10:25:10	76	0.1	230	20.2	2300	2745 G	25.17465	84.540655	Normal
14/3/21	10:25:10	76	0.1	290	20.2	2900	3426 G	25.17372	84.540892	Normal
14/3/21	10:25:46	76	0.1	260	20.2	2600	3086 G	25.173148	84.541598	Normal
14/3/21	10:26:0	76	0.1	220	20.2	2200	2631 G	25.172728	84.542508	Normal
14/3/21	10:26:21	76	0.1	260	20.2	2600	3086 G	25.172192	84.543315	Normal
14/3/21	10:26:21	76	0.1	240	20.2	2400	2858 G	25.171828	84.544308	Normal
14/3/21	10:26:21	76	0.1	240	20.2	2400	2858 G	25.171495	84.54515	Normal
14/3/21	10:27:0	76	0.1	230	20.2	2300	2745 G	25.171292	84.54611	Normal
14/3/21	10:27:32	76	0.1	230	10.1	2300	2745 G	25.170913	84.547103	Normal
14/3/21	10:28:0	76	0.1	290	20.2	2900	3426 G	25.1706	84.54808	Normal
14/3/21	10:28:7	76	0.1	250	20.2	2500	2972 G	25.17032	84.54904	Normal
						AVERAGE	3165	25.170072	84.55	Normal

$$Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$$

$$X \approx 4700$$

$$Y \approx 5471$$

(R) RURAL ROAD

Good Average Poor


<4000 4001-500 >5001

14/3/2021
J.E.

14/3/21
J.E.

14/3/21
J.E.

File : C:\Users\BRRDA95\Desktop\NEW MR\KAMTA.Xls, Section No. : 76, Eqn : $Y = 0 * X^2 + 1.136 * X + 132.5$
 Name of Customer : Maa Kamakhya Construction And Company, Name of Work/ Road : NIRANJANPUR TO KAMTA.

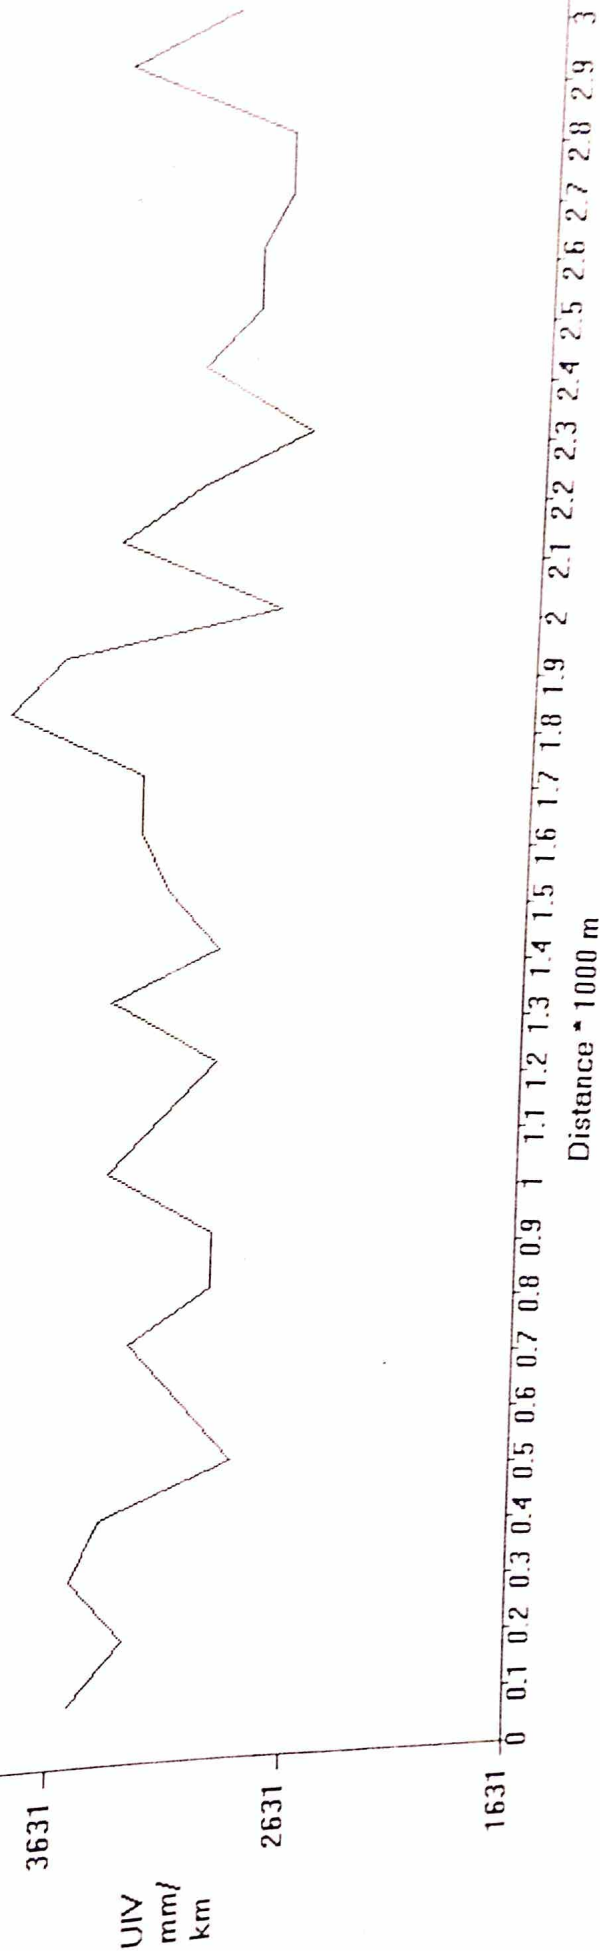

Handwritten signature
 19.01.2024

Handwritten signature
 19.01.2024

Handwritten signature
 19.01.2024
