

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, औरंगाबाद
Email ID:-cerwdaurangabad1@gmail.com Mob:- 8986915333

पत्रांक 793/2018 औरंगाबाद/दिनांक 12/03/21

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, औरंगाबाद

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :- नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :- यथोक्त।

विश्वास भाजन

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, औरंगाबाद

(HMD)
12/03/21

OFFICE OF EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, Aurangabad

Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Sl no.	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative		Agreement Amount		Agreement No& Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in lakh)	up-to-date expenditure as per MIS (in lakh)	Requisition against work done (in lakh)	Remarks
					Length (in km)	Amount of (in lakh)	Initial Rectification with Surface Renewal (in lakh)	5 Year Routine Maintenance (in lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RN/AL/AL/R/ 19/0031	Madanpur Deo Road - Barabhar	10602802124	3140/22.07.2019	2.98	91.51	58.63	23.67	61NIBD-2019-20 05.02.2020	04.11.2020	07.01.2020	3163	25.00MM	5.002%	29.31500	29.31500	29.31500	Comp.
2	RN/AL/AL/R/ 19/0025	Amba Jeeva Bigha Road - Kasauri	10602802020	3140/22.07.2019	3.6	115.39	73.31	30.44	72NIBD-2019-20 15.02.2020	14.11.2020	07.01.2020	2962	25.00MM	5.0367%	36.65500	36.65500	36.65500	Comp.
3	RN/AL/AL/R/ 19/0025	Const of Rd from Mahirganj Schoolaya to Sarwar	10602801017	3140/22.07.2019	3.4	126.80	73.92	32.66	72NIBD-2019-20 15.02.2020	14.11.2020	04.01.2021	2701	25.00MM	5.0533%	36.96000	36.96000	36.96000	Comp.
4	RN/AL/AL/R/ 19/0001	madanpurkasma - basant	NEA22000205	835/24.06.2019	1.4	55.04	31.39	12.875	81NIBD-2019-20 20.02.2020	19.11.2020	22.12.2020	3129	25.00MM	5.0553%	15.69500	15.69500	15.69500	Comp.
5	RN/AL/AL/R/ 19/0001	Tika Kasma Bigha - Pany	10602802139	835/24.06.2019	1.45	54.55	30.36	13.56	81NIBD-2019-20 20.02.2020	19.11.2020	22.12.2020	3340	25.00MM	5.1153%	15.18000	15.18000	15.18000	Comp.
6	RN/AL/AL/R/ 19/0001	Madanpur Kasma Road - Paraiya	10602902022	835/24.06.2019	1.75	68.36	40.61	15.42	81NIBD-2019-20 20.02.2020	19.11.2020	22.12.2020	3026	25.00MM	5.0867%	20.30500	20.30500	20.30500	Comp.
7	RN/AL/AL/R/ 19/0018	Judahi Nahar Pail to Barrow village Road	10602901034	3140/22.07.2019	1.8	61.34	39.55	15.57	83NIBD-2019-20 24.02.2020	23.02.2020	04.01.2021	3148	25.00MM	5.020%	19.77500	19.77500	19.77500	Comp.
8	RN/AL/AL/R/ 19/0020	Riship Nuharajganj - Baraunda	10602902032	3140/22.07.2019	1.3	44.83	28.45	11.81	86NIBD-2019-20 05.03.2020	04.12.2020	04.01.2021	3511	25.00MM	5.066%	14.22500	14.22500	14.22500	Comp.
9	RN/AL/AL/R/ 19/0021	1093-T03 NIBA JEEVA BIGHA TO DE NIRA (TRAC/K93)	NEA22000198	3140/22.07.2019	1.85	67.219	40.11	16.33	85NIBD-2019-20 05.03.2020	04.12.2020	04.01.2021	2782	25.00MM	5.033%	20.05500	20.05500	20.05500	Comp.
10	RN/AL/AL/R/ 19/0021	Village Baselha to Pokhrani Road	10602901042	3140/22.07.2019	2.1	64.08	40.99	16.57	85NIBD-2019-20 05.03.2020	04.12.2020	04.01.2021	3047	25.00MM	5.001%	20.49500	20.49500	20.49500	Comp.

21/09/20

OFFICE OF EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, WORKS DIVISION, Aurangabad
Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)
 Name of Works Division:- Aurangabad

Sl no.	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative		Agreement Amount		Agreement No& Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
11	RW/AL/AL/R/ 19/0013	NABINAGAR BARTIN ROAD - KHANDA	NEA2200060	31/07/22.07.2019	2.3	86.66	60.07	17.90	70NIBD-2019-20 15.02.2020	14.11.2020	16.01.2021	2440	25.00MM	5.069%	30.03500	30.03500	30.03500	Comp.
12	RW/AL/AL/R/ 19/0025	rishipmaharajpurj - hanaya	NEA22000176	31/07/22.07.2019	2.8	89.68	55.71	24.95	72NIBD-2019-20 15.02.2020	14.11.2020	16.01.2021	3009	25.00MM	5.0630%	27.85500	27.85500	27.85500	Comp.
13	RW/AL/AL/R/ 19/0017	KACHANPUR - BAKA PATH	10602902019	31/07/22.07.2019	3.3	119.90	77.21	30.56	82NIBD-2019-20 16.09.2020	15.06.2021	16.01.2021	2492	25.00MM	5.0440%	38.60500	38.60500	38.60500	Comp.
14	RW/AL/AL/R/ 19/0010	Khaira to Gram Sonahi Road	10602901035	31/07/22.07.2019	2.05	78.8	50.88	19.97	84NIBD-2019-20 25.02.2020	24.11.2020	13.11.2020	3549	25.00MM	5.011%	25.44000	25.44000	25.44000	Comp.
15	RW/AL/AL/R/ 19/0012	1029 - T01 G.T.ROAD TO KLSA (TRACK29)	10602802064	31/07/22.07.2019	5.76	203.59	130.86	52.30	20.02.2020 76NIBD-2019-20	19.11.2020	19.12.2020	3021	25.00MM	5.020%	58.88700	58.88700	71.97500	Comp.
Total					37.84												122.56800	

[Signature]
 Divisional Account's Officer
 Rural Works Department, Works
 Division, Aurangabad

[Signature]
 Executive Engineer
 Rural Works Department
 Works Division, Aurangabad
 12/02/21

Name Of Road Tika Kasma Bigha - Poay

Date	Time	Section	Length	Bumps	Speed	OR		CATEGORY	IRI	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	UIV	ROAD				
22/12/20	17:26:0	7	0.1	150	20.2	1500	1836	G	2.6	24.70251	84.68916	Normal
22/12/20	17:27:3	7	0.1	290	20.2	2900	3426	G	3.53	24.70194	84.68845	Normal
22/12/20	17:27:3	7	0.1	250	20.2	2500	2972	G	3.99	24.70156	84.68771	Normal
22/12/20	17:27:38	7	0.1	300	20.2	3000	3540	G	3.66	24.70156	84.687	Normal
22/12/20	17:27:38	7	0.1	300	30.3	3000	3540	G	3.66	24.70145	84.68571	Normal
22/12/20	17:28:14	7	0.1	320	20.2	3200	3767	G	3.93	24.70204	84.68535	Normal
22/12/20	17:28:14	7	0.1	240	30.3	2400	2858	G	3.85	24.70295	84.68557	Normal
22/12/20	17:28:14	7	0.1	270	20.2	2700	3199	G	3.26	24.70396	84.68556	Normal
22/12/20	17:29:0	7	0.1	260	30.3	2600	3086	G	4.13	24.7057	84.68577	Speed Breaker
22/12/20	17:29:0	7	0.1	360	20.2	3200	3810	G	3.46	24.70643	84.68517	Normal
22/12/20	17:29:24	7	0.1	310	30.3	3100	3654	G	3.8	24.70696	84.68436	Normal
22/12/20	17:29:24	7	0.1	300	20.2	3000	3540	G	4.66	24.70737	84.68357	Speed Breaker
22/12/20	17:30:0	7	0.1	320	20.2	3200	3767	G	3.93	24.70827	84.68389	Normal
22/12/20	17:30:0	7	0.1	320	20.2	3200	3767	G	3.93	24.70876	84.68333	Normal

Total Length

1.4

P. K. Singh
22/12/20
J.E

[Signature]
22/12/20
A.E

[Signature]
22/12/20
E.E

$Y = 0 * X^2 + 1.136 * X + 132.5$
 $X = 2821$
 $Y = 3340$
 (R) RURAL ROAD
 Good Average Poor
 <4000 4001-5000 >5001

Name of Customer : Bhole Shankar Constructions P
Name of Work/ Road : Tika Kasma Bigha - Poay
Lab Job number : 07
Date : 22-12-2020
Section No. : 7


Test Date : 22-12-2020 Road Name : Tika Kasma Bigha - Poay
Machine No : 377 Road Type : (R) RURAL ROAD
Start S No : 82 Side : MADANPUR Interval
Start E No : 95
Weather : Normal UV Range : 836 To 5000 1000 mm/km
Start Location : 24.702508 84.1 Dist Range : 0 To 1.5 0.1 * 1000 m
End Location : 24.708763 84.1 Equation : $Y = 0 * X^2 + 1.136 * X + 132.5$

Print

Generate Report and Graph

Redraw Graph

Map View

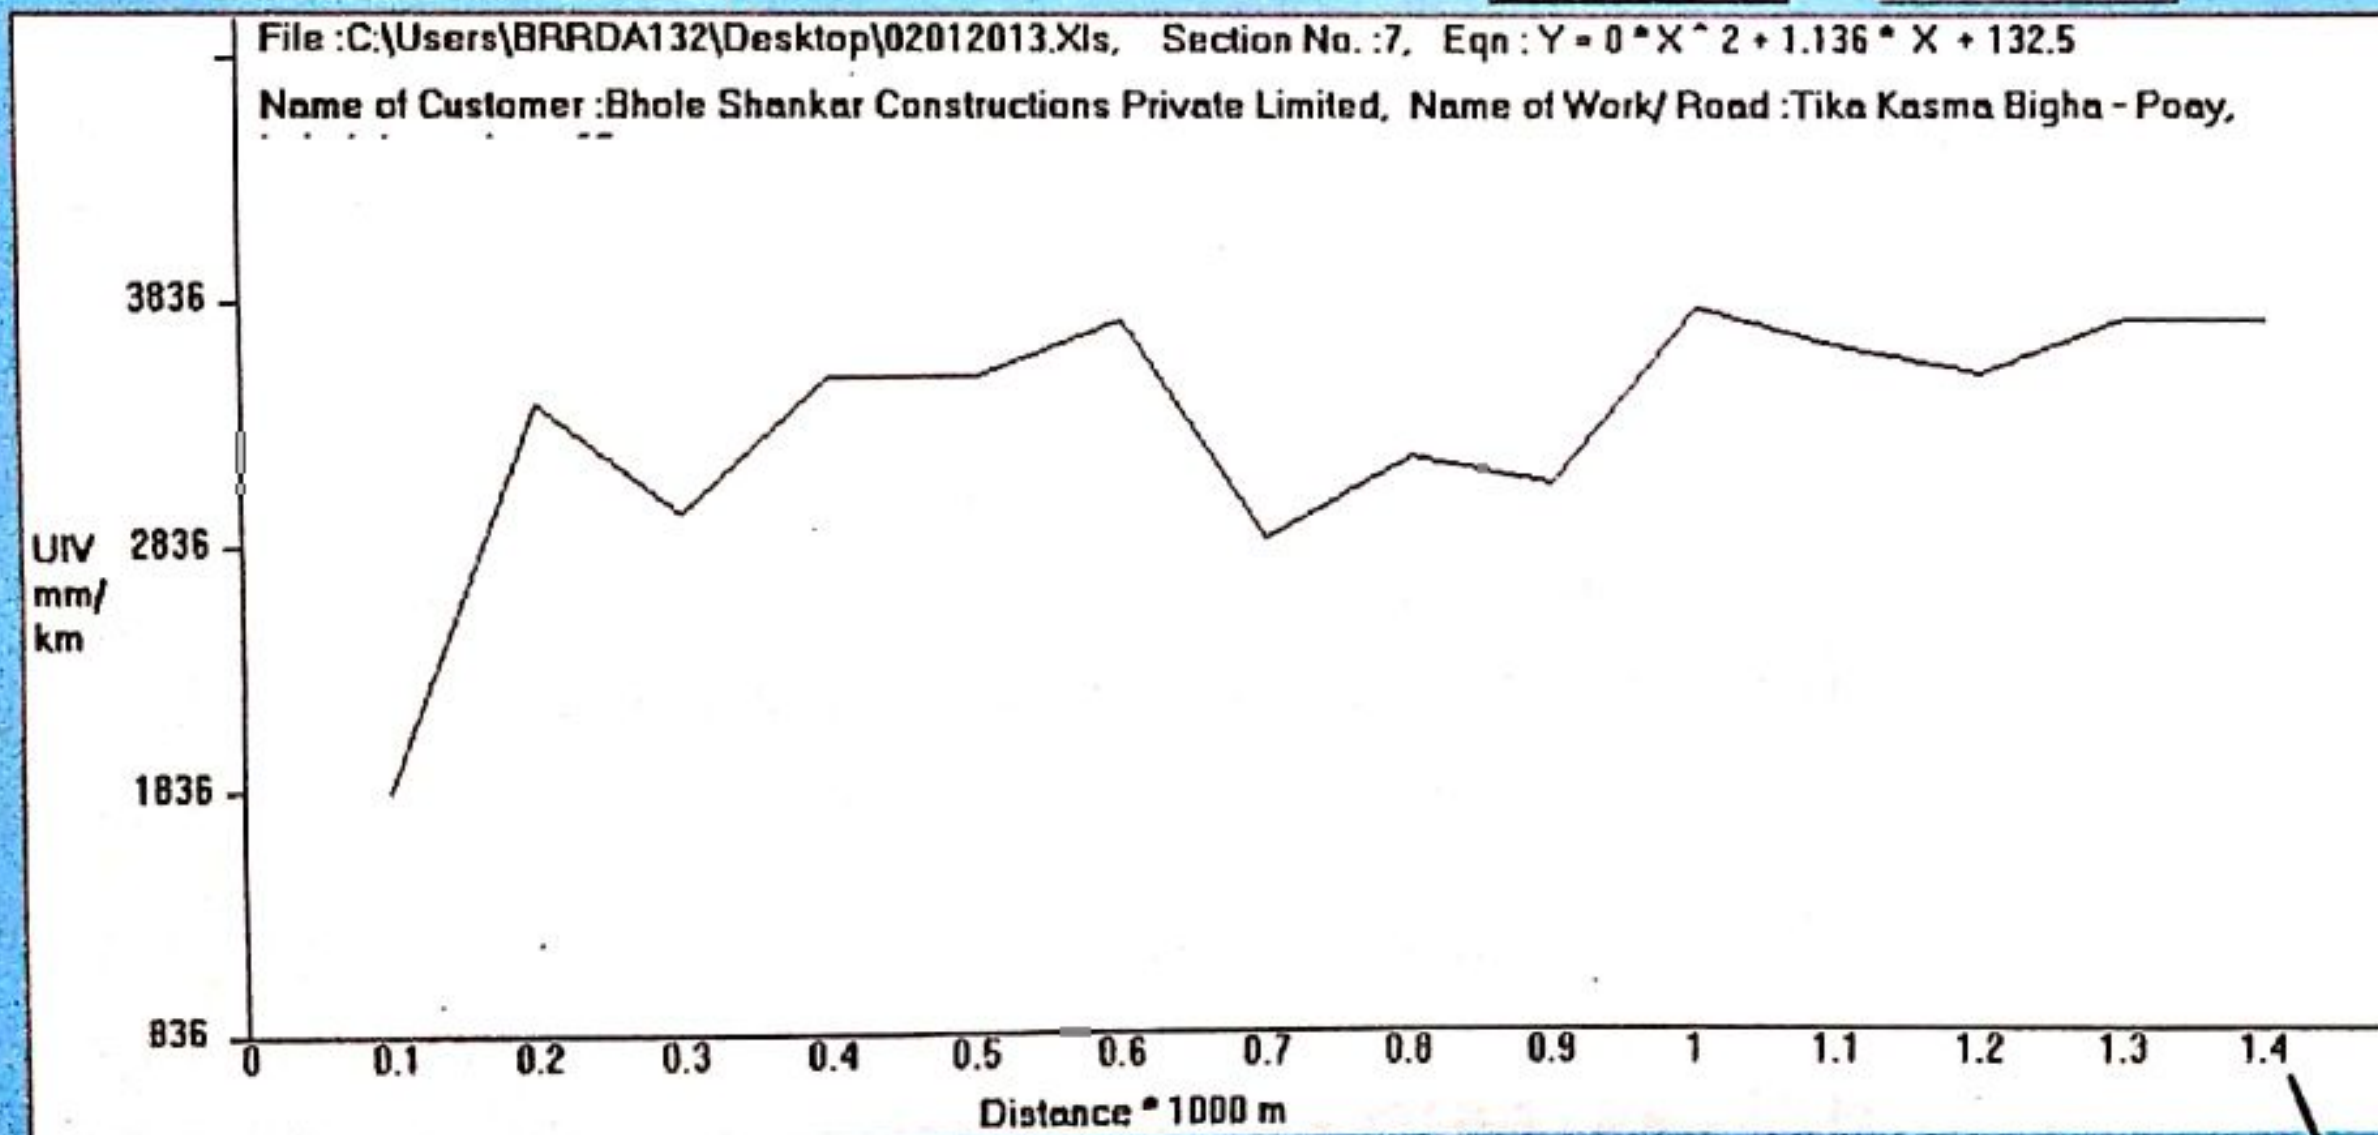

Portelli
22.12.20
J.E

22.12.20
A.E

22.12.20

**REPORT ON
BITUMEN CONTENT TEST
FOR THE PROPOSED
C/O**

**TIKA KASMA BIGHA TO POAY ROAD
UNDER SCHEME MR 3054
AGREEMENT NO -81 MBD/2019-20**

**SUBMITTED TO:
EXECUTIVE ENGINEER
RWD. WORKS DIVISION, AURANGABAD**

**AGENCY NAME :
BHOLE SHANKAR CONST. PVT LTD
AURANGABAD BIHAR**

**TESTING BY :
OM SAI TESTING AND RESEARCH
LABORATORY**

*2nd Floor Maheswari Complex Fraser Road Patna
PIN CODE 800001*

OM SAI TESTING AND RESEARCH LABORATORY

2nd floor maheswari complex fraser road patna

PIN CODE 800001

Ref..... Date

BITUMEN CONTENT TEST OF SEMI-DENSE BITUMINOUS CONCRETE

Name of Road : TIKA KASMA BIGHA TO POAY ROAD UNDER SCHEME MR 3054

Type Of Material : SEMI-DENSE BITUMINOUS CONCRETE

DATE OF COLLECTION 20-Nov-20

DATE OF TESTING 24-Nov-20

SAMPLE NO.		A1	A2	A3
Chainage & Section:				
S.NO.	Observations	1	2	3
1	Wt. of Mix taken before extration	500	500	500
2	Wt. of filter paper before extration	6.01	6.09	6.02
3	Wt. of Mix after extration	471.69	471.51	472.02
4	Wt. of filter paper after extration	6.81	6.98	6.71
5	Wt. of filler collected from extract after allowing for seting	1.89	1.96	1.820
6	Wt. of filler collected in filter paper	0.8	0.89	0.69
7	Wt. of Aggregate + Filler collected after extration	474.38	474.36	474.5
8	Percentage of Bitumen (in the Mix) $\frac{(A-G) \times 100}{A}$	5.12	5.128	5.09
Layer		Value		
		Avg. Value	5.1153%	
SEMI-DENSE BITUMINOUS CONCRETE				

Checked By

