

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, मोहनियाँ।

Email ID:- ee.rwdworkmohania@gmail.com

Mob:- 8986915825

पत्रांक.....6133130

मोहनियाँ/दिनांक.....20/03/2021

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मोहनियाँ।

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :- नई अनुरक्षण नीति-2018MR (3054)योजना के अंतर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054)योजना के अंतर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :- यथोक्त।

विश्वासभाजु


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मोहनियाँ।
19.3.21

FORM GFR 19-A

(See Government of India's Decision (I) below Rule-150)

Form of Utilization Certificate up to 19 March 2021


Sl.No	Name of Scheme	Sanction No.&Date With Amount (In lace Rs.)	Amount Received (In lace Rs.)	Particulars
1	Construction of Rural roads Under MR	New Maintenance Policy-2018 MR (3054) BRRDA PATNA	7587.58770	Certified that out of Rs. 7587.58770 lakh of grants-in-aid sanctioned during the years 2020-21 In favor of EE,RWD works division mohania a sum of Rs. 6260.89485 lakh has been utilized for the purpose of MR (3054) Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 1326.69285 lakh remaining unutilized at the end of the period under report.
	Total:		7587.58770	

- 3 . Certified that I have satisfied my self that the conditions on which the grant-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was utilized for the purpose for which it was sanctioned.

Kind of Checks exercised:-

- lvi. Works have been supervised by Executive Engineer/ Superintending Engineer.
 - lvii. Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
 - lviii. Construction materials have been tested.
 - lix. Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/ Executive Engineer.
 - lx. All other caudal formalities have been observed.
- 4 . **Physical Progress achieved:-**
- xii. Construction of Road Works.
 - ii. Construction of CD works.

Divisional Accounts Officer
R.W.D, works Division
Mohania.


Executive Engineer
R.W.D, works Division
Mohania.


OFFICE OF EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, WORKS DIVISION, Mohania (KAIMUR)

Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)
Name of Works Division:- Mohania (Kaimur)

Sl no.	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	Awati (Rampur Banglo)			6	7	8	9	10	11	12	13	14	15	16	17	18	19
29		Mourth via Suthwan with link road	NEA220002238	5463/16.10.2019	13.400	583.86040	463.47991	121.67568	34M/BD/28.05.2020	21.02.2021	-	2461	25.00	5.01	0.00	0.00	463.47991	
Total					13.400	583.860	463.480	121.676							0.000	0.000	463.480	

Divisional Accounts Officer
Rural Works Department,
Works Division, Mohania,
(Kaimur)

Executive Engineer
Rural Works Department
Works Division, Mohania
(Kaimur)
19.3.21

Section of Road - Awari (Rampur Banglo) Mouth via Suthwan with link road

Date	Time	Section	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEG ORY	Latitude	Longitude	Event
18/3/21	17:37:0	No.									
18/3/21	17:37:23	22	0.1	270	10.1	2700	2549	G	25.348115	83.766347	Normal
18/3/21	17:38:0	22	0.1	330	10.1	3300	3075	G	25.348725	83.76682	Normal
18/3/21	17:38:0	22	0.1	320	10.1	3200	2987	G	25.349223	83.767423	Normal
18/3/21	17:38:32	22	0.1	270	10.1	2700	2549	G	25.349193	83.76842	Normal
18/3/21	17:38:32	22	0.1	330	20.2	3300	3075	G	25.349082	83.769393	Normal
18/3/21	17:38:32	22	0.1	280	20.2	2800	2636	G	25.349348	83.770285	Normal
18/3/21	17:39:8	22	0.1	280	20.2	2800	2636	G	25.349403	83.771347	Normal
18/3/21	17:39:8	22	0.1	250	20.2	2500	2373	G	25.349965	83.771835	Curve
18/3/21	17:39:43	22	0.1	240	20.2	2400	2286	G	25.350325	83.772727	Normal
18/3/21	17:40:0	22	0.1	310	20.2	3100	2900	G	25.35036	83.77372	Normal
18/3/21	17:40:18	22	0.1	310	20.2	3100	2812	G	25.350558	83.774578	Normal
18/3/21	17:41:0	22	0.1	250	10.1	2900	2724	G	25.35104	83.775218	Normal
18/3/21	17:41:0	22	0.1	210	30.3	2100	2023	G	25.350803	83.77616	Normal
18/3/21	17:41:0	22	0.1	240	30.3	2400	2286	G	25.350635	83.777103	Normal
18/3/21	17:41:29	22	0.1	270	30.3	2700	2549	G	25.350555	83.778147	Normal
18/3/21	17:41:29	22	0.1	280	20.2	2800	2636	G	25.350588	83.77914	Normal
18/3/21	17:42:0	22	0.1	310	20.2	3100	2900	G	25.350873	83.78	Normal
18/3/21	17:42:4	22	0.1	210	20.2	2100	2023	G	25.351768	83.78007	Curve
18/3/21	17:42:4	22	0.1	290	20.2	2900	2724	G	25.352002	83.780975	Normal
18/3/21	17:42:39	22	0.1	280	20.2	2800	2636	G	25.352123	83.781952	Normal
18/3/21	17:42:39	22	0.1	340	20.2	3400	3163	G	25.352123	83.782878	Normal
18/3/21	17:43:15	22	0.1	270	10.1	2700	2549	G	25.353022	83.783097	Normal
18/3/21	17:43:15	22	0.1	270	20.2	2700	2549	G	25.353878	83.783332	Normal
18/3/21	17:43:15	22	0.1	290	30.3	2900	2724	G	25.353527	83.784225	Normal
18/3/21	17:43:50	22	0.1	300	30.3	3000	2812	G	25.353093	83.78503	Normal
18/3/21	17:44:0	22	0.1	250	30.3	2500	2373	G	25.352838	83.78601	Normal
18/3/21	17:44:0	22	0.1	290	40.4	2900	2724	G	25.352685	83.787037	Normal
18/3/21	17:44:25	22	0.1	270	20.2	2700	2549	G	25.352638	83.787978	Normal
18/3/21	17:44:25	22	0.1	240	20.2	2400	2286	G	25.352803	83.789007	Normal
18/3/21	17:45:0	22	0.1	330	20.2	3300	3075	G	25.352442	83.78978	Curve
18/3/21	17:45:0	22	0.1	260	20.2	2600	2461	G	25.352322	83.790673	Normal
18/3/21	17:45:0	22	0.1	260	30.3	2600	2461	G	25.352355	83.792	Normal
18/3/21	17:45:0	22	0.1	260	30.3	2600	2461	G	25.35237	83.792642	Normal
18/3/21	17:45:0	22	0.1	260	30.3	2600	2461	G	25.352378	83.793047	Normal

$$Y = 0 \cdot X^2 + 0.877 \cdot X + 181.3$$

$$X = 2900$$

$$Y = 2724$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

Executive Engineer
R.V.D. Work Div. Mohania

ae of Road- Awati (Rampur Banglo) Mouth via Suthwan with link road

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEG ORY	Latitude	Longitude	Event
18/3/21	17:45:36	22	0.1	300	30.3	3000	2812	G	25.352395	83.793063	Normal
18/3/21	17:45:36	22	0.1	300	30.3	3000	2812	G	25.352808	83.795622	Normal
18/3/21	17:46:2	22	0.1	260	20.2	2600	2461	G	25.353235	83.796043	Normal
18/3/21	17:46:2	22	0.1	200	30.3	2000	1935	G	25.353252	83.796127	Normal
18/3/21	17:46:2	22	0.1	290	30.3	2900	2724	G	25.353053	83.797575	Normal
18/3/21	17:46:37	22	0.1	320	20.2	3200	2987	G	25.35332	83.799023	Normal
18/3/21	17:46:37	22	0.1	230	30.3	2300	2198	G	25.35333	83.799862	Normal
18/3/21	17:46:37	22	0.1	250	20.2	2500	2373	G	25.35332	83.799027	Normal
18/3/21	17:47:13	22	0.1	340	20.2	3400	3163	G	25.35182	83.799055	Normal
18/3/21	17:47:13	22	0.1	240	20.2	2400	2286	G	25.357143	83.799057	Normal
18/3/21	17:47:48	22	0.1	330	20.2	3300	3075	G	25.357212	83.799073	Normal
18/3/21	17:47:48	22	0.1	210	20.2	2100	2023	G	25.357378	83.799243	Normal
18/3/21	17:48:0	22	0.1	220	20.2	2200	2110	G	25.359722	83.799932	Normal
18/3/21	17:48:3	22	0.1	300	20.2	3000	2812	G	25.359738	83.79842	Normal
18/3/21	17:48:3	22	0.1	270	20.2	2700	2549	G	25.359772	83.798752	Normal
18/3/21	17:48:39	22	0.1	310	30.3	3100	2900	G	25.35982	83.798923	Normal
18/3/21	17:48:39	22	0.1	250	30.3	2500	2373	G	25.3597	83.79893	Normal
18/3/21	17:48:39	22	0.1	270	20.2	2700	2549	G	25.35974	83.799455	Normal
18/3/21	17:49:14	22	0.1	300	20.2	3000	2812	G	25.358965	83.806043	Normal
18/3/21	17:49:14	22	0.1	270	20.2	2700	2549	G	25.35912	83.806093	Normal
18/3/21	17:50:3	22	0.1	230	20.2	2300	2198	G	25.35903	83.807658	Normal
18/3/21	17:50:3	22	0.1	270	10.1	2700	2549	G	25.357875	83.808063	Normal
18/3/21	17:51:0	22	0.1	290	10.1	2900	2724	G	25.357503	83.808147	Normal
18/3/21	17:52:0	22	0.1	320	10.1	3200	2987	G	25.356553	83.808	Normal
18/3/21	17:52:3	22	0.1	260	10.1	2600	2461	G	25.356252	83.808652	Normal
18/3/21	17:54:0	22	0.1	340	10.1	3400	3163	G	25.35555	83.809697	Normal
18/3/21	17:54:25	22	0.1	240	20.2	2400	2286	G	25.355465	83.811548	Normal
18/3/21	17:54:25	22	0.1	310	20.2	3100	2900	G	25.354687	83.811093	Normal
18/3/21	17:54:25	22	0.1	240	30.3	2400	2286	G	25.35387	83.811177	Normal
18/3/21	17:55:0	22	0.1	320	20.2	3200	2987	G	25.35652	83.812727	Normal
18/3/21	17:55:0	22	0.1	240	20.2	2400	2286	G	25.35676	83.814345	Normal
18/3/21	17:55:35	22	0.1	340	20.2	3400	3163	G	25.35198	83.812037	Normal
18/3/21	17:55:35	22	0.1	240	20.2	2400	2286	G	25.35198	83.813935	Normal
18/3/21	17:55:35	22	0.1	290	20.2	2900	2724	G	25.35363	83.815787	Normal
18/3/21	17:56:11	22	0.1	310	20.2	3100	2900	G	25.349727	83.812457	Normal

Executive Engineer
R.W.D. Work Div. Mohania

ie of Road- Awati (Rampur Banglo) Mournth via Suthwan with link road

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEG ORY	Latitude	Longitude	Event
18/3/21	17:56:11	22	0.1	250	30.3	2500	2373	G	25.346425	83.81372	Normal
18/3/21	17:56:11	22	0.1	280	30.3	2800	2636	G	25.337552	83.81432	Normal
18/3/21	17:56:46	22	0.1	330	20.2	3300	3075	G	25.339475	83.812052	Normal
18/3/21	17:57:0	22	0.1	300	20.2	3000	2812	G	25.34117	83.8102	Curve
18/3/21	17:57:11	22	0.1	260	10.1	2600	2461	G	25.348597	83.817172	Normal
18/3/21	17:58:0	22	0.1	230	10.1	2300	2198	G	25.34752	83.81734	Normal
18/3/21	17:58:23	22	0.1	330	10.1	3300	3075	G	25.346632	83.817087	Normal
18/3/21	17:59:0	22	0.1	270	10.1	2700	2549	G	25.345785	83.816835	Normal
18/3/21	17:59:14	22	0.1	250	10.1	2500	2373	G	25.345673	83.816868	Normal
18/3/21	18:0:13	22	0.1	280	10.1	2800	2636	G	25.344653	83.815875	Normal
18/3/21	18:0:48	22	0.1	250	10.1	2500	2373	G	25.344123	83.815505	Normal
18/3/21	18:0:48	22	0.1	330	10.1	3300	3075	G	25.343455	83.802342	Normal
18/3/21	18:0:48	22	0.1	280	20.2	2800	2636	G	25.343962	83.81501	Curve
18/3/21	18:1:24	22	0.1	250	20.2	2500	2373	G	25.34274	83.814342	Curve
18/3/21	18:1:24	22	0.1	260	20.2	2600	2461	G	25.344403	83.812672	Normal
18/3/21	18:1:59	22	0.1	290	30.3	2900	2724	G	25.34607	83.81434	Normal
18/3/21	18:1:59	22	0.1	310	30.3	3100	2900	G	25.339405	83.80601	Normal
18/3/21	18:1:59	22	0.1	220	30.3	2200	2110	G	25.337745	83.809343	Normal
18/3/21	18:2:34	22	0.1	280	30.3	2800	2636	G	25.341748	83.804343	Normal
18/3/21	18:3:0	22	0.1	310	10.1	3100	2900	G	25.337777	83.812053	Normal
18/3/21	18:3:0	22	0.1	270	10.1	2700	2549	G	25.339637	83.81389	Normal
18/3/21	18:3:0	22	0.1	300	20.2	3000	2812	G	25.342547	83.814868	Normal
18/3/21	18:3:0	22	0.1	250	20.2	2500	2373	G	25.346145	83.809818	Normal
18/3/21	18:3:5	22	0.1	290	20.2	2900	2724	G	25.347977	83.811505	Normal
18/3/21	18:3:5	22	0.1	320	10.1	3200	2987	G	25.344978	83.816645	Normal
18/3/21	18:3:5	22	0.1	300	20.2	3000	2812	G	25.344978	83.816645	Normal
18/3/21	18:20:38	23	0.1	320	10.1	3200	2987	G	25.359827	83.808013	Normal
18/3/21	18:21:0	23	0.1	240	20.2	2400	2286	G	25.360597	83.808552	Normal
18/3/21	18:21:14	23	0.1	320	20.2	3200	2987	G	25.361465	83.808888	Normal
18/3/21	18:21:14	23	0.1	290	10.1	2900	2724	G	25.362362	83.808888	Normal
18/3/21	18:21:49	23	0.1	320	20.2	3200	2987	G	25.363262	83.80867	Normal
18/3/21	18:22:0	23	0.1	220	20.2	2200	2110	G	25.36412	83.808502	Normal
18/3/21	18:22:0	23	0.1	300	20.2	3000	2812	G	25.365058	83.8084	Normal
18/3/21	18:22:23	23	0.1	240	20.2	2400	2286	G	25.365942	83.808332	Normal
18/3/21	18:22:23	23	0.1	290	20.2	2900	2724	G	25.366847	83.808198	Normal

Executive Engineer
R.W.D. Work Div. Mihanika

ae of Road - Awati (Rampur Banglo) Mounth via Suthwan with link road

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEG ORY	Latitude	Longitude	Event
18/3/21	18: 23: 0	23	0.1	240	20.2	2400	2286	G	25.36776	83.80808	Normal
18/3/21	18: 23: 0	23	0.1	300	20.2	3000	2812	G	25.368677	83.807962	Normal
18/3/21	18: 23: 34	23	0.1	290	20.2	2900	2724	G	25.3696	83.807862	Normal
18/3/21	18: 24: 9	23	0.1	240	10.1	2400	2286	G	25.370297	83.807693	Normal
18/3/21	18: 37: 20	24	0.1	310	10.1	3100	2900	G	25.353232	83.790892	Normal
18/3/21	18: 37: 20	24	0.1	240	20.2	2400	2286	G	25.354127	83.79079	Normal
18/3/21	18: 37: 20	24	0.1	240	20.2	2400	2286	G	25.355003	83.790892	Normal
18/3/21	18: 38: 0	24	0.1	290	20.2	2900	2724	G	25.355927	83.790757	Normal
18/3/21	18: 38: 0	24	0.1	240	10.1	2400	2286	G	25.356802	83.79074	Curve
18/3/21	18: 39: 4	24	0.1	220	10.1	2200	2110	G	25.357458	83.791228	Normal
18/3/21	18: 47: 32	25	0.1	230	20.2	2300	2198	G	25.352735	83.783972	Normal
18/3/21	18: 47: 32	25	0.1	250	20.2	2500	2373	G	25.352038	83.78468	Normal
18/3/21	18: 47: 32	25	0.1	290	30.3	2900	2724	G	25.351395	83.785302	Normal
18/3/21	18: 48: 0	25	0.1	320	30.3	3200	2987	G	25.35066	83.786027	Normal
18/3/21	18: 48: 6	25	0.1	250	30.3	2500	2373	G	25.350025	83.786632	Normal
18/3/21	18: 48: 6	25	0.1	260	30.3	2600	2461	G	25.349305	83.787322	Normal
18/3/21	18: 48: 6	25	0.1	250	30.3	2500	2373	G	25.348673	83.787945	Normal
18/3/21	18: 48: 41	25	0.1	300	30.3	3000	2812	G	25.347973	83.788618	Normal
18/3/21	18: 48: 41	25	0.1	270	40.4	2700	2549	G	25.34728	83.789292	Normal
18/3/21	18: 49: 0	25	0.1	260	30.3	2600	2461	G	25.346573	83.789998	Normal
18/3/21	18: 49: 17	25	0.1	220	10.1	2200	2110	G	25.345895	83.790638	Normal
18/3/21	18: 49: 17	25	0.1	320	20.2	3200	2987	G	25.345197	83.791347	Normal
18/3/21	18: 49: 52	25	0.1	280	30.3	2800	2636	G	25.344568	83.791952	Normal
18/3/21	18: 51: 2	25	0.1	220	10.1	2200	2110	G	25.343818	83.792693	Normal
18/3/21	18: 51: 2	25	0.1	300	10.1	3000	2812	G	25.343187	83.793298	Normal
18/3/21	18: 51: 38	25	0.1	260	20.2	2600	2461	G	25.342465	83.793988	Normal
18/3/21	18: 51: 38	25	0.1	240	30.3	2400	2286	G	25.341825	83.794612	Normal
18/3/21	18: 52: 0	25	0.1	300	30.3	3000	2812	G	25.34112	83.795302	Normal
18/3/21	18: 52: 13	25	0.1	290	10.1	2900	2724	G	25.340607	83.79569	Normal
18/3/21	18: 52: 13	25	0.1	320	10.1	3200	2987	G	25.344112	83.797395	Normal
Total Length			13.400								

Executive Engineer
R.W.D. Work Div. Mohania

Name of Customer : Shushil Kumar
 Name of Work/ Road : Awati (Rampur Banglo) Mounth
 Lab Job number : 22
 Date : 19-03-2021
 Section No. : 22

Test Date : 18-03-2021
 Machine No : 405
 Start S No : 2412
 Start E No : 2506
 Weather : Normal
 Start Location : 25.34912, 83.7
 End Location : 25.34438, 83.6
 Road Name : Awati (Rampur Banglo) Mounth
 Road Type : (R) RURAL ROAD
 Side : Paragath
 UV Range : 935 To 4000 mm/km
 Dist Range : 0 To 96 0.1 - 1000 m
 Equation : $Y = 0 \cdot X^2 + 0.877 \cdot X + 181.3$


Print Generate Report and Graph

Redraw Graph

Map View

File : E:\Steco\19030818.Xls, Section No. 22, Eqn : $Y = 0 \cdot X^2 + 0.877 \cdot X + 181.3$

Name of Customer : Shushil Kumar, Name of Work/ Road : Awati (Rampur Banglo) Mounth via Suthwan with link Road.

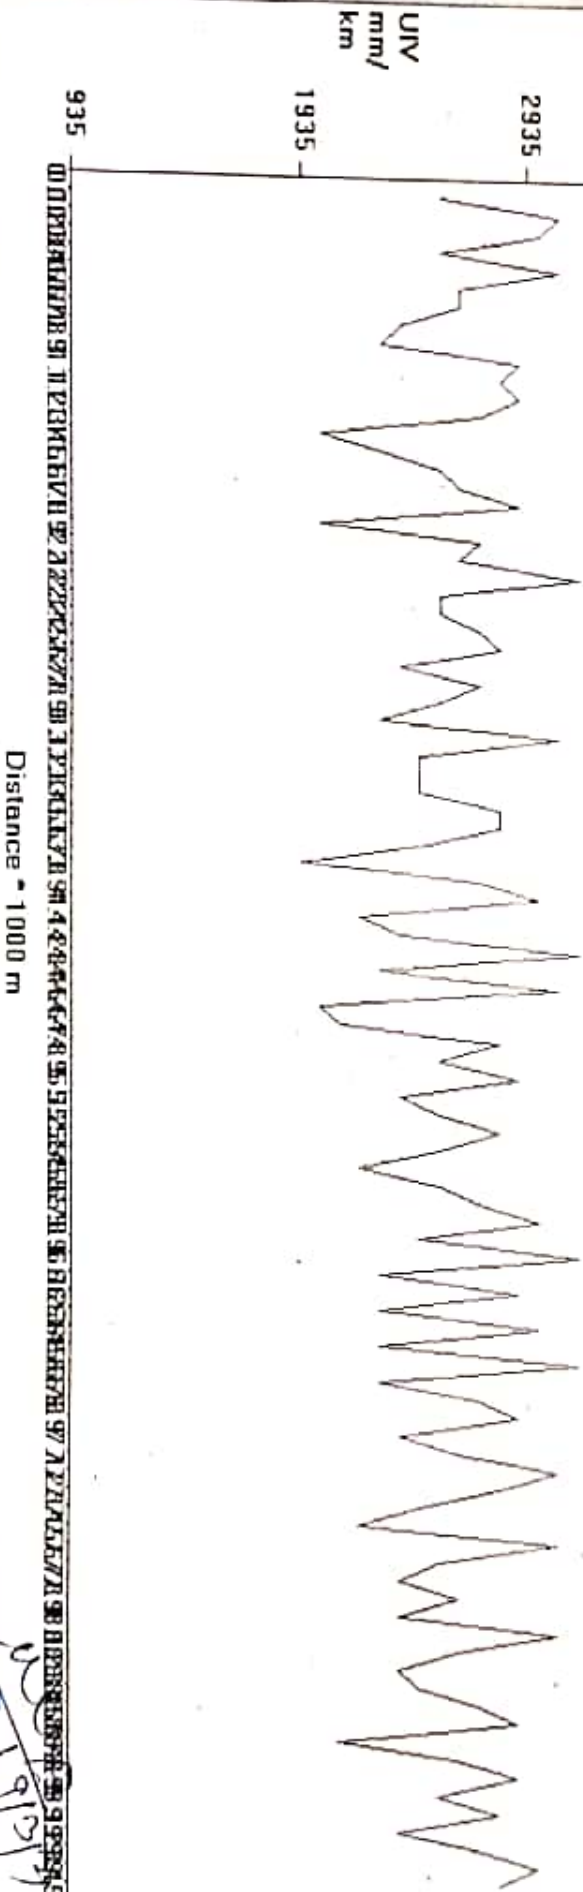

Excavation Engineer
 R.W.D. Work Div. Mohania

Name of Customer : Shushil Kumar
Name of Work/ Road : Awati (Rampur Banglo) Mouth
Lab Job number : 23
Date : 18-03-2021
Section No. : 23

Test Date : 18-03-2021
Machine No. : 405
Start S No. : 2507
Start E No. : 2519
Weather : Normal
Start Location : 25.26983, 83.8
End Location : 25.37030, 83.8
Road Name : Awati (Rampur Banglo) Mouth
Road Type : (R) RURAL ROAD
Side : Ramgarh
Interval :
U/V Range : 1110 To 4000 mm/km
Dist Range : 0 To 14 101 - 1000 m
Equation : $Y = 0 \cdot X^2 + 0.877 \cdot X + 181.3$


Print
 Generate Report and Graph

Redraw Graph

Map View

File : E:\Steco\19030818.Xls. Section No. : 23. Eqn : $Y = 0 \cdot X^2 + 0.877 \cdot X + 181.3$

Name of Customer : Shushil Kumar, Name of Work/ Road : Awati (Rampur Banglo) Mouth via Suthwan with link Road.

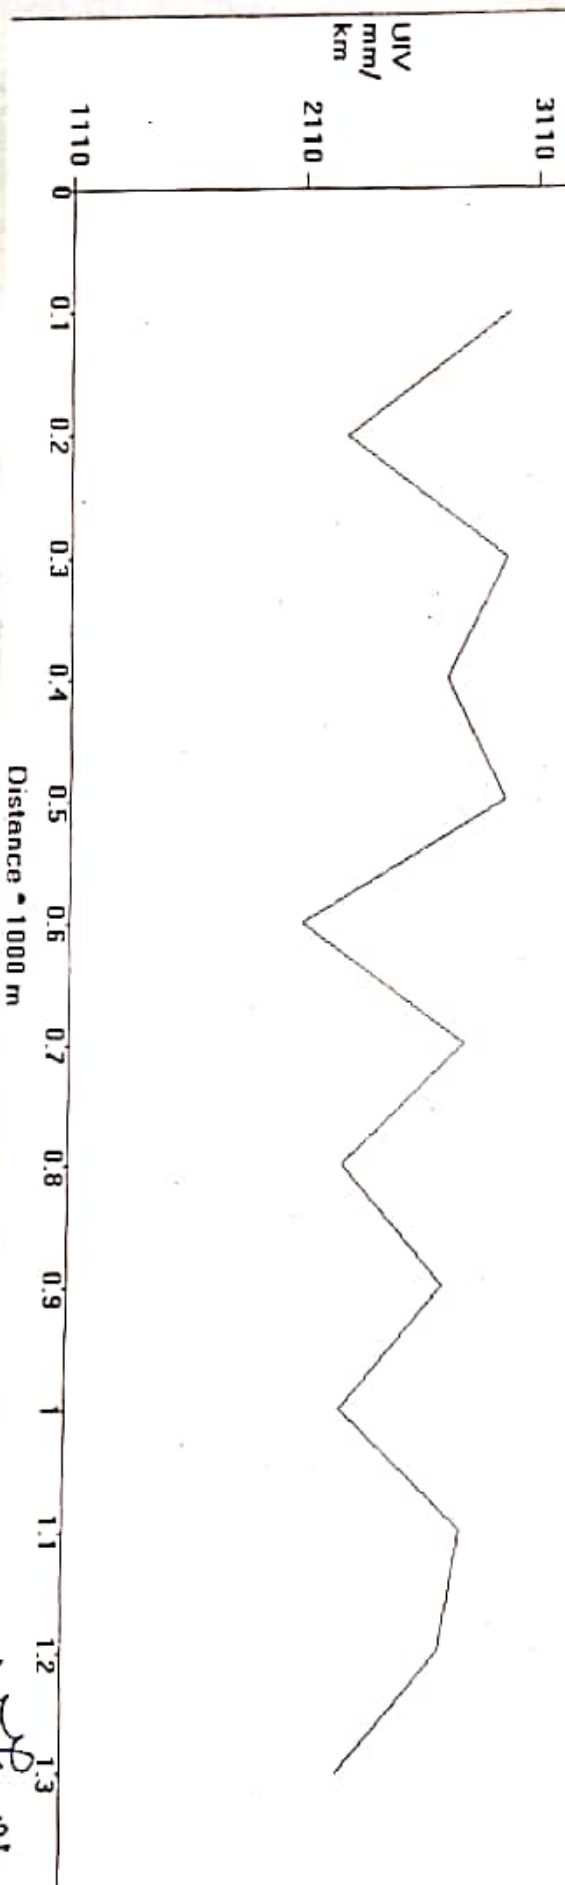

EXECUTIVE ENGINEER
 R.A.W.D. WORK DIV. MOHANIA

Name of Customer : Shushil Kumar
 Name of Work / Road : Awati (Rampur Banglo) Mouth
 Lab Job number : 24
 Date : 18-03-2021
 Section No. : 24

Test Date : 18-03-2021
 Machine No : 405
 Start S No : 2520
 Start E No : 2525
 Weather : Normal
 Start Location : 25.35323, 83.7
 End Location : 25.35746, 83.7
 Road Name : Awati (Rampur Banglo) Mouth
 Road Type : (R) RURAL ROAD
 Side : Ramgarh
 UIV Range : 1110 To 4000
 Dist Range : 0 To 0.7
 Equation : $Y = 0 \cdot X^2 + 0.877 \cdot X + 181.3$
 Interval : 1000 mm/km
 To 1000 m

Print


Generate Report and Graph

Redraw Graph

Map View

File : E:\Stereo\19030818 Xls. Section No. : 24. Eqn : $Y = 0 \cdot X^2 + 0.877 \cdot X + 181.3$

Name of Customer : Shushil Kumar. Name of Work / Road : Awati (Rampur Banglo) Mouth via Suthwan with link Road.

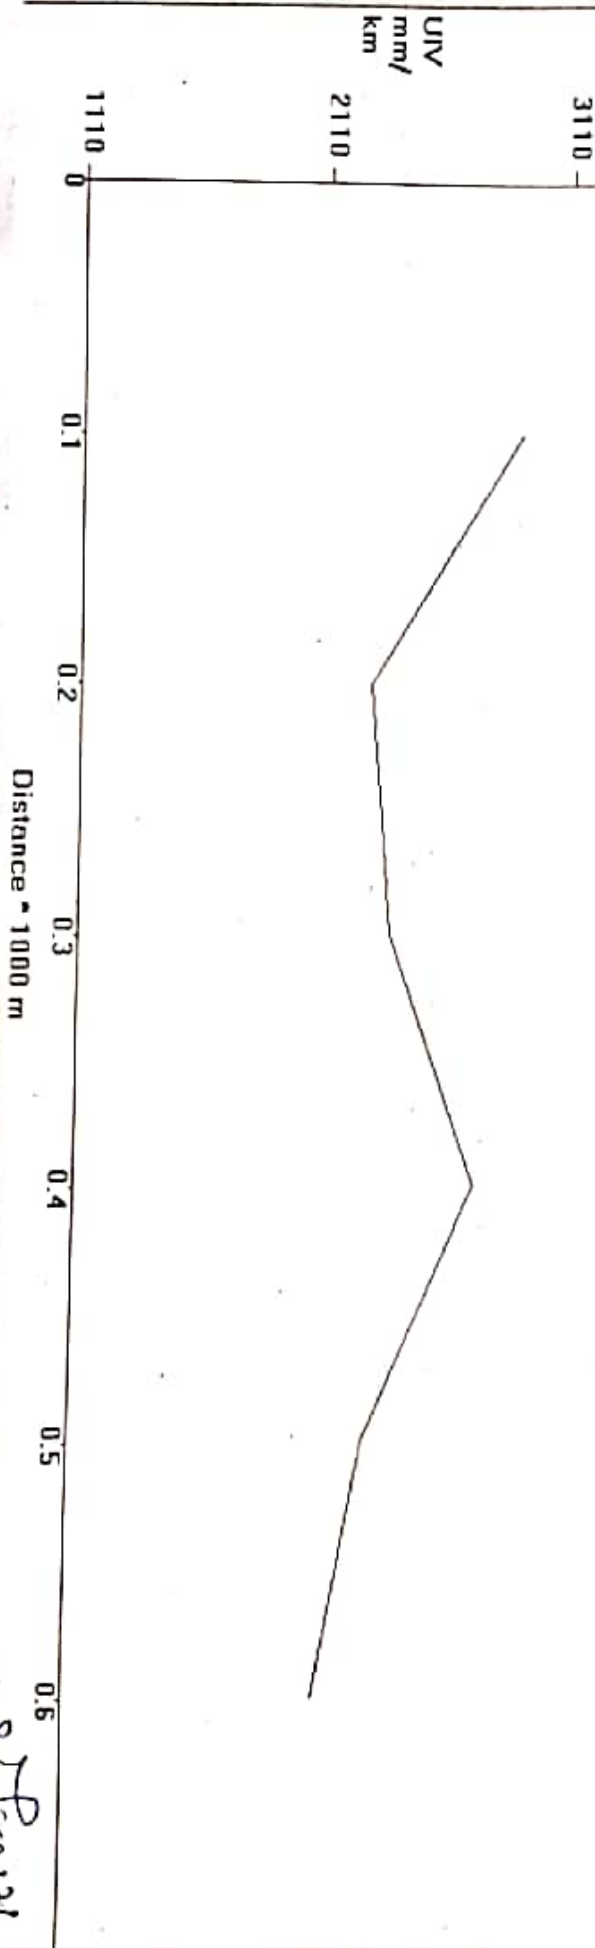

Excavating Engineer
 R.V.D. Work Div. Mohania

Name of Customer :	Shushil Kumar
Name of Work / Road :	Awali (Rampur Banglo) Mouth
Lab Job number :	25
Date :	18-03-2021
Section No. :	25

Test Date :	18-03-2021	Road Name :	Awali (Rampur Banglo) Mouth
Machine No :	405	Road Type :	(R) RURAL ROAD
Start S No :	2526	Side :	Remgarh
Start E No :	2545	Interval	
Weather :	Normal	UJV Range :	1110 To 4000 mm/km
Start Location :	25.35274, 83.7	Dist Range :	0 To 2.1 0.1 - 1000 m
End Location :	25.34411, 83.7	Equation :	$Y = 0 - X^2 + 0.877 \cdot X + 181.3$


Print Generate Report and Graph

Redraw Graph

Map View

File : E:\Steco\19030818.Xls, Section No : 25, Egn : $Y = 0 - X^2 + 0.877 \cdot X + 181.3$

Name of Customer : Shushil Kumar, Name of Work / Road : Awali (Rampur Banglo) Mouth via Suthwan with link Road.

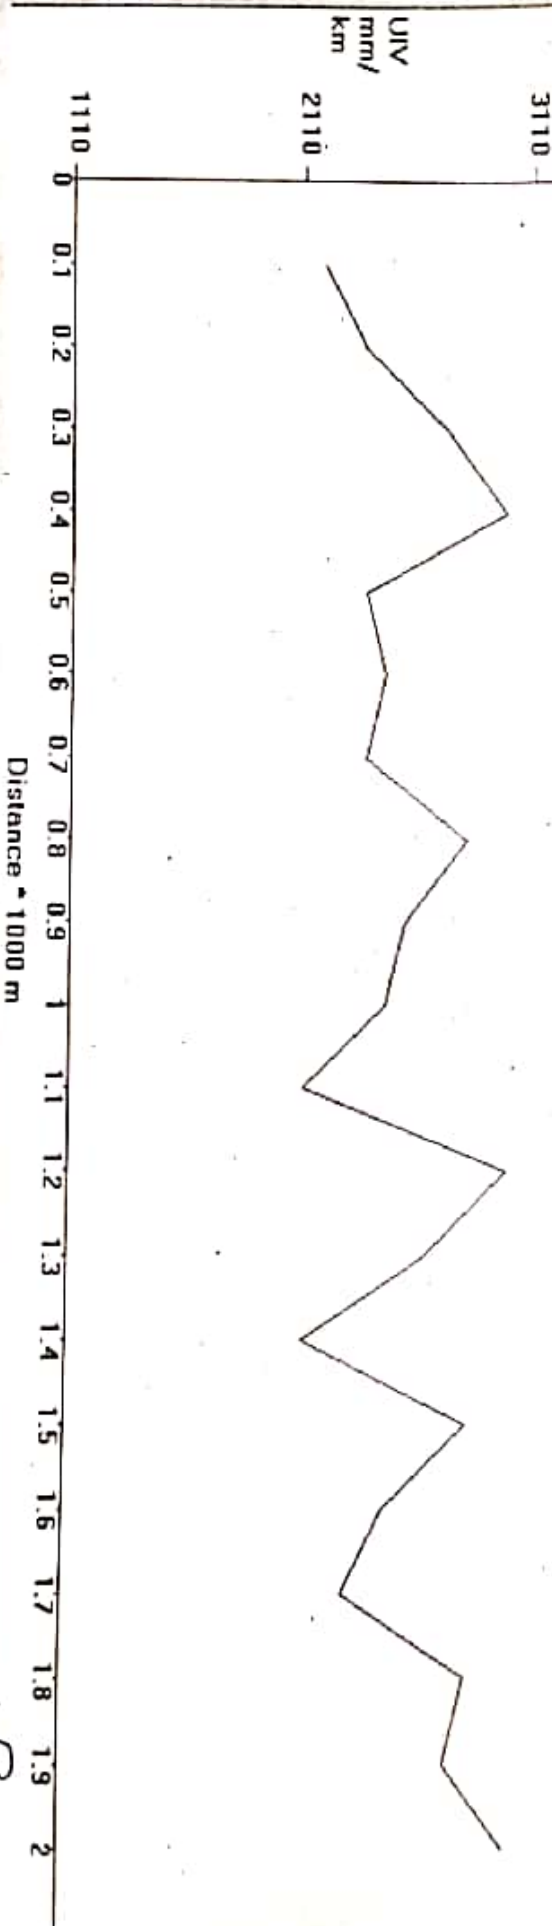

Distance * 1000 m

Executive Engineer
R.W.D. Work Div. Mohania
