

ABSTRACT

Road Name- Temporary Restoration of Road from NH T02 to Bela dullah

Block-DARBHANGA


RWD (W) DIVISION DARBHANGA -1

Road Actual Length - 1.60 KM

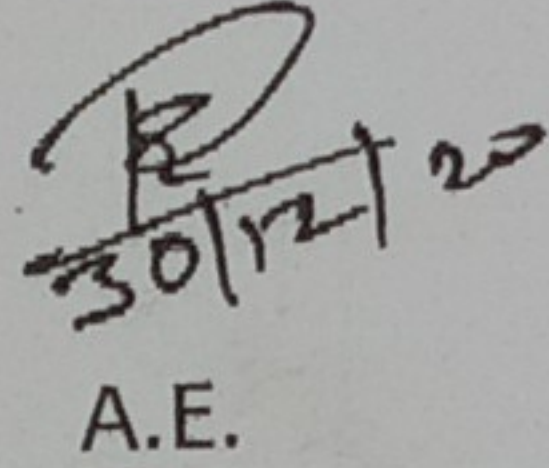
Effect Road Length - 47.25 M.

S.No.		UNIT	QUANTITY	RATE	AMOUNT (Rs)
1	Providing and filling bricks bats in ditches including cost of bricks bats and labour all complete job as per specification and direction of E/I .	CUM	26.325 27.000	1867.76	49169.25 50430
	Add G.S.T. 12 %				6052 59002.00
	Add 1 % Labor cess				504 492.00
	Seigniorage Fee @1063.00/cum x0.10				2870 27982.00
					59855 58,359.25

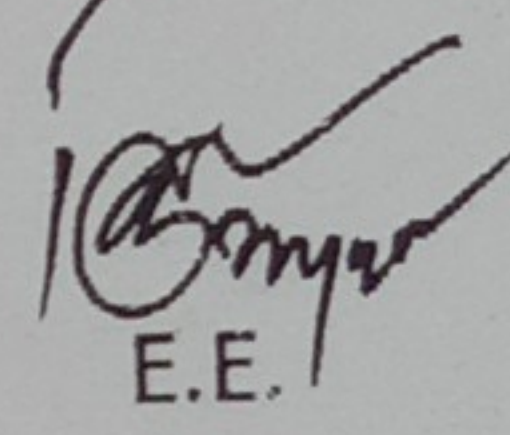
Rs - 58,359.25


J.E.

Work Section Darbhanga-2


A.E.

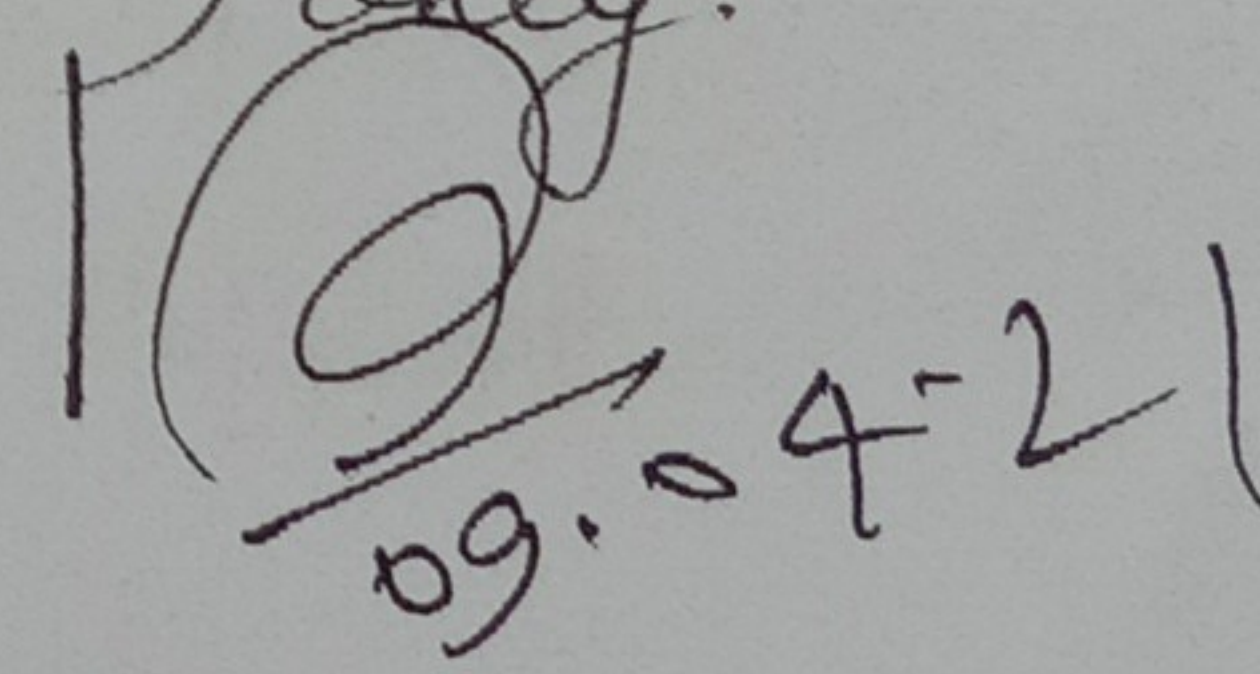
Work Sub-Division
Darbhanga


E.E.

RWD Darbhanga -1

कार्यपालक अभिर्भवा ग्राह कार वि. कार्य प्रमंडल - फुलपारा के पत्रांक 542 अनुं /
दिनांक 07/04/2021 के द्वारा समर्पित ऑय प्रविष्टि के आधार पर।

Post-Facto T/A for Rs - 58,359.25 (Rupees Fifty eight thousand three hundred fifty nine) only.


09.04.21

Superintending Engineer
RWD, Works Circle, Darbhanga
09/04/2021

Detailed Estimate for Temporary Restoration of NH T02 to Bela dullah for the year 2020
-21.


Block -Darbhanga


Total Restoration Length -47.25 M

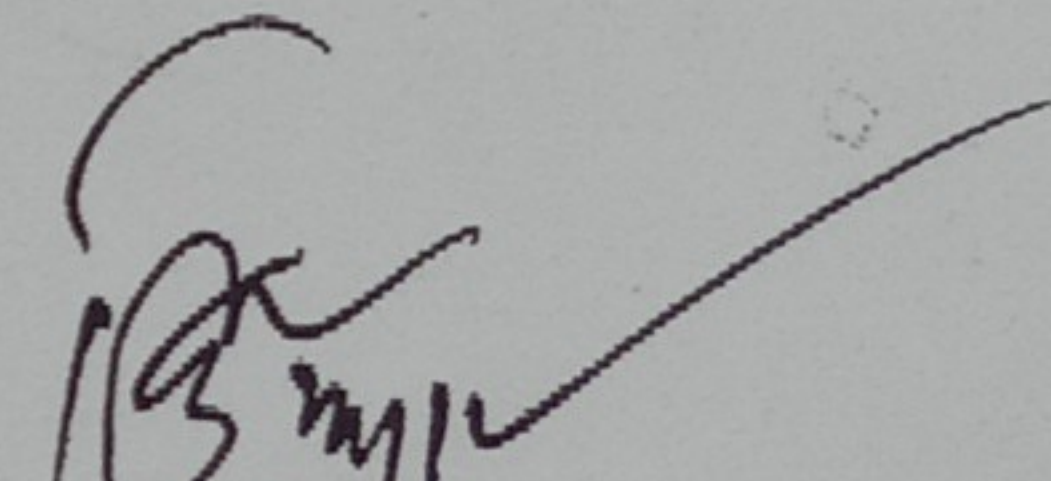
R.W.D.[W] Division -Darbhanga -1

Length -1.60 KM

S.N.	item	No.	Length (M)	Width(M)	Depth (M)(AV)	Quantity (cum)
1	Providing and filling bricks bats in ditches including cost of bricks bats and labour all complete job as per specification and direction of E/I .					
	Chainage in M					
	200	1	21.00	1.60	0.450	15.120
	to	1	18.00	1.35	0.250	6.075
		1	6.00	1.35	0.300	2.430
	500	1	2.25	1.50	1.000 ^{0.80}	3.375 ^{2.70}
	Total Qty.					27.000 26.325


J.E.


A.E.


E.E.

RWD(W) Division Darbhanga -1
