

कार्यालय
कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, बिक्रमगंज (रोहतास)।

पत्रांक 678 अगु / बिक्रमगंज / दिनांक 05/05/2021

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, बिक्रमगंज।

सेवा में,

नोडल पदाधिकारी, (MR-3054)
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:- नई अनुरक्षण नीति 2018 (MR-3054) योजनान्तर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि नई अनुरक्षण नीति 2018 (MR-3054) योजनान्तर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अनुलग्नक:-यथोक्त।

विश्वासभाजन

05/05/2021
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, बिक्रमगंज।
05/05/21

Requisition Format for Scheme Head- MR(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)
Name of Works Division:- Bikramganj

Sl. No.	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter no. & DT.	Administrative Approval		Agreement Amount (in Lakhs)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakhs)	Up-to-Date expenditure as per MIS (in Lakh)	Requisition against work done. (in Lakh)	Remarks
					Length	Amount of (in Lakhs)	Initial Rectification with Surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/19-20 Bikramganj/ 02	Bikramganj Nabwar PWD Road - Kharua Via Canal Service Road	10301002067	3054-04- 139/2019- 2065 DT.- 04.07.2019	4.24	214.8816	137.891	40.57937	54 MBD/ 2019-20 Date- 13.02.2020	07.10.2020	-	2686.59	25	5.1	0.00	0.00	137.891	BT Complete
2	MR-N/19-20 Bikramganj/ 03	From Bikramganj Nabwar P.W.D. Road to Maighra	10301001011	3054-04- 139/2019- 2065 DT.- 04.07.2019	1.5	44.7056	26.410	10.96643	55 MBD/ 2019-20 Date- 13.02.2020	07.10.2020	-	2572.06	25	5.1	0.00	0.00	26.410	BT Complete
3	MR-N/19-20 Bikramganj/ 03	Rohatas Jila antargat bikramganj pikhand me guljarbag- bikramganj se ghushiyo kalagaon tak path nirman	10301303001	3054-04- 139/2019- 2065 DT.- 04.07.2019	3.3	131.4156	78.398	31.46695	55 MBD/ 2019-20 Date- 13.02.2020	07.10.2020	-	2591.24	25	5.1	0.00	0.00	78.398	BT Complete

- 1 Signed Hard Copy and Soft Copy (in excel) of Recorded IRI is enclosed.
2 UP-to date Physical Progress has been Uploaded in MIS.


Executive Engineer
PWD, Works Div. Bikramganj
05/05/21
05/05/21

Name of Customer :	Dhanlaxmi Constuction
Name of Work/ Road :	Bikramganj Nawar PWD Path to
Lab Job number :	93
Date :	28-04-2021
Section No. :	93

Test Date :	28-04-2021	Road Name :	Bikramganj Nawar PWD Path to
Machine No. :	405	Road Type :	(R) RURAL ROAD
Start S No. :	1059	Side :	Bikramganj
Start E No. :	1077	Interval :	
Weather :	Normal	UIV Range :	935 To 4000 mm/km
Start Location :	25.25928, 84.1	Dist Range :	0 To 0.46
End Location :	25.26492, 84.1	Equation :	$Y = 0 * X^2 + 0.877 * X + 181.3$

Print


Generate Report and Graph

Redraw Graph

Map View

File : E:\Steco\29041216.Xls, Section No. : 93, Eqn : $Y = 0 * X^2 + 0.877 * X + 181.3$

Name of Customer : Dhanlaxmi Constuction, Name of Work/ Road : Bikramganj Nawar PWD Path to Kharua via Canal

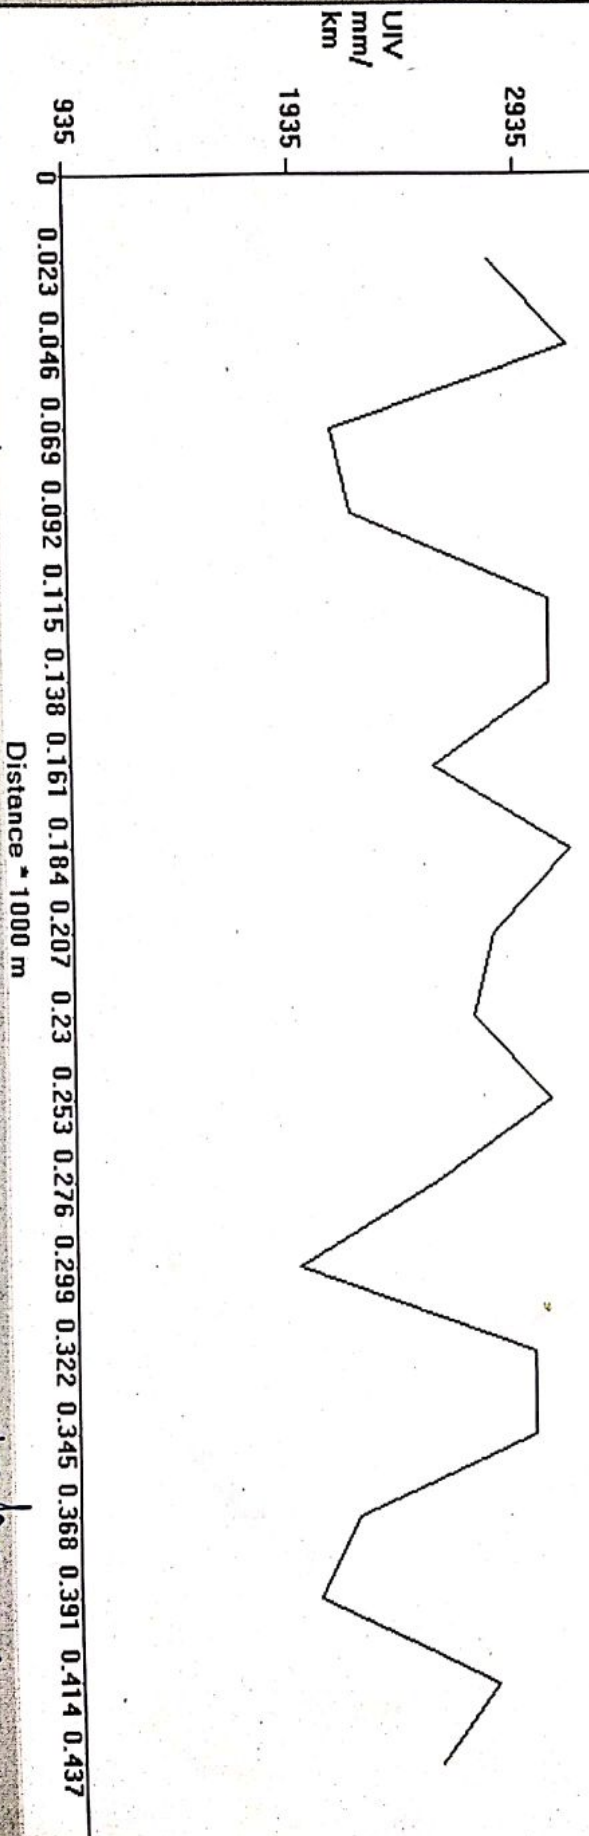

Adhikari
28-04-2021
1077

Hydro
28-04-2021
1077

Name of Customer : Dhanlaxmi Construction
Name of Work/ Road : Bikramganj Nawar PWD Path to
Lab Job number : 95
Date : 28-04-2021
Section No. : 95

Test Date : 28-04-2021
Machine No. : 405
Start S No. : 1078
Start E No. : 1084
Weather : Normal
Start Location : 25.25945, 84.1
End Location : 25.26460, 84.1
Road Name : Bikramganj Nawar PWD Path to
Road Type : (R) RURAL ROAD
Side : Bikramganj
Interval :
U/V Range : 1110 To 4000
Dist Range : 0 To 0.184
Equation : $Y = 0 * X^2 + 0.877 * X + 181.3$


Print Generate Report and Graph

Redraw Graph

Map View

File : E:\Steco\29041216.Xls. Section No. : 95, Eqn : $Y = 0 * X^2 + 0.877 * X + 181.3$

Name of Customer : Dhanlaxmi Construction, Name of Work/ Road : Bikramganj Nawar PWD Path to Kharua via Canal

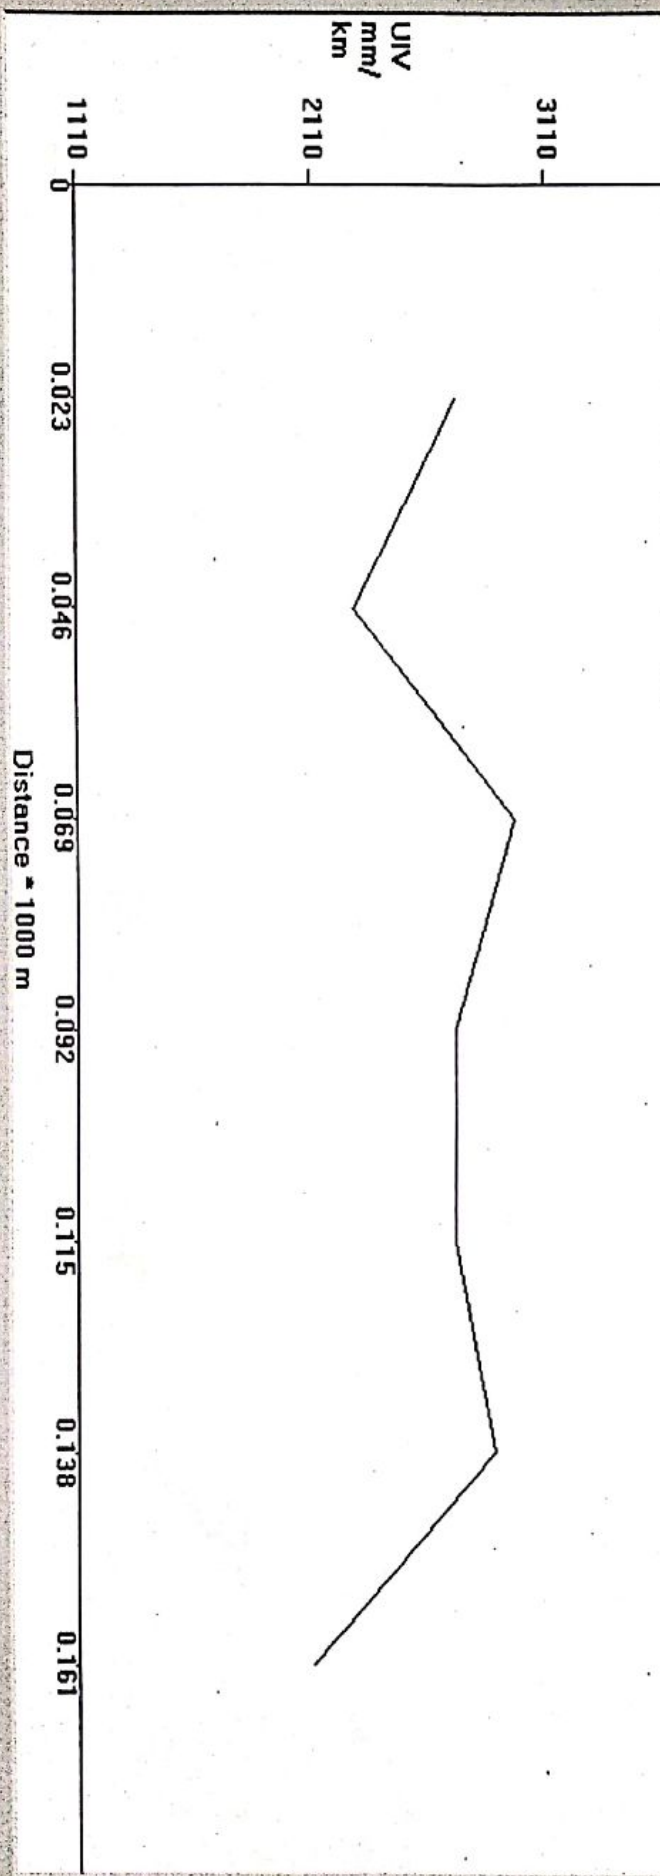

28-04-2021
150-1-V

U/V station
1110

Name of Customer :	Dhanlaxmi Construction
Name of Work/ Road :	Bikramganj Newar PWD Path to
Lab Job number :	96
Date :	28-04-2021
Section No. :	96

Test Date :	28-04-2021	Road Name :	Bikramganj Newar PWD Path to
Machine No. :	405	Road Type :	(R) RURAL ROAD
Start S No. :	1085	Side :	Bikramganj
Start E No. :	1097	Interval	
Weather :	Normal	U/V Range :	1023 To 4000 mm/km
Start Location :	25.26535, 84.1	Dist Range :	0 To 0.322
End Location :	25.27276, 84.1	Equation :	$Y = 0 * X^2 + 0.877 * X + 181.3$


Print Generate Report and Graph

Redraw Graph

Map View

File : E:\Steco\29041216.Xls, Section No. : 96, Eqn : $Y = 0 * X^2 + 0.877 * X + 181.3$

Name of Customer : Dhanlaxmi Construction, Name of Work/ Road : Bikramganj Newar PWD Path to Kharua via Canal

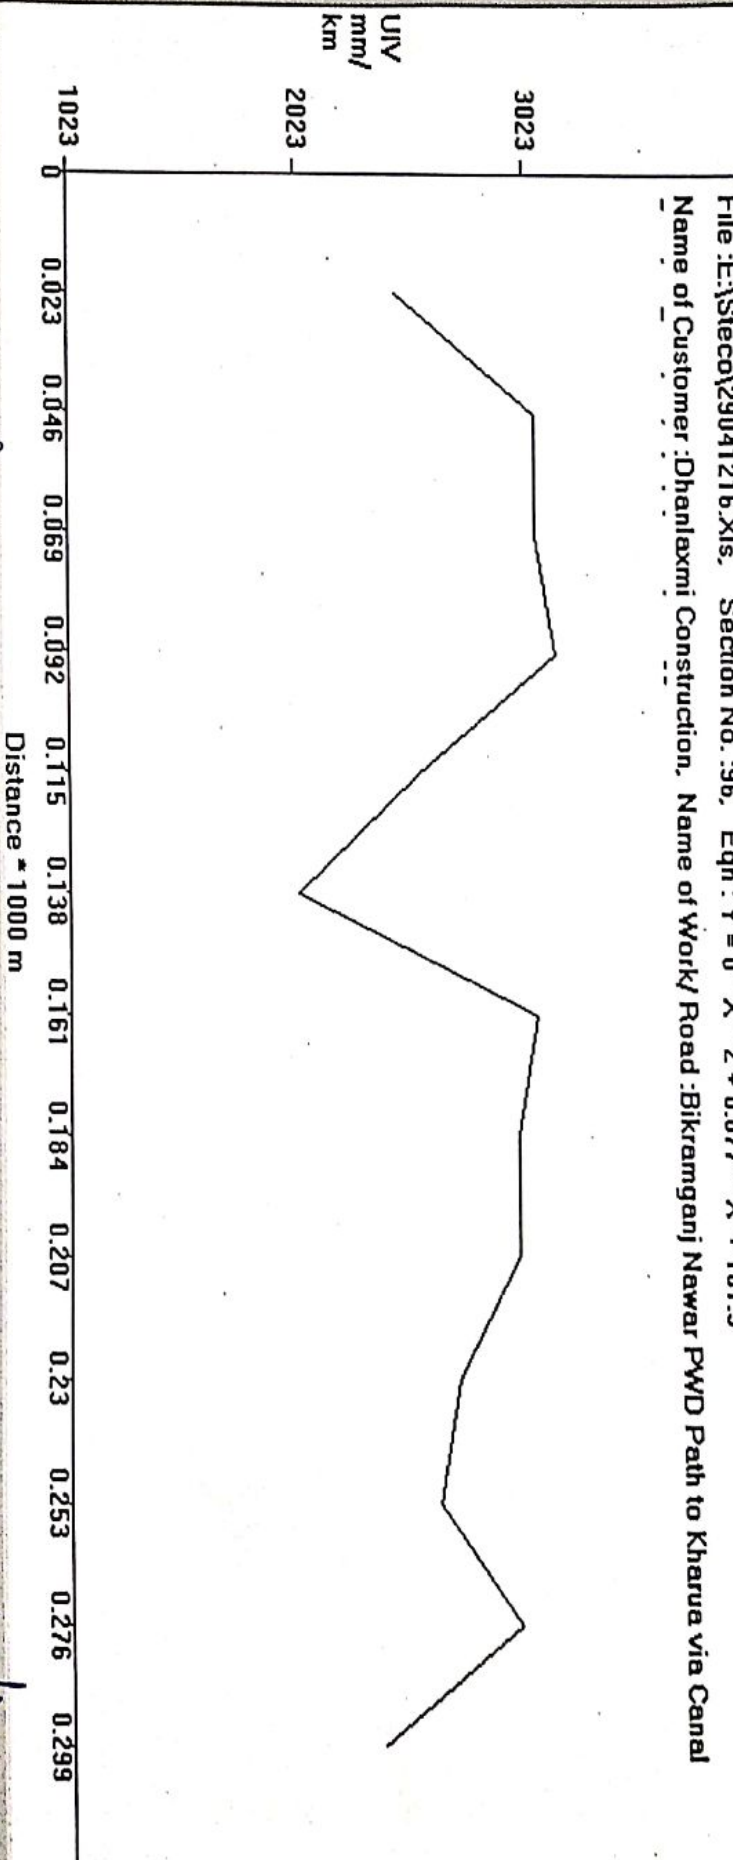

Handwritten signature and date: 28-04-2021

Handwritten signature and date: 28-04-2021

Name of Customer :	Dhanlexmi Construction
Name of Work/ Road :	Bikramganj Nawar PWD Path to
Lab Job number :	98
Date :	28-04-2021
Section No.	98

Test Date :	28-04-2021	Road Name :	Bikramganj Nawar PWD Path to
Machine No :	405	Road Type :	(R) RURAL ROAD
Start S No :	1098	Side :	Bikramganj
Start E No :	1100	Interval	
Weather :	Normal	UIV Range :	935 To 4000
Start Location :	25.24897, 84.1	Dist Range :	0 To 0.092
End Location :	25.23554, 84.1	Equation :	$Y = 0 * X^2 + 0.877 * X + 181.3$
			mm/km
			1000 m

Print


Generate Report and Graph

Redraw Graph

Map View

File : E:\Steco\29041216.Xls, Section No. : 98, Eqn : $Y = 0 * X^2 + 0.877 * X + 181.3$

Name of Customer : Dhanlexmi Construction, Name of Work/ Road : Bikramganj Nawar PWD Path to Kharua via Canal

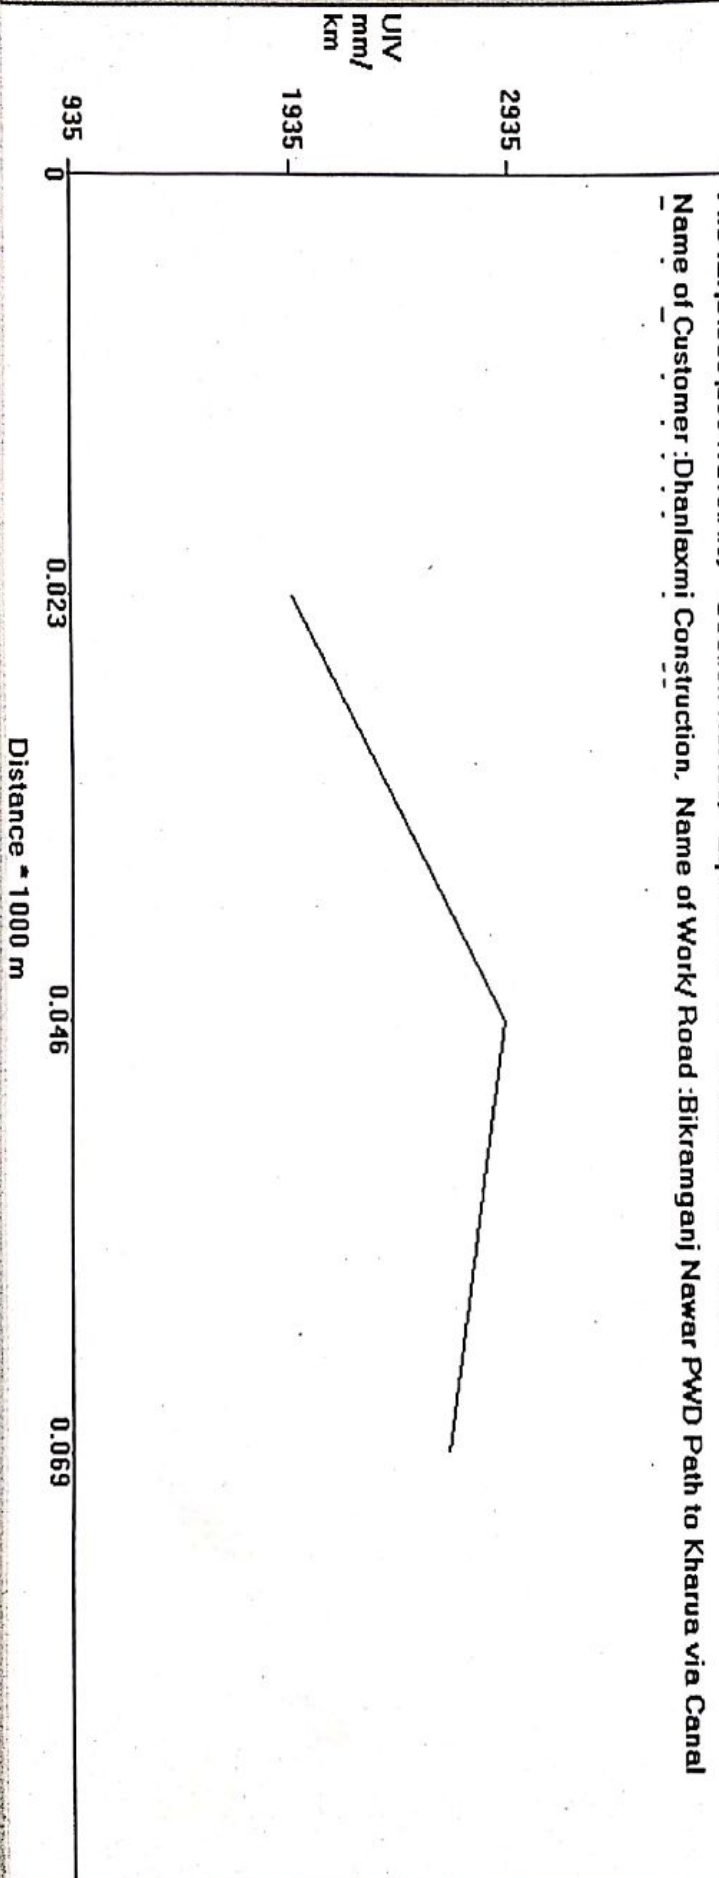

14.1.14.2021

1507

14.1.14.2021

1507

Name of Road - Bikramganj Nawar PWD Path to Kharua via Canal Service Road

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEG ORY	Latitude	Longitude	Event
28/4/21	13:25:23	93	0.1	300	10.1	3000	2812	G	25.25928	84.169882	Normal
28/4/21	13:25:58	93	0.1	340	10.1	3400	3163	G	25.261132	84.17005	Normal
28/4/21	13:28:55	93	0.1	220	10.1	2200	2110	G	25.26297	84.171902	Normal
28/4/21	13:28:55	93	0.1	230	20.2	2300	2198	G	25.264818	84.170587	Normal
28/4/21	13:28:55	93	0.1	330	20.2	3300	3075	G	25.266503	84.172438	Normal
28/4/21	13:29:30	93	0.1	330	30.3	3300	3075	G	25.251875	84.17429	Normal
28/4/21	13:29:30	93	0.1	270	30.3	2700	2549	G	25.256923	84.17597	Normal
28/4/21	13:29:30	93	0.1	340	30.3	3400	3163	G	25.265443	84.176488	Normal
28/4/21	13:30:5	93	0.1	300	10.1	3000	2812	G	25.263158	84.170263	Speed Breaker
28/4/21	13:30:41	93	0.1	290	20.2	2900	2724	G	25.25613	84.172825	Speed Breaker
28/4/21	13:30:41	93	0.1	330	30.3	3300	3075	G	25.252088	84.170315	Speed Breaker
28/4/21	13:30:41	93	0.1	270	20.2	2700	2549	G	25.254332	84.170893	Normal
28/4/21	13:31:16	93	0.1	200	30.3	2000	1935	G	25.264237	84.183115	Normal
28/4/21	13:31:16	93	0.1	320	30.3	3200	2987	G	25.25928	84.1831	Normal
28/4/21	13:31:16	93	0.1	320	30.3	3200	2987	G	25.264247	84.181637	Normal
28/4/21	13:31:51	93	0.1	230	10.1	2300	2198	G	25.26349	84.18077	Normal
28/4/21	13:41:51	93	0.1	210	20.2	2100	2023	G	25.26305	84.174745	Normal
28/4/21	13:41:51	93	0.1	300	20.2	3000	2812	G	25.25982	84.180925	Normal
28/4/21	13:42:26	93	0.1	270	10.1	2700	2549	G	25.26492	84.18283	Normal
28/4/21	13:45:43	95	0.1	290	20.2	2900	2724	G	25.259447	84.171548	Normal
28/4/21	13:45:43	95	0.1	240	20.2	2400	2286	G	25.258758	84.172108	Normal
28/4/21	13:46:18	95	0.1	320	30.3	3200	2987	G	25.25928	84.178308	Normal
28/4/21	13:46:18	95	0.1	290	30.3	2900	2724	G	25.266338	84.1721	Normal
28/4/21	13:46:18	95	0.1	290	30.3	2900	2724	G	25.25976	84.180937	Normal
28/4/21	13:46:54	95	0.1	310	20.2	3100	2900	G	25.25258	84.16706	Normal
28/4/21	13:47:29	95	0.1	220	10.1	2200	2110	G	25.264597	84.17968	Normal
28/4/21	13:54:36	96	0.1	260	20.2	2600	2461	G	25.265347	84.163	Normal
28/4/21	13:55:46	96	0.1	330	20.2	3300	3075	G	25.265823	84.162508	Normal
28/4/21	13:56:22	96	0.1	330	10.1	3300	3075	G	25.26487	84.163832	Normal
28/4/21	13:56:22	96	0.1	340	20.2	3400	3163	G	25.26088	84.164982	Normal
28/4/21	13:56:57	96	0.1	270	10.1	2700	2549	G	25.26061	84.164177	Normal
28/4/21	13:57:41	96	0.1	210	10.1	2100	2023	G	25.279795	84.164118	Normal
28/4/21	13:57:41	96	0.1	330	20.2	3300	3075	G	25.280992	84.159477	Normal
28/4/21	13:57:41	96	0.1	320	20.2	3200	2987	G	25.272603	84.16642	Normal
28/4/21	13:57:41	96	0.1	320	30.3	3200	2987	G	25.27764	84.163162	Normal
28/4/21	13:58:16	96	0.1	290	30.3	2900	2724	G	25.270275	84.164432	Normal
28/4/21	13:58:16	96	0.1	280	20.2	2800	2636	G	25.282968	84.164297	Normal
28/4/21	13:58:16	96	0.1	320	20.2	3200	2987	G	25.283078	84.16645	Normal
28/4/21	13:58:51	96	0.1	250	10.1	2500	2373	G	25.272757	84.16641	Normal
28/4/21	14:15:50	98	0.1	200	20.2	2000	1935	G	25.248968	84.172037	Normal
28/4/21	14:16:25	98	0.1	310	20.2	3100	2900	G	25.244185	84.17272	Normal
28/4/21	14:16:25	98	0.1	280	20.2	2800	2636	G	25.235543	84.175192	Normal
Total Length			4.200								

$$Y = 0 * X^2 + 0.877 * X + 181.3$$

$$X = 3100$$

$$Y = 2900$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

18/06/2021

45/05/2021
