

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल मसौढ़ी।

पत्रांक....४१...६३०१..... मसौढ़ी.

दिनांक ..10.5.21..

प्रेषक,

कार्यपालक अभियंता

ग्रामीण कार्य विभाग,

कार्य प्रमंडल मसौढ़ी

सेवा में,

नोडल पदाधिकारी,

नई अनुरक्षण निति-2018(3054)

ग्रामीण कार्य विभाग, बिहार पटना।


विषय:- नई अनुरक्षण निति-2018 शीर्ष 3054 के अंतर्गत वितीय वर्ष 2021-22 में व्यय हेतु आवंटन की मांग।

महाशय,

उपर्युक्त विषय के संबध में नई अनुरक्षण निति-2018 शीर्ष 3054 के अंतर्गत वितीय वर्ष 2021-22 में व्यय हेतु संलग्न विवरणी के अनुसार रु0 1,76,82,857 (एक करोड़ छिहत्तर लाख बयासी हजार आठ सौ संतावन) रुपये का आवंटन उपलब्ध करने की कृपा की जाए ताकि किये गये कार्यों का भुगतान किया जा सके।

अनुलग्नक: विहित प्रपत्र में अधियाचना।

विश्वासभाजन


कार्यपालक अभियंता

ग्रामीण कार्य विभाग, कार्य प्रमंडल मसौढ़ी।

Requisition Formate for Scheme Head - MR (3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works

Division : Masaurhi

Division : Masaurhi																						
Road Details				A A Details				Agreement Details														
SL no	Road Name	Batch No.	Project ID	Main Work Amount	Maintenance Amount	Emergency Amount	Total Amount	Total Length	AA Date	Main Work Amount	Maintenance	Date	Date Of Completion As per It no. 1145dt 24.03.2021(CEI RWD)	Ref.No.	Length	Value of IRI (in MM/Km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (In Lakh)	Upto Date expenditure as per MIS (In Lakh)	Requisition Against Work done (In Lakh)	Remarks
1	Construction of Special Repair of Masaurhi Pail road to Kazichak	RM/PA/MAS/1 9/0003	10100408080	27.08	10.35	0	37.43	1	24-Jun-19	20.915	8.3899	02-Nov-19	15.06.2021	14/SBD/ 19-2020	1	2328	25mm	5%	0	0	20.91500	Demand for Allotment will be Rs. 19.65687 due to work has been done in 790 meter rest 440 meter fresh pcc has been done by panchayat scheme
2	MORHARPUL - BIJAWAR (BR-26R-247)	RM/PA/MAS/1 9/0003	10100402041	37.32	11.3	0	48.62	1.23	24-Jun-19	26.78	10.749	02-Nov-19	15.06.2021	14/SBD/ 19-2020	1.23	3462.875	25mm	5%	0	0	19.65687	
3	MUSNAPAR MASAUDHI PATH - MAJHAULI (BR-26R-265)	RM/PA/MAS/1 9/0003	10100402043	46.76	17.37	0	64.13	1.79	24-Jun-19	38.297	16.467	02-Nov-19	15.06.2021	14/SBD/ 19-2020	1.79	2563.778	25mm	5%	0	0	38.29700	Demand for Allotment 400 Meter work has been done and 70 meter taken by Four lane Scheme.
4	MUSNAPAR MASAUDHI PATH - SEVDAHA (BR-26R-259)	RM/PA/MAS/1 9/0003	10100402047	16.02	4.02	0	20.04	0.47	24-Jun-19	10.154	3.5889	02-Nov-19	15.06.2021	14/SBD/ 19-2020	0.47	2267	25mm	5%	0	0	8.64170	
5	NADAWAN OTYARA - KASHINAGAR (BR-26R-248)	RM/PA/MAS/1 9/0003	10100402059	46.27	16.32	0	62.59	1.73	24-Jun-19	36.778	13.93	02-Nov-19	15.06.2021	14/SBD/ 19-2020	1.73	2430.889	25mm	5%	0	0	36.77800	
6	NADAWAN OTYARA ROAD - Sasaura (BR-26R-245)	RM/PA/MAS/1 9/0003	10100402061	27.73	9.13	0	36.86	0.88	24-Jun-19	20.824	7.2966	02-Nov-19	15.06.2021	14/SBD/ 19-2020	0.88	2428.222	25mm	5%	0	0	20.82400	
7	Spm Road to Bhargawan (BR2601)	RM/PA/MAS/1 9/0003	10100402134	40.09	15.45	0	55.54	1.5	24-Jun-19	31.716	13.358	02-Nov-19	15.06.2021	14/SBD/ 19-2020	1.5	2493.133	25mm	5%	0	0	31.71600	
				241.270	83.940	0	325.210	8.600		185.464	73.779				8.600	2472.866			0.000	0.000	176.82857	

1. Signed Hard Copy and Soft copy (in Excel) of recorded IRI is Enclosed
2. Up to Date Physical Progress has been Uploaded in MIS

EXECUTIVE ENGINEER
RURAL WORKS DEPARTMENT
WORKS DIVISION, MASAUHRI

10.05.21

NAME OF THE ROAD : MUSNAPAR MASAU RH I PATH TO SEWDHA

LENGTH OF THE ROAD : 0.40 KM

PACKAGE NO. : MR-N/19-20/MASAU RH I/01

DIVISION : MASAU RH I

BLOCK : DHANARUA

AGENCY : PATILPUTRA INFRA CONSTRUCTION PVT LTD

Date	Time	Section	Length	Bumps	Speed	OR	UIV	CATEGORY	IRI	Latitude	Longitude	Event	Y = 0 * X ^ 2 + 0.936 * X + 278.4		
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD					X = 2700		
8/5/21	9:31:0	90	0.1	230	0	2300	2431	G	3.34	25.39628	85.15707	Normal	Y = 2805		
8/5/21	9:31:23	90	0.1	170	30.3	1700	1869	G	2.64	25.396528	85.156127	Normal			
8/5/21	9:31:53	90	0.1	180	30.3	1800	1963	G	2.76	25.396698	85.15512	Normal			
8/5/21	9:32:20	90	0.1	270	30.3	2700	2805	G	3.79	25.39693	85.154123	Normal	(R) RURAL ROAD		
TOTAL			0.4	850	90.9	8500	9068		12.53	101.586436	340.62244		Good	Average	Poor
AVERAGE						2125	2267		3.1325				<4000	4001-5000	>5001

8/5/21
Assistant Engineer
 R.W.D. Sub-Division, Dhanarua

9/5/21
Executive Engineer
 R.W.D. Works Div, Masaurhi

Name of
 Construction: PATLUPUTRA INFRA CONST
 Repair of: MUSNAPAR MASAUHRI PATH
 Name of Work: MUSNAPAR MASAUHRI PATH
 Road:


Lab Job number:
 Date: 03-05-2021
 Section No.: 90

Test Date:	08-05-2021	Road Name:	ASAUHRI PATH TO SEWCHA
Machine No.:		Road Type:	(R) RURAL ROAD
Start S No.:		Side:	
Start E No.:		Interval	
Weather:		U/V Range:	863 To 4000 1000 mm/km
Start Location:		Dist Range:	0 To 0.5 0.1 - 1000 m
End Location:		Equation:	

Print
 Generate Report and Graph

File: C:\Users\SHAZID\Desktop\90.Xls, Section No.: 90, Eqn:
 Name of Customer: PATLUPUTRA INFRA CONST PVT LTD, Name of Work/ Road: MUSNAPAR MASAUHRI PATH

Redraw Graph
 Map View

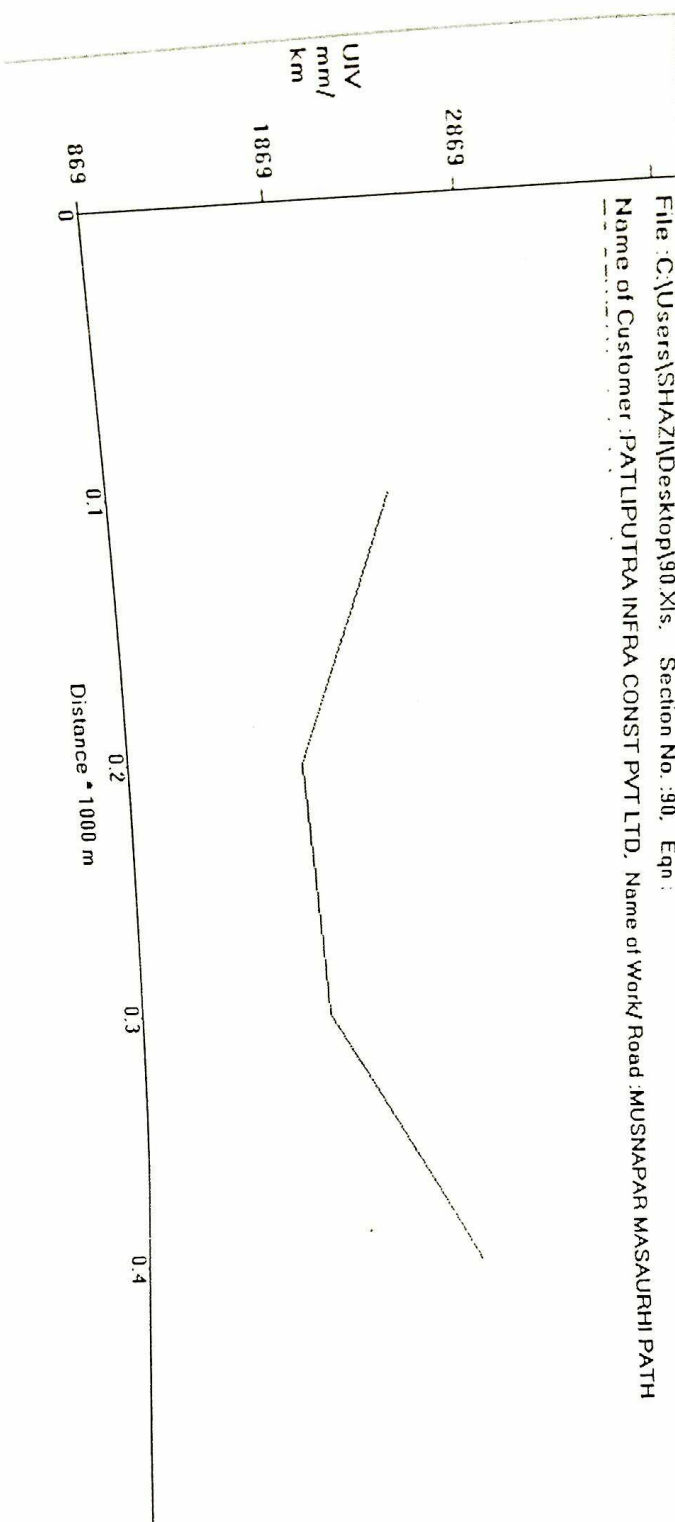

R.W.D. Works Div. Masaurhi
 Executive Engineer
 21/5/21
