

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, रक्सौल।

पत्रांक 533 3780

रक्सौल, / दिनांक 18.05.2021

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास एजेन्सी,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय :- शीर्ष-3054 अन्तर्गत बिहार ग्रामीण पथ अनुक्षण नीति-2018 के तहत आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपर्युक्त विषयक गैर योजना शीर्ष-3054 अन्तर्गत बिहार ग्रामीण पथ अनुक्षण नीति-2018 संलग्न सूची के अनुसार आवंटन अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

विश्वासभाजन,

अनुलग्नक :- संलग्न सूची

1. पथों का आवंटन अधियाचना प्रपत्र।


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

Requisition of Allotment under Head MR HEAD-3054 Under Bihar Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)


Division :- Raxaul

Sl. No.	Package No.	Name of Road	Contractor Name	Project ID as Pes MIS	Administrative Approval (AA) Letter No. & Date	A.A.		Agreement Value		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount	up-to-date Expenditure as per MIS (In Lakh)	Requisition against work done. (In Lakh)	Remarks
						Length (in KM)	Total (Amount) (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Yrs Routine Maintenance (in Lakh)										
1	MR-N/19-20/Raxaul/15	New Bypass to Siwantola Via Ekdarwa	M/S Ganpati Construction	317851031985	मुअ०-४ (मु०) 3054-04-117-2019, 5128 / पटना, दिनांक-24.09.2019	2.300	84.61960	54.517	23.8896	184MBD/2020-21	17-06-2021	-	2765	25mm	5	0	0	54.51700	Work in Progress
																		54.51700	


 Executive Engineer,
 Rural Works Department,
 Works Division, Raxaul

Name of Customer : M/S Ganpati Construction
 Name of Work : Road to Siman tola via Ekdarma
 Road :
 Lab Job number :
 Date : 16/05/2021
 Section No : 14

Test Date : 16/05/2021
 Road Name : Road to Siman tola via Ekdarma
 Machine No : 378
 Road Type : (P) RURAL ROAD
 Start S No : 4000 FM
 Side :
 Start E No : 230 FM
 Interval :
 Weather : Normal
 UV Range : 1205 To 4000 mm/Km
 Start Location : 26.99828
 Dist Range : 0 To 21 01 - 1000 m
 End Location : 34.83441
 Equation : $Y = 0.0002 \cdot X^2 + 0.998 \cdot X + 1095$

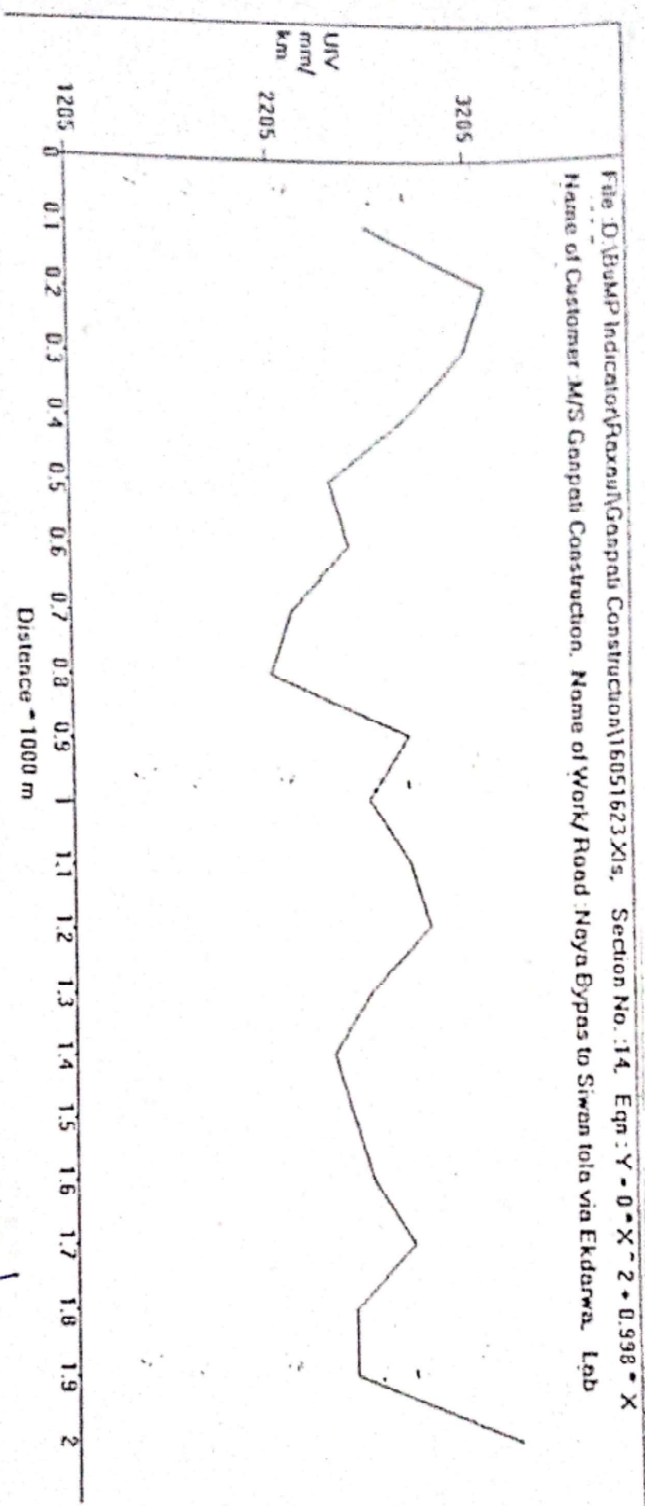

16/5/21
 JE

18/5/21

17/5/21
 JE

Road Name-Naya Bypass to Siwan tola via Ekdarwa, Contractor-M/S Ganpati Construction

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI in UIV	IRI in ROAD	CATEGORY	Latitude	Longitude	Event
16/5/21	14:37:49	14	0.1	260	0	2600	2704 G	26.99828	84.83089	Normal		
16/5/21	14:38:23	14	0.1	320	20.2	3200	3303 G	26.99861	84.82988	Normal		
16/5/21	14:40:09	14	0.1	310	20.2	3100	3203 G	27.1472	84.82909	Normal		
16/5/21	14:40:44	14	0.1	280	20.2	2800	2903 G	27.2325	84.82939	Normal		
16/5/21	14:41:00	14	0.1	240	30.3	2400	2504 G	27.3182	84.82978	Normal		
16/5/21	14:41:00	14	0.1	250	30.3	2500	2604 G	27.403	84.83007	Normal		
16/5/21	14:41:20	14	0.1	220	20.2	2200	2305 G	27.4885	84.83047	Normal		
16/5/21	14:41:20	14	0.1	210	20.2	2100	2205 G	27.5697	84.83061	Normal		
16/5/21	14:42:00	14	0.1	280	20.2	2800	2903 G	27.6572	84.83094	Normal		
16/5/21	14:42:00	14	0.1	260	20.2	2600	2704 G	27.7382	84.83141	Normal		
16/5/21	14:42:30	14	0.1	280	20.2	2800	2903 G	27.8187	84.83172	Normal		
16/5/21	14:42:30	14	0.1	290	30.3	2900	3003 G	27.9085	84.83189	Normal		
16/5/21	14:42:30	14	0.1	260	30.3	2600	2704 G	27.9918	84.83224	Normal		
16/5/21	14:43:00	14	0.1	240	30.3	2400	2504 G	27.1078	84.83259	Normal		
16/5/21	14:43:00	14	0.1	250	30.3	2500	2604 G	27.11588	84.83295	Normal		
16/5/21	14:43:00	14	0.1	260	30.3	2600	2704 G	27.1247	84.83332	Normal		
16/5/21	14:44:16	14	0.1	280	30.3	2800	2903 G	27.13363	84.83359	Normal		
16/5/21	14:44:16	14	0.1	250	30.3	2500	2604 G	27.14185	84.83387	Normal		
16/5/21	14:44:16	14	0.1	250	30.3	2500	2604 G	27.15085	84.83418	Normal		
16/5/21	14:45:00	14	0.087	290	10.1	3333	3435 G	27.15873	84.83441	Normal		
Total IRI							53306					
Average IRI							2765.3					

$$Y = 0 \cdot X^2 + 0.998 \cdot X + 109.5$$

$$X = 3333$$

$$Y = 3435$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

JE 16/5/21

AE 16/5/2021

Executive Engineer
Rural Works Department
Works Division Raipur
