

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पटना ।

पत्रांक 745 (3/20)

दिनांक 25/05/2021

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पटना।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बी.आर.आर.डी.ए.,
ग्रामीण कार्य विभाग,
बिहार, पटना ।

विषय :- शीर्ष-MR(3054) under Bihar Rural Road Maintenance
Policy-2018 योजना अन्तर्गत आवंटन का अध्याचना के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि शीर्ष-MR(3054) under Bihar
Rural Road Maintenance Policy-2018 योजना अन्तर्गत पथ का आवंटन का
अध्याचना का मांग विहित-प्रपत्र में तैयार कर अध्याचना हेतु भेजी जा रही है। पथ का
कार्य विशिष्टियों के अनुरूप किया जा चुका है।


अतः आपसे अनुरोध है कि उक्त योजना का आवंटन उपलब्ध कराने की कृपा
की जाये ताकि संवेदक का भुगतान किया जा सके।

अनु० :- यथोक्त।

विश्वासभाजन


25/5/21

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पटना।


25/5/21


25/5/21

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division : Patna

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	15	NH-30A NIVAZIPUR TO MOHINPUR	10100102193	5548 dated 23.10.2019	1.85000	93.65900	77.96500	14.90982	24-NHDD/2020-21 Dated 07.09.2020	06.06.2021	-	2344.473	25 mm	5%	0.00000	0.00000	62.67594	Surface Complete
Total																	62.67594	

- Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
- Up-to-Date Physical Progress has been uploaded in MIS.

Executive Engineer
RRWD Works Division, Patna
25/10/2021

Name of The Road : NH-30A Niyazipur To Mominpur

Length of The Road : 1.850

Packagr No.: MR-N/2019-2020/PATNA/15

Division : Patna

Block : Fatuha

Contractor Name : M/S Vinod Kumar Mishra

Date	Time	Section	No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event			
25/5/21	8:52:0	30	30	0.1	210	0	2100	2244	G	25.48748	85.30335	Normal			
25/5/21	8:52:0	30	30	0.1	190	30.3	1900	2056	G	25.48733	85.304343	Normal			
25/5/21	8:52:24	30	30	0.1	180	30.3	1800	1963	G	25.48719	85.30537	Normal			
25/5/21	8:52:24	30	30	0.1	210	30.3	2100	2244	G	25.48701	85.306347	Normal			
25/5/21	8:52:24	30	30	0.1	220	30.3	2200	2337	G	25.48685	85.307357	Normal			
25/5/21	8:53:0	30	30	0.1	180	30.3	1800	1963	G	25.48663	85.30835	Normal			
25/5/21	8:53:0	30	30	0.1	220	30.3	2200	2337	G	25.48641	85.309292	Normal			
25/5/21	8:53:0	30	30	0.1	180	30.3	1800	1963	G	25.48616	85.310302	Normal			
25/5/21	8:53:34	30	30	0.1	220	30.3	2200	2337	G	25.48585	85.311228	Normal			
25/5/21	8:53:34	30	30	0.1	180	30.3	1800	1963	G	25.48553	85.312188	Normal			
25/5/21	8:54:0	30	30	0.1	180	30.3	1800	1963	G	25.4852	85.313147	Culvert			
25/5/21	8:54:9	30	30	0.1	230	20.2	2300	2431	G	25.48467	85.313922	Curve			
25/5/21	8:54:9	30	30	0.1	310	20.2	3100	3180	G	25.4839	85.314175	Normal			
25/5/21	8:54:44	30	30	0.1	190	30.3	1900	2056	G	25.48302	85.313955	Normal			
25/5/21	8:54:44	30	30	0.1	210	30.3	2100	2244	G	25.48205	85.313905	Normal			
25/5/21	8:55:19	30	30	0.1	310	10.1	3100	3180	G	25.48132	85.314242	Speed Breaker			
25/5/21	8:55:19	30	30	0.1	240	20.2	2400	2524	G	25.481	85.315168	Normal			
25/5/21	8:55:19	30	30	0.1	270	20.2	2700	2805	G	25.48067	85.316143	Speed Breaker			
25/5/21	8:56:0	30	30	0.05	90	20.2	2647	2755	G	25.48003	85.317322	Speed Breaker			
Total				1.85	4020	474.7	41947	44545		484.2083	1620.9101				
Average							2207.736	2344.473							

25.05.21
ST Engineer

25.05.2021.
J.E

25.05.21
ME


25/5/21
E.E

Name of Customer: M/S Vinod Kumar Mishra
 Name of Work: NH-30A Miyazipur To Moninpur
 Road:
 Lab Job number:
 Date: 25/05/2021
 Section No. 30

Test Date: 25/05/2021
 Road Name: NH-30A Miyazipur To Moninpur
 Machine No:
 Start S No:
 Start E No:
 Weather:
 Start Location:
 End Location:
 Road Type: (R) RURAL ROAD
 Side:
 UV Range: 963 To 4000 Interval 1000 mm/km
 Dist Range: 0 To 2 01 1000 m
 Equation: $Y = 0 \cdot X^2 + 0.936 \cdot X + 278.4$

Print Generate Report and Graph
 Redraw Graph Map View

File: C:\Users\BRRDA23\OneDrive\Desktop\25050056.Xls, Section No: 30, Eqn: $Y = 0 \cdot X^2 + 0.936 \cdot X + 278.4$
 Name of Customer: M/S Vinod Kumar Mishra, Name of Work/Road: NH-30A Miyazipur To Moninpur, Lab Job

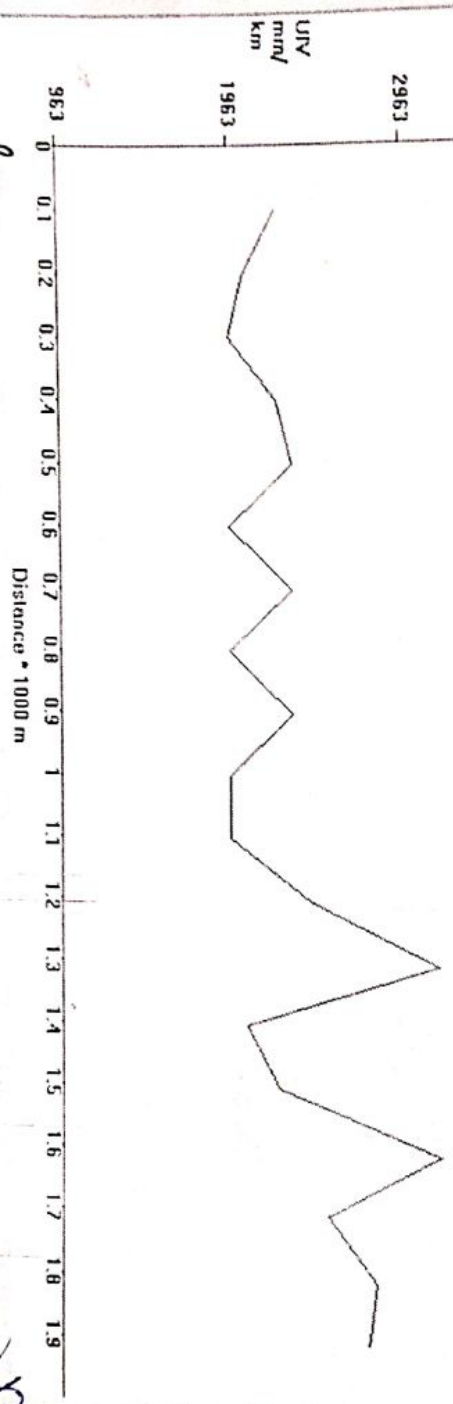

25.05.21
 25.05.2021
 J.E.
 25.05.21
 E.E.

Sch. XLV-Form No. 1					Contents of area
Particulars	Details of actual measurement				
	No.	L.	B.	D.	
ABSTRACT OF COST					
(1)	Clearing & grubbing road land do etc				
0.370 Hect wide Tm Blage (2)					
	at 51/161 = 75/1000 — R				
(2)	Scraping the existing RT road surface do etc				
656.25 m ² wide Tm Blage (2)					
	at 15 = 43/1000 — R				
(3)	Construction of sub-grade & earth				
1050.00 m ² wide Tm Blage (2)					
	at 161 = 56/1000 — R				
(4)	Construction of G.S.D. G-1 by brick with 900 - dead material do etc				
124.30 m ² wide Tm Blage (2)					
	at 1865 = 32/1000 — R				
(5)	Brick facing, spreading & compacting stone app. & gates & 6" concrete to 100 m G.D. do etc				
103.25 m ² wide Tm Blage (2)					
	at 3493 = 17/1000 — R				
at 791572 = 00					

Continuation

Continuation

Continuation

Scanned with CamScanner
