

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, फारबिसगंज ।

पत्रांक - 3110 अ३०

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, फारबिसगंज ।

सेवा में,

अपर-मुख्य-कार्यपालक-पदाधिकारी
ग्रामीण कार्य विभाग,
ब्राड़ा, पटना बिहार।

फारबिसगंज, दिनांक 18-11-2021

विषय:- M/R Maintenance policy-2018 मद में राशि की अधियाचना पत्र का प्रेषण।


महाशय,

उपर्युक्त विषयक प्रसांगिक पत्र के संबंध में कहना है कि M/R Maintenance policy-2018 में संवेदक द्वारा कराये गये कार्य के अनुरूप विहित प्रपत्र में अधियाचना तैयार किया गया है।

अतः अनुरोध है कि अधियाचना पत्र में उल्लेखित योजना में राशि विमुक्त करने की कृपा करेंगे ताकि संवेदक द्वारा कराये गये कार्य का भुगतान किया जा सके।

अनु:- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, फारबिसगंज

Requisition Format for Scheme Head- MR (3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Sl No	Package No	Name of Road	Project Id	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date Of Completion as per Agreement	Value of IBT (In million)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Allotted Amount (In Lakh)	up-to-date expenditure as per MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification With Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)									
1	MR-N/19-20 FORBESGANJ/03	Normal ambarsa to majbar	21261102751	Letter No-1837 dt-24.06.19	1.00	27.23800	27.23800	10.31400	51 MBD MR/ 2020-21 & 08/08/2020	07.04.2021	3068.30	25 mm	5.01%	0.000000	-	25.500	Complete
2	MR-N/19-20 FORBESGANJ/03	Near Hat Poithia (P.W.D.) road from House to Dhumgarh tola	21206001014	Letter No-1837 dt-24.06.19	3.00	82.15000	82.15000	31.12200	51 MBD MR/ 2020-21 & 08/08/2020	07.04.2021	2690.00	25 mm	5.01%	0.000000	-	81.200	Complete
3	MR-N/19-20 FORBESGANJ/16	Rupauli To Abarnadpur	21206002077	Letter No-1837 dt-24.06.19	6.80	167.83500	167.83500	64.96300	11 MBD MR/ 2020-21 & 06/06/2020	05.03.2021	3049.41	25 mm	5.01%	0.000000	-	165.500	Complete
	MR-N/19-20 FORBESGANJ/23	Remaining Part of Vinodpur to Karahia	NEA32000278	Letter No-1595 dt-22.08.19	12.70	335.49900	335.49900	134.12000	13 MBD MR/ 2020-21 & 20/06/2020	19.03.2021	2909.33	25 mm	5.01%	0.000000	-	332.50	Complete
														Total=		604.70	

2. Up-to-date Physical Progress has been uploaded in MIS

Executive Engineer
RWD (W), Div.-Forbesganj

20/11/21

Lab Job number :46

Date :07-11-2021

Name of Customer :V.B. Buildcon

Name of Work/ Road :Rupauli To Ahamadpur

Sr.no	Location of test(in km)	Corrected U.I value(mm/km)	Road catagory
1	0.1	2981	G
2	0.2	2593	G
3	0.3	2303	G
4	0.4	2109	G
5	0.5	3078	G
6	0.6	3078	G
7	0.7	2593	G
8	0.8	3078	G
9	0.9	2981	G
10	1	2593	G
11	1.1	3272	G
12	1.2	2690	G
13	1.3	2884	G
14	1.4	2884	G
15	1.5	3562	G
16	1.6	2690	G
17	1.7	3078	G
18	1.8	2690	G
19	1.9	3078	G
20	2	2981	G
21	2.1	3078	G
22	2.2	3853	G
23	2.3	2884	G
24	2.4	2884	G
25	2.5	2884	G
26	2.6	2884	G
27	2.7	3369	G
28	2.8	2109	G
29	2.9	2884	G
30	3	3853	G
31	3.1	3562	G
32	3.2	3466	G
33	3.3	2400	G
34	3.4	2787	G
35	3.5	2787	G
36	3.6	3466	G
37	3.7	3078	G
38	3.8	3466	G

18/11/21
JE

18/11/21

Executive Engineer
Rural Work Department
Work Division, Forbesganj

Sr.no	Location of test(In km)	Corrected U.I value(mm/km)	Road catagory
39	3.9	2884	G
40	4	3272	G
41	4.1	3562	G
42	4.2	3272	G
43	4.3	3369	G
44	4.4	2981	G
45	4.5	2981	G
46	4.6	3272	G
47	4.7	2884	G
48	4.8	3756	G
49	4.9	3078	G
50	5	2981	G
51	5.1	3659	G
52	5.2	3078	G
53	5.3	2593	G
54	5.4	3272	G
55	5.5	3078	G
56	5.6	3659	G
57	5.7	3659	G
58	5.8	3853	G
59	5.9	2497	G
60	6	2787	G
61	6.1	3659	G
62	6.2	2884	G
63	6.3	3175	G
64	6.4	3272	G
65	6.5	3078	G
66	6.6	2400	G
67	6.7	3078	G
68	6.8	2497	G


18/11/21
j.e

18/11/21

C/18/11
Executive Engineer
Rural Work Department
WORK DIVISION, P. O. ...

File :F:\Forbesganj\46\07111504.Xls. Section No. :46. Eqn : $Y = 0 \cdot X^2 + 0.969 \cdot X + 74.60$

Name of Customer :V.B. Buildcon, Name of Work/ Road :Rupauli To Ahamedpur, Lab Job number :46

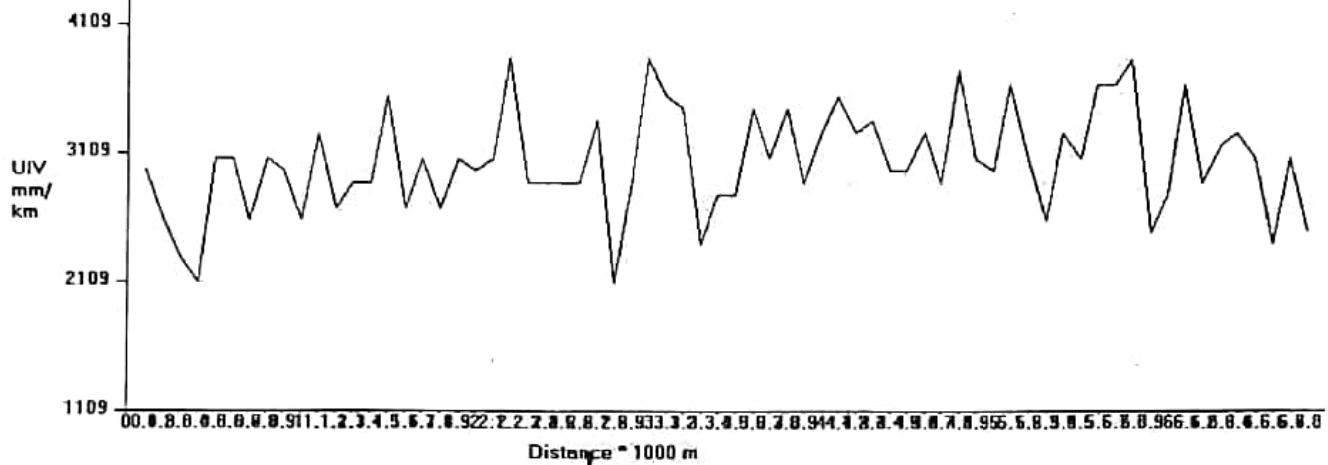

g
R/11/14
j-E

g
18/11/21

C
18/11

Executive Engineer
Rural Work Department
Work Division, Forbesganj


Section Analyzer

Name of Customer: V.B. Buldon
 Name of Work/Road: Rupauli To Ahmadpur
 Lab Job number: 46
 Date: 07/11/2021
 Section No.: 46

Test Date: 07/11/2021 Road Name: Rupauli To Ahmadpur
 Machine No: 196 Road Type: (R) RURAL ROAD
 Start S No: Side: Interval:
 Start E No:
 Weather: UV Range: 1109 To 5000 1000 mm/km
 Start Location: 963 87.355218 Dist Range: 0 To 63 01 * 1000 m
 End Location: 96 87.378265 Equation: $Y = 0 * X^2 + 0.969 * X + 74.60$

Print Generate Report and Graph

Redraw Graph Map View

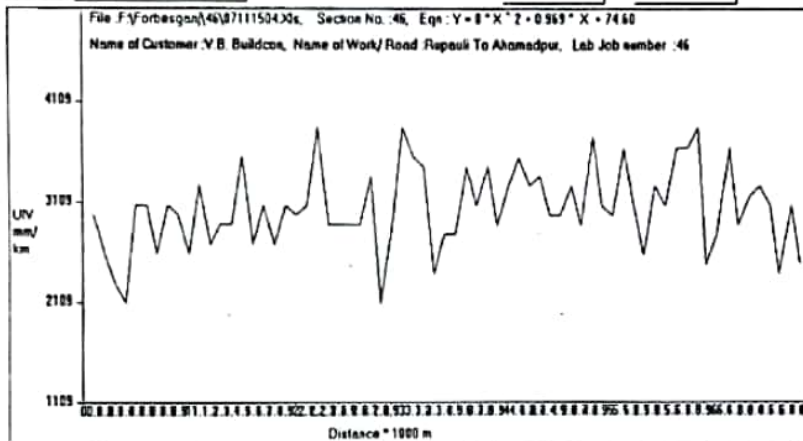

18/11/21
J.E


18/11/21

Executive Engineer
 Rural Work Department
 Work Division, Forbesganj

 Map View

- 2 -

File :F:\Forbesganj\46\07111504\Xls, Section No. :46, Eqn : $Y = 0 * X^2 + 0.969 * X + 74.60$

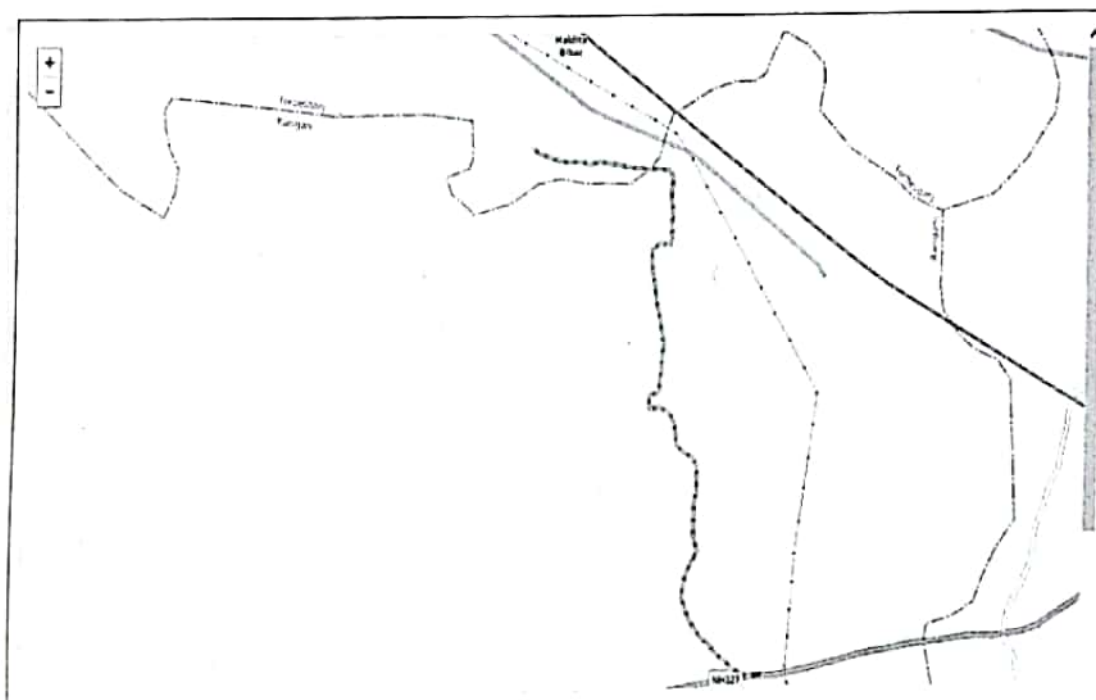

18/11/24
J.E

$$\frac{B_8}{18} \approx 0.22$$

Executive Engineer
Rural Work Department
Work Division, Forbesganj

Name of Customer : V.B. Buildcon
Name of Work/ Road : Rupauli To Ahamadpur

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR		CATEGORY ROAD	IRI	Latitude	Longitude	Event
						mm/km	UV					
7/11/21	14:37:0	45	0.1	300	10.1	3000	2981	G	4	26.15686	87.35522	Normal
7/11/21	14:37:13	46	0.1	260	10.1	2600	2593	G	3.53	26.1564	87.35609	Normal
7/11/21	14:37:13	46	0.1	230	10.1	2300	2303	G	3.18	26.15609	87.357	Normal
7/11/21	14:38:0	46	0.1	210	10.1	2100	2109	G	2.94	26.15585	87.35796	Normal
7/11/21	14:38:24	46	0.1	310	10.1	3100	3078	G	4.12	26.15574	87.35896	Normal
7/11/21	14:39:0	46	0.1	310	10.1	3100	3078	G	4.12	26.1558	87.35997	Normal
7/11/21	14:39:0	46	0.1	260	10.1	2600	2593	G	3.53	26.15562	87.36091	Normal
7/11/21	14:39:35	46	0.1	310	10.1	3100	3078	G	4.12	26.15575	87.36189	Normal
7/11/21	14:40:0	46	0.1	300	10.1	3000	2981	G	4	26.15566	87.36288	Normal
7/11/21	14:40:10	46	0.1	260	10.1	2600	2593	G	3.53	26.15553	87.36386	Normal
7/11/21	14:40:45	46	0.1	330	10.1	3300	3272	G	4.35	26.1554	87.36485	Normal
7/11/21	14:41:0	46	0.1	270	10.1	2700	2690	G	3.65	26.15526	87.36579	Normal
7/11/21	14:41:20	46	0.1	290	10.1	2900	2884	G	3.88	26.15521	87.36678	Normal
7/11/21	14:41:20	46	0.1	290	10.1	2900	2884	G	3.88	26.1552	87.36779	Normal
7/11/21	14:42:0	46	0.1	360	10.1	3600	3562	G	4.69	26.15514	87.36879	Normal
7/11/21	14:42:31	46	0.1	270	10.1	2700	2690	G	3.65	26.15465	87.36923	Normal
7/11/21	14:42:31	46	0.1	310	10.1	3100	3078	G	4.12	26.15375	87.36912	Normal
7/11/21	14:43:6	46	0.1	270	10.1	2700	2690	G	3.65	26.15282	87.36914	Normal
7/11/21	14:43:42	46	0.1	310	10.1	3100	3078	G	4.12	26.15194	87.36918	Normal
7/11/21	14:44:0	46	0.1	300	10.1	3000	2981	G	4	26.15105	87.36914	Normal
7/11/21	14:44:17	46	0.1	310	10.1	3100	3078	G	4.12	26.15016	87.36923	Normal
7/11/21	14:45:0	46	0.1	390	10.1	3900	3853	G	5.03	26.1497	87.36896	Normal
7/11/21	14:45:27	46	0.1	290	10.1	2900	2884	G	3.88	26.14981	87.36796	Normal
7/11/21	14:45:27	46	0.1	290	10.1	2900	2884	G	3.88	26.14934	87.36721	Normal
7/11/21	14:46:3	46	0.1	290	10.1	2900	2884	G	3.88	26.14846	87.3671	Normal

$Y = 0 \cdot X^2 + 0.969 \cdot X + 74.60$
 $X = 2500$
 $Y = 2497$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

18/11/21
J-E

18/11/21

Executive Engineer
Rural Work Department
Work Division, Forbessganj

Date	Time	Section No.	Length In km	Bumps In mm	Speed Rate	OR		CATEGORY ROAD	IRI	Latitude	Longitude	Event
						mm/km	UIV					
7/11/21	14:56:38	46	0.1	310	10.1	3100	3078	G	4.12	26.128	87.37165	Normal
7/11/21	14:57:13	46	0.1	260	10.1	2600	2593	G	3.53	26.1271	87.372	Normal
7/11/21	14:58:0	46	0.1	330	0	3300	3272	G	4.35	26.12625	87.37141	Speed Breaker
7/11/21	14:58:24	46	0.1	310	10.1	3100	3078	G	4.12	26.12548	87.37096	Normal
7/11/21	14:58:24	46	0.1	370	10.1	3700	3659	G	4.8	26.1246	87.37069	Normal
7/11/21	14:59:0	46	0.1	370	10.1	3700	3659	G	4.8	26.12373	87.37047	Normal
7/11/21	14:59:34	46	0.1	390	10.1	3900	3853	G	5.03	26.12291	87.37081	Normal
7/11/21	15:0:9	46	0.1	250	10.1	2500	2497	G	3.42	26.12209	87.37126	Speed Breaker
7/11/21	15:0:9	46	0.1	280	10.1	2800	2787	G	3.77	26.1214	87.37185	Speed Breaker
7/11/21	15:1:0	46	0.1	370	10.1	3700	3659	G	4.8	26.12067	87.37246	Speed Breaker
7/11/21	15:1:20	46	0.1	290	10.1	2900	2884	G	3.88	26.12023	87.37322	Normal
7/11/21	15:1:55	46	0.1	320	10.1	3200	3175	G	4.23	26.11965	87.37394	Normal
7/11/21	15:2:0	46	0.1	330	10.1	3300	3272	G	4.35	26.11911	87.37473	Normal
7/11/21	15:2:31	46	0.1	310	10.1	3100	3078	G	4.12	26.11856	87.37554	Normal
7/11/21	15:2:31	46	0.1	240	10.1	2400	2400	G	3.3	26.11805	87.3764	Normal
7/11/21	15:3:6	46	0.1	310	10.1	3100	3078	G	4.12	26.11789	87.37729	Normal
7/11/21	15:3:41	46	0.1	250	10.1	2500	2497	G	3.42	26.11796	87.37827	Normal

Total 207360
Average UIV 3049.411765

18/11/21
J.C

18/11/21

Executive Engineer
Rural Work Department
Work Division, Forbani

$Y = 0 \cdot X^2 + 0.969 \cdot X + 74.60$
