

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, कटिहार।**

पत्रांक :- 1847

/कटिहार, दिनांक- 20-10-21

प्रेषक,

कार्यपालक अभियंता,
ग्रा0का0वि0, कटिहार।

सेवा में,

अपर-मुख्य-कार्यपालक-पदाधिकारी,
BRRDA, 3री मंजिल, भूमि विकास बैंक भवन,
बिहार, पटना।


विषय :- शीर्ष **New Maintenance Policy-2018** योजनान्तर्गत निर्माण हेतु आवंटन की अधियाचना के संबंध में।


महाशय,

उपर्युक्त विषय के संबंध में कहना है, कि शीर्ष **New Maintenance Policy-2018** योजनान्तर्गत ग्रा0का0वि0, कार्य प्रमंडल, कटिहार द्वारा विहित प्रपत्र में अधियाचना तैयार कर आपके अग्रेतर कार्रवाई हेतु समर्पित की जाती है।

अनु0:-यथोक्त।

विश्वासभाजन,



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।



20-10-21

ज्ञापांक:- 1847

/कटिहार, दिनांक:- 20-10-21

प्रतिलिपि:- नोडल पदाधिकारी, 3054 MR, ग्रामीण कार्य विभाग, बिहार, पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,


कार्य प्रमंडल, कटिहार।

RWD, Works Division, Katihar

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Initial Rectification and Surface Renewal)

Sl. No	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Allocated Amount (in Lac)	up to date expenditure as per MIS (in Lac)	Requisition Against work done (in lac)	Remarks
					Length (In Km)	Amount (in Lac)	Initial Rectification with Surface Renewal (in lac)	5 years Routine Maintenance (in lac)										
1	MR-N/19-20 Katihar/04	Madhubani Chowk to Shaishya via Kajra and Geruwa	21105602035	1847/24.06.19	6.900	246.72680	157.63513	71.41774	10MBD/20-21, 08.08.2020	07.05.2021	-	2245.22	25mm	5.1%	0.00000	0.00000	149.54000	Surface Complete
2	MR-N/19-20 Katihar/10	NH-31 Petrol Pump to Basgarha via Akama primary School	211551033037	5129/24.09.19	2.400	171.05900	135.21632	24.55849	01MBD/20-21, 29.06.2020	28.03.2021	-	1818.17	25mm	5.1%	0.00000	0.00000	130.32000	Surface Complete
3	MR-N/19-20 Katihar/10	Korha NH-31 Durga Ashan to Baura	211551031957	5129/24.09.19	5.800	301.844	200.66941	59.42511	01MBD/20-21, 29.06.2020	28.03.2021	25.03.21	2053.78	25mm	5.1%	80.26400	80.26400	120.10473	Completed
Total															80.26400	80.26400	399.96473	

RWD, Works Division, Katihar

Executive Engineer

[Signature]

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate upto the month of Sep, 2021

Form of Utilisation Certificate upto the month of Sep, 2021

New Maintenance Policy-2018						
Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars		
I	New Maintenance Policy-2018	Lt, No.- 017 Dt.- 26.02.21	80.03702	Certified that out of Rs. 791.93456 lacs received upto the year-2021-22 in favour of Ex. Engineer, RWD, Katihar a sum of Rs. 662.97780 lacs has been utilized for the purpose of NMP-2018 rural roads Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 128.95676 lacs remaining unutilized at the end of the period under.		
		Lt, No.- 027 Dt.- 04.05.21	70.40501			
		Lt, No.- 040 Dt.- 14.06.21	368.10325			
		Lt, No.- 052 Dt.- 24.08.21	273.38928			
			Total :-		791.93456	

Kind of Checks exercised :-

- i. Works have been supervised by Executive Engineer/Superintending Engineer.
- ii. Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- iii. Construction materials have been tested.
- iv. Measurements have been recorded in the MBs and test check conducted by the Assistant.
- v. All other codal formalities have been observed.

- i. Construction of Road Works.
- ii. Construction of CD Works.

Executive Engineer,
D(W) Division, Katihar.

Lab Job number :5

Date :25-07-2021

Name of Customer :Gajmattia Infrastructure Pvt. Ltd.


Name of Work/ Road :Korha NH-31 Durga Asthan to Baura

Sr.no	Location of test (in km)	Corrected U.I value (mm/km)	Road catagory
1	0.100	2303	G
2	0.200	2206	G
3	0.300	1624	G
4	0.400	2109	G
5	0.500	1721	G
6	0.600	1721	G
7	0.700	2303	G
8	0.800	1721	G
9	0.900	1431	G
10	1.000	2109	G
11	1.100	1818	G
12	1.200	2206	G
13	1.300	2109	G
14	1.400	2109	G
15	1.500	2109	G
16	1.600	1818	G
17	1.700	1624	G
18	1.800	1915	G
19	1.900	2303	G
20	2.000	2690	G
21	2.100	2593	G
22	2.200	2981	G
23	2.300	3659	G
24	2.400	2497	G
25	2.500	2109	G
26	2.600	2787	G
27	2.700	1528	G
28	2.800	2012	G
29	2.900	2206	G
30	3.000	1624	G
31	3.100	1915	G
32	3.200	1721	G
33	3.300	1624	G
34	3.400	1818	G
35	3.500	1528	G
36	3.600	1915	G
37	3.700	1528	G
38	3.800	2012	G
39	3.900	1915	G
40	4.000	1624	G
41	4.100	2206	G
42	4.200	2012	G
43	4.300	1818	G
44	4.400	1915	G
45	4.500	2690	G
46	4.600	2109	G


25.07.2021
D.E


20/07/21
Executive Engineer
P.W.D (W) Division Katihar

Sr.no	Location of test (in km)	Corrected U.I value (mm/km)	Road catagory
47	4.700	2012	G
48	4.800	2012	G
49	4.900	1721	G
50	5.000	2400	G
51	5.100	2206	G
52	5.200	2497	G
53	5.300	2206	G
54	5.400	1818	G
55	5.500	2206	G
56	5.600	1528	G
57	5.700	2012	G
58	5.800	2206	G
Average IRI Value		2053.78	


 25.07.2021
 A-E


 Executive Engineer
 R.W.D (W) Division Katihar

Lab Job number :5
Date :25-07-2021

Name of Customer :Gajmattia Infrastructure Pvt. Ltd.
Name of Work/ Road :Korha NH-31 Durga Asthan to Baura

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
25/7/21	11:45:0	5	0.1	230	0	2300	2303	G	25.62081	87.41010	Normal
25/7/21	11:45:25	5	0.1	220	20.2	2200	2206	G	25.62170	87.41017	Normal
25/7/21	11:45:25	5	0.1	160	20.2	1600	1624	G	25.62257	87.41037	Curve
25/7/21	11:46:0	5	0.1	210	20.2	2100	2109	G	25.62316	87.41113	Normal
25/7/21	11:46:0	5	0.1	170	20.2	1700	1721	G	25.62351	87.41202	Normal
25/7/21	11:46:35	5	0.1	170	20.2	1700	1721	G	25.62416	87.41266	Normal
25/7/21	11:46:35	5	0.1	230	20.2	2300	2303	G	25.62479	87.41340	Normal
25/7/21	11:46:35	5	0.1	170	30.3	1700	1721	G	25.62524	87.41389	Normal
25/7/21	11:47:6	5	0.1	140	20.2	1400	1431	G	25.62613	87.41480	Normal
25/7/21	11:47:6	5	0.1	210	30.3	2100	2109	G	25.62683	87.41551	Normal
25/7/21	11:47:6	5	0.1	180	20.2	1800	1818	G	25.62749	87.41611	Normal
25/7/21	11:47:6	5	0.1	220	20.2	2200	2206	G	25.62824	87.41641	Curve
25/7/21	11:47:41	5	0.1	210	20.2	2100	2109	G	25.62842	87.41729	Normal
25/7/21	11:48:0	5	0.1	210	20.2	2100	2109	G	25.62874	87.41813	Curve
25/7/21	11:48:20	5	0.1	210	20.2	2100	2109	G	25.62926	87.41880	Normal
25/7/21	11:48:20	5	0.1	210	20.2	2100	2109	G	25.62985	87.41966	Normal
25/7/21	11:48:55	5	0.1	180	20.2	1800	1818	G	25.63028	87.42047	Normal
25/7/21	11:49:0	5	0.1	160	20.2	1600	1624	G	25.63059	87.42144	Curve
25/7/21	11:49:0	5	0.1	190	20.2	1900	1915	G	25.63068	87.42180	Curve
25/7/21	11:49:31	5	0.1	230	20.2	2300	2303	G	25.63129	87.42285	Normal
25/7/21	11:49:31	5	0.1	270	20.2	2700	2690	G	25.63162	87.42315	Normal
25/7/21	11:49:31	5	0.1	260	20.2	2600	2593	G	25.63282	87.42429	Speed Breaker
25/7/21	11:50:6	5	0.1	300	20.2	3000	2981	G	25.63350	87.42490	Normal
25/7/21	11:50:41	5	0.1	370	10.1	3700	3659	G	25.63427	87.42537	Normal
25/7/21	11:51:0	5	0.1	250	10.1	2500	2497	G	25.63411	87.42632	Normal
25/7/21	11:51:16	5	0.1	210	20.2	2100	2109	G	25.63402	87.42727	Normal
25/7/21	11:51:51	5	0.1	280	10.1	2800	2787	G	25.63409	87.42798	Curve
25/7/21	11:51:51	5	0.1	150	20.2	1500	1528	G	25.63408	87.42893	Normal
25/7/21	11:51:51	5	0.1	200	20.2	2000	2012	G	25.63411	87.43032	Speed Breaker
25/7/21	11:52:0	5	0.1	220	10.1	2200	2206	G	25.63424	87.43132	Normal
25/7/21	11:52:35	5	0.1	160	10.1	1600	1624	G	25.63431	87.43233	Normal
25/7/21	11:52:35	5	0.1	190	20.2	1900	1915	G			

$$Y = 0 * X^2 + 0.969 * X + 74.60$$

$$X = 2200$$

$$Y = 2206$$

(R) RURAL ROAD
Good Average Poor
4000 4001-5000 >5001

[Signature]
Executive Engineer
R.W.D (W) Division Kathihar

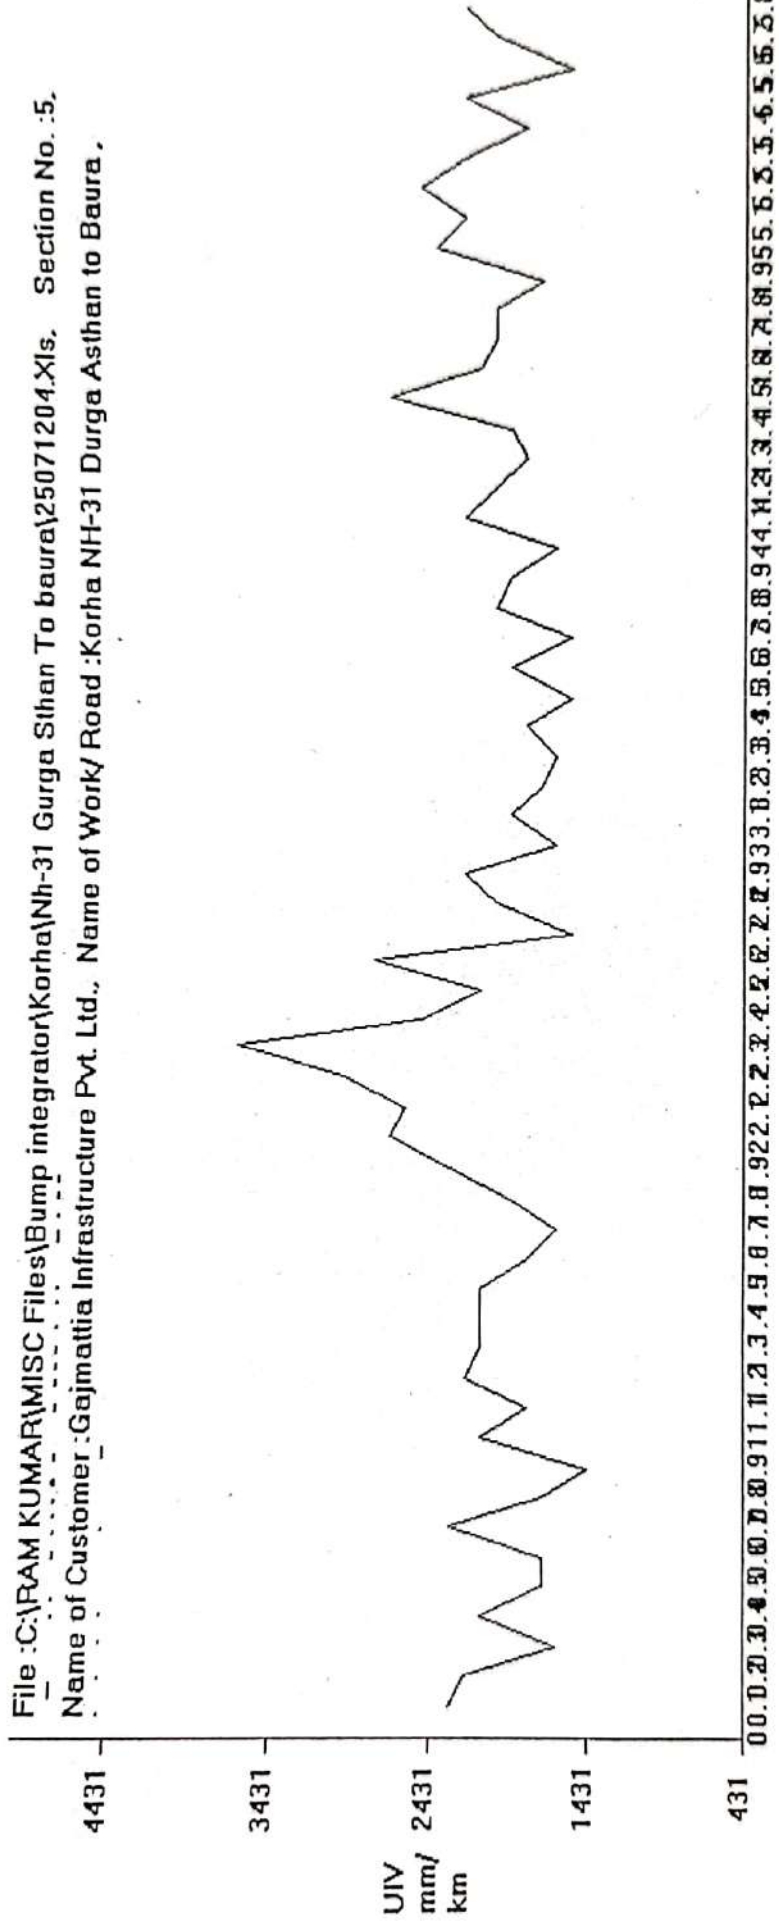
[Signature]
25.07.2021
A.E

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
25/7/21	11:53:6	5	0.1	170	10.1	1700	1721	G	25.63436	87.43325	Normal
25/7/21	11:53:41	5	0.1	160	10.1	1600	1624	G	25.63458	87.43423	Normal
25/7/21	11:54:18	5	0.1	180	10.1	1800	1818	G	25.63469	87.43466	Normal
25/7/21	11:54:18	5	0.1	150	10.1	1500	1528	G	25.63494	87.43569	Normal
25/7/21	11:55:4	5	0.1	190	10.1	1900	1915	G	25.63523	87.43652	Normal
25/7/21	11:55:39	5	0.1	150	10.1	1500	1528	G	25.63584	87.43718	Curve
25/7/21	11:55:39	5	0.1	200	10.1	2000	2012	G	25.63556	87.43783	Normal
25/7/21	11:56:14	5	0.1	190	10.1	1900	1915	G	25.63499	87.43877	Normal
25/7/21	11:56:49	5	0.1	160	10.1	1600	1624	G	25.63418	87.43985	Normal
25/7/21	11:57:25	5	0.1	220	10.1	2200	2206	G	25.63376	87.44067	Normal
25/7/21	11:58:0	5	0.1	200	10.1	2000	2012	G	25.63339	87.44150	Normal
25/7/21	11:58:0	5	0.1	180	20.2	1800	1818	G	25.63305	87.44226	Normal
25/7/21	11:59:0	5	0.1	190	10.1	1900	1915	G	25.63261	87.44328	Normal
25/7/21	11:59:29	5	0.1	270	10.1	2700	2690	G	25.63187	87.44361	Speed Breaker
25/7/21	12:0:4	5	0.1	210	10.1	2100	2109	G	25.63173	87.44445	Normal
25/7/21	12:0:4	5	0.1	200	10.1	2000	2012	G	25.63161	87.44540	Normal
25/7/21	12:0:39	5	0.1	200	10.1	2000	2012	G	25.63145	87.44630	Normal
25/7/21	12:1:14	5	0.1	170	10.1	1700	1721	G	25.63117	87.44730	Normal
25/7/21	12:1:14	5	0.1	240	20.2	2400	2400	G	25.63094	87.44823	Normal
25/7/21	12:1:50	5	0.1	220	20.2	2200	2206	G	25.63074	87.44923	Normal
25/7/21	12:1:50	5	0.1	250	20.2	2500	2497	G	25.63048	87.45016	Normal
25/7/21	12:2:25	5	0.1	220	20.2	2200	2206	G	25.63013	87.45110	Normal
25/7/21	12:2:25	5	0.1	180	10.1	1800	1818	G	25.62985	87.45249	Normal
25/7/21	12:3:0	5	0.1	220	20.2	2200	2206	G	25.62953	87.45339	Normal
25/7/21	12:3:0	5	0.1	150	30.3	1500	1528	G	25.62927	87.45423	Normal
25/7/21	12:3:36	5	0.1	200	20.2	2000	2012	G	25.62908	87.45526	Curve
25/7/21	12:3:36	5	0.1	220	10.1	2200	2206	G	25.62865	87.45643	Normal

Rumun
27/7/21
Executive Engineer
R.W.D (W) Division Katihar

25.7.2021
25.7.2021
A.E.

File : C:\RAM KUMAR\MISC Files\Bump integrator\Korha\Nh-31 Gurga Sthan To baura\25071204.Xls, Section No. :5,
 Name of Customer : Gajmattia Infrastructure Pvt. Ltd., Name of Work/ Road : Korha NH-31 Durga Asthan to Baura ,



Distance * 1000 m

[Signature]
 25.07.2021
 A-E

[Signature]
 Executive Engineer
 R.W.D (W) Division Katihar
