

कार्यपालक अभियंता का कार्यालय ग्रामीण कार्य विभाग, कार्य प्रमण्डल, मोतिहारी।

पत्रांक 1134 / दिनांक 29.03.2022

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल मोतिहारी।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
सह सचिव BRRDA,
बिहार, पटना।

विषय - MR-3054(New Maintenance Policy 2018) के अन्तर्गत 5 (पाँच) वर्षीय
अनुस्क्षण हेतु अधियाचना के संबंध में।

प्रमाण - अभियंता प्रमुख, ग्रामीण कार्य विभाग, बिहार पटना के पत्रांक मु0अ0 4 (मु0)
3054 04-229/2021-2021-1135 अनु0 पटना दिनांक 09.03.2022

संदर्भ -

उपर्युक्त विषयक प्रासंगिक पत्र में दिये गये निर्देश के आलोक में नई
अनुस्क्षण नीति 2018 अन्तर्गत पथों के अनुस्क्षण की राशि के आवंटन हेतु विहित प्रपत्र में
तैयार कर आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः MR-3054(New Maintenance Policy 2018) के अन्तर्गत (MR-
N/19-20 Motihari-07) 1. Dharampur to Bhawanipur 2. Raipatti to dumdumwa
3. Raghunathpur RHO road to Parsauna पथ के अनुस्क्षण हेतु अधियाचित प्रपत्र में
दर्शाये गए राशि उपलब्ध कराने की कृपा की जाए। कार्य का निरीक्षण किया गया एवं
कराया गया कार्य सतोषप्रद है। उक्त पथों में ए0टी0आर0 लंबित नहीं है।

अनु0 - यथावत।

विश्वासभाजन


कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, मोतिहारी।

R.W.D Work Division Motihari

FORM GFR 19A

(See Government of India's Decision (1) below Rule-150)

Form of Utilisation Certificate up to the month of 21.03.2022

MR HEAD-3054 (Initial Rectification with Surface Renewal)

Sl. No.	Name of Scheme	Selection No. of Date with Amount (in Rs. In Lacs)	Amount Received (in Rs. In Lacs)	Particulars
1	Construction of Rural Roads under MR HEAD-3054 (Initial Rectification with Surface Renewal)		0.00000	Certified that out of Rs.0.00 Lacs received during the years 2020-21 in favour of Executive Engineer, R.W.D. Works Division, Motihari A sum of Rs.0.00 Lacs has been utilised for the purpose of MR HEAD-3054 (Initial Rectification with Surface Renewal) Scheme as given in the margin or whichever sanctioned and that the balance Rs.0.00 Lacs remaining unutilised at the end of the period under.
			0.00000	

- 2 Certified that I have satisfied myself that the conditions on which the grant-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilised for the purpose for which it was sanctioned.

Kinds of exercised :-

- Works have been supervised by Executive Engineer/ Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction Material have been testes.
- Measurement have been recorded in the MBs and test check conducted by the Assistant.
- All other codal formalities have been observed.

- 3 Physical Progress achieved : _

- Construction of Road Works.
- Construction of CD Works.

For signature
28/3/22
Executive Engineer,
Rural Works Department,
Works Division, Motihari

Standrad Format For Roads Quarterly Statement (1 st Quarter)

PIU Name:- R.W.D.(W)Division Motihari

1	Name of the Road	Raghunathpur REO road to Parsauna		
2	Batch No.			
3	Project ID	31708201019		
4	Total Length of Road(in K.M.)	2.00		
5	Length of Road to Meet Required Service Level (Completed Length)(in K.M.)	2.00		
6	No of Total Quarter(ie 3 Months as a Unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount For Maintenance(in Lakh)	20.25762		
8	Quarterly Payment: 1/20 of Ordinary Maintennance Cost as per Schedule (in Lakh)	1.01288		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment (6) = (3) / (1)*(2)*(4)
		Length Non Compliant	Weightred Value for Payment Reduction (%)	
	Paved Roads(Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Total Payment Reduction for the Quarter (in Lakh)				0
To be Paid for the Quarter/ Demand (in Lakh)				1.01288

Date of Inspection by E/I or his agent

Prepared by Contractor's self Control unit

Name and Designation of Person inspecting road

(Signature)

Date:-

Signature of Person inspecting road

Certify by E/I (Signature) Date

Standrad Format For Roads Quarterly Statement (2 nd Quarter)

PIU Name:- R.W.D.(W)Division Motihari

1	Name of the Road	Raghunathpur REO road to Parsauna		
2	Batch No.			
3	Project ID	31708201019		
4	Total Length of Road(in K.M.)	2.00		
5	Length of Road to Meet Required Service Level (Completed Length)(in K.M.)	2.00		
6	No of Total Quarter(ie 3 Months as a Unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount For Maintenance(in Lakh)	20.25762		
8	Quarterly Payment: 1/20 of Ordinary Maintennance Cost as per Schedule (in Lakh)	1.01288		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment (6) = (3) / (1)*(2)*(4)
		Length Non Compliant	Weightred Value for Payment Reduction (%)	
	Paved Roads(Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Total Payment Reduction for the Quarter (in Lakh)				0
To be Paid for the Quarter/ Demand (in Lakh)				1.01288

Date of Inspection by E/I or his agent

Prepared by Contractor's self Control unit

Name and Designation of Person inspecting road

(Signature)

Date:-

Signature of Person inspecting road

Certify by E/I (Signature) Date

Standrad Format For Roads Quarterly Statement(3rd Quarter)

PIU Name:- R.W.D.(W)Division Motihari

1	Name of the Road	Raghunathpur REO road to Parsauna		
2	Batch No.			
3	Project ID	31708201019		
4	Total Length of Road(in K.M.)	2.00		
5	Length of Road to Meet Required Service Level (Completed Length)(in K.M.)	2.00		
6	No of Total Quarter(ie 3 Months as a Unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount For Maintenance(in Lakh)	20.25762		
8	Quarterly Payment: 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh)	1.01288		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment (6) = (3) / (1)*(2)*(4)
		Length Non Compliant	Weightred Value for Payment Reduction (%)	
	Paved Roads(Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Total Payment Reduction for the Quarter (in Lakh)				0
To be Paid for the Quarter/ Demand (in Lakh)				1.01288

Date of Inspection by E/I or his agent

Prepared by Contractor's self Control unit

A 24/04/22

Vijay
25/3/22
Name and Designation of Person inspecting road

Date:-

(Signature)

Signature of Person inspecting road

Certify by E/I (Signature) Date

Standrad Format For Roads Quarterly Statement(4 th Quarter)

PIU Name:- R.W.D.(W)Division Motihari

1	Name of the Road	Raghunathpur REO road to Parsauna		
2	Batch No.			
3	Project ID	31708201019		
4	Total Length of Road(in K.M.)	2.00		
5	Length of Road to Meet Required Service Level (Completed Length)(in K.M.)	2.00		
6	No of Total Quarter(ie 3 Months as a Unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount For Maintenance(in Lakh)	20.25762		
8	Quarterly Payment: 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh)	1.01288		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment (6) = (3) / (1)*(2)*(4)
		Length Non Compliant	Weightred Value for Payment Reduction (%)	
	Paved Roads(Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Total Payment Reduction for the Quarter (in Lakh)				0
To be Paid for the Quarter/ Demand (in Lakh)				1.01288

Date of Inspection by E/I or his agent

Prepared by Contractor's self Control unit

Ans 10/4/22

K. Singh
23/3/22
Name and Designation of Person inspecting road

Date:-

(Signature)

Signature of Person inspecting road

Certify by E/I (Signature) Date

Standrad Format For Roads Quarterly Statement(5 th Quarter)

PIU Name:- R.W.D.(W)Division Motihari

1	Name of the Road	Raghunathpur REO road to Parsauna		
2	Batch No.			
3	Project ID	31708201019		
4	Total Length of Road(in K.M.)	2.00		
5	Length of Road to Meet Required Service Level (Completed Length)(in K.M.)	2.00		
6	No of Total Quarter(ie 3 Months as a Unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount For Maintenance(in Lakh)	20.25762		
8	Quarterly Payment: 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh)	1.01288		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment (6) = (3) / (1)*(2)*(4)
		Length Non Compliant	Weightred Value for Payment Reduction (%)	
	Paved Roads(Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Total Payment Reduction for the Quarter (in Lakh)				0
To be Paid for the Quarter/ Demand (in Lakh)				1.01288

Date of Inspection by E/I or his agent

Prepared by Contractor's self Control unit

Name and Designation of Person inspecting road

Date:-

(Signature)

Signature of Person inspecting road

Certify by E/I (Signature) Date

Standrad Format For Roads Quarterly Statement(6 th Quarter)

Project Name : D. W. D. (W) Division (Mithun)

1	Name of the Road	Paghunathpur REC road to Parsauna		
2	Batch No.			
3	Project ID	11708201019		
4	Total Length of Road in K.M.	2.00		
5	Length of Road to Meet Required Service Level (Completed Length) in K.M.	2.00		
6	No. of Total Quarter (ie 3 Months as a Unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount For Maintenance) in Lakh	20.25762		
8	Quarterly Payment 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh)	1.01288		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment (6) = (3) / (1)*(2)*(4)
		Length Non Compliant	Weightred Value for Payment Reduction (%)	
	Paved Roads(Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Total Payment Reduction for the Quarter (in Lakh)				0
To be Paid for the Quarter/ Demand (in Lakh)				1.01288

Date of Inspection by E/I or his agent

Prepared by Contractor's self Control unit

22/04/22
JF

22/04/22
Name and Designation of Person inspecting road

(Signature)

Date:-

Signature of Person inspecting road

Certify by E/I (Signature) Date

Standrad Format For Roads Quarterly Statement(7 th Quarter)

PIU Name:- R.W.D.(W)Division Motihari

1	Name of the Road	Raghnathpur REO road to Parsauna		
2	Batch No.			
3	Project ID	31708201019		
4	Total Length of Road(in K.M.)	2.00		
5	Length of Road to Meet Required Service Level (Completed Length)(in K.M.)	2.00		
6	No of Total Quarter(ie 3 Months as a Unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount For Maintenance(in Lakh)	20.25762		
8	Quarterly Payment: 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh)	1.01288		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment (6) = (3) / (1)*(2)*(4)
		Length Non Compliant	Weightred Value for Payment Reduction (%)	
	Paved Roads(Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Total Payment Reduction for the Quarter (in Lakh)				0
To be Paid for the Quarter/ Demand (in Lakh)				1.01288

Date of Inspection by E/I or his agent

Prepared by Contractor's self Control unit

28/04/22
JE

Name and Designation of Person inspecting road

(Signature)

Date:-

Signature of Person inspecting road

Certify by E/I (Signature) Date

Requisition Form for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Works Division Motihari

1 Year (1st Quarter)

Department Of Bihar

11 Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

From:- Raghunathpur REO road to Parsauna
Kage No.MR-N/19-20 Motihari/08)

To:-

Executive Engineer
RWD, Works Division Motihari

Date:-

Length of Road :- 2.00 Km

Period :- From:- 12-06-2020 To 11-09-2020

Inspector :- A.E. RWD Sub Division : Motihari

Position :- A.E.

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
OM100	Sealed payment		1	2	3	4	5	6	7	8	9	10	
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							No Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Raveling)	m ²	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Raveling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	○ Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	N/A	N/A	N/A	N/A							
107	Concrete pavement	m ³	N/A	N/A	N/A	N/A							
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							Not Required
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil							Not Required
OM300	Other activities (Rain Cuts)												
OM301	Drainage including culverts major												
OM302	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required

Date:-

Signature of Person in Charge

23/09/20

23/9/20

Requisition Formlet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

D. Works Division Motihari

Government Of Bihar

OM01

Rural Works Department

1 Year (2 nd Quarter)

Road From:- Raghunathpur REO road to Parsauna
(Package No.MR-N/19-20 Motihari/08)

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Length of Road :- 2.00 Km
Period :- From:- 12-09-2020 To 11-12-2020
Inspector :- A.E RWD Sub Division : Motihari

To:-

Executive Engineer
RWD, Works Division Motihari

Date:-

Position :- A.E

No	Standard Of Work Item	Work Unit	Unit Of Required in each Kilometer										Comments
No	Name	Unit	1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	© Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	Nil	Nil	Nil	Nil							
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil							Not Required
OM300	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil							Not Required
OM301	Drainage including culverts major												Not Required
OM302	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required

28/09/22
jw

[illegible]

Bidder

Appendix

Executive Engineer,
RWD. Works Division, Motihari

Executive Engineer,
29/3/22

Requisition Form for Scheme Head-MR-43054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RD, Works Division Mothari

1 Year (3 rd Quarter)

Government Of Bihar
OM01
Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Raghunathpur REO road to Parsauna
(Package No.MR-N 19-20 Mothari 08)

To:-

Executive Engineer
RWD, Works Division Mothari

Date:-

Length of Road :- 2.00 Km

Period :- From:- 12-12-2020 To 11-03-2021

Inspector :- A.E.RWD Sub Division : Mothari

Position :- A.E

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed pavement												
OM101	Pothole Patching	m ²	7.5	11.25	Nil	Nil							Defects Rectified within stipulated time
OM102	Surface Depression and Rut patching	m ³	0.56	Nil	Nil	Nil							Defects Rectified within stipulated time
OM103	Crack Sealing	Lm	320	480	Nil	Nil							Defects Rectified within stipulated time
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Raveling)	m ²	7.5	11.25	Nil	Nil							Defects Rectified within stipulated time
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	0.56	0.84	N.A	N.A							Defects Rectified within stipulated time
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	89.92	134.88	Nil	Nil							Defects Rectified within stipulated time
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M ³	13.5	20.25	Nil	Nil							Defects Rectified within stipulated time
	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil							Not Required
OM300	Drainage including culverts major												
OM301	Surface Drains & Verges	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	2	1	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	2	1	Nil	Nil							Defects Rectified within stipulated time
	Other activities (Whirl washing)	M ³	76	38	Nil	Nil							Defects Rectified within stipulated time

A.E. RWD
7/2

29/07

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												Not Required
	Grass Control												Not Required
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
OM402	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Defects Rectified within stipulated time
	Cutting Of Shrubs From Road Way	No	320	480	Nil	Nil							Defects Rectified within stipulated time
	Other activities (Trimming of Grass)	M ²	720	1080	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Defects Rectified within stipulated time
OM501	Signs Maintenance	No	1	1	Nil	Nil							Defects Rectified within stipulated time
OM502	Guard Stones	Lm	2.68	4.01	N.A	N.A							Defects Rectified within stipulated time
OM503	Distance Stones	No	1	1	N.A	N.A							Defects Rectified within stipulated time
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

Bidder

Appendix

RWD. Works Division, Motihari

28/04/22
78

28/04/22

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

A/D, Works Division Mothari

1 Year (4 th Quarter)

Government Of Bihar

OM/01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Raghunathpur REO road to Parsauna
(Package No.MR-N/19-20 Mothari/08)

To:-

Executive Engineer
RWD, Works Division Mothari

Date:-

Length of Road :- 2.00 Km

Period :- From:- 12-03-2021 To 11-06-2021

Inspector :- A.E RWD Sub Division : Mothari

Position :- A.E

No	Standard Of Work Item	Work Unit	Unit Of Required in each Kilometer	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed payment													
OM101	Pothole Patching	m ²	11.25	16.88	Nil	Nil	Nil							Defects Rectified within stipulated time
OM102	Surface Depression and Rut patching	m ³	0.056	Nil	Nil	Nil	Nil							Defects Rectified within stipulated time
OM103	Crack Sealing	Lm	480	720	Nil	Nil	Nil							Defects Rectified within stipulated time
	Surface Treatment													
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	11.25	16.88	Nil	Nil	Nil							Defects Rectified within stipulated time
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	© Crocodile Cracking	m ²	Nil	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	0.84	1.27	N.A	N.A	N.A							Defects Rectified within stipulated time
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A	N.A							
	Other activities													
OM200	Shoulder													
	Unsealed Shoulder													
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	134	202	Nil	Nil	Nil							Defects Rectified within stipulated time
	(c) Holding water	Lm	Nil	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M ³	20.25	30.38	Nil	Nil	Nil							Defects Rectified within stipulated time
	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil	Nil							Not Required
OM300	Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	1	1	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	2	1	Nil	Nil	Nil							Defects Rectified within stipulated time
	Other activities(Whilw washing)	M ²	76	38	Nil	Nil	Nil							Defects Rectified within stipulated time

Asst Engineer
7-2

6/2/21

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

AD, Works Division Mothari

2 Year (1st Quarter)

Government Of Bihar

OM101

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Raghnathpur REO road to Parsauna
(Package No.MR-N/19-20 Mothari/08)

To:-

Executive Engineer
RWD, Works Division Mothari

Date:-

Length of Road :- 2.00 Km

Period :- From:- 12-06-2021 To 11-09-2021

Inspector :- A.E RWD Sub Division : Mothari

Position :- A.E

No	Standard Of Work Item	Work Unit	Unit Of Required in each Kilometer	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed payment													
OM101	Pothole Patching	m ²	7.5	11.25	Nil	Nil	Nil							Defects Rectified within stipulated time
OM102	Surface Depression and Rut patching	m ³	0.56	Nil	Nil	Nil	Nil							Defects Rectified within stipulated time
OM103	Crack Sealing	Lm	320	480	Nil	Nil	Nil							Defects Rectified within stipulated time
	Surface Treatment													
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	7.5	11.25	Nil	Nil	Nil							Defects Rectified within stipulated time
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	0.56	0.84	N.A	N.A	N.A							Defects Rectified within stipulated time
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A	N.A							
	Other activities													
OM200	Shoulder													
	Unsealed Shoulder													
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	89.92	134.88	Nil	Nil	Nil							Defects Rectified within stipulated time
	(c) Holding water	Lm	Nil	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M ³	13.5	20.25	Nil	Nil	Nil							Defects Rectified within stipulated time
	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil	Nil							Not Required
OM300	Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	2	1	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	2	1	Nil	Nil	Nil							Defects Rectified within stipulated time
	Other activities (Whilw washing)	M ²	76	38	Nil	Nil	Nil							Defects Rectified within stipulated time

28/07/21

28/07/21

No	standard Of Work Item	Work	Unit	1	2	3	4	5	6	7	8	9	10	Comments
M400	Vegetation													
	Grass Control													
	(a) Roadside- General Tidy	Ha		Nil	Nil	Nil	Nil							Not Required
OM401	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha		Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No		Nil	Nil	Nil	Nil							Not Required
OM402	Cutting Of Branches Of Trees	No		Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No		320	480	Nil	Nil							Defects Rectified within stipulated time
OM500	Other activities (Trimming of Grass)	M ²		720	1080	Nil	Nil							Defects Rectified within stipulated time
OM501	Safety Signage and Road			Nil										Not Required
	Signs Maintenance	No		1	1	Nil	Nil							Defects Rectified within stipulated time
OM502	Guard Stones	Lm		2.68	4.01	N.A	N.A							Defects Rectified within stipulated time
OM503	Distance Stones	No		1	1	N.A	N.A							Defects Rectified within stipulated time
OM504	Road Marking	M ²		Nil	Nil	Nil	Nil							Not Required
	Other activities													

Bidder

Appendix

Executive Engineer,
RWD, Works Division, Motihari

Date:-

28/04/22

Name and Designation of person

Requisition Formlet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RD, Works Division Motihari

2 Year (2 nd Quarter)

Government Of Bihar
OM101
Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Raghunathpur REO road to Parsauna
(Package No.MR-N/19-20 Mothari/08)

To:-

Length of Road :- 2.00 Km

Period :- From:- 12-09-2021 To 11-12-2021

Inspector :- A.E RWD Sub Division : Motihari

Executive Engineer
RWD, Works Division Motihari

Date:-

Position :- A.E

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed payment													
OM101	Pothole Patching	m ²	11.25	16.88	Nil	Nil	Nil							Defects Rectified within stipulated time
OM102	Surface Depression and Rut patching	m ³	0.056	Nil	Nil	Nil	Nil							Defects Rectified within stipulated time
OM103	Crack Sealing	Lm	480	720	Nil	Nil	Nil							Defects Rectified within stipulated time
	Surface Treatment													
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	11.25	16.88	Nil	Nil	Nil							Defects Rectified within stipulated time
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Di-cuts	m ²	0.84	1.27	N.A	N.A	N.A							Defects Rectified within stipulated time
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A	N.A							
	Other activities													
OM200	Shoulder													
	Unsealed Shoulder													
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	134	202	Nil	Nil	Nil							Defects Rectified within stipulated time
	(c) Holding water	Lm	Nil	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M ³	20.25	30.38	Nil	Nil	Nil							Defects Rectified within stipulated time
	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil	Nil							Not Required
OM300	Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	1	1	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	2	1	Nil	Nil	Nil							Defects Rectified within stipulated time
	Other activities(Whilw washing)	M ²	76	38	Nil	Nil	Nil							Defects Rectified within stipulated time

A.E RWD
7/8

2/9/21

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
A/400	Vegetation												Not Required
	Grass Control												Not Required
	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Defects Rectified within stipulated time
	Cutting Of Shrubs From Road Way	No	480	720	Nil	Nil							Defects Rectified within stipulated time
	Other activities (Trimming of Grass)	M ²	1080	1620	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Defects Rectified within stipulated time
OM501	Signs Maintenance	No	1	1	Nil	Nil							Defects Rectified within stipulated time
OM502	Guard Stones	Lm	4.01	6.02	N.A	N.A							Defects Rectified within stipulated time
OM503	Distance Stones	No	1	1	N.A	N.A							Defects Rectified within stipulated time
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

Signature
7/5

Appendix

Executive Engineer,
RWD, Works Division, Mithari

Signature
30/3/22

Bidder

9
4

ing

Requisition Form for Scheme Head-MR-4(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

2 Year (3 rd Quarter)

2. Works Division Motihari

Government Of Bihar

OM101

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Raeghunathpur REO road to Parsauna
(Package No.MR-N-19-20 Motihari/08)

Length of Road :- 2.00 Km

Period :- From:- 12-12-2021 To 11-03-2022

Inspector :- A.E RWD Sub Division : Motihari

To:-

Executive Engineer
RWD, Works Division Motihari

Date:-

Position :- A.E

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed payment													
OM101	Pothole Patching	m ²	7.5	11.25	Nil	Nil	Nil							Defects Rectified within stipulated time
OM102	Surface Depression and Rut patching	m ³	0.56	Nil	Nil	Nil	Nil							Defects Rectified within stipulated time
OM103	Crack Sealing	Lm	320	480	Nil	Nil	Nil							Defects Rectified within stipulated time
	Surface Treatment													
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	7.5	11.25	Nil	Nil	Nil							Defects Rectified within stipulated time
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	0.56	0.84	N.A	N.A	N.A							Defects Rectified within stipulated time
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A	N.A							
	Other activities													
OM200	Shoulder													
	Unsealed Shoulder													
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	89.92	134.88	Nil	Nil	Nil							Defects Rectified within stipulated time
	(c) Holding water	Lm	Nil	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M ³	13.5	20.25	Nil	Nil	Nil							Defects Rectified within stipulated time
	Other activities (Rain Cus)		Nil	Nil	Nil	Nil	Nil							Not Required
OM300	Drainage including culverts major	Lm	N.A	N.A	N.A	N.A	N.A							Not Required
OM301	Surface Drains & Verge	No	2	1	Nil	Nil	Nil							Not Required
OM302	Culvert Cleaning	M ³	2	1	Nil	Nil	Nil							Defects Rectified within stipulated time
OM303	Culvert and pit Repair	M ³	2	1	Nil	Nil	Nil							Defects Rectified within stipulated time
	Other activities (Whitewashing)	M ²	76	38	Nil	Nil	Nil							Defects Rectified within stipulated time

(Signature)

(Signature)

10/01/22

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												Not Required
	Grass Control												Not Required
	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM401	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	320	480	Nil	Nil							Defects Rectified within stipulated time
	Other activities (Trimming of Grass)	M ²	720	1080	Nil	Nil							Defects Rectified within stipulated time
OM500	Safety Signage and Road												Not Required
OM501	Signs Maintenance	No	1	1	Nil	Nil							Defects Rectified within stipulated time
OM502	Guard Stones	Lm	2.68	4.01	N.A	N.A							Defects Rectified within stipulated time
OM503	Distance Stones	No	1	1	N.A	N.A							Defects Rectified within stipulated time
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

Signature
21/2

Appendix

Executive Engineer,
RWD, Works Division, Morihari

Signature
29/3/22

Name of Road:- REO road Raghunathpur to Parsauna
Name of Contractor:-Virendra Kumar Singh

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	CATEGORY ROAD	Latitude	ongitude	Event	
28/2/22	13:4:32	12	0.1	260	0	2600	2704 G	26.80498	84.81074	Normal		$Y = 0 * X^2 + 0.998 * X + 109.5$
28/2/22	13:5:0	12	0.1	370	20.2	3700	3802 G	26.80567	84.81133	Normal		$X = 2800$
28/2/22	13:5:28	12	0.1	300	20.2	3000	3103 G	26.80632	84.81202	Normal		$Y = 2903$
28/2/22	13:5:59	12	0.1	310	20.2	3100	3203 G	26.80675	84.81278	Normal		
28/2/22	13:6:28	12	0.1	340	20.2	3400	3502 G	26.80671	84.81372	Normal		
28/2/22	13:6:54	12	0.1	370	20.2	3700	3802 G	26.80722	84.81444	Normal		(R) RURAL ROAD
28/2/22	13:7:34	12	0.1	310	20.2	3100	3203 G	26.80809	84.81473	Normal		Good
28/2/22	13:7:56	12	0.1	310	20.2	3100	3203 G	26.80886	84.8152	Culvert		<4000
28/2/22	13:8:30	12	0.1	280	20.2	2800	2903 G	26.80952	84.81588	Normal		Average
28/2/22	13:8:59	12	0.1	300	20.2	3000	3103 G	26.81031	84.81635	Normal		Poor
28/2/22	13:9:27	12	0.1	240	10.1	2400	2504 G	26.8112	84.81658	Normal		
28/2/22	13:9:56	12	0.1	240	10.1	2400	2504 G	26.81182	84.81825	Normal		
28/2/22	13:10:25	12	0.1	200	20.2	2000	2105 G	26.81122	84.81892	Normal		
28/2/22	13:10:52	12	0.1	210	20.2	2100	2205 G	26.81084	84.81988	Normal		
28/2/22	13:11:27	12	0.1	330	20.2	3300	3402 G	26.81047	84.82077	Normal		
28/2/22	13:11:50	12	0.1	300	20.2	3000	3103 G	26.81013	84.82172	Normal		
28/2/22	13:12:22	12	0.1	310	20.2	3100	3203 G	26.81001	84.82266	Normal		
28/2/22	13:12:55	12	0.1	330	20.2	3300	3402 G	26.8099	84.82369	Culvert		
28/2/22	13:13:28	12	0.1	230	10.1	2300	2403 G	26.81023	84.82411	Normal		
28/2/22	13:13:58	12	0.1	280	10.1	2800	2903 G	26.81073	84.82443	Normal		
Total IRI							61926					
Average IRI							3096.3					

28/2/22
J.E

28/2/22
AE

Name of Customer : Virender Kumar Singh
 Name of Work : REO road Raghunathpur to Pa Road
 Lab Job number : 06
 Date : 28-02-2022
 Section No. : 12

Test Date :	28-02-2022	Road Name :	REO road Raghunathpur to Pa
Machine No :	378	Road Type :	(R) RURAL ROAD
Start S No :	000km	Side :	
Start E No :	2000km	Interval	
Weather :	Normal	UV Range :	1105 To 5000 1000 mm/km
Start Location :	Raghunathpur	Dist Range :	0 To 21 01 * 1000 m
End Location :	Parasana Tal	Equation :	$Y = 0 * X^2 + 0.998 * X + 109.5$


Print Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\FWD-ATM\Desktop\Bump Mothari\Mothari\REO Road Raghunathpur To Parasana Tak

Name of Customer : Virender Kumar Singh. Name of Work / Road : REO road Raghunathpur to Parasana Tak. Lab

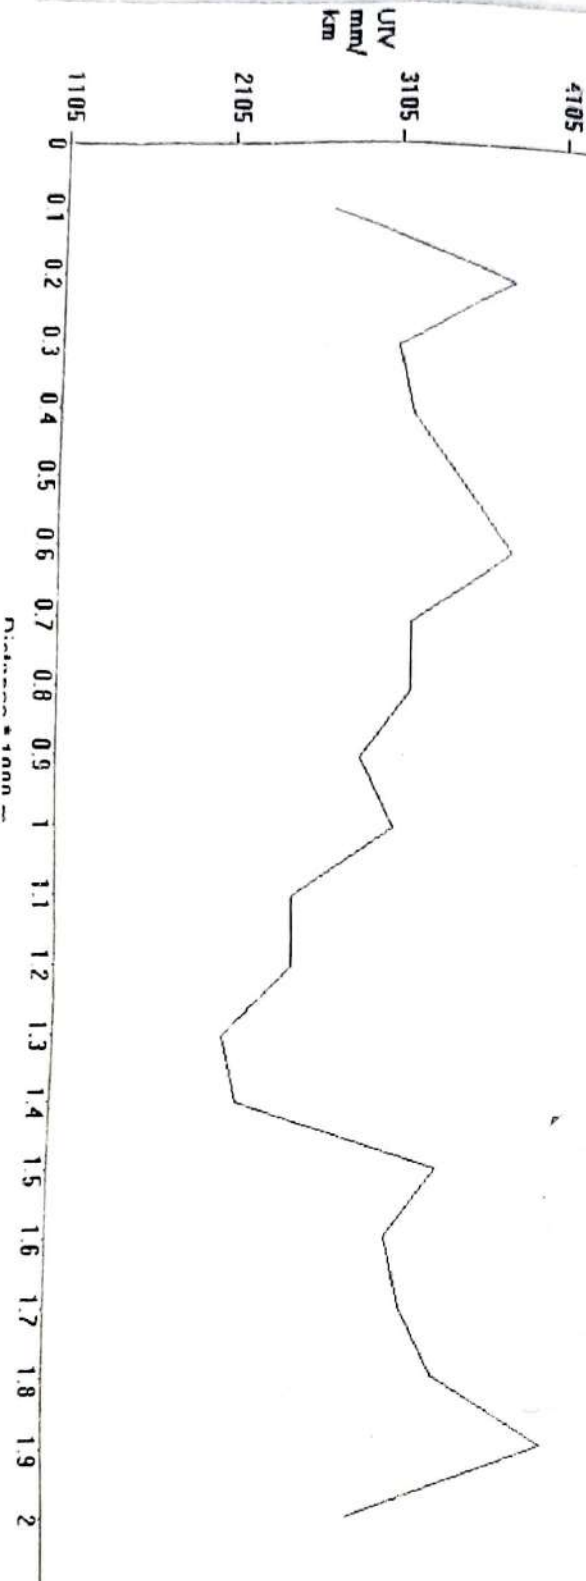

Total Pay :
 be Paid :

28/2/22
 12

28/04/22
 12
