

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

पत्रांक.....544013

दिनांक.....29/03/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।


विषय: नई अनुरक्षण नीति 2018 अंतर्गत वित्तीय वर्ष 2021-22 में अनुरक्षण मद में व्यय हेतु आवंटन की मांग।

महाशय,

उपर्युक्त विषय के संबंध में नई अनुरक्षण नीति 2018 अंतर्गत वित्तीय वर्ष 2021-22 में अनुरक्षण मद में व्यय हेतु संलग्न विवरणी के अनुसार 8.62289 (आठ लाख बासठ हजार दो सौ नवासी) रुपये का आवंटन उपलब्ध कराने की कृपा की जाये ताकि किये गये कार्यों का भुगतान किया जा सके।

अनुलग्नक:- यथोक्त।

विश्वासभाजन



29.3.22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

Maintenance Requisition Formate for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018

Name of Works Division - Muzaffarpur East-1

Name of Works Division - Muzaffarpur East-1				Actual Date of Completion	AA Details		Agreement							Actual Maintenance Expenditure							Length as per Bump Report	IRT As per Bump Report	Current Maintenance Demand						Remarks	
Road Details					Main Work Amount (in Lakh)	Maintenance Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	Length (in Km)	1st. Year Maintenance	2nd. Year Maintenance	3rd. Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintenance Expenditure			1st QTR Maintenance	2nd QTR Maintenance	3rd QTR Maintenance	4th QTR Maintenance	5th QTR Maintenance	6th QTR Maintenance		Total
Sl. No.	Name of Roads	Batch No.	Project ID																											
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31
1	Fatehpur Bhagwan - Mathurapur	RM/MUNUZ/19/0012	3160790329	12.07.2020	39.16	20.15000	35.19600	1.06800	2.00310	5.09677	2.41789	5.60401	16.18977	1.940	0.000	0.000	0.000	0.000	0.000	0.000	1.94	2520.947	0.80949	0.80949	0.80949	0.80949	0.80949		4.04744	
2	Rampur Kasi - Murapur	RM/MUNUZ/19/0012	3160790329	25.06.2021	19.13	9.75860	17.16700	0.51830	0.97115	2.46983	1.17150	2.71499	7.84577	0.940	0.000	0.000	0.000	0.000	0.000	0.000	0.94	2722.22	0.39229						0.39229	
3	NH - 77 (Akara B Bridge) to Jamin Kantaui (2001-02)	RM/MUNUZ/19/0012	3160790329	19.05.2023	39.90	20.86200	33.16700	1.11031	2.07385	5.26280	2.50070	5.78458	16.73264	2.000	0.000	0.000	0.000	0.000	0.000	0.000	2.00	1701.90	0.83663	0.83663	0.83663	0.83663	0.83663		4.18316	
Total																													8.62289	


 29.3.22
 Executive Engineer
 R.W.D. Works Division
 Muzaffarpur East-1

Road Name :- Fatehpur Bahgwanpur to mathurapur

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	U/V	TEGORY ROAD	IRI	Latitude	ongtitude	Event
4/2/22	14:2:12	13	0.1	260	0	2600		2557 G	3.49	25.95095	85.36929	Normal
4/2/22	14:2:24	13	0.1	210	20.2	2100		2063 G	2.88	25.95213	85.37045	Normal
4/2/22	14:2:52	13	0.1	190	20.2	1900		1865 G	2.63	25.95245	85.37146	Normal
4/2/22	14:3:7	13	0.1	290	20.2	2900		2854 G	3.85	25.95256	85.37246	Normal
4/2/22	14:3:20	13	0.1	350	10.1	3500		3447 G	4.55	25.95291	85.3732	Bridge
4/2/22	14:3:32	13	0.1	180	20.2	1800		1766 G	2.51	25.95374	85.37306	Normal
4/2/22	14:3:53	13	0.1	220	20.2	2200		2162 G	3	25.95462	85.37308	Normal
4/2/22	14:4:4	13	0.1	330	20.2	3300		3250 G	4.32	25.95554	85.37337	Normal
4/2/22	14:4:18	13	0.1	250	20.2	2500		2458 G	3.37	25.95629	85.37386	Normal
4/2/22	14:4:33	13	0.1	210	20.2	2100		2063 G	2.88	25.95612	85.37478	Normal
4/2/22	14:8:5	13	0.1	220	0	2200		2162 G	3	25.95546	85.37562	Normal
4/2/22	14:8:25	13	0.1	230	10.1	2300		2261 G	3.13	25.95467	85.37579	Normal
4/2/22	14:8:40	13	0.1	230	20.2	2300		2261 G	3.13	25.95427	85.3767	Normal
4/2/22	14:9:0	13	0.1	230	20.2	2300		2261 G	3.13	25.95375	85.37729	Normal
4/2/22	14:9:15	13	0.1	270	20.2	2700		2656 G	3.61	25.9534	85.37801	Normal
4/2/22	14:9:33	13	0.1	240	10.1	2400		2360 G	3.25	25.95332	85.37906	Normal
4/2/22	14:10:0	13	0.1	240	10.1	2400		2360 G	3.25	25.95329	85.38008	Normal
4/2/22	14:10:17	13	0.1	350	0	3500		3447 G	4.55	25.95353	85.38062	Normal
4/2/22	14:11:5	13	0.1	370	10.1	3700		3645 G	4.79	25.95387	85.38135	Normal
Avg.									2520.947			

$$Y = 0 * X^2 + 0.989 * X - 13.58$$

$$X = 3700$$

$$Y = 3645$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

Signature
5/6/22
J.C

Signature
5/6/22
J.C

Signature
29.3.22

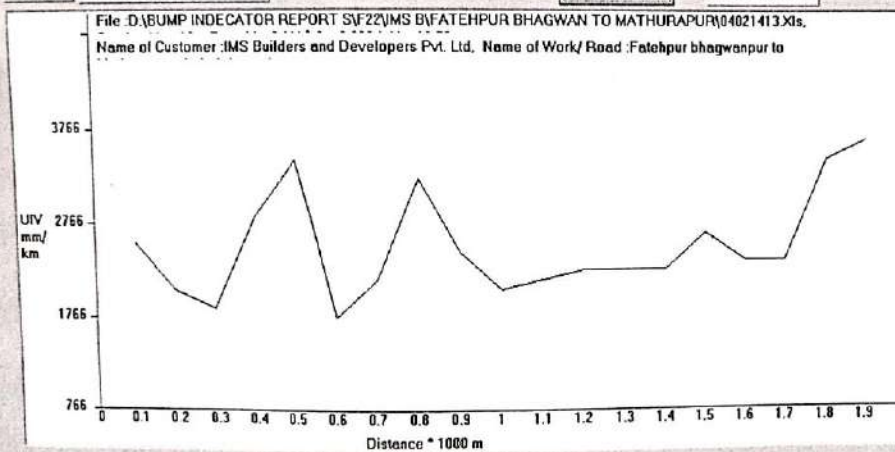
Name of Customer : IMS Builders and Developers Pvt.
Name of Work/ Road : Fatehpur bhagwanpur to Mathu
Lab Job number :
Date : 02-06-2009
Section No. : 13

Test Date : 28-04-2010 Road Name : ipur bhagwanpur to Mathurapur
Machine No : 376 Road Type : (R) RURAL ROAD
Start S No : Side :
Start E No : Interval
Weather : UIV Range : 766 To 5000 1000 mm/km
Start Location : Dist Range : 0 To 2 01 * 1000 m
End Location : Equation : $Y = 0 * X^2 + 0.989 * X - 13.58$

Print Generate Report and Graph

Redraw Graph

Map View



[Signature]
29/3/2012
J.C

[Signature]
02/03/2012
AE

[Signature]
29.3.22

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Muzaffarpur East-1

Government of Bihar
OM01
Rural works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From- Fatehpur Bhagwan - Mathurapur
Length of Road: 1.94 KM
Period : From.....
Inspector: A.E RWD Sub Division, Kudhani

To: Executive Engineer
RWD Works Division Muzaffarpur East-1
Position: A.E

Date:

Standard Work item			Work		Units of work required in each kilometre										Comments
S No	Name	Units	1	2	3	4	5	6	7	8	9	10			
OM100 Sealed Pavement															
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							No. Pothole found.		
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching found		
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing found		
OM104	Surface Treatment														
	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil							No Loss of Agreegate (Surface Ravelling) found		
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							No Bleeding/Flushing Required		
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil							No Crocodile Cracking found		
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil							No Edge Repair Required		
OM106	Digouts	m2	N/A	N/A	N/A	N/A									
OM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A									
	Other activities	Lm													
OM200 Shoulder															
OM201	Unsealed Shoulder	No													
	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil							No Edge Drop off Required		
	(b) Roughness, Scouring or Potholes	Lm	Nil	3%	2%	Nil							Defects rectified within stipulated time.		
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							No Holding water found		
OM202	Embankment Repair	No	Nil	Nil	Nil	Nil							No Embankment Repair Required		
	Other Activite (Raincut)		3%	1%	2%								Defects rectified within stipulated time.		
OM 300 Drainage including culverts major															
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A							Not Required		
OM302	Culvert Cleaning	Lm											Culvert maintain within stipulated time		
OM303	Culvert and Pit repair	m2	Nil	Nil	Nil	Nil							Not Required		

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	Fatehpur Bhagwan - Mathurapur
2	Batch No.	RM/MU/MUZ/19/0012
3	Project ID	31507202120
4	Total Length of Road (in Km)	1.94
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	1.94
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	16.18977
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	0.80949

Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.80949

Date of inspection by E/I or his agent Prepared by
Contractor's self Control unit

Name and Designation of person inspecting road
(Signature)

Date

Signature of person inspecting road

[Signature]
5/10/2022
Tc

[Signature]
07/10/2022
AE

[Signature]
29.3.22
Certify by E/I (signature) Date
