

कार्यालय
कार्यपालक अभियंता, ग्रामीण कार्य विभाग
कार्य प्रमंडल, दलसिंहसराय, समस्तीपुर

पत्रांक 422 अनु दलसिंहसराय / दिनांक 30/03/2022

प्रेषक, कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, दलसिंहसराय

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
सचिव -सह- प्राधिकृत पदाधिकारी, बिहार
ग्रामीण पथ विकास ऐजेंसी पटना।

विषय— **New Maintenance Policy 2018** योजनान्तर्गत पथ में आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि **New Maintenance Policy 2018** योजनान्तर्गत चल रहे पथ के निर्माणधीन कार्य के विरुद्ध चल रहे योजनाओं का भुगतान हेतु मो0— 273.42000 लाख की आवश्यकता है। अधियाचना का निर्माण कार्य विशिष्टियों के अनुरूप है तथा कार्य संतोषप्रद है।


अतः अनुरोध है कि अधियाचना पत्र के आधार पर आवंटन हेतु मो0— 273.42000 लाख उपलब्ध कराने की कृपा की जाय।

अनु0— 1) अधियाचना प्रपत्र।

2) 19ए फॉर्म।

3) IRI Report की छायाप्रति संलग्न।

विश्वासभाजन


30/3/2022

कार्यपालक अभियंता

ग्रामीण कार्य विभाग


30/3/2022 कार्य प्रमंडल, दलसिंहसराय

FORM GFR-19-A

(See Govt. of India's decision(i) below rule 150)
Form of Utilisation Certificate upto ~~MAR~~ 2022

New Maintenance Policy 2018(MR New)

PIU:- RWD Works Division Dalsinghsarai

Sl No	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lakh)	Amount Received (in Lakh)	Particulars
1	2	3	4	5
1	New Maintenance Policy 2018 (MR New)	2187.17861	2187.17861	Certified that out of Rs-2187.17861 Lakh received till date in favour of Executive Engineer, RWD Works Division Dalsinghsarai a Sum of Rs-2175.46317 Lakh has been utilized for the New Maintenance Policy 2018(MR New) Scheme as given in the margine for which it was Sanctioned and that the Balance of Rs-11.71544 Lakh remaining unutilized at the end of period under the time of completion
		2187.17861	2187.17861	

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was

Kind of Checks Exercised:-


- (i) Workers have been supervised by Executive Engineer/ Superintending Engineer
- (ii) Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer
- (iii) Construction materials have been tested
- (iv) Measurments have been recorded in the MB's and test check conducted by the
- (v) All other codal formalities have osverved

3. Physical Progress Achieved

- (i) Construction of Road Works
- (ii) Construction of CD Works


Sr.DAO

Rural Works Department,
Works Division Dalsinghsarai


Executive Engineer

Rural Works Department,
Works Division Dalsinghsarai


2019/22

Rural Works Department, Works Division Dalsinghsarai
Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018
(Initial Rectification and Surface Renewal)

Office of Division : PU(Dalsinghsarai)

Sl. No.	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Allotted Amount (Lac)	up to date expenditure as per MIS (in Lac)	Requisition Against work done (in lac)	Remarks
					Length (in Km)	Amount (in Lac)	Initial Rectification Surface Renewal (in Lac)	5 years Routine Maintenance (in Lac)										
1	RRM/SA/DAL/19/0007	MDR KABIR CHOWK - BOKIA MOHINPUR DHALA	NEA22000532	1855/24.06.2019	4.800	143.030	74.838	42.139	09 MBD/2021-22 24.06.2020	19-Nov-20	30.03.2022	2182	25mm	5.10%	0.00000	0.00000	74.82000	
2	RM/SA/DAL/19/0007	APPROACH ROAD - MEHSI	NEA22000543	1855/24.06.2019	124.88	61.62	112.395	55.458	8MBD/20212 0.02.2020	19-Nov-20	30.03.2022	2402	25mm	5.10%	0.00000	0.00000	112.35000	
3	RM/SA/DAL/19/0007	MDR - DESRI	NEA22000527	1855/24.06.2019	95.889	50.175	86.301	45.158	8MBD/2021 20.02.2020	19-Nov-20	30.03.2022	2204	25mm	5.10%	0.00000	0.00000	86.25000	
TOTAL					225.57	254.83	273.53	142.75							0.00	0.00	273.42000	

- Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed
- Up-to-date Physical Progress has been uploaded in MIS.

Divisional Account Officer,
Rural Works Department,
Works Division Dalsinghsarai


Executive Engineer
Rural Works Department,
Works Division Dalsinghsarai


30/12/20


कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, दलसिंहसराय

नयी अनुरक्षण निति - 2018 के अधियाचना हेतु प्रमाण-पत्र

क्र०सं०	शर्त	अभ्युक्ति
1	मापी पुस्त पर इस आशय का प्रमाण पत्र दर्ज है कि कार्य गुणवत्ता पूर्ण कराया गया है एवं विशिष्टियों के अनुरूप है।	एप्रोच रोड से महेसी डीह पथ का निर्माण कार्य गुणवत्ता पूर्ण कराया गया है एवं विशिष्टियों के अनुरूप है।
2	कराये गए कार्यों के सभी अवयवों के अवयववार 100 प्रतिशत कार्य का दर्ज मापी का सत्यापन कणीय अभियंता, कम से कम 50 प्रतिशत मापी का सत्यापन सहायक अभियंता एवं कम से कम 10 प्रतिशत मापी का सत्यापन कार्यपालक अभियंता द्वारा किये जाने का प्रमाण-पत्र को विभागीय MIS पर अपलोड किया जाय।	एप्रोच रोड से महेसी डीह पथ का कराये गए कार्यों का सभी अवयवों के अवयववार मापी का सत्यापन कणीय अभियंता, सहायक अभियंता, एवं कार्यपालक अभियंता द्वारा किया गया है।


3/4/22
कणीय अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल दलसिंहसराय

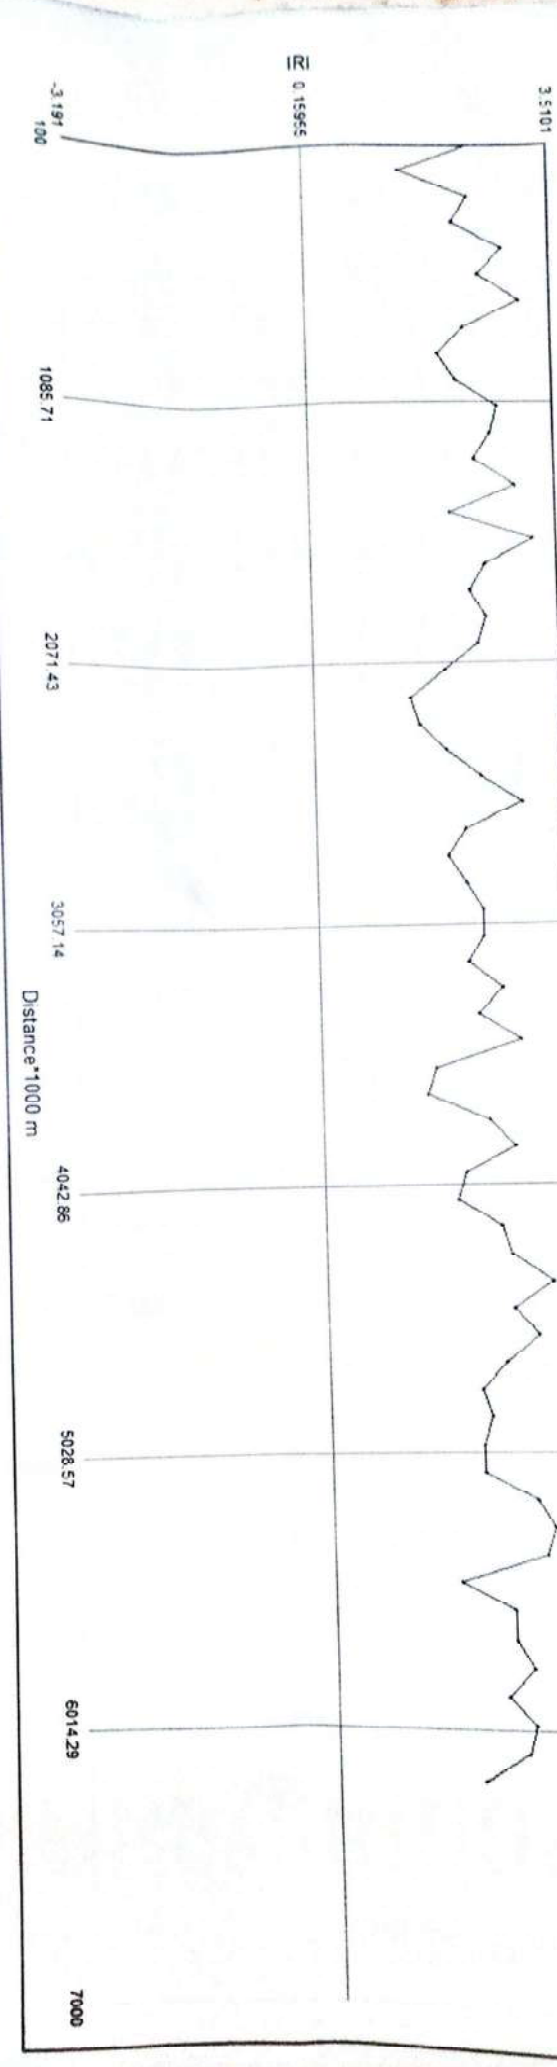

30/03/2022
सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल दलसिंहसराय


30/3/2022
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल दलसिंहसराय

(Amount in
lakhs)

13

Name of Customer: SONA INFRACON PRIVATE LIMITED, Machine no: 19192, Road: APPROACH ROAD - MEHSI, Date: 23-03-22, Section No: 16, Equation: $Y = 0.889 X + 355$



[Signature]
30.3.22
N

[Signature]
30/03/2022
AE

0%	10%	10%	15
Pr	men	ent in	Ar
ue of			

ce Poli

Name of the work: APPROACH ROAD - MEHSI

Date	Time	Test No	Distance (meter)	Total Distance (meter)	BUMP (cm)	Speed (Km/Hr)	UI (mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
23-03-22	10:54:16	16	100	100	15.0 cm	6.7 Km/Hr	1500.0 mm/Km	1688.5	2.411	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	10:54:41	16	100	200	7.0 cm	14.2 Km/Hr	700.0 mm/Km	977.3	1.48	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	10:55:03	16	100	300	15.0 cm	16.0 Km/Hr	1500.0 mm/Km	1688.5	2.411	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	10:55:21	16	100	400	13.0 cm	20.4 Km/Hr	1300.0 mm/Km	1510.7	2.183	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	10:55:39	16	100	500	19.0 cm	19.6 Km/Hr	1900.0 mm/Km	2044.1	2.86	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	10:55:54	16	100	600	16.0 cm	24.3 Km/Hr	1600.0 mm/Km	1777.4	2.525	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	10:56:12	16	100	700	21.0 cm	19.8 Km/Hr	2100.0 mm/Km	2221.9	3.081	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	10:56:32	16	100	800	14.0 cm	17.4 Km/Hr	1400.0 mm/Km	1599.6	2.298	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	10:56:49	16	100	900	11.0 cm	21.1 Km/Hr	1100.0 mm/Km	1332.9	1.952	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	10:57:56	16	100	1000	13.0 cm	7.9 Km/Hr	1300.0 mm/Km	1510.7	2.183	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	10:58:21	16	100	1100	18.0 cm	14.2 Km/Hr	1800.0 mm/Km	1955.2	2.749	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	10:58:54	16	100	1200	17.0 cm	11.3 Km/Hr	1700.0 mm/Km	1866.3	2.637	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	10:59:21	16	100	1300	15.0 cm	13.0 Km/Hr	1500.0 mm/Km	1688.5	2.411	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	10:59:49	16	100	1400	20.0 cm	12.8 Km/Hr	2000.0 mm/Km	2133	2.971	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	11:00:19	16	100	1500	12.0 cm	12.0 Km/Hr	1200.0 mm/Km	1421.8	2.068	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	11:00:50	16	100	1600	22.0 cm	11.9 Km/Hr	2200.0 mm/Km	2310.8	3.191	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	11:01:27	16	100	1700	16.0 cm	9.5 Km/Hr	1600.0 mm/Km	1777.4	2.525	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	11:01:53	16	100	1800	14.0 cm	13.5 Km/Hr	1400.0 mm/Km	1599.6	2.298	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	11:02:20	16	100	1900	16.0 cm	13.7 Km/Hr	1600.0 mm/Km	1777.4	2.525	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	11:02:49	16	100	2000	15.0 cm	12.4 Km/Hr	1500.0 mm/Km	1688.5	2.411	Good	25.7184516	N	85.9030634	E	Normal
23-03-22	11:03:36	16	100	2100	11.0 cm	7.6 Km/Hr	1100.0 mm/Km	1332.9	1.952	Good	25.7256146	N	85.9140872	E	Normal
23-03-22	11:04:16	16	100	2200	7.0 cm	8.9 Km/Hr	700.0 mm/Km	977.3	1.48	Good	25.7256146	N	85.9140872	E	Normal
23-03-22	11:04:50	16	100	2300	8.0 cm	10.8 Km/Hr	800.0 mm/Km	1066.2	1.6	Good	25.7256146	N	85.9140872	E	Normal
23-03-22	11:11:27	16	100	2400	11.0 cm	0.8 Km/Hr	1100.0 mm/Km	1332.9	1.952	Good	25.7256146	N	85.9140872	E	Normal
23-03-22	11:11:59	16	100	2500	15.0 cm	11.3 Km/Hr	1500.0 mm/Km	1688.5	2.411	Good	25.7256146	N	85.9140872	E	Normal
23-03-22	11:12:41	16	100	2600	20.0 cm	8.4 Km/Hr	2000.0 mm/Km	2133	2.971	Good	25.7358694	N	85.9165237	E	Normal
23-03-22	11:13:36	16	100	2700	13.0 cm	6.7 Km/Hr	1300.0 mm/Km	1510.7	2.183	Good	25.7358694	N	85.9165237	E	Normal
23-03-22	11:14:20	16	100	2800	11.0 cm	8.0 Km/Hr	1100.0 mm/Km	1332.9	1.952	Good	25.7358694	N	85.9165237	E	Normal
23-03-22	11:14:51	16	100	2900	13.0 cm	12.0 Km/Hr	1300.0 mm/Km	1510.7	2.183	Good	25.7358694	N	85.9165237	E	Normal
23-03-22	11:15:27	16	100	3000	15.0 cm	9.9 Km/Hr	1500.0 mm/Km	1688.5	2.411	Good	25.7358694	N	85.9165237	E	Normal
23-03-22	11:15:57	16	100	3100	15.0 cm	11.7 Km/Hr	1500.0 mm/Km	1688.5	2.411	Good	25.7358694	N	85.9165237	E	Normal
23-03-22	11:16:28	16	100	3200	13.0 cm	11.5 Km/Hr	1300.0 mm/Km	1510.7	2.183	Good	25.7436568	N	85.9269532	E	Normal

30-3-22

30/03/2022

23-03-22	11:17:03	16	100	3300	17.0 cm	10.4 Km/Hr	1700.0 mm/Km	1866.3	2.637	Good	25.7436568	N	85.9269532	E	Normal
23-03-22	11:17:34	16	100	3400	14.0 cm	11.5 Km/Hr	1400.0 mm/Km	1599.6	2.298	Good	25.7436568	N	85.9269532	E	Normal
23-03-22	11:18:04	16	100	3500	19.0 cm	11.8 Km/Hr	1900.0 mm/Km	2044.1	2.86	Good	25.7436568	N	85.9269532	E	Normal
23-03-22	11:18:27	16	100	3600	9.0 cm	15.2 Km/Hr	900.0 mm/Km	1155.1	1.718	Good	25.7436568	N	85.9269532	E	Normal
23-03-22	11:18:50	16	100	3700	8.0 cm	16.2 Km/Hr	800.0 mm/Km	1066.2	1.6	Good	25.7436568	N	85.9269532	E	Normal
23-03-22	11:19:10	16	100	3800	15.0 cm	17.5 Km/Hr	1500.0 mm/Km	1688.5	2.411	Good	25.7436568	N	85.9269532	E	Normal
23-03-22	11:19:31	16	100	3900	18.0 cm	17.2 Km/Hr	1800.0 mm/Km	1955.2	2.749	Good	25.7436568	N	85.9269532	E	Normal
23-03-22	11:19:53	16	100	4000	12.0 cm	16.5 Km/Hr	1200.0 mm/Km	1421.8	2.068	Good	25.7436568	N	85.9269532	E	Normal
23-03-22	11:20:17	16	100	4100	11.0 cm	15.0 Km/Hr	1100.0 mm/Km	1332.9	1.952	Good	25.757282	N	85.9347147	E	Normal
23-03-22	11:20:42	16	100	4200	16.0 cm	14.5 Km/Hr	1600.0 mm/Km	1777.4	2.525	Good	25.757282	N	85.9347147	E	Normal
23-03-22	11:21:09	16	100	4300	17.0 cm	13.1 Km/Hr	1700.0 mm/Km	1866.3	2.637	Good	25.757282	N	85.9347147	E	Normal
23-03-22	11:21:34	16	100	4400	22.0 cm	14.6 Km/Hr	2200.0 mm/Km	2310.8	3.191	Good	25.757282	N	85.9347147	E	Normal
23-03-22	11:21:58	16	100	4500	17.0 cm	15.0 Km/Hr	1700.0 mm/Km	1866.3	2.637	Good	25.757282	N	85.9347147	E	Normal
23-03-22	11:22:21	16	100	4600	20.0 cm	15.6 Km/Hr	2000.0 mm/Km	2133	2.971	Good	25.757282	N	85.9347147	E	Normal
23-03-22	11:22:45	16	100	4700	16.0 cm	14.7 Km/Hr	1600.0 mm/Km	1777.4	2.525	Good	25.757282	N	85.9347147	E	Normal
23-03-22	11:23:31	16	100	4800	13.0 cm	7.9 Km/Hr	1300.0 mm/Km	1510.7	2.183	Good	25.757282	N	85.9347147	E	Normal
23-03-22	12:11:29	16	100	4900	14.0 cm	10.4 Km/Hr	1400.0 mm/Km	1599.6	2.298	Good	25.757282	N	85.9347147	E	Normal
23-03-22	12:11:48	16	100	5000	13.0 cm	18.4 Km/Hr	1300.0 mm/Km	1510.7	2.183	Good	25.757282	N	85.9347147	E	Normal
23-03-22	12:12:08	16	100	5100	13.0 cm	18.9 Km/Hr	1300.0 mm/Km	1510.7	2.183	Good	25.757282	N	85.9347147	E	Normal
23-03-22	12:12:39	16	100	5200	19.0 cm	11.4 Km/Hr	1900.0 mm/Km	2044.1	2.86	Good	25.7623255	N	85.9410331	E	Normal
23-03-22	12:12:59	16	100	5300	21.0 cm	17.4 Km/Hr	2100.0 mm/Km	2221.9	3.081	Good	25.7623255	N	85.9410331	E	Normal
23-03-22	12:13:19	16	100	5400	20.0 cm	18.0 Km/Hr	2000.0 mm/Km	2133	2.971	Good	25.7623255	N	85.9410331	E	Normal
23-03-22	12:13:51	16	100	5500	10.0 cm	11.7 Km/Hr	1000.0 mm/Km	1244	1.836	Good	25.7623255	N	85.9410331	E	Normal
23-03-22	12:14:25	16	100	5600	16.0 cm	10.2 Km/Hr	1600.0 mm/Km	1777.4	2.525	Good	25.7623255	N	85.9410331	E	Normal
23-03-22	12:14:51	16	100	5700	16.0 cm	14.2 Km/Hr	1600.0 mm/Km	1777.4	2.525	Good	25.7623255	N	85.9410331	E	Normal
23-03-22	12:15:15	16	100	5800	18.0 cm	15.0 Km/Hr	1800.0 mm/Km	1955.2	2.749	Good	25.7623255	N	85.9410331	E	Normal
23-03-22	12:15:38	16	100	5900	15.0 cm	15.0 Km/Hr	1500.0 mm/Km	1688.5	2.411	Good	25.7623255	N	85.9410331	E	Normal
23-03-22	12:16:00	16	100	6000	18.0 cm	16.8 Km/Hr	1800.0 mm/Km	1955.2	2.749	Good	25.7623255	N	85.9410331	E	Normal
23-03-22	12:16:36	16	100	6100	17.0 cm	10.5 Km/Hr	1700.0 mm/Km	1866.3	2.637	Good	25.7623255	N	85.9410331	E	Normal
23-03-22	12:17:30	16	100	6200	12.0 cm	10.5 Km/Hr	1200.0 mm/Km	1421.8	2.068	Good	25.7623255	N	85.9410331	E	Normal

IRI VALUE 2402
MACHINE ID 19192

30.3.22

30/03/2022
AB
