

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पश्चिम

पत्रांक :- 1196 अ.अ. मुज०.

दिनांक :- 25/7/22

प्रेषक:- कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पश्चिम।

सेवा में,
अपर मुख्य कार्यपालक पदाधिकारी
-सह-सचिव,
ग्रामीण कार्य विभाग, बिहार, पटना।


विषय:- शीर्ष नई अनुरक्षण नीति-2018 (MR) अनुरक्षण अन्तर्गत वित्तीय वर्ष 2022-23 में व्यय हेतु
आवंटन की मांग।

महाशय,

उपर्युक्त विषयक शीर्ष नई अनुरक्षण नीति-2018 (MR) अनुरक्षण अन्तर्गत वित्तीय वर्ष 2022-23 में व्यय हेतु आवंटन संलग्न विवरणी के अनुसार रु० 31.49128 (एकतीस लाख उनचास हजार एक सौ अठाईस) रुपये मात्र का आवंटन उपलब्ध कराने की कृपा की जाये, ताकि किये गये कार्य का भुगतान किया जा सके।

अनुलग्नक- 1. विहित प्रपत्र में अधियाचना।

विश्वासभाजन


25/07/2022

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पश्चिम

Maintenance Requisition Formate for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018

Name of Works Division - Muzaffarpur West

Road Details										AA Details		Agreement						Actual Maintenance Expenditure						Current Maintenance Demand					Remarks
Sl. No.	Name of Raods	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh)	Minteanu ee Amount (in lakh)	Main Work Amount (in Lakh)	Agre emen t-1	Agree ment-2	Agree ment-3	Agreem ent-4	Agree ment-5	Total Maintenance (in K.M)	Length as per Bump Report	1st. Year Maintenance	2nd. Year Maintenance	3rd. Year Maintenance	4th. Year Maintenance	5th. Year Maintenance	Total Maintenance Expenditure	Length as per Bump Report	IRI As per bump Report	1st OTR Maintenance	2nd OTR Maintenance	3rd OTR Maintenance	4th OTR Maintenance	Total		
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	31	32	
1	Improvement of Shyampr Bhaja to Hehra Chowk Via Dalit Basti Road	RM/MU/MUZ/190022	31507201002	19/05/2021	35.810	17.260	32.17200	1.13792	1.68992	4.93297	2.20158	5.47845	15.44084	2.000	0.000	0.000	0.000	0.000	0.000	0.000	2.000	2427.000	0.77204	0.77204			1.54408		
2	HARDARPUR - NARAYANPUR PATH	RM/MU/MUZ/190022	NEA220002413	28/05/2021	56.090	21.350	50.39500	1.39634	2.09055	6.14856	2.73856	6.83885	19.21286	2.500	0.000	0.000	0.000	0.000	0.000	0.000	2.500	1996.000	0.96064	0.96064			1.92129		
3	NH-28 Near Narsanda Chowk - Madhuban via Pasi Tola	RM/MU/MUZ/190022	NEA220002449	04/06/2021	20.830	11.310	18.67100	0.73777	1.06181	3.27588	1.43476	3.64666	10.15688	1.350	0.000	0.000	0.000	0.000	0.000	0.000	1.350	1625.000	0.50784				0.50784		
4	kanti marwan - bheruayahi pingsy road	RM/MU/MUZ/190022	NEA220002477	19/05/2021	60.599	31.838	54.38000	2.05132	3.07124	9.12957	4.07700	10.14475	28.47388	3.700	0.000	0.000	0.000	0.000	0.000	0.000	3.700	2017.000	1.42369	1.42369			2.84739		
5	MARWAN-TERIAPUR - CHAINPUR	RM/MU/MUZ/190024	NEA220002399	17/11/2020	157.680	58.270	141.75100	3.01952	5.46912	17.24543	7.25090	19.22649	52.21146	7.300	0.000	0.000	0.000	0.000	0.000	0.000	7.300	2354.000	2.61057	2.61057	2.61057		10.44229		
6	ROKSA - ROKSH SOUTHERN	RM/MU/MUZ/190024	NEA220002423	17/11/2020	76.441	33.185	68.74900	1.74488	3.13151	9.78165	4.14470	10.90735	29.71009	4.120	0.000	0.000	0.000	0.000	0.000	0.000	4.120	2538.000	1.48550	1.48550	1.48550	1.48550	5.94282		
7	Bishundaipur - Fatehpur	RM/MU/MUZ/190024	NEA220002444	17/11/2020	58.981	25.155	52.88300	1.36208	2.40217	7.40106	3.15489	8.23862	22.55882	3.100	0.000	0.000	0.000	0.000	0.000	0.000	3.100	1310.000	1.12794	1.12794	1.12794	1.12794	4.51179		
8	NH102 - SUBHANKARPUR PATH	RM/MU/MUZ/190024	NEA220002487	17/11/2020	43.762	21.046	39.32200	1.13969	2.90582	6.19711	2.63427	6.89612	18.87301	2.600	0.000	0.000	0.000	0.000	0.000	0.000	2.600	1924.000	0.94365	0.94365	0.94365	0.94365	3.77460		
Total																										31.49128			

Signature
Executive Engineer
R.W.D. Works Division
Muzaffarpur West

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	HARDARPUR - NARAYANPUR PATH		
2	Batch No.	RM/MU/MUZ/19/0022		
3	Project ID	NEA220002413		
4	Total Length of Road (in Km)	2.500		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	2.500		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	19.21286		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	0.96064		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.96064

Date of inpection by E/1 or his agent Prepared by
Contractor's self Control unit

Date

17/11/22
JF

Signature of person inspecting road

[Signature]

Name and Designation of person inspecting road
(Signature)

[Signature]
35107/22

CAUTIONED (Signature)
Rular Work's Department
Mark's Division Muzaffarpur West

Requisition Format for Scheme Head - MIR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)													
Name of Works Division :- Muzaffarpur West				SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT									
Government of Bihar OM01 Rural works Department				To: Executive Engineer RWD Works Division Muzaffarpur West Date:									
Road From:----- HARDARPUR - NARAYANPUR PATH				Position: A.E									
Length of Road- 2.500 KM													
Period :----- From:-----													
Inspector:----- A.E RWD Sub Division, Kanti													
S No	Standard Work item	Work Units	Units of work required in each kilometre										Comments
	Name		1	2	3	4	5	6	7	8	9	10	
	OM100 Sealed Pavement												
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							No Pothole found
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing found
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil							No Crocodile Cracking found
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil							No Edge Repair Required
OM106	Digouts	m2	N/A	N/A	N/A	N/A							
OM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A							
	Other activities	Lm											
OM200 Shoulder													
OM201	Unsealed Shoulder	No											
	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil							No Edge Drop off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	3%	2%	Nil							Defects rectified within stipulated time.
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							No Holding water found
OM202	Embankment Repair	No	Nil	Nil	Nil	Nil							No Embankment Repair Required
	Other Activities (Raincut)		3%	1%	2%								Defects rectified within stipulated time.
OM 300 Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A							Not Required
OM302	Culvert Cleaning	Lm											Culvert maintain within stipulated time
OM303	Culvert and Pit repair	m2	Nil	Nil	Nil	Nil							Not Required

[illegible]

Bidder

25/07/10
Executive Engineer, Rural Work Department,
Work Division, Muzaffarpur West

2015/10/22

Appendix

$$Y = 927$$

(R) RURAL ROAD

Name of Road - Hardarpur to Narayanpur Path

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	IRI CATEGORY		Latitude	ongitude	Event
						OR mm/km	ROAD UIV			
15/6/22	17:2:1	16	0.1	300	0	3000	2953 G	3.97	26.18221	85.25685 Normal
15/6/22	17:2:36	16	0.1	220	10.1	2200	2162 G	3	26.18136	85.25655 Normal
15/6/22	17:3:13	16	0.1	210	10.1	2100	2063 G	2.88	26.18046	85.25631 Normal
15/6/22	17:3:13	16	0.1	190	10.1	1900	1865 G	2.63	26.17959	85.25608 Culvert
15/6/22	17:4:0	16	0.1	230	10.1	2300	2261 G	3.13	26.17901	85.25646 Normal
15/6/22	17:4:22	16	0.1	150	20.2	1500	1469 G	2.13	26.17877	85.25741 Normal
15/6/22	17:4:22	16	0.1	190	10.1	1900	1865 G	2.63	26.17859	85.25843 Culvert
15/6/22	17:5:0	16	0.1	260	10.1	2600	2557 G	3.49	26.17811	85.25929 Normal
15/6/22	17:5:0	16	0.1	180	20.2	1800	1766 G	2.51	26.17775	85.2602 Normal
15/6/22	17:5:33	16	0.1	210	10.1	2100	2063 G	2.88	26.17742	85.26111 Normal
15/6/22	17:6:0	16	0.1	150	10.1	1500	1469 G	2.13	26.17713	85.2621 Normal
15/6/22	17:6:8	16	0.1	280	10.1	2800	2755 G	3.73	26.17666	85.26298 Normal
15/6/22	17:6:43	16	0.1	260	10.1	2600	2557 G	3.49	26.17615	85.26379 Normal
15/6/22	17:7:0	16	0.1	220	10.1	2200	2162 G	3	26.17566	85.26468 Normal
15/6/22	17:7:19	16	0.1	290	10.1	2900	2854 G	3.85	26.1752	85.26556 Normal
15/6/22	17:7:54	16	0.1	210	20.2	2100	2063 G	2.88	26.17504	85.26652 Normal
15/6/22	17:8:0	16	0.1	180	10.1	1800	1766 G	2.51	26.17471	85.26741 Normal
15/6/22	17:8:29	16	0.1	160	20.2	1600	1568 G	2.26	26.17415	85.26818 Normal
15/6/22	17:8:29	16	0.1	150	20.2	1500	1469 G	2.13	26.17352	85.26891 Normal
15/6/22	17:8:29	16	0.1	150	20.2	1500	1469 G	2.13	26.17322	85.26987 Normal
15/6/22	17:9:4	16	0.1	220	20.2	2200	2162 G	3	26.17295	85.27082 Normal
15/6/22	17:9:4	16	0.1	170	20.2	1700	1667 G	2.38	26.1727	85.27184 Normal
15/6/22	17:9:40	16	0.021	20	10.1	952	927 G	1.41	26.17265	85.27204 Normal
						AVG:-	1996			


AVG:-

1996

Salvador
Executive Engineer
Rural Work's Department
Work's Division, Mazatlan, Nayarit

File : E:\Software\Bump Indicator Software\Reports\Maintenance\A.P. CONSTRUCTION\Hardarpur to Narayanpur

Name of Customer : Name of Work/ Road : Lab Job number :

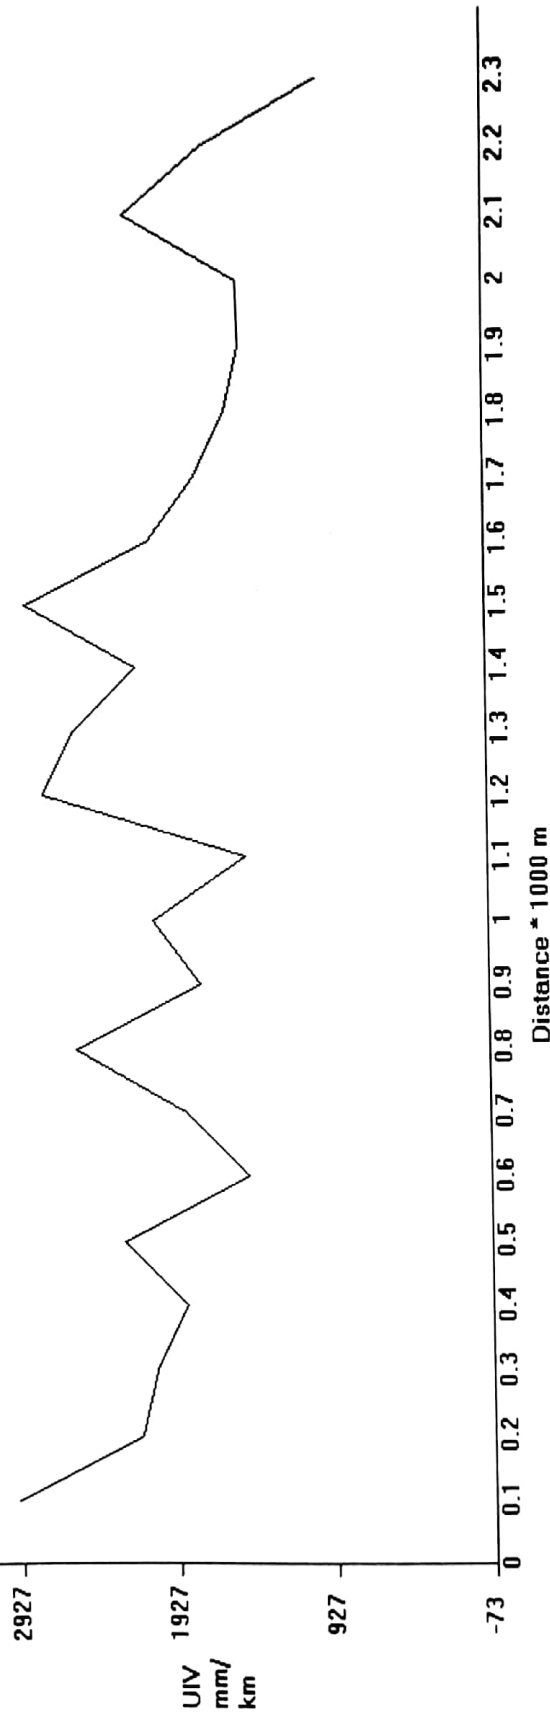

Signature
25/07/22
Executive Engineer
Rural Work's Department
Work's Division, Muzaffarpur West
