

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पालीगंज।

पत्रांक : 1082 (अब्ज)

पालीगंज/दिनांक : 27/7/2022

प्रेषक :

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
—सह—सचिव,
बिहार ग्रामीण पथ विकास, अभिकरण
ग्रामीण कार्य विभाग, पटना।

विषय:—शीर्ष—MR, 3054 Under-Bihar Rural Road Maintenance Policy-2018 योजना अन्तर्गत आवंटन का
अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष—MR, 3054 Under-Bihar Rural Road Maintenance
Policy-2018 योजना अन्तर्गत पथों का अधियाचना का मॉग विहित प्रपत्र में तैयार कर Signed Hard Copy
of Recorded IRI के साथ अधियाचना हेतु भेजी जा रही है।

अतः अनुरोध है कि उक्त योजना का आवंटन उपलब्ध करने की कृपा की जाय, ताकि संवेदक
का भुगतान हो सके।

अनु.:—यथोक्त।

विश्वासभाजन

23/7/22

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।

23/7/22
Sr. Divisional Accounts Officer
Rural Work Department
Works Division Patiganj

27/7/2022

Requisition Format for Scheme Head-MR (305-1) under Bharat Rural Road Maintenance Policy- 2018 (Initial Rectification and Surface Renewal)

Name of Work Division-Paliganj

Name of Work Division-Paliganj																			
S.L no	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. and Date	Administrative Approval (AA)		Agreement Amount			Agreement No.&Date	Date of completion as per agreement	Actual date of completion	Value of IRI (in mm/km) (Average)	Thickness of bitumen Layer (in mm)	Value of Bitumen content in Percentage	Previous Total Allowed Amount (in lakh)	Up-to-date expenditure as per Mis (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length in KM	Amount of (in Lakh)	Initial Rectification With Surface Renewal (lakh)	5 Year Routine Maintenance (in Lakh)											
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	
1	RM/PA/P AL/15/005	Patut Nisarpu ra road to Barah	10100102230	Lt no.-3662 Dt.- 26.08.2019	1.55	50.976	31.5882	13.64116	03/MBD/M R3054New Maintenance Policy 2018 2021-22&23.12.2021	22.08.22	-	3.346	SDBC (25 mm)	5.01%	0	0	20.85351	Surface work is completed as per specification & verification of surface by a Bump Indicator Machine 100% measurement by A.E. & 50% F.F.	
Total																		20.85351	

Total Amount:- 20.85351.00

(Twenty Lacs Eighty Five thousand Three hundred Fifty one only)

24.07.22
Sr. Divisional Accounts Officer
Rural Work Department
Works Division Paliganj

27.7.22
Executive Engineer
Rural Works Deptt.
Works Division Paliganj

27.7.2022

FORM GFR 19-A

(See Government of India's Decision (1) below Rule-150)
Form of utilisation Certificate up to the end of July 2022

PIU: RWD Works Division , Paliganj

Sl No.	Name of Scheme	Sanction No. & Date with Amount	Amount Received (In Rs.)	Particulars
1	Construction of Rural roads under RURAL ROAD MAINTENANCE POLICY 2018		327734014.00	Certified that out of Rs 327734014.00 received during the year 2022-23 in favour of Ex. Engineer, RWD, Works Div. Paliganj Bihar a sum of Rs 325947339.00 has been utilized for the purpose of const of road under Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 1786675.00 remaining unutilized at the end to the period under
Total			327734014.00	

2. Certified that I have satisfied myself that the conditions of which the grants sanction Sanctioned have been duly fulfilled/are being fulfilled and I have exercised the checks to see the money was actually utilised for the purpose for which it was sanctioned.

Krishna 27/7/22
Sr. Divisional Accounts Officer
Rural Works Department
Works Division, Paliganj
27/7/22
Executive Engineer
Rural works Deptt.
Works Division, Paliganj
27/7/22

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग , क्षेत्रीय प्रयोगशाला, गुलजारबाग
पटना - 800007

पत्रांक : 323/313

पटना/दिनांक : 16-06-2022

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना-7

सेवा में,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल पालीगंज

विषय :- योजना / गैर योजना शीर्ष M.R. 355 अंतर्गत निर्माणाधीन पथ/पुल/पुलिया कार्यों में प्रयुक्त निर्माण सामग्रियों की गुणवत्ता के जाँचफल प्रतिवेदन के संबंध में।

प्रसंग :- कार्यपालक अभियंता/सहायक अभियंता कार्य प्रमण्डल/कार्य अवर प्रमण्डल का पत्रांक दिनांक

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के संदर्भ में योजना / गैर योजना शीर्ष M.R. 355 अंतर्गत निर्माणाधीन पथ/पुल/पुलिया कार्यों में प्रयुक्त निर्माण सामग्रियों के गुणवत्ता जाँचफल प्रतिवेदन आवश्यक कारवाई हेतु भेजी जाती है जो निम्नवत है:-

क्रम संख्या	पथ/पुल/पुलिया का नाम	जाँच का प्रकार
1.	Patul Nisarpura Path & Barah Path	SDSC chips Ratuman Constant for 80x
2.		

अनु० :- यथोक्त

पटना - 7

विश्वासभाजन

16/6/22
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, गुलजारबाग

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D., GULZARBAGH, PATNA - 7

PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

Name of Project/Road :- Patat Nisarpara Path to Barah Path

Name of Scheme :- MR-3554

Name of Agency :- Swati Eng'g Cons Pvt. Ltd.

Nature of sample :- Semi Dense Bituminous Concrete Date of Collection/Received :- 21/6/22

Location :- 210 M

Date of Test :- 16/6/2022

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division

vide letter No. ----- Dt. -----

Agreement No / Package No. :

Material collected by AE & B. S. K.

Sl. No.	A.I.V.	
	Average Test Value	Required Value(Max)
1.		30%

Sl. No.	Sieve Size in (mm)	Weight of Sample Taken Kgs 10.650					Remarks
		Weight Retd.	% of Wt. Retained	% of Cum. Retained	% of Passing	Required value	
1	13.2	0.000	0.00	0.00	100	100	
2	9.5	0.564	5.30	5.30	94.70	90-100	
3	4.75	5.059	47.50	52.80	47.20	35-51	
4	2.36	1.560	14.65	67.45	32.55	24-39	
5	1.18	0.453	4.25	71.70	28.30	15-30	
6	0.300	1.214	11.40	83.10	16.90	9-19	
7	0.075	1.246	11.70	94.80	5.20	3-8	

Copy Submitted to/forwarded to:

E.E. R.W.D. Works Division :-

Patat
16.6.2022
Regional Laboratory
R.W.D. Guljarbagh patna - 7

Patat
16/06/2022
A.E.
Regional Laboratory
R.W.D. Guljarbagh patna - 7

Patat
16/6/22
E. E.
Regional Laboratory
R.W.D. Guljarbagh patna - 7

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D., GULZARBAGH, PATNA - 7

PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

Name of Project/Road :- Patut Nisarpura Path to Barah Path.

Name of Scheme :- M/R - 3054

Name of Agency :- Shree Engicon Pvt Ltd

Nature of sample :- Semi Dense Bituminous Concrete Date of Collection/Received :- 03.06.2022

Location :- 1420m

Date of Test :- 16.06.2022

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division -----

vide letter No. ----- Dt. -----

Agreement No / Package No. : material Collected by A.E. & Quality Staff.

Sl. No.	A.I.V.	
	Average Test Value	Required Value(Max)
1.		30%

Sl. No.	Sieve Size in (mm)	Weight of Sample Taken Kgs 9.460					Remarks
		Weight Retd.	% of Wt. Retained	% of Cumm. Retained	% of Passing	Required value	
1	13.2	0.000	0.00	0.00	100	100	
2	9.5	0.435	4.60	4.60	95.40	90-100	
3	4.75	4.654	49.20	53.80	46.20	35-51	
4	2.36	0.710	7.50	61.30	38.70	24-39	
5	1.18	1.149	12.15	73.45	26.55	15-30	
6	0.300	1.130	11.95	85.40	14.60	9-19	
7	0.075	0.951	10.05	95.45	4.55	3-8	

Copy Submitted to/forwarded to:

E.E. R.W.D. Works Division :-

Bois
16.6.2022

Regional Laboratory
R.W.D. Guljarbagh patna - 7

SR
16/06/2022

Regional Laboratory
R.W.D. Guljarbagh patna - 7

Prabhat
16/6/22

E. E.
Regional Laboratory
R.W.D. Guljarbagh patna - 7

Letter No. _____

Date ____/____/____

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D., GULJARBAUGH, PATNA - 7

Bituminous mix

Name of Project/Road :- Patna Misarpura Pk. as Barak Pk.

Name of Scheme :- MR-354

Name of Agency :- Swift Engineers Pvt. Ltd.

Nature of sample :- Bitumen Content for SORC

Location :- 200M

Date of Collection/Received :- 31/6/2022

Date of Test :- 16/06/2022

Ref :- Material sent by E.E./A.E.R.W.D. WORKS Division/Sub Division ----- vide letter No. ----- Dt. -----

Agreement No / Package No. :

Material collected by AE & Ac Staff.

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	500.00	500.00	502.00	
2	Wt. of Dry chips after extraction (b)	475.00	474.88	476.91	
3	Percentage of bitumen (in the mix) [(a-b)*100/a] (%)	5.00	5.02	5.00	
4	Average % bitumen	5.01			

Regional Laboratory
R.W.D. Guljarbaugh patna - 7Regional Laboratory
R.W.D. Guljarbaugh patna - 7Regional Laboratory
R.W.D. Guljarbaugh patna - 7

Letter No. _____

Date ____/____/____

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D., GULZARBAGH, PATNA - 7

Bituminous mix

Name of Project/Road :- Patna Nisarapur Path to Bank Path.

Name of Scheme :- M/R-3054

Name of Agency :- Swati Engineering Pvt. Ltd.

Nature of sample :- Bitumen Content for SSB

Location :- Ch-1420mk

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division _____

Date of Collection/Received :- 02/06/2022

Date of Test :- 16/6/2022

vide letter No. _____ Dt. _____

Agreement No / Package No. :

Material Collected by Me @ 8.30 shift.

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	500.00	503.00	500.00	
2	Wt. of Dry chips after extraction (b)	474.95	477.85	474.92	
3	Percentage of bitumen (in the mix) [(a-b)*100/a] (%)	5.01	5.00	5.01	
4	Average % bitumen	5.01			

02/06/2022
T.A.

02/06/2022
A.E.

02/06/2022
E.E.

Regional Laboratory
R. W. D. Guljarbagh patna - 7

Regional Laboratory
R. W. D. Guljarbagh patna - 7

Regional Laboratory
R. W. D. Guljarbagh patna - 7

Name of work : Patut Nisarapura Road to Barah	
Name of customer : Swift Engicon Pvt Ltd	
(R)Rural Road	
Good	Average
< 4000	4001 - 5000
	Poor
	> 5000


Date	Time	Test No	Distance(m)	Total Distance(m)	BUMF(cm)	Speed(Km/Hr)	U/(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
04-07-22	16:05:01	24	100	100	20.0 cm	28.7 Km/Hr	2000.0 mm/Km	1919	2.7	Good	25.4556683	N	84.78712483	E	Normal
04-07-22	16:05:19	24	100	200	22.0 cm	30.3 Km/Hr	2200.0 mm/Km	2104	2.93	Good	25.4559773	N	84.78904495	E	Normal
04-07-22	16:05:46	24	100	300	39.0 cm	20.6 Km/Hr	3900.0 mm/Km	3671	4.82	Good	25.4562663	N	84.78966507	E	Breaker
04-07-22	16:06:18	24	100	400	23.0 cm	29.0 Km/Hr	2300.0 mm/Km	2196	3.05	Good	25.4565953	N	84.78986519	E	Normal
04-07-22	16:06:39	24	100	500	38.0 cm	17.0 Km/Hr	3800.0 mm/Km	3579	4.72	Good	25.4569043	N	84.79080531	E	Breaker
04-07-22	16:07:08	24	100	600	24.0 cm	31.7 Km/Hr	2400.0 mm/Km	2288	3.16	Good	25.4572133	N	84.79172543	E	Normal
04-07-22	16:07:27	24	100	700	20.0 cm	30.3 Km/Hr	2000.0 mm/Km	1919	2.7	Good	25.4575223	N	84.79264555	E	Normal
04-07-22	16:07:42	24	100	800	25.0 cm	31.6 Km/Hr	2500.0 mm/Km	2380	3.28	Good	25.4578313	N	84.79356567	E	Normal
04-07-22	16:07:04	24	100	900	38.0 cm	16.0 Km/Hr	3800.0 mm/Km	3579	4.72	Good	25.4581403	N	84.79448579	E	Breaker
04-07-22	16:08:23	24	100	1000	32.0 cm	31.0 Km/Hr	3200.0 mm/Km	3025	4.06	Good	25.4584493	N	84.79540591	E	Normal
04-07-22	16:08:41	24	100	1100	22.0 cm	28.7 Km/Hr	2200.0 mm/Km	2104	2.93	Good	25.4587583	N	84.79632603	E	Normal
04-07-22	16:09:03	24	100	1200	23.0 cm	29.3 Km/Hr	2300.0 mm/Km	2196	3.05	Good	25.4590673	N	84.79724615	E	Normal
04-07-22	16:09:26	24	100	1300	27.0 cm	30.6 Km/Hr	2700.0 mm/Km	2565	3.5	Good	25.4593763	N	84.79816627	E	Normal
04-07-22	16:09:45	24	100	1400	22.0 cm	32.0 Km/Hr	2200.0 mm/Km	2104	2.93	Good	25.4596853	N	84.79908639	E	Normal
04-07-22	16:10:07	24	100	1500	33.0 cm	31.5 Km/Hr	3300.0 mm/Km	3118	4.17	Good	25.4599443	N	84.80000651	E	Normal

NIRUPMA
A/7/2022
21/7/2022

04/07/2022
A.E

30/7/22
E.E

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग
काठमाडौं पालीख

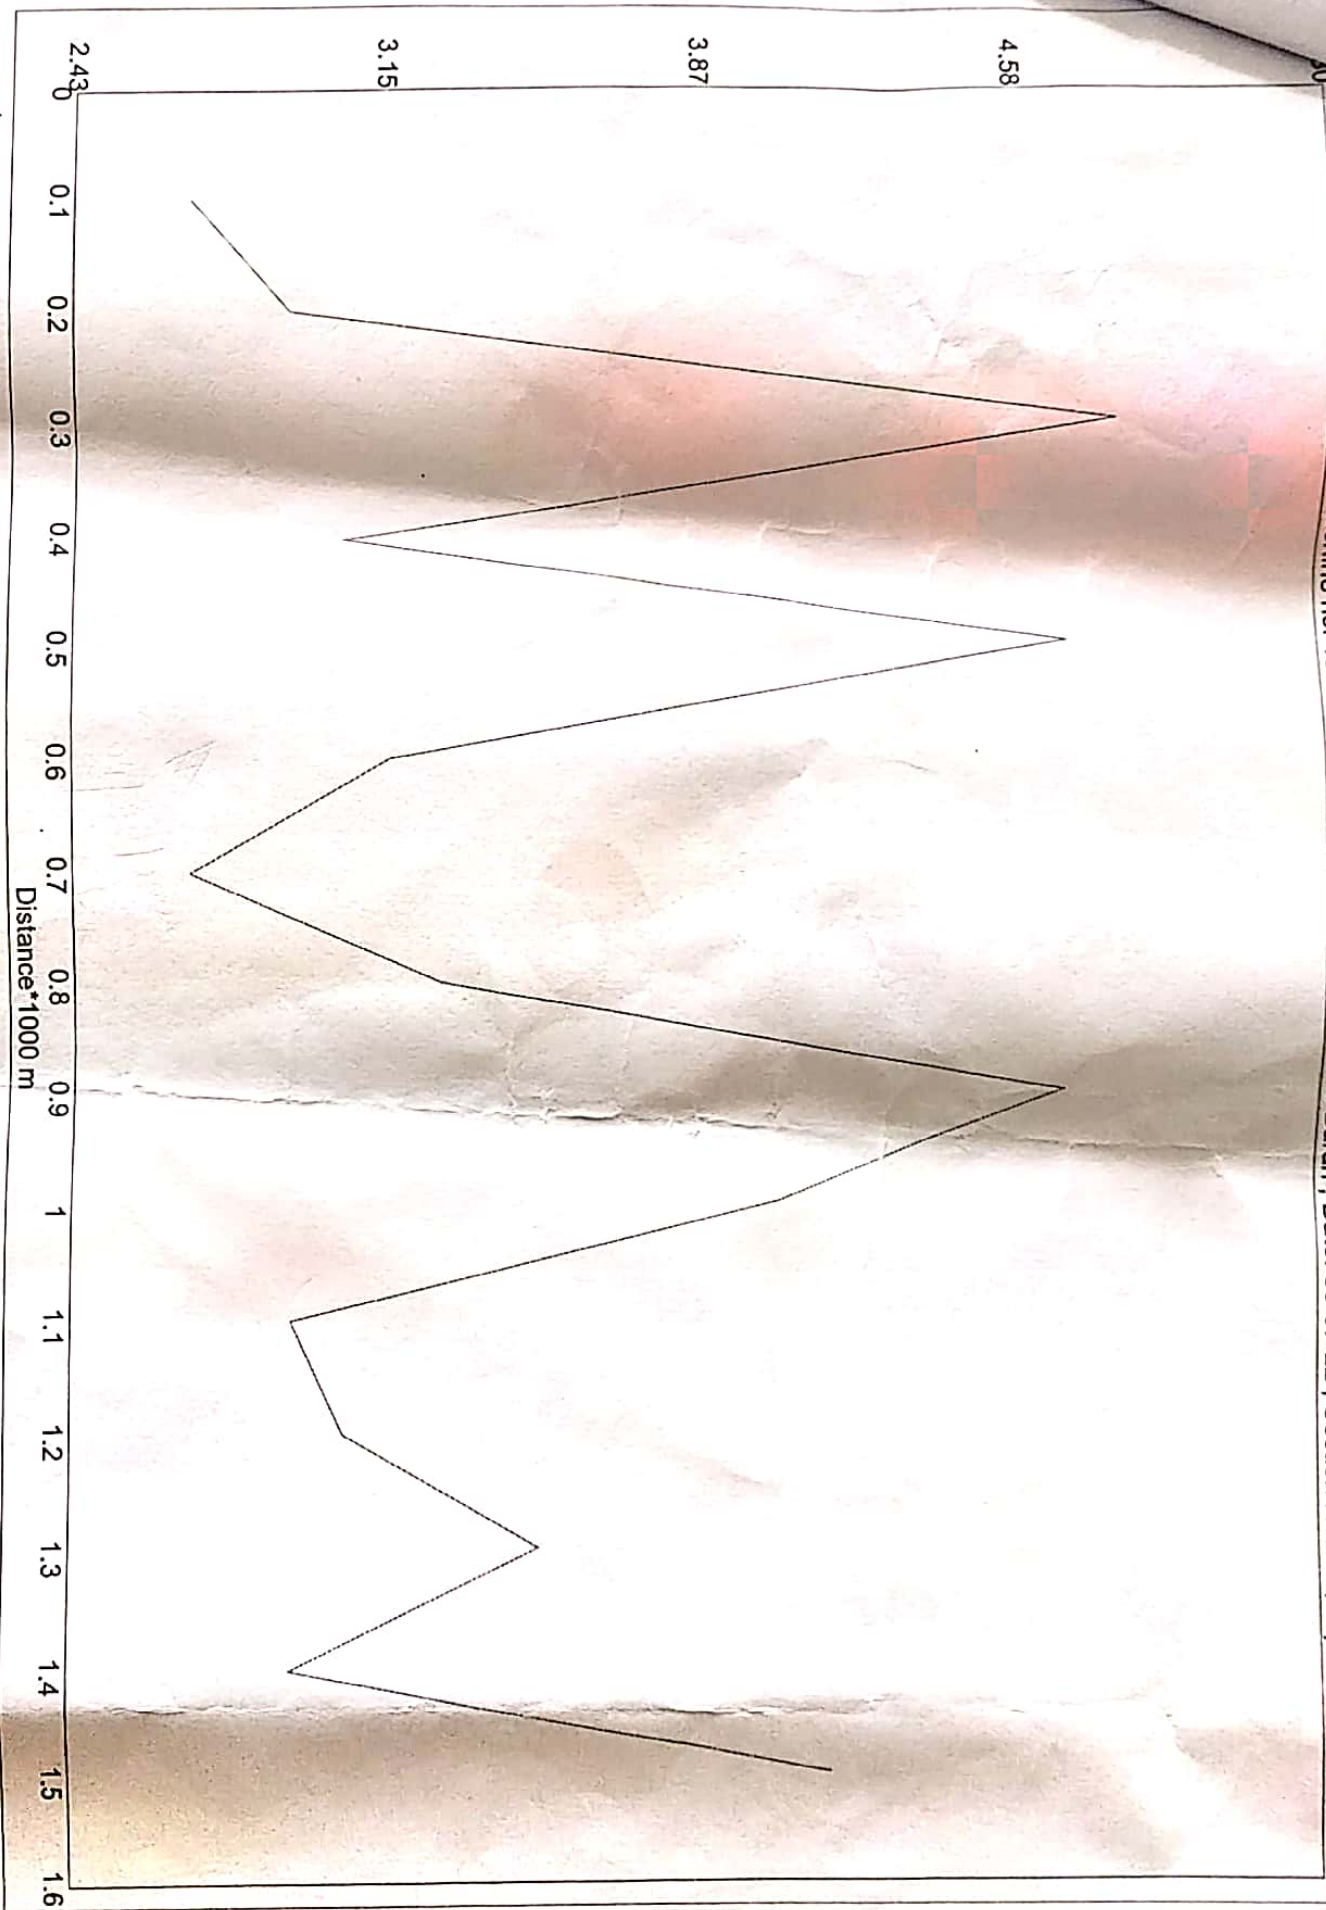

Nirupma
4/7/2022
30/7/22
6/8/22
6/8/22
6/8/22
