

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सहरसा।

पत्रांक- 1258 / सहरसा

दिनांक- 06/08 / 2022

प्रेषक:-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल सहरसा।

सेवा में,

नोडल पदाधिकारी,
MR 3054,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय:-

नई अनुरक्षण नीति 2018 शीर्ष अंतर्गत वित्तीय वर्ष 2020-21 एवं 2021-22 में व्यय हेतु
अनुरक्षण मद में आवंटन की मांग।

महाशय,

उपर्युक्त विषयक नई अनुरक्षण नीति 2018 शीर्ष अंतर्गत वित्तीय वर्ष 2020-21 एवं
2021-22 में व्यय हेतु अनुरक्षण मद में संलग्न विवरणी के अनुसार रुपये 40,66,798.00 (चालिस लाख
छयासठ हजार सात सौ अनठानवे रुपये) मात्र का आवंटन उपलब्ध कराने की कृपा की जाय, ताकि
किये गये कार्यों का भुगतान किया जा सके।

अनुलग्नक:- यथोक्त।

विश्वासभाजन

06-08-2022

कार्यपालक अभियंता
ग्रामीण कार्य विभाग

कार्य प्रमण्डल, सहरसा।

Maintenance Requisition for Scheme Head MR(054) Under Bihar Rural Road Maintenance Policy- 2018
Name of Work Division:- Saharsa

Road Details				A. A. Details		Agreement Details					Actual Maintenance Expenditure							Current Demand for Maintenance Amount (in Lacs)						Remarks							
Sl. No.	Road Name	Batch No	Project ID	Actual Date of Completion	Main work Amount	Maintenance Amount	Main Work Amount	Maintenance of Agreement 1st Year	Agreement 2	Agreement 3	Agreement 4	Agreement 5	Total Main Amount	Length of Road in Km	1st Year Maint. Exp.	2nd Year Maint. Exp.	3rd Year Maint. Exp.	4th Year Maint. Exp.	5th Year Maint. Exp.	Total Maint. Exp.	Length as per Bump Report 1st Year	IRI As per Bump Report	1st Quarter		2nd Quarter	3rd Quarter	4th Quarter	5th Quarter	6th Quarter	Total	
1	SANDA - DHANSEVA	RM/SA/SA/H/20/0007	20904302147	22/02/2021	40.36	19.948	32.109	1.3928	2.4035	5.8617	2.93078	6.47502	19.28380	1.712	0	0	0	0	0	0	1.742		0.964	0.964	0.964					2.892	
2	NH- 107 to Kojjani	RM/SA/SA/H/20/0007	209431033437	18/05/2021	32.925	23.023	55.41	1.9934	2.8483	6.6829	3.5223	7.2209	22.4678	2.051	0	0	0	0	0	0	1.6		1.1234	1.123						2.2468	
3	Approach road of Bridge over River Tila near Ranpur village Ganhariya panchayat under Sour Bazar Block	RM/SA/SA/H/20/0007	29431033532	22/01/2021	75.094	31.387	74.763	2.43273	3.78977	9.47607	4.7441	10.53833	30.9812	3.04	0	0	0	0	0	0	3.04		1.54906	1.549	1.549					4.64718	
4	Part Chowk Bajjandpur to Ihara Ranpur Sopha	RM/SA/SA/H/19/0002	20904304016	04/06/2020	112.94	63.85	109.697	6.385	6.885	19.796	9.323	21.371	63.76	6.795	0	0	0	0	0	0	6.795		3.188	3.188	3.188	3.188	3.188			19.128	
5	Saharsa Zila Anjaral Sour Bazar Probhand Kc Kachhija Panchayat Se Farscha Panchamuni Sadak se Mahadevi Tola Rice Huc Gomia Pakhi Sadak Tak	RM/SA/SA/H/19/0002	20904305006	29/06/2020	74.64	41.77	72.177	4.209	4.696	11.705	6.007	12.565	39.182	3.8	0	0	0	0	0	0	3.8		1.959	1.959	1.959	1.959	1.959			11.754	
40.66798																															

Executive Engineer
RMD Work Division
Saharsa
6/18/22

2022-08-09

40.66798

STANDARD FORMAT FOR QUARTERLY STATEMENT

PIU NAME- RWD, Saharsa

3rd Quarter (07.07.2021 to 06.10.2021)

1	Name of the Road	Approach road of Bridge over River Tilawe Near Rampur village Samhariga Panchayat		
2	Batch No / Package no	MR-N/19-20 Saharsa/12		
3	Project ID	29431033532		
4	Total Length of Road (In Km)	3.040 Km		
5	Length of Road to Meet Required Service Level [Completed Length] (in KM) [1]	3.040 Km		
6	No of Total Quarter (ie 3 Months as a unit) In 5 years.	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	30.98177 Lakh		
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.5490 Lakh		
Compliance criteria	Standard Job Description	Non- Compliance.		Reduction Payment [6] = [3] / [1] * [2] * [4]
		Length Non- Compliance [3]	Weighted Value for Payment Reduction (%) [4]	
1	PAVED ROADS (CARRIAGEWAY)	0.00	60%	0.00
2	SHOULDERS AND EMBANKMENTS	0.00	10%	0.00
3	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00	15%	0.00
4	SIGNAGE AND ROAD SAFETY	0.00	10%	0.00
5	VEGETATION	0.00	5%	0.00
TOTAL PAYMENT REDUCATION FOR THE QUARTER (in Lakh) [5]				0.00
TOTAL PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				1.5490

M/s Jay Mata Di Construction

Rajendra Kumar

Partner

Date of inspection by E / I his agent prepared by Contractor's self Control unit

Shacib Akhtar
Name and Designation of person inspecting road

29/7/22
Signature of person inspecting road

29-07-2022
EXECUTIVE ENGINEER-
R.W.D Works Division
Saharsa

Government of Bihar
OM01

Rural Works Department

ORDINARY MAINTENANCE INSPECTION REPORT
From OM01

Date : 29.07.2022

Road From: Approach road of Bridge over Tiliawe near Rampur village Gamhariya
Panchayat
Length of Road : 3.040 KM
Period : 3rd Quarter (07.07.2021 to 06.10.2021)
Inspector : JE, RWD, Sub Division, Sour Bazar

To,
Executive Engineer,
RWD, Works Division, Saharsa
Position : J.E

No.	Standard work item	Work Units	Unit of work required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed Pavement												No Pothole found.
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							No surface Depression and Rut Patching found.
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil							No Crack Sealing found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface)
OM104	Surface Treatment												No Bleeding/Flushing required.
	(a) Loss of Aggregate	m2	Nil	Nil	Nil	Nil							No Crocodile cracking found.
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							No Edge Repair required.
OM105	(c) Crocodile cracking	m2	Nil	Nil	Nil	Nil							
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil							
OM106	Digouts	m2	N.A	N.A	N.A	N.A							
OM107	Concrete Pavement	m3	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												
OM201	Unsealed Shoulder												No Edge Drop-Off required.
	(a) Edge Drop-Off	Lm	Nil	Nil	Nil	Nil							No Roughness, Scouring or Potholes required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							No Holding Water Found.
OM202	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							No Embankment Repair required.
OM202	Embankment Repair	m3	Nil	Nil	Nil	Nil							
	Other activities												
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not required.
OM302	Culvert Cleaning	No.	Nil	Nil	Nil	Nil							Not required.
OM303	Culvert and Pit repair	m3	Nil	Nil	Nil	Nil							Not required.
	Other activities	m2	Nil	Nil	Nil	Nil							

29/7/22

29/7/22

M/s Jay Mata Di Construction
Rajendra Kumar
Partner

Executive Engineer
RWD, Works Division

Saharsa

Standard work item		Work	Unit of work required in each kilometre										Comments
No.	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												
	(a) Road side - General Tidy	Ha	Nil	Nil	Nil	Nil							Not required.
	(b) clean near safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not required.
OM402	Tree and Shrub Management												
	Cutting tree	No.	Nil	Nil	Nil	Nil							Not required.
	Cutting Shrubs	No.	Nil	Nil	Nil	Nil							Not required.
	Other activities												
OM500 Safety Signage and Road													
OM501	Signs Maintenance	No.	Nil	Nil	Nil	Nil							Not required.
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Not required.
OM503	Distance Stone	No.	N.A	N.A	N.A	N.A							Not required.
OM504	Road Marking	m2	Nil	Nil	Nil	Nil							Not required.
	Other activities												

M/s Jay Mata Di Construction
 Rajender Kumar
 Partner

(Signature of Contractor/Authorized representative)

Date 29.07.22 Time

Place

[Signature]
 29/7/22

EXECUTIVE ENGINEER
 RWD Works Division
 Sateen
[Signature]
 29-07-2022

Approach road of bridge over river tilawe near rampur village gambaria panchayat under saur bazar block

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event	Y = 0 * X + 2 + 1.137 * X - 181.0
29/7/22	14:35:45	50	0.1	300	20.2	3000	3230	G	25.902449	86.645837	Normal	X = 5700
29/7/22	14:36:4	50	0.1	310	20.2	3100	3343	G	25.916329	86.638642	Normal	Y = 6299
29/7/22	14:36:22	50	0.1	300	20.2	3000	3230	G	25.916336	86.637516	Normal	
29/7/22	14:36:38	50	0.1	350	30.3	3500	3798	G	25.916494	86.636517	Normal	
29/7/22	14:36:52	50	0.1	320	30.3	3200	3457	G	25.917158	86.635819	Normal	(B) RURAL ROAD
29/7/22	14:37:8	50	0.1	330	30.3	3300	3571	G	25.917551	86.634116	Normal	Good
29/7/22	14:37:26	50	0.1	290	20.2	2900	3116	G	25.917568	86.633336	Normal	<4000
29/7/22	14:37:45	50	0.1	270	20.2	2700	2888	G	25.917624	86.632347	Normal	Average
29/7/22	14:38:5	50	0.1	350	20.2	3500	3798	G	25.917219	86.632093	Normal	4001-5000
29/7/22	14:38:20	50	0.1	300	30.3	3000	3230	G	25.916554	86.631717	Normal	Poor
29/7/22	14:38:38	50	0.1	320	20.2	3200	3457	G	25.915844	86.6313	Normal	
29/7/22	14:38:51	50	0.1	320	30.3	3200	3457	G	25.915034	86.631236	Normal	
29/7/22	14:39:6	50	0.1	290	30.3	2900	3116	G	25.913791	86.630158	Normal	
29/7/22	14:39:26	50	0.1	330	20.2	3300	3571	G	25.913628	86.629051	Normal	
29/7/22	14:39:41	50	0.1	320	20.2	3200	3457	G	25.913573	86.628131	Normal	
29/7/22	14:40:0	50	0.1	330	20.2	3300	3571	G	25.913716	86.627279	Normal	
29/7/22	14:40:18	50	0.1	300	20.2	3000	3230	G	25.913838	86.626418	Normal	
29/7/22	14:40:32	50	0.1	320	30.3	3200	3457	G	25.913885	86.625526	Normal	
29/7/22	14:40:50	50	0.1	330	20.2	3300	3571	G	25.913788	86.624742	Normal	
29/7/22	14:41:12	50	0.1	310	20.2	3100	3343	G	25.913343	86.624032	Normal	
29/7/22	14:41:30	50	0.1	300	20.2	3000	3230	G	25.912923	86.623371	Normal	
29/7/22	14:41:46	50	0.1	310	20.2	3100	3343	G	25.911938	86.622634	Normal	
29/7/22	14:42:06	50	0.1	330	20.2	3300	3571	G	25.911778	86.621035	Normal	
29/7/22	14:42:25	50	0.1	320	20.2	3200	3457	G	25.912025	86.621313	Normal	
29/7/22	14:42:42	50	0.1	330	20.2	3300	3571	G	25.912165	86.619414	Normal	
29/7/22	14:43:0	50	0.1	350	30.3	3500	3798	G	25.912308	86.618639	Normal	
29/7/22	14:43:17	50	0.1	280	20.2	2800	3002	G	25.912165	86.617802	Normal	
29/7/22	14:43:35	50	0.1	270	20.2	2700	2888	G	25.912117	86.616036	Normal	
29/7/22	14:43:55	50	0.1	350	20.2	3500	3798	G	25.912257	86.615815	Normal	
29/7/22	14:44:10	50	0.1	350	20.2	3500	3798	G	25.912765	86.614989	Normal	
29/7/22	14:44:20	50	0.04	350	10.1	3500	3798	G	25.912979	86.612736	Normal	

29/7/22

OFFICE IN CHARGE
R.M.C. WORKS DIVISION
29-07-2022

Machine No:
 Work Aspect:
 Number:
 Date: 29.07.2022


Test Date: 29.07.2022 Road Name:
 Machine No: 379 Road Type: (R) RURAL ROAD
 Start S No: Side:
 Start E No:
 Weather:
 UV Range: 1800 To 5000 Interval 1000 mm/km
 Start Location: 0 Dist Range: 0 To 32 01 1000 m
 End Location: 304 Equalization: 1.0 * X + 2.0 * 100 * X - 1800

Generate Report and Graph

Redraw Graph

Map View

File C:\Users\BRDDA135\OneDrive\Desktop\Babbar\Tilawe River Approach Road.xlsx Section No 50. Egn Y =
 Name of Customer M/S Jai Mata Di Construction. Name of Work/ Road Approach road of Bridge over River Tilaway

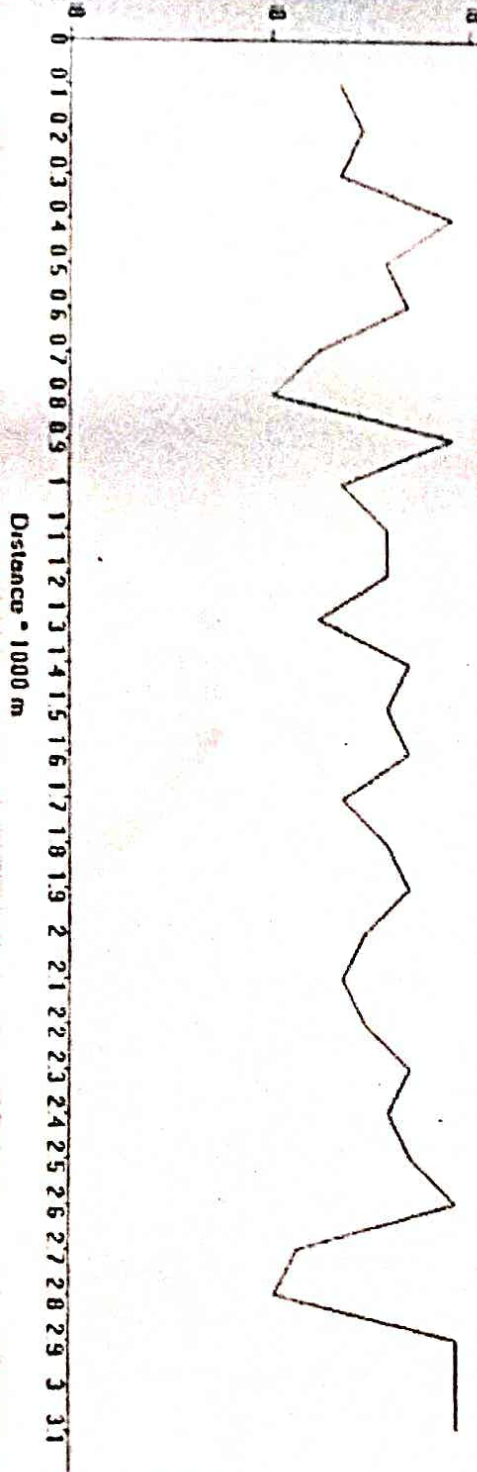

Signature

EXECUTIVE ENGINEER
 R.W.D Works Division
 Saharsa
 29.07.2022
