

कार्यपालक अभियंता का कार्यालय, ग्रामीण कार्य विभाग,
कार्य प्रमंडल बगहा-1

पत्रांक.....988 अ-5..... बगहा-1 / दिनांक.....04/05/2021

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बगहा-1।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी
-सह-सचिव, नोडल पदाधिकारी,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :- MR 3054 New Maint Policy 2018 के अन्तर्गत 5 (पाँच) वर्षीय
अनुरक्षण का आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि MR 3054 New Maint Policy
2018 के अन्तर्गत 5 (पाँच) वर्षीय अनुरक्षण का आवंटन उपलब्ध कराने के लिए सूची बनाकर
इस पत्र में सलग्न कर अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जाती है।

- अनु0- 1. उपयोगिता प्रमाण-पत्र Form GFR 19A
2. अधियाचना पत्र

विश्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बगहा-1


FORM GFR 19-A

(See Government of India's decision (I) below rule- 150)
Form of Utilization certificate up to the month of April - 2022

PIU:- E.E RWD(W)DIV-BAGAHA-1

SL.NO.	Name of Schemes	Sanction No.& Amount	Date with (In Lacs)	Amount received (In Lacs)	Particulars
1	2	3	4	5	
1	Maintenance Fund of MR(3054) New Maintenance Policy 2018			NIL	Certified that out of Rs. 0.0 Lacs of grants-in-aid sanctioned during the years 2020-21 in favour of Executive Engineer R. W. D. Works Division, BAGAHA-1 a sum of Rs. 0.00 Lacs has been utilized for the purpose of Maintenance Fund of MR(3054) New Maint Policy 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs NIL Lac remaining unutilized at the end of the period under report.
		TOTAL		NIL	

2. Certified that I have satisfied myself that the conditions on which the grant-in-aid was sanctioned have been duly fulfilled, are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.


04/05/22
Divisional Accounts Officer
RWD Works Div. Bagaha-1

Kinds of checks exercised:-

- Works has been supervised by Executive Engineer / Superintending Engineer.
- Periodic as inspection has been conducted by Executive Engineer / Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer / Executive Engineer.
- All other codal formalities have been observed.

Physical Progress achieved:-

- Construction of Road Works.
- Construction of CD Works.


04/05/22
Executive Engineer
RWD Works Div. Bagaha-1

Requisition Format for Scheme Head - 5 Year Maintenance of MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Rectification and surface Renewal)

Name of Division :- Bagaha-1

Name of Circle :- Bettiah

Sl. No	Package No.	Name of Road	Project ID as per MIS	Administrative Sanction Letter No & Date.	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Current Maintenance Demand (In Lacs)				Remarks.
					Length (in km)	Amount of (in Lakh)	Initial Rectification with surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)				1st Qtr Maint Demand	2nd Qtr Maint Demand	3rd Qtr Maint Demand	4th Qtr Maint Demand	
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
1	M/R-N/19-Bagaha-1/14	PWD Narkatiaganj To Mathiya	318901031855	3309 31.07.2019	4.21	168.6587	112.92771	43.92791	19MBD /2020-21 30.06.2020	29.03.2021	17.01.2021	2.19639	2.19639	2.19639	-	
2	M/R-N/19-Bagaha-1/14	Deurwa To Telpur	318901034001	3309 31.07.2019	2.50	119.834	84.43619	26.63484	19MBD /2020-21 30.06.2020	29.03.2021	18.12.2020	1.33174	1.33174	1.33174	-	
3	M/R-N/19-Bagaha-1/14	PWD Narkatiaganj To Sihpur	318901034000	3309 31.07.2019	3.84	149.5600	108.38700	40.36805	19MBD /2020-21 30.06.2020	29.03.2021	24.01.2021	2.01840	2.01840	2.01840	-	
4	M/R-N/19-Bagaha-1/18	Harnatd To Bairiya Kala	318901031864	3309 31.07.2019	3.5	126.0376	80.584	36.85827	37MBD/ 2020-21 24.09.2020	23.06.2021	02.12.2020	1.84291	1.84291	1.84291	1.84291	
5	M/R-N/19-Bagaha-1/18	Songadhwa To Naurangiya	318901033994	3309 31.07.2019	7.8	333.3438	228.13219	82.26853	37MBD/ 2020-21 24.09.2020	23.06.2021	02.12.2020	4.11342	4.11342	4.11342	4.11342	
6	M/R-N/19-Bagaha-1/14	Sathi Panchayat Antargat Parsauni Gawn To Pandai Nadi hote Hue Bettiah Narkatiaganj Mukhya Path Tak	318901031882	3309 31.07.2019	1.00	47.555	23.80200	10.61759	19MBD /2020-21 30.06.2020	29.03.2021	16.01.2021	0.53087	0.53087	0.53087	-	
7	M/R-N/19-Bagaha-1/14	PWD Ramnagar To Barbiro	318901031853	3309 31.07.2019	2.70	110.9385	74.62834	27.89922	19MBD /2020-21 30.06.2020	29.03.2021	18.02.2021	1.39496	1.39496	1.39496	-	
8	M/R-N/19-Bagaha-1/13	Bharchhi To Taruanwa PCC Road	31809007012	2180 08.07.2019	2.00	79.612	47.00014	19.95086	50MBD/ 2019-20 21.11.2019	20.08.2020	18.02.2020	0.99754	0.99754	0.99754	0.99754	
9	M/R-N/19-Bagaha-1/13	Barwa Se Chanki Tola Pakki Sadak Nirman	31809007011	2180 08.07.2019	4.04	151.839	88.33669	39.46084	50MBD/ 2019-20 21.11.2019	20.08.2020	25.02.2020	1.94304	1.94304	1.94304	1.94304	

[Signature]
04/05/22
DIVISIONAL ACCOUNTS OFFICER
R.W.D. Works Division, BAGAHA-1

[Signature]
04/05/22
Executive Engineer
Rural Works Department
Works Division, Bagaha-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :- RWD, Works Division, Bagaha-1

4th Quarter

1	Name of the Road	Bharchhi to Taruanwa PCC Road		
2	Batch No.	RM/WE/BAG/19/0013		
3	Project ID	31809007012		
4	Total Lenth of Road (in KM)	2.00		
5	Length of Road to Meet Required Service Level [Completed length](in Km) [1]	2.00		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	19.95086		
8	Quarterly Payment : 4/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.997543		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non- Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00
II	SHOULDERS AND EMBANMENTS	0	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00
V	VEGATION	0	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (IN Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.997543

Date of inspection by E/I or his agent
Prepare by Contractor's self Control unit

Sudakshwaha
04/05/2022
A.E.
Name and Designation of person inspecting road

Date

Signature of person inspecting road

(Signature)

Certify by E/I [signature] Date:-
Executive Engineer
Rural Works Department
Works Division, Bagaha-1

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD, Works Division Bagaha-1

4th Quarter

Government Of Bihar

OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Bharchhi to Taruwa PCC Road

To:-

Executive Engineer
RWD, Works Division Bagaha-1

Date:-

Length of Road :- 2.00 KM

Inspector :- A.E. RWD WORKS SUB DIVISION, Bagaha-2

Position :- A.E.

No	standard Of Work Item Name	Work Unit	Unit OF Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												No pothole found
OM101	Pothole Patching	m ²	NIL	NIL									No Surface Depression and Rut patching found
OM102	Surface Depression and Rut patching	m ³	NIL	NIL									No crack
OM103	Crack Sealing	Lm	NIL	NIL									Not required
OM104	Surface Treatment		NIL	NIL									No Loss of Aggregate (Surface ravelling) found
	(a) Loss of Aggregate (Surface Ravelling)	m ²	NIL	NIL									No bleeding / furnishing found
	(b) Bleeding / Flushing	m ²	NIL	NIL									No Crocodile cracking found
	(c) Crocodile Cracking	m ²	NIL	NIL									Notified & repaired
OM105	Edge Repair	m ²	N.A.	N.A.									
OM106	Digouts	m ³	N.A.	N.A.									
OM107	Concrete pavement												
	Other activities												
OM200	Shoulder												No Edge Drop off found
OM201	Unsealed Shoulder	Lm	NIL	NIL									No Roughness, Scouring or Potholes found
	(a) Edge Drop-off	Lm	NIL	NIL									No Holding Water Found
	(b) Roughness, Scouring or Potholes	Lm	NIL	NIL									Notified & repaired
	(c) Holding water	M ³	NIL	NIL									
OM202	Embankment Repair		N.A.	N.A.									NA
	Other activities (Rain Cuts)												DONE
OM300	Drainage including culverts major	Lm	N.A.	N.A.									DONE
OM301	Surface Drains & Verge	No	NIL	NIL									Not required
OM302	Culvert Cleaning	M ³	NIL	NIL									
OM303	Culvert and pit Repair	M ²	NIL	NIL									
	Other activities (Whitewashing)												

for

T.E. Subodh Kumar

Subodh Kumar
04/05/2022
A.E.

04/05/2022

No	standard Of Work Item		Unit Of Required in each Kilometere										Comments
	Name	Work Unit	1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												
OM401	(a) Roadside- General Tidy	Ha	NIL	NIL									Done
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	NIL	NIL									Done
OM402	Tree and Shrub Management	No	NIL	NIL									Done
	Cutting Of Branches Of Trees	No	NIL	NIL									Done
	Cutting Of Shrubs From Road Way	No	NIL	NIL									Done
	Other activities (Trimming of Grass)	M ²	NIL	NIL									Done
OM500	Safety Signage and Road												Done
OM501	Signs Maintenance	No	NIL	NIL									Not Required
OM502	Guard Stones	Lm	NA	NA									Not Required
OM503	Distance Stones	No	NA	NA									N.A.
OM504	Road Marking	M ²	NIL	NIL									N.A.
	Other activities												Not Required

John

J-F.

3-1-2022

Satishkumar
04/05/2022
I.A.E.

04/05/2022

Executive Engineer
Rural works Department
Works Division, Bagaha-1



अक्षांश: 27.274839
देशान्तर: 84.069149
उन्नयन: 111.71±14 m
सटीकता: 7.3 m
समय: 04-26-2022 10:03
नोट: भड़ही से तरुअनवा

सडक

Powered by NoteCam



अक्षांश: 27.278551
देशान्तर: 84.057309
उन्नयन: 106.66±22 m
सटीकता: 10.6 m
समय: 04-26-2022 09:56
नोट: भडझी।से।तरूअनवा

सडक

Powered by NoteCam



अक्षांश: 27.276445
देशान्तर: 84.060362
उन्नयन: 107.66±18 m
सटीकता: 9.8 m
समय: 04-26-2022 09:57
नोट: भदड़ी।से।तरूनवा

सडक

Powered by NoteCam



अक्षांश: 27.279861
देशान्तर: 84.055274
उन्नयन: 113.66±28 m
सटीकता: 13.6 m
समय: 04-26-2022 09:55
नोट: भदली।से।तरूननवा

सडक

Powered by NoteCam

ROAD NAME- BHARCHHI TO TARUANWA ROAD, CONTRACTOR NAME- MUNNA KUMAR JAISWAL

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI.TEGORY mm/km ROAD	Latitude Longitude	Event
27/2/22	14:27:0	61	0.1	300	0	3000	3077 G	27.27942 84.55975	Normal
27/2/22	14:27:25	61	0.1	200	20.2	2000	2030 G	27.27891 84.5673	Normal
27/2/22	14:27:25	61	0.1	330	20.2	3300	3391 G	27.27841 84.57473	Normal
27/2/22	14:28:0	61	0.1	320	20.2	3200	3285 G	27.27785 84.58265	Normal
27/2/22	14:28:0	61	0.1	220	30.3	2200	2240 G	27.27733 84.5904	Normal
27/2/22	14:28:0	61	0.1	230	30.3	2300	2344 G	27.27681 84.5983	Normal
27/2/22	14:28:35	61	0.1	210	20.2	2100	2135 G	27.27629 84.60605	Normal
27/2/22	14:28:35	61	0.1	260	20.2	2600	2658 G	27.27576 84.61363	Normal
27/2/22	14:29:0	61	0.1	280	20.2	2800	2985 G	27.27523 84.62172	Normal
27/2/22	14:29:11	61	0.1	210	30.3	2100	2135 G	27.27473 84.62878	Normal
27/2/22	14:29:11	61	0.1	200	30.3	2000	2030 G	27.27418 84.63687	Normal
27/2/22	14:29:46	61	0.1	280	20.2	2800	2868 G	27.27362 84.64562	Speed Breaker
27/2/22	14:30:0	61	0.1	360	20.2	3600	3705 G	27.27311 84.65302	Normal
27/2/22	14:30:0	61	0.1	220	20.2	2200	2240 G	27.27259 84.66093	Normal
27/2/22	14:30:21	61	0.1	190	30.3	1900	1925 G	27.27204 84.66902	Normal
27/2/22	14:30:21	61	0.1	230	20.2	2300	2344 G	27.27149 84.67743	Speed Breaker
27/2/22	14:31:0	61	0.1	250	10.1	2500	2658 G	27.27199 84.6808	Normal
27/2/22	14:31:0	61	0.1	280	10.1	2800	2800 G	27.27283 84.684	Normal
27/2/22	14:31:32	61	0.1	310	20.2	3100	3182 G	27.27359 84.69007	Normal
27/2/22	14:32:7	61	0.1	310	10.1	3100	3182 G	27.27446 84.69242	Normal

$$Y = 0 * X^2 + 1.047 * X - 63.36$$

$$X = 2800$$

$$Y = 2868$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

CUMULATIVE 53214
AVERAGE IRI 2660

Signature
27-2-2022
J. K.

Signature
04/05/22
A.E


Signature
04/05/22
Executive Engineer
R.W.D. (W) Division
Bagaha-1

Name of Customer: MUNNA KUMAR JAISWAL
 Name of Work/Road: BHARCHHI TO TARUANWA
 Lab Job number:
 Date: 27/02/22
 Section No: 61

Test Date: 27/02/22	Road Name: BHARCHHI TO TARUANWA
Machine No:	Road Type: (H) RURAL ROAD
Start S No:	Side:
Start E No:	Interval:
Weather:	UV Range: 925 To 5000 1000 mm/km
Start Location: BHARCHHI	Dist Range: 0 To 2.1 0.1 * 1000 m
End Location: TARUANWA	Equation: $Y = 0.0002X^2 + 1.047X + 63.36$

Print Generate Report and Graph

Redraw Graph Map View

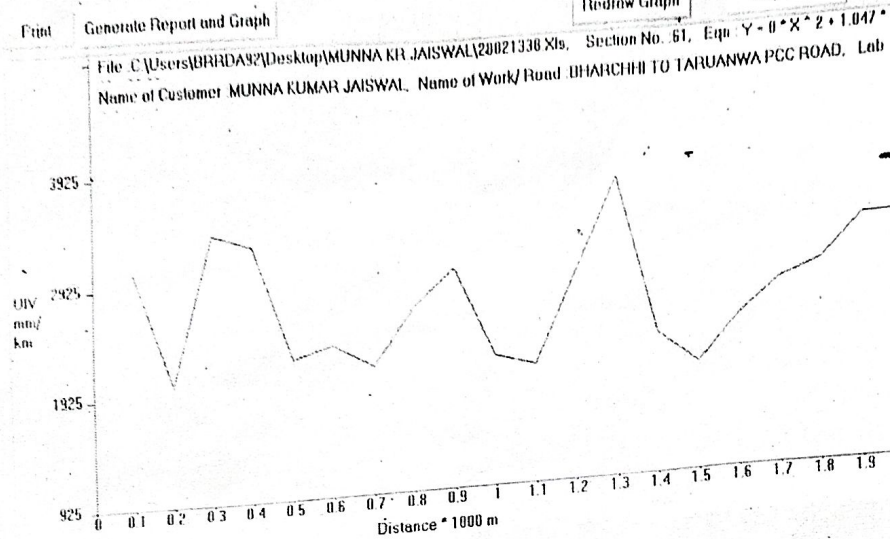

Japu
 27-02-2022
 J.E.

Santakrishna
 04/05/22
 A.E.

[Signature]
 04/5/22
 Executive Engineer
 R.W.D. (W) Division,
 Bagaha-1
