

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पालीगंज।

पत्रांक : 1157 (3130)

पालीगंज/दिनांक : 18/08/2022

प्रेषक :

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
—सह—सचिव,
बिहार ग्रामीण पथ विकास, अभिकरण
ग्रामीण कार्य विभाग, पटना।

विषय:—शीर्ष—MR, 3054 Under-Bihar Rural Road Maintenance Policy-2018 योजना अन्तर्गत आवंटन का
अधियाचना के संबंध में।


महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष—MR, 3054 Under-Bihar Rural Road Maintenance Policy-2018 योजना अन्तर्गत पथों का अधियाचना का मॉग विहित प्रपत्र में तैयार कर Signed Hard Copy of Recorded IRI के साथ अधियाचना हेतु भेजी जा रही है।

अतः अनुरोध है कि उक्त योजना का आवंटन उपलब्ध करने की कृपा की जाय, ताकि संवेदक का भुगतान हो सके।

अनु.:-यथोक्त।

विश्वासभाजन


18/8/22

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।
18/8/2022

Requisition Format for Scheme Head -MR (3054) Under Bihar Rural Road Maintenance Policy 2018 (Initial Rectification and surface Renewal)
Name Of Work division- Paliganj

SI	Pakage No	Name Of Road	Project ID as per MIS	Administrative Approval Letter No (AA) & Date	Length (in KM)	Amount of (in Lakh)	Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)	Agreement no & Date	Date of completion as per Agreement	Actual Date of completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
		NH 98 Chiraura RM/PA/PAL/2 Se Naubatpur 11/0001 Khagaul PWD path	1151037320	1064 dt 26.03.2021	1.8	103.84000	94.95625	17.38551	04/MBD/N ew Maintenance ce policy 2018/MR- 3054/ 2021-22 & 25.01.2022	24.10.2022		3.889444	25 mm (SDBC)	5.04%	0.00000	0.00000	90.16100	Work has been completed as per specification and verification Hundred percent of work has been completed and Hundred per cent by Executive Engineer has been done.

18/8/22
Executive Engineer
Rural Works Department
Works Division Paliganj

18/8/22


FORM GFR 19-A

(See Government of India's Decision (1) below Rule-150)
Form of utilisation Certificate up to the end of 16th august 2022


PIU: RWD Works Division, Paliganj				
Sl No.	Name of Scheme	Sanction No. & Date with Amount	Amount Received (In Rs.)	Particulars
1	Construction of Rural roads under RURAL ROAD MAINTENANCE POLICY 2018		216554097.00	Certified that out of Rs 216554097.00 received during the year 2022-23 in favour of Ex. Engineer, RWD, Works Div. Paliganj Bihar a sum of Rs 212324960.00 has been utilized for the purpose of const of road under Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 4229137.00 remaining unutilized at the end to the period under
Total			216554097.00	

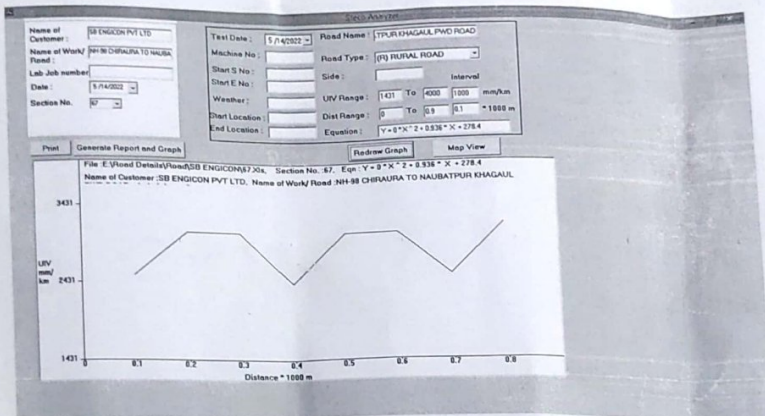
2. Certified that I have satisfied myself that the conditions of which the grants sanction Sanctioned have been duly fulfilled/are being fulfilled and I have exercised the checks to see the money was actually utilised for the purpose for which it was sanctioned.

Trishr
18/8/22


18/8/22

Executive Engineer
Rural works Deptt.
Works Division, Paliganj

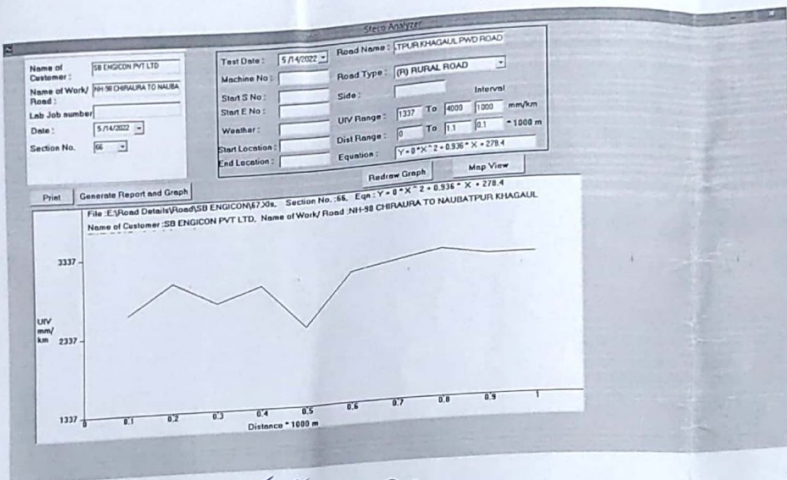

18/8/2022



14/05/2022
J E

14.5.22
AE

18/8/22
CE



AG
14/05/22
J.E

AG
14.5.2022

EG
18/8/22
EG

NAME OF THE ROAD: NH-98 CHIRAURA TO NAUBATPUR KHAGAU PWD ROAD

LENGTH OF THE ROAD: 1.80 KM

PACKAGE NO.: MR-N/21-22/PALIGANI/01

DIVISION: PALIGANI

BLOCK: NAUBATPUR

AGENCY: S.B. ENGICON PVT LTD

Date	Time	Section	Length	Bumps	Speed	OR	UIV	CATEGORY	IRI	Latitude	Longitude	Event			
		No.	In km	In mm	Rate	mm/km	mm/km	ROAD							
14/5/22	10:19:29	66	0.1	250	0	2500	2618	G	3.56	25.52221	84.98936	Normal	$Y = 0 * X^2 + 0.936 * X + 278.4$		
14/5/22	10:20:4	66	0.1	290	30.3	2900	2992	G	4.01	25.52228	84.98935	Normal	$X = 3300$		
14/5/22	10:20:24	66	0.1	260	30.3	2600	2712	G	3.68	25.52225	84.98939	Normal	$Y = 3367$		
14/5/22	10:20:50	66	0.1	280	30.3	2800	2899	G	3.9	25.52231	84.98861	Normal			
14/5/22	10:20:50	66	0.1	280	30.3	2800	2899	G	3.9	25.52231	84.98861	Normal	(R) RURAL ROAD		
14/5/22	10:21:10	66	0.1	220	30.3	2200	2337	G	3.22	25.52242	84.98838	Normal	Good	Average	Poor
14/5/22	10:21:20	66	0.1	290	30.3	2900	2992	G	4.01	25.52255	84.98774	Normal	<4000	4001-5000	>5001
14/5/22	10:21:35	66	0.1	300	30.3	3000	3086	G	4.13	25.52273	84.98725	Normal			
14/5/22	10:21:55	66	0.1	310	30.3	3100	3180	G	4.24	25.5231	84.98674	Normal			
14/5/22	10:22:5	66	0.1	300	30.3	3000	3086	G	4.13	25.52398	84.9872	Normal			
14/5/22	10:22:20	66	0.1	300	30.3	3000	3086	G	4.13	25.52453	84.98765	Normal			
14/5/22	10:22:40	67	0.1	240	30.3	2400	2524	G	3.45	25.52478	84.98727	Normal			
14/5/22	10:23:5	67	0.1	300	30.3	3000	3086	G	4.13	25.52509	84.98645	Normal			
14/5/22	10:23:25	67	0.1	300	30.3	3000	3086	G	4.13	25.52572	84.98494	Normal			
14/5/22	10:23:41	67	0.1	230	30.3	2300	2431	G	3.34	25.52615	84.98345	Normal			
14/5/22	10:24:11	67	0.1	300	30.3	3000	3086	G	4.13	25.52657	84.9819	Normal			
14/5/22	10:24:26	67	0.1	300	30.3	3000	3086	G	4.13	25.52686	84.98115	Culvert			
14/5/22	10:24:40	67	0.1	240	30.3	2400	2524	G	3.45	25.52725	84.97976	Curve			
14/5/22	10:24:58	67	0.05	310	30.3	3100	3180	G	4.24	25.52761	84.97921	Normal			
TOTAL			1.75	5020	515.1	50200	51991		70.01	459.4384	1529.7458				
AVERAGE						2788.889	2888.389		3.889444						

Sd/-
14/05/22
J.EA
14.5.22
AESd/-
18/8/22
GG

Ref No. _____

Date ____/____/____

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D., GULZARBAGH, PATNA - 7

Bituminous mix

Name of Project/Road :- NH-98 Chiraura to Naulatpur Khegam PWD Road

Name of Scheme :- MR-354

Name of Agency :- S. B. Engineers Pvt. Ltd.

Nature of sample :- Bitumen content for - SBC

Location :- BSDM

Date of Collection/Received :- 24/5/2022

Date of Test :- 01.06.2022

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub-Division Naulatpur vide letter No. 32 Dt. 19/05/2022

Agreement No / Package No. :

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	503.0	502.0	505.0	
2	Wt. of Dry chips after extraction (b)	477.85	476.61	479.45	
3	Percentage of bitumen (in the mix) [(a-b)*100/a] (%)	5.0	5.02	5.02	
4	Average % bitumen	5.04			

Rais
11/4/22

Regional Laboratory
R.W.D. Guljarbagh patna - 7

S
01/06/2022
A.E.

Regional Laboratory
R.W.D. Guljarbagh patna - 7

P. S. S.
01/6/22
E.E.

Regional Laboratory
R.W.D. Guljarbagh patna - 7

er No. _____

Date 11/06/2022

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D., GULZARBAGH, PATNA - 7

Bituminous mix

Name of Project/Road :- NH-98 Chiraura to Nawabpur Khegaul Puro Road

Name of Scheme :- MR-3054

Name of Agency :- S. B. Engineering Pvt. Ltd.

Nature of sample :- Bitumen content for - SBC

Location :- 1450 M

Date of Collection/Received :- 24/5/2022

Date of Test :- 01.06.2022

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division Nawabpur vide letter No. 32 Dt. 19/05/2022

Agreement No / Package No. : 1450

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	506.0	508.0	504.0	
2	Wt. of Dry chips after extraction (b)	480.55	482.60	478.64	
3	Percentage of bitumen (in the mix) $[(a-b)*100/a]$ (%)	5.03	5.00	5.03	
4	Average % bitumen	5.02			

Rajesh
11/6/22

G
01/06/2022
A.E.

V. K. Singh
01/06/22
A.E.

Regional Laboratory
R. W. D. Guljarbagh patna - 7

Regional Laboratory
R. W. D. Guljarbagh patna - 7

Regional Laboratory
R. W. D. Guljarbagh patna - 7
