

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर

पत्रांक..... 1282 अनुप सोनपुर, दिनांक..... 22.8.22

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर

सेवा में,

अपर मुख्य कार्यपालक
पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण
(BRRDA)
बिहार, पटना।

विषय:- बिहार ग्रामीण पथ अनुरक्षण निति-2018 योजनान्तर्गत अनुरक्षण हेतु राशि की अधियाचना के संबंध में।


महाशय,

उपर्युक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ अनुरक्षण निति-2018 के अंतर्गत पथों का अनुरक्षण की राशि की मांग रुपये 16,85,499.00 (सोलह लाख पचासी हजार चार सौ निन्यानबे) मात्र विहित प्रपत्र में अंकित कर आवश्यक कार्रवाई हेतु समर्पित किया जा रहा है।


अनुरोध है कि उपर्युक्त योजना में आवंटन उपलब्ध कराने की कृपा की जाये। कार्य का निरीक्षण किया गया कार्य संतोषप्रद है। उक्त पथ में ए0टी0आर0 लंबित नहीं है।

अनु0:-Standard Formate for Roads
Quarterly Statement

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर


22/8/22

FORM GER 19-A

(See Government of India's Decision (I) below Rule-150
Form of Utilization Certificate up to the month of **August-2022**

PIU:- E.E.,R.W.D. Works Division Sonapur.

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in lacs Rs.)	Amount Received (in lac Rs.)	Particulars
1	2	3	4	5
1	Construction of Rural Roads under New Maintenance Policy-18		5016.42589	Certified that out of Rs 5016.42589 lakh received during the years 2020-21 to 2022-23 in favour of E.E.R.W.D. works division Sonapur a sum of Rs 4997.81834 Lakh has been utilized for the purpose of New Maintenance Policy-18 Scheme as given in the margin for which it was sanctioned and that the balance of Rs 18.60755 Lakh remaining unutilized at the end of the period under report.

Certified that I have satisfied that the condition of which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually for the purpose for which it was sanctioned.

Kind of Checks:-

- Works have been supervised by Executive/superintending Engineer.
 - Periodical inspection has been conducted by Executive Engineer/ superintending Engineer.
 - Construction material has been tested.
 - Measurements have been recorded in the MBS and test conducted by the Assistant Engineer/ Executive Engineer.
 - All other nodal formalities have been observed.
- 3 physical Progress achieved-
- Construction of Road Works.
 - Construction of CD works

D.A.O

R.W.D. Works Division Sonpur.

EXECUTIVE ENGINEER

R.W.D. Works Division Sonpur.

Maintenance Requisition Formate for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018

Name of Works Division:- SONPUR

Road Details				AA Details		Agreement								Actual Maintenance Expenditure							Current Maintenance Demand					Remarks			
Sl. No.	Name of Raods	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh	Maintenan ce Amount (in lakh)	Main Work Amount (in Lakh)	Agre emen t-1	Agree ment-2	Agree ment-3	Agreem ent-4	Agree ment-5	Total Maintenance	Length (in KM)	1st. Year Maintenance	2nd. Year Maintenance	3rd. Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintenance Expenditure	Length as per Bump Report	IRI As per Bump Report	1st QTR Maintenance	2nd QTR Maintenance	3rd QTR Maintenance		4 th QTR Maintenance	Total	
1	Benkarwa Devi Sthan Se Bajdiha up to Sonpur rewa road via Parsuna Bazzar	RM/SA/SON /20/0014	313641037331	05-04-2021	118.89800	58.52300	118.84900	11.64762	11.64762	11.64762	11.64762	11.64761	58.23809	5.35	0.000	0.000	0.000	0.000	0.000	0.000	0.000	5.35	2489.00	2.91190	2.91190	0.00000	0.00000	5.82381	31
2	FATEHPUR - BEDAULIYA	RM/SA/SON /20/0014	31306402028	15-01-2021	87.69400	40.82700	87.99100	7.96188	7.96188	7.96188	7.96188	7.96188	39.80940	3.72	0.000	0.000	0.000	0.000	0.000	0.000	0.000	3.72	2357.00	1.99047	1.99047	0.00000	0.00000	5.97141	
3	GOPALPUR - BARIYARPUR	RM/SA/SON /20/0014	31306402029	15-01-2021	71.48500	34.62300	71.47300	6.74636	6.74636	6.74636	6.74636	6.74636	33.73180	3.16	0.000	0.000	0.000	0.000	0.000	0.000	0.000	3.16	2546.00	1.68659	1.68659	0.00000	0.00000	5.05977	
Total																												16.85499	

22/08/22

12/08/22

22/8/22

Executive Engineer
B.W.D. Works Division
SONPUR

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	FATEHPUR - BEDAULIYA		
2	Batch No.			
3	Project ID	RM/SA/SON/20/0014		
4	Total Length of Road (in Km)	31306402028		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	3.720		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	39.80940		
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	1.99047		

Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.99047

Date of inspection by E/1 or his agent Prepared by
Contractor's self Control unit

Date

Signature of person inspecting road

Name and Designation of person inspecting road

Certify by E/1 (signature) Date

Report Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Sonpur

3rd Quarter

Government of Bihar

OM01

Rural works Department

Road From- FATEHPUR - BEDAULIYA

Length of Road: 3.720 KM

Period : From.....

Inspector: A.E RWD Sub Division, Parsa

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

To: Executive Engineer

RWD Works Division Sonpur

Date:

Position: A.E

Standard Work item			Work	Units of work required in each kilometre										Comments
S No	Name	Units	1	2	3	4	5	6	7	8	9	10		
OM100 Sealed Pavement														
OM101	Pothole Patching	m2											No. Pothole found.	
OM102	Surface Depression and Rut Patching	m2											No Surface Depression and Rut Patching found	
OM103	Crack Sealing	Lm											No Crack Sealing found	
Surface Treatment														
OM104	(a) Loss of Aggregate (Surface Ravelling)	m2											No Loss of Aggregate (Surface Ravelling) found	
	(b) Bleeding/Flushing	m2											No Bleeding/Flushing Required	
	(c) Crocodile Cracking	m2											No Crocodile Cracking found	
OM105	Edge Repair	m2											No Edge Repair Required	
OM106	Digouts	m2												
OM107	Concrete Pavement	m3												
	Other activities	Lm												
OM200 Shoulder														
OM201	Unsealed Shoulder	No												
	(a) Edge Drop off	Lm											No Edge Drop off Required	
	(b) Roughness, Scouring or Potholes	Lm											Not required	
	(c) Holding Water	Lm											No Holding water found	
OM202	Embankment Repair	No											No Embankment Repair Required	
	Other Activities (Raincut)												Defects rectified within stipulated time.	
OM 300 Drainage including culverts major														
OM301	Surface Drains & Verge	Lm											Not Required	
OM302	Culvert Cleaning	Lm											Culvert maintain within stipulated time	
OM303	Culvert and Pit repair	m2											Not Required	

Signature
Rural Works Division
Sonpur
22/10/22

22/10/22

Name of work : FATEHPUR - BEDAULIYA

Name of customer : Rohan Raj Infra Projects Private Limited

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	U1(mm/Km)	Corrected U1 (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
09/07/22	15:26:15	61	0	0	0.0 cm	19.6 Km/Hr	0.0 mm/Km	127	0.24	Good	25.8535898	N	84.9464884	E	Normal
09/07/22	16:00:05	61	100	100	23.0 cm	8.4 Km/Hr	2300.0 mm/Km	2262	3.13	Good	25.8848601	N	84.9448100	E	Normal
09/07/22	16:00:21	61	100	200	26.0 cm	21.3 Km/Hr	2600.0 mm/Km	2540	3.47	Good	25.8848601	N	84.9448100	E	Normal
09/07/22	16:00:37	61	100	300	19.0 cm	23.6 Km/Hr	1900.0 mm/Km	1890	2.67	Good	25.8848601	N	84.9448100	E	Normal
09/07/22	16:00:53	61	100	400	28.0 cm	22.2 Km/Hr	2800.0 mm/Km	2726	3.7	Good	25.9017783	N	85.0203104	E	Normal
09/07/22	16:01:07	61	100	500	30.0 cm	24.9 Km/Hr	3000.0 mm/Km	2911	3.92	Good	25.9017783	N	85.0203104	E	Normal
09/07/22	16:01:21	61	100	600	18.0 cm	25.2 Km/Hr	1800.0 mm/Km	1798	2.55	Good	25.9017783	N	85.0203104	E	Normal
09/07/22	16:01:32	61	100	700	18.0 cm	34.9 Km/Hr	1800.0 mm/Km	1798	2.55	Good	25.9017783	N	85.0203104	E	Normal
09/07/22	16:01:44	61	100	800	26.0 cm	30.0 Km/Hr	2600.0 mm/Km	2540	3.47	Good	25.9017783	N	85.0203104	E	Normal
09/07/22	16:02:09	61	100	900	22.0 cm	14.6 Km/Hr	2200.0 mm/Km	2169	3.02	Good	25.9017783	N	85.0203104	E	Normal
09/07/22	16:02:31	61	100	1000	28.0 cm	16.3 Km/Hr	2800.0 mm/Km	2726	3.7	Good	25.9017783	N	85.0203104	E	Normal
09/07/22	16:02:56	61	100	1100	23.0 cm	14.8 Km/Hr	2300.0 mm/Km	2262	3.13	Good	25.9017783	N	85.0203104	E	Normal
09/07/22	16:03:15	61	100	1200	29.0 cm	18.7 Km/Hr	2900.0 mm/Km	2819	3.81	Good	25.9017783	N	85.0203104	E	Normal
09/07/22	16:03:36	61	100	1300	24.0 cm	15.8 Km/Hr	2400.0 mm/Km	2355	3.24	Good	25.9017783	N	85.0203104	E	Normal
09/07/22	16:03:50	61	100	1400	27.0 cm	24.9 Km/Hr	2700.0 mm/Km	2633	3.59	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:04:03	61	100	1500	28.0 cm	28.8 Km/Hr	2800.0 mm/Km	2726	3.7	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:04:14	61	100	1600	27.0 cm	32.4 Km/Hr	2700.0 mm/Km	2633	3.59	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:04:32	61	100	1700	25.0 cm	21.4 Km/Hr	2500.0 mm/Km	2447	3.36	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:04:52	61	100	1800	18.0 cm	17.1 Km/Hr	1800.0 mm/Km	1798	2.55	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:05:05	61	100	1900	20.0 cm	27.5 Km/Hr	2000.0 mm/Km	1983	2.78	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:05:20	61	100	2000	29.0 cm	24.4 Km/Hr	2900.0 mm/Km	2619	3.81	Good	25.9108286	N	85.0186014	E	Normal

22/8/22

Signature

Executive Engineer
Rural Works Department
Mark Division, Sonapatna
22/8/22

1141

Rohan Raj Infra Projects Private Limited

(R)Rural Road


Good	Average	Poor
< 4000	4001 - 5000	> 5000

09/07/22	16:05:36	61	100	2100	20.0 cm	22.7 Km/Hr	2000.0 mm/Km	1983	2.78	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:05:56	61	100	2200	23.0 cm	17.8 Km/Hr	2300.0 mm/Km	2262	3.13	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:06:09	61	100	2300	25.0 cm	27.9 Km/Hr	2500.0 mm/Km	2447	3.36	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:06:30	61	100	2400	23.0 cm	18.0 Km/Hr	2300.0 mm/Km	2262	3.13	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:06:57	61	100	2500	23.0 cm	13.1 Km/Hr	2300.0 mm/Km	2262	3.13	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:07:37	61	100	2600	28.0 cm	29.1 Km/Hr	2800.0 mm/Km	2726	3.7	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:08:05	61	100	2700	27.0 cm	12.8 Km/Hr	2700.0 mm/Km	2633	3.59	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:08:27	61	100	2800	21.0 cm	16.2 Km/Hr	2100.0 mm/Km	2076	2.9	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:08:50	61	100	2900	21.0 cm	16.2 Km/Hr	2100.0 mm/Km	2076	2.9	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:09:19	61	100	3000	27.0 cm	12.0 Km/Hr	2700.0 mm/Km	2633	3.59	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:10:02	61	100	3100	21.0 cm	26.2 Km/Hr	2100.0 mm/Km	2076	2.9	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:10:15	61	100	3200	27.0 cm	11.9 Km/Hr	2700.0 mm/Km	2633	3.59	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:10:26	61	100	3300	17.0 cm	27.2 Km/Hr	1700.0 mm/Km	1705	2.43	Good	25.9108286	N	85.0186014	E	Normal
09/07/22	16:10:36	61	100	3400	20.0 cm	33.1 Km/Hr	2000.0 mm/Km	1983	2.78	Good	25.9144736	N	85.0035028	E	Normal
09/07/22	16:10:47	61	100	3500	27.0 cm	36.0 Km/Hr	2700.0 mm/Km	2633	3.59	Good	25.9139243	N	85.0035181	E	Normal
09/07/22	16:10:58	61	100	3600	28.0 cm	32.4 Km/Hr	2800.0 mm/Km	2726	3.7	Good	25.9131918	N	85.0035334	E	Normal
09/07/22	16:11:09	61	100	3700	27.0 cm	32.0 Km/Hr	2700.0 mm/Km	2633	3.59	Good	25.9131918	N	85.0035334	E	Normal
09/07/22	16:11:09	61	100	3800	19.0 cm	32.7 Km/Hr	1900.0 mm/Km	1890	2.67	Good	25.9131918	N	85.0035334	E	Normal

Handwritten signature: [Signature]
12/10/2012

Am
Executive Engineer
Rural Works Department
Work Division, Sonapur
22/8/22

Name of Customer: Rohan Raj Infra Projects Private Limited , Machine no: 19205 , Road: Rohan Raj Infra Projects Private Limited , Date: 09-07-22 , Section No: 61 , Equation: $Y=0.928X+127.3$

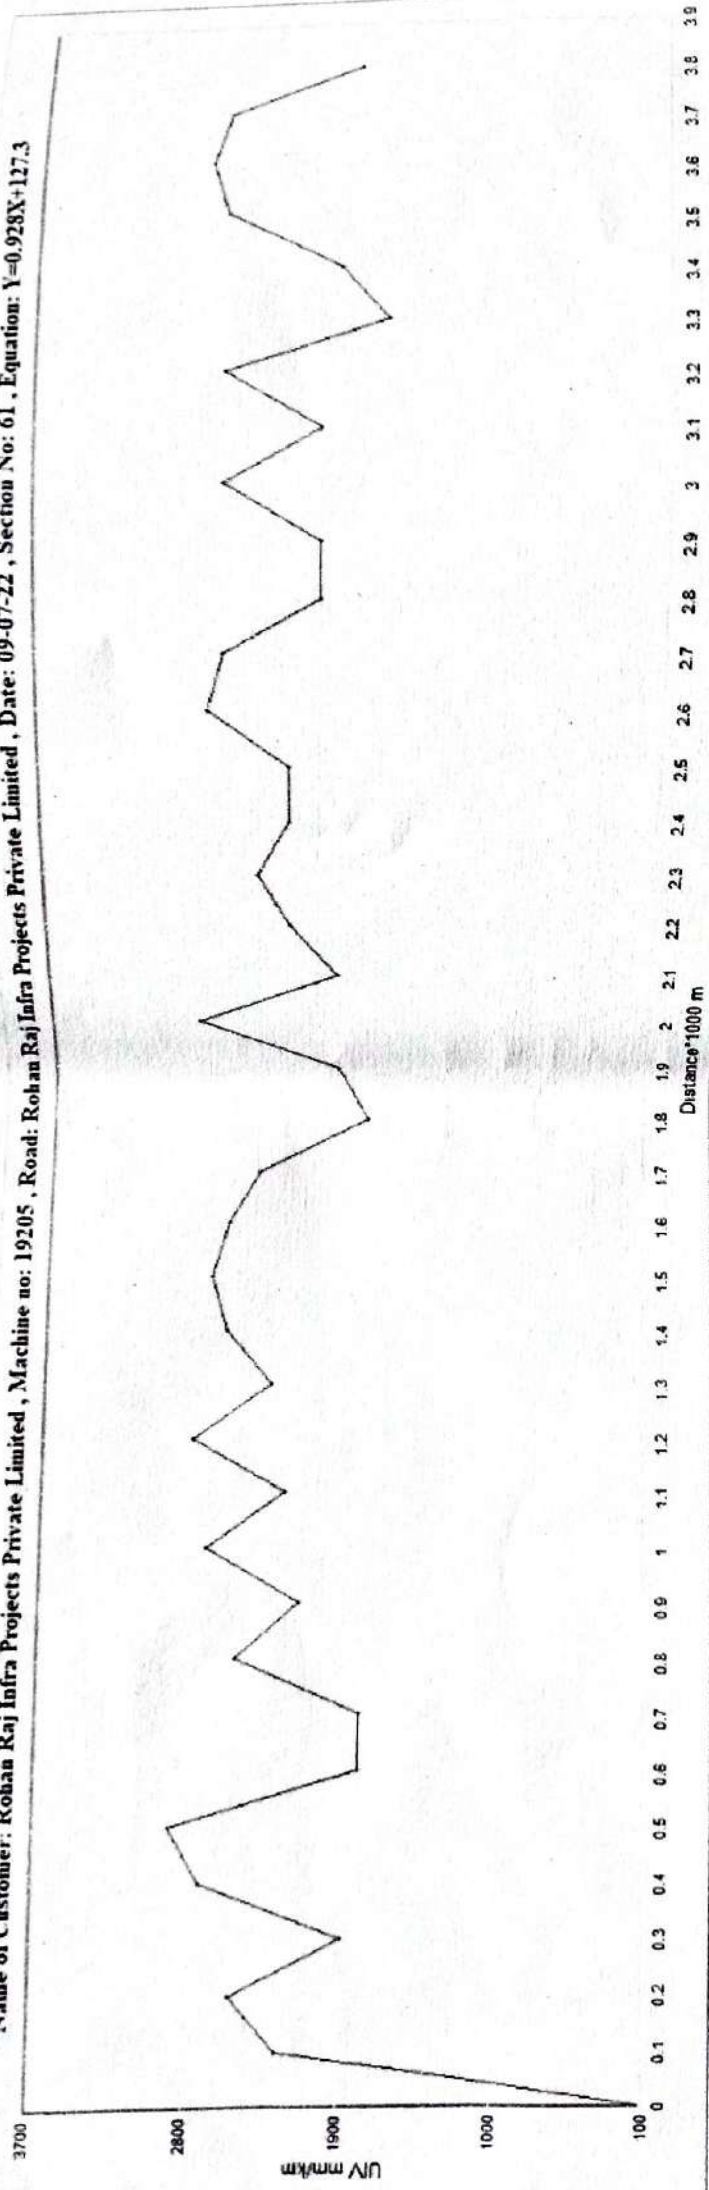

[Signature]
22/8/22

[Signature]
22/8/22
A.E.

[Signature]
22/8/22
Executive Engineer
Rural Works Department
Work Division, Sonapur
22/8/22
