

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सिकहरना, ढाका।

पत्रांक - 1202(अ-40)/सिकहरना, ढाका, दिनांक-22-08-2022

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिकहरना, ढाका।

सेवा में,


अपर मुख्य कार्यपालक पदाधिकारी,
ग्रामीण कार्य विभाग,
विश्वसरैया भवन, पाच्चा तल्ला, बिहार, पटना।

विषय :- M/R (3054) New Maintenance Police 2018 (Maintenance) योजना हेतु
आवंटन अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि इस प्रमंडलान्तर्गत M/R (3054)
New Maintenance Police 2018 (Maintenance) योजना के अधीन कराये गये कार्य के विरुद्ध
भुगतान हेतु आवंटन अधियाचना विहित-प्रपत्र में संलग्न कर समर्पित किया जाता है।
अनुलग्नक :- यथोक्त।

विश्वासभाजन


22/8/22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
सिकहरना, ढाका।

Requisition Formate for Scheme Head- 5 Year Maintenance of MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and surface Renewal)
 Division :- Dhaka
 of Circle :- Motihari

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Sanction Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Current Maintenance Demand (In Lacs)					Remarks
					Length (In km)	Amount of (in lakh)	Initial Rectification with surface Renewal (in lakh)	5 Year Routine Maintenance (In lakh)				1st Qtr Maint. Demand	2nd Qtr Maint. Demand	3rd Qtr Maint. Demand	4th Qtr Maint. Demand	5th Qtr Maint. Demand	
1	RM/EA/SIK/19/0003	Motihari Dhaka PwD road to Partapur	31708602173	1873/24.06.2019	0.66	27.74300	13.99200	6.29650	Dt-28.01.2020 38MBD/2019-20	27.10.2020	19.01.2021	0.31467	0.31467	0.31467	0.31467	0.31467	
2		Motihari Dhaka road to Shitalpatti	3.1709E+10		3.86	159.86700	97.84100	39.59455		27.10.2020	19.01.2021	1.97874	1.97874	1.97874	1.97874	1.97874	
3		REO Road Kathmaliya Chowk to Kapoor Pakari Path	NEA22000193		3.60	150.29200	91.25300	36.67588		27.10.2020	19.01.2021	1.83287	1.83287	1.83287	1.83287	1.83287	
					337.90200	203.08600	203.08600	82.56693				4.12628	4.12628	4.12628	4.12628	4.12628	

Divisional Accounts Officer
 Rural Works Div, Dhaka

- उपरोक्त पथों का मूल कार्य विशिष्टियों के अनुरूप पूर्ण कराया जा चुका है।
- सर्वेदकों के द्वारा किये गये अनुसंधान कार्य का मासिक विपत्र प्रमंडल में प्राप्त है।

Executive Engineer
 RWD (W) Div. Dhaka
 17/08/22


FORM GFR 19-A

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate Upto the Month of upto.....

MR 3054 New Maintenance Policy-2018 (Maintenance)**PIU :- EE RWD (W) DIVISION DHAKA**

Sl.	Name of the Scheme	Sanction No. & Date with Amount (Rs. In Lakh)	Amount Received (Rs. In Lakh)	Particulars
1	Construction of Rural Roads Under MR-3054 New Maintenance Policy-2018 (Maintenance)			Certified that out of Rs. Nil Lacs received the year 2022-23 in favor of Executive Engineer, R.W.D. (W), Division Dhaka a sum of Rs. Nil lacks has been utilized for the purpose of MR 3054 New Maintenance Policy-2018 (Maintenance) Schemes as given in the margin for which it was sanctioned of Rs. Nil Remaining unutilized at the end of the period under.
Total :-				

Certified that I have satisfied my self that the condition on which the grants-in-aid was sanctioned have been duly fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.




Divisional Account Officer
R.W.D. (W) Div., Dhaka

Kind of Checks Exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conduct by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurement have been recorded in the MBs and test check conducted by the Assistant.
- All other codal Formalities have been observed.

Physical Progress achieved :-

- Construction of Road Works.
- Construction of CD Works.


Executive Engineer
R.W.D.(W) Div., Dhaka

17/08/22

Steco Analyzer

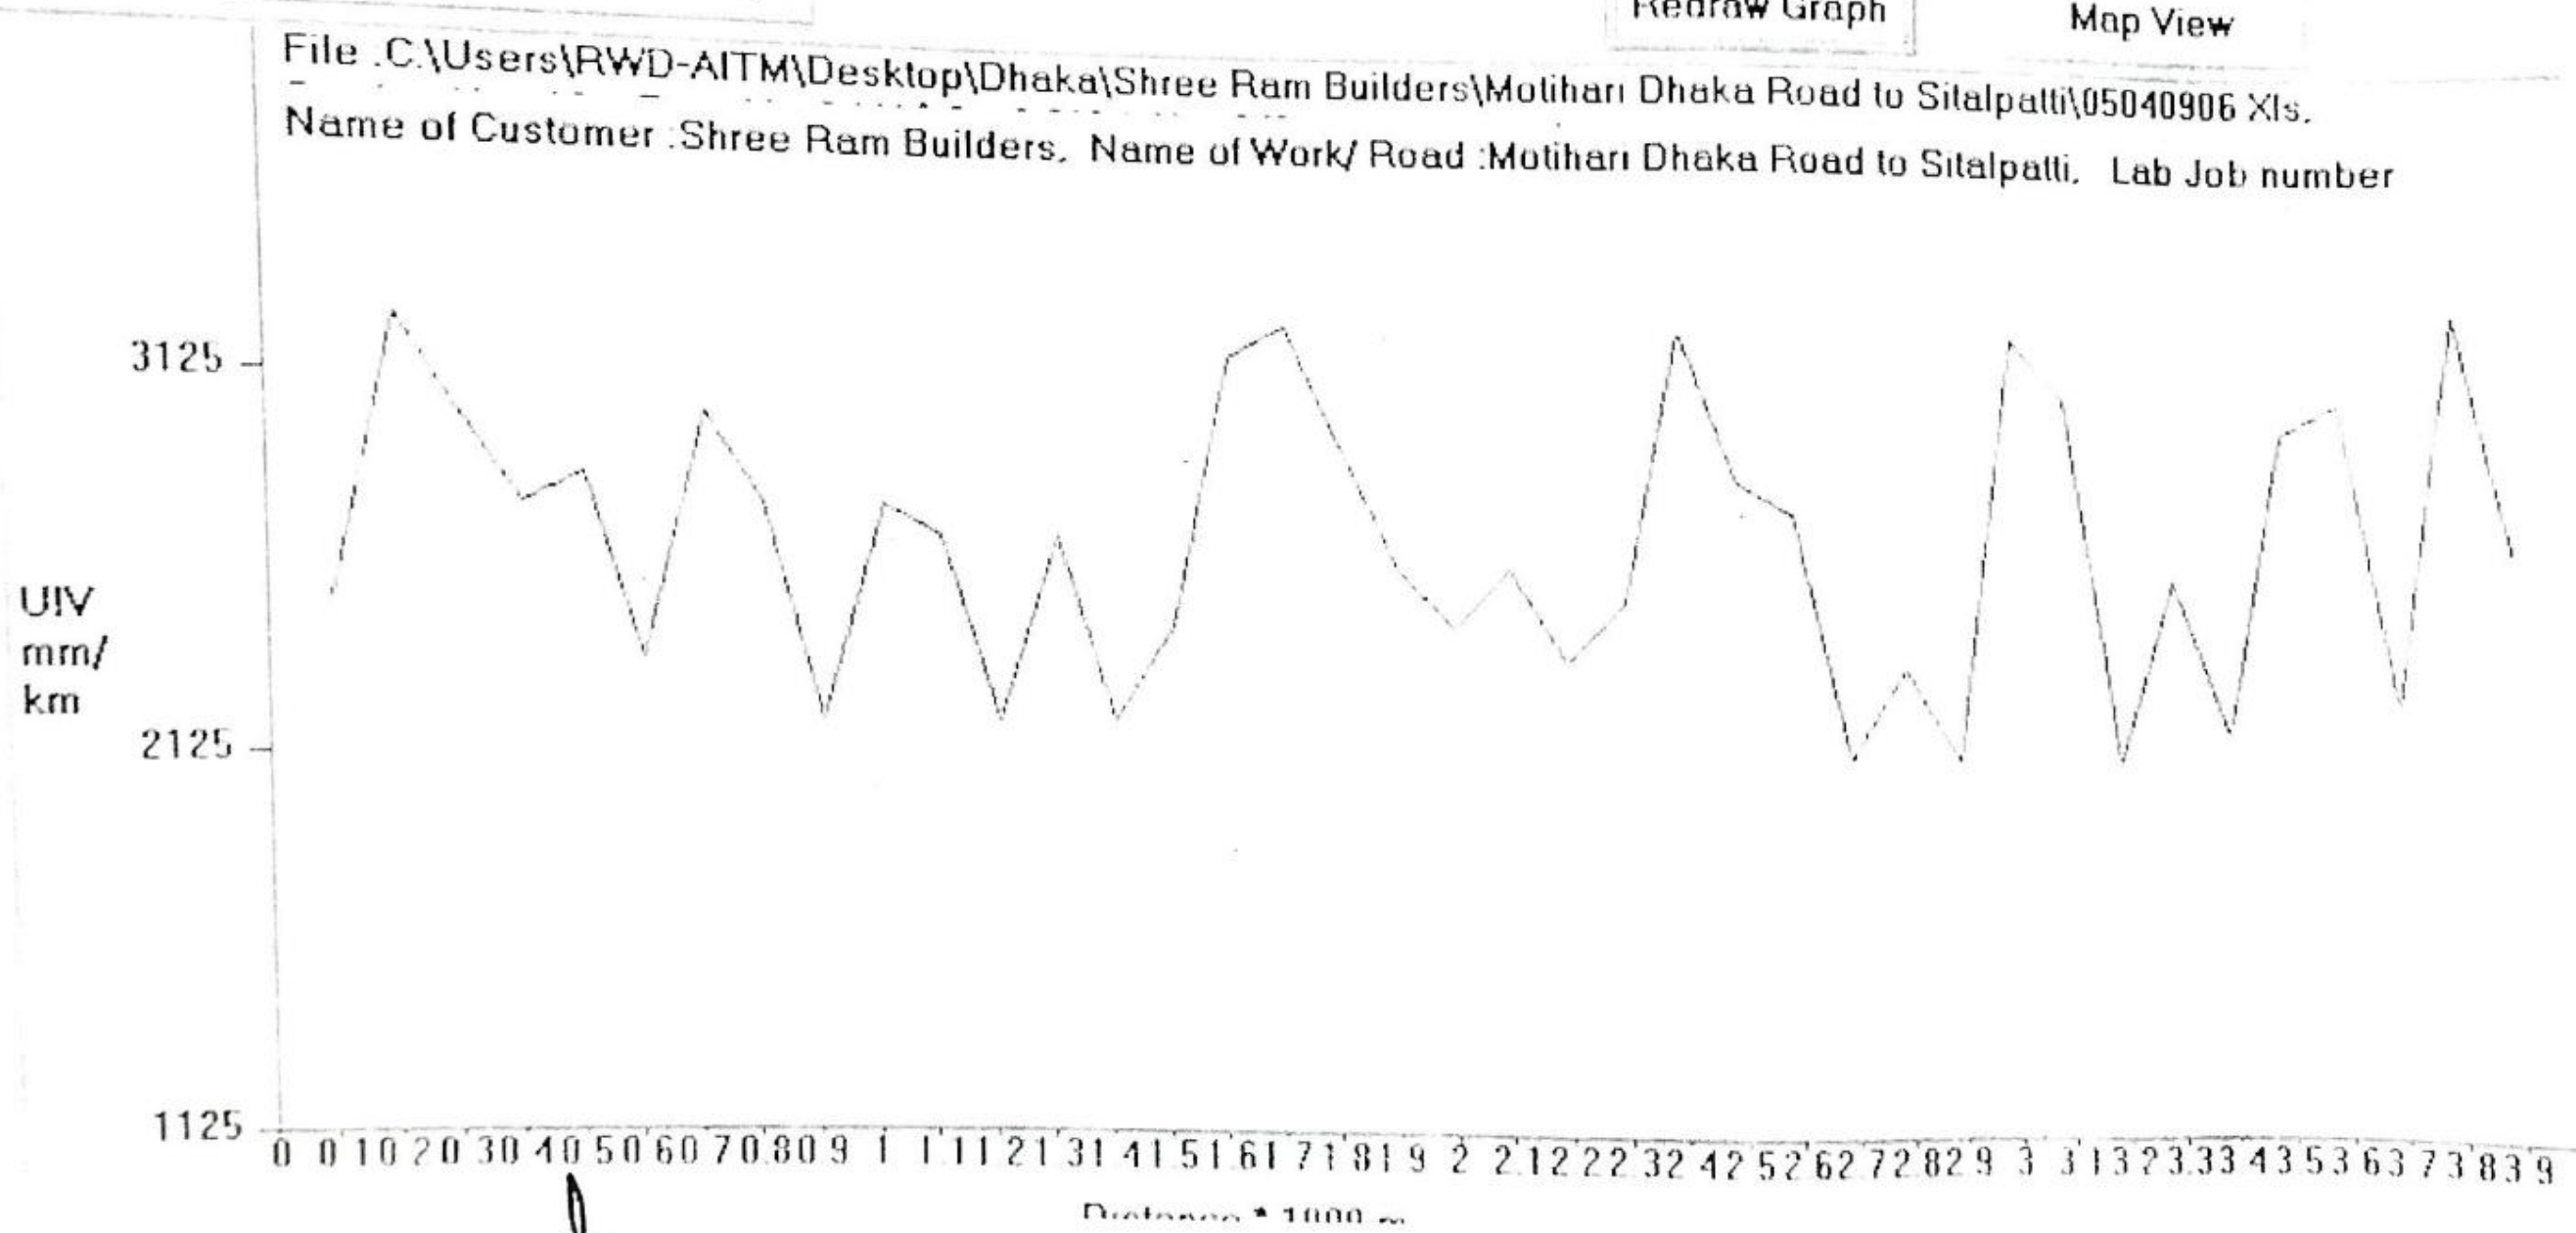
Name of Customer: Shree Ram Builders
Name of Work/ Road: Motihari Dhaka Road to Sitalpatti
Lab Job number:
Date: 07-06-2022
Section No.: 10

Test Date: 07-06-2022 Road Name: Motihari Dhaka Road to Sitalpatti
Machine No: 371 Road Type: (R) RURAL ROAD
Start S No.: Side:
Start E No.: Interval
Weather: N UIV Range: 1125 To 4000 1000 mm/km
Start Location: Motihari Dhaka Dist Range: 0 To 4 0.1 * 1000 m
End Location: Sitalpatti Equation: $Y = 0 \cdot X^2 + 0.816 \cdot X + 249$

Print Generate Report and Graph

Redraw Graph

Map View



07/06/2022
JE

15.6.22
EE

Name of Road :-Motihari Dhaka Road to Sitalpatti
Name of Contractor:-Shree Ram Builders

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	TEGORY ROAD
7/6/22	8:53:19	10	0.1	280	20.2	2800	2533	G
7/6/22	8:54:0	10	0.1	370	20.2	3700	3268	G
7/6/22	8:54:0	10	0.1	340	20.2	3400	3023	G
7/6/22	8:54:30	10	0.1	310	10.1	3100	2778	G
7/6/22	8:55:5	10	0.1	320	20.2	3200	2860	G
7/6/22	8:55:5	10	0.1	260	20.2	2600	2370	G
7/6/22	8:55:40	10	0.1	340	10.1	3400	3023	G
7/6/22	8:56:0	10	0.1	310	10.1	3100	2778	G
7/6/22	8:56:15	10	0.1	240	20.2	2400	2207	G
7/6/22	8:56:15	10	0.1	310	10.1	3100	2778	G
7/6/22	8:56:51	10	0.1	300	20.2	3000	2696	G
7/6/22	8:57:0	10	0.1	240	20.2	2400	2207	G
7/6/22	8:57:0	10	0.1	300	20.2	3000	2696	G
7/6/22	8:57:26	10	0.1	370	10.1	3700	3268	G
7/6/22	8:57:26	10	0.1	350	10.1	3500	3104	G
7/6/22	8:57:26	10	0.1	350	10.1	3600	3186	G
7/6/22	8:58:1	10	0.1	360	10.1	3700	3268	G
7/6/22	8:58:1	10	0.1	370	10.1	3300	2941	G
7/6/22	8:58:37	10	0.1	330	10.1	3300	2941	G
7/6/22	8:59:0	10	0.1	290	20.2	2900	2615	G
7/6/22	8:59:12	10	0.1	270	20.2	2700	2452	G
7/6/22	8:59:12	10	0.1	290	20.2	2900	2615	G
7/6/22	8:59:47	10	0.1	380	10.1	3800	3349	G
7/6/22	9:0:0	10	0.1	280	20.2	2800	2533	G
7/6/22	9:0:22	10	0.1	370	10.1	3700	3268	G
7/6/22	9:0:22	10	0.1	320	20.2	3200	2860	G
7/6/22	9:0:22	10	0.1	310	10.1	3100	2778	G
7/6/22	9:1:0	10	0.1	230	10.1	2300	2125	G
7/6/22	9:1:0	10	0.1	260	20.2	2600	2370	G
7/6/22	9:1:33	10	0.1	230	20.2	2300	2125	G
7/6/22	9:1:33	10	0.1	370	10.1	3700	3268	G
7/6/22	9:2:8	10	0.1	350	10.1	3500	3104	G
7/6/22	9:2:8	10	0.1	370	10.1	3700	3268	G
7/6/22	9:2:44	10	0.1	320	20.2	3200	2860	G
7/6/22	9:3:0	10	0.1	240	20.2	2400	2207	G
7/6/22	9:3:19	10	0.1	340	10.1	3400	3023	G
7/6/22	9:3:19	10	0.1	350	10.1	3500	3104	G
7/6/22	9:4:0	10	0.1	250	20.2	2500	2288	G
7/6/22	9:4:0	10	0.1	380	10.1	3800	3349	G
7/6/22	9:4:29	10	0.1	300	10.1	3000	2696	G
7/6/22	9:5:5	10	0.1					

Total IRI	109241
Average IRI	2801.051

Latitude Longitude

26.67737	85.12995	Normal	$Y = 0 * X^2 + 0.816 * X + 249$ $X \approx 3300$ $Y \approx 2941$
26.67781	85.12988	Normal	
26.67874	85.12946	Normal	
26.67969	85.12918	Normal	
26.6805	85.12919	Normal	(R) RURAL ROAD
26.68082	85.13005	Normal	
26.68092	85.13097	Normal	
26.68161	85.13127	Speed Breaker	
26.68252	85.13119	Normal	Good <4000 Average 4001-5000 Poor >5001
26.68362	85.13116	Normal	
26.68457	85.1313	Normal	
26.68546	85.13154	Normal	
26.68635	85.13185	Normal	
26.68667	85.13236	Normal	
26.68627	85.13332	Normal	
26.68564	85.13394	Normal	
26.68511	85.13458	Normal	
26.68482	85.13575	Normal	
26.68452	85.13658	Speed Breaker	
26.68433	85.13768	Normal	
26.68417	85.13882	Normal	
26.68417	85.13882	Normal	
26.68399	85.13965	Normal	
26.68382	85.14068	Normal	
26.68374	85.14156	Normal	
26.68332	85.14274	Normal	
26.68305	85.14329	Normal	
26.68287	85.14418	Normal	
26.6827	85.145	Normal	
26.68236	85.14602	Culvert	
26.68192	85.1468	Normal	
26.68156	85.14795	Normal	
26.6811	85.14842	Normal	
26.68059	85.14904	Normal	
26.68029	85.15025	Normal	
26.67956	85.15104	Normal	
26.67904	85.15211	Normal	
26.67868	85.15228	Normal	
26.67856	85.15277	Curve	

07/06/2022
JE

15.6.22
EE

Standard Format For Roads Quarterly Statement

3rd Quarter

U Name :- R.W.D., Works Div. Dhaka

1	Name of Road	Motihari Dhaka road to Shitalpatti		
2	Batch No.	RM/EA/SIK/19/0003		
3	Project ID	31708602114		
4	Total Length of road (in K.M)	3.856		
5	Length of road to Meet Required Service Level (Completed Length) (In K.M.)	3.856		
6	No. of Total Quarter (ie 3 months as a unit) in 5 Year	20		
7	Ordinary Maintenance Cost as per Schedule {Agreement Amount For maintenance (In Lakh)}	39.59455		
8	Quarterly Payment : ¼ of Ordinary Maintenance Cost as per Schedule (In Lakh)	1.97973		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment (6) = (3)/(1)*(2)*(4)
		Length Non Compliant	Weighted Value for Payment Reduction (%)	
	Paved Roads (Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Total Payment Reduction for the Quarter (in Lakh)				0
Quarterly Payment as per Agreement				1.97973
Agreement Below 0.05%				0.00099
To be paid for the Quarter/Demand (In Lakh)				1.97874

Date of Inspection by E/I or his agent

Prepared by Contractor's self Control unit

Name of Designation of Person inspecting


13/08/2022
JE

(Signature) 22-8-22

Date :-

Signature of Person inspecting road

Certified by E/I (Signature) Date

Format for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)
RWD, Works Division, Dhaka

Government of Bihar
OM01
Rural Works Department

(3rd Quarter)

Summary of Ordinary Maintenance Inspection Report

Road From :- Motihari Dhaka road to Shitalpatti
(Package No.- MR-N/19-20 Dhaka/03)

To
Executive Engineer
RWD, Works Division, Dhaka

Date :-

Length of Road : 3.856 Km

Period From :- 20.07.2021 to 19.10.2021

Inspector :- AE, RWD, Sub Division,

Position :- A.E

No.	Standard of Works Item Name	Work Unit	Unit of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Seales Payment												
OM101	Pothole Patching	m2	12.32	32.65	80.03	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Defects Rectified within Stipulated time
OM102	Surface Depression and Rut Patching	m3	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
OM103	Crack Sealing	Lm	400	600	900	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Defects Rectified within Stipulated time
OM104	Surface Treatment			Nil	Nil								
	(a) Loss of Agreegate (Surface Ravelling)	m2	11.32	30.65	78.03	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Defects Rectified within Stipulated time
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							Not Required
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil							Not Required
105	Edge Repair	m2	Nil	Nil	Nil	Nil							
106	Digouts	m2	Nil	Nil	Nil	Nil							Defects Rectified within Stipulated time
107	Concrete pavement	m3	Nil	Nil	Nil	Nil							
	Other Activities		Nil	Nil	Nil	Nil							
OM200	Shoulder		Nil	Nil	Nil	Nil							
	Unsealed Shoulder		Nil	Nil	Nil	Nil							
OM201	(a) Edge Drop-off		150	200	350	Nil	Nil	Nil	Nil				Defects Rectified within Stipulated time
	(b) Roughness Scouring or potholes	Lm	Nil	Nil	Nil	Nil							
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							
OM202	Embankment Repair	Lm	30	35	45	Nil	Nil	Nil	Nil				Defects Rectified within Stipulated time
	Other activities (Rain Cuts)	M3	Nil	Nil	Nil	Nil							
OM300	Drainage including culverts major		Nil	Nil	Nil	Nil							
OM301	Surface Drains & Verge	Lm	Nil	Nil	Nil	Nil							
OM302	Culvert Cleanning	No	Nil	Nil	Nil	Nil							Culvert Cleaning within stipulated time
OM303	Culvert and Pit Repair	M3	Nil	Nil	Nil	Nil							Not Required
	Other activities (Whilw Washing)	M2	Nil	Nil	Nil	Nil							
	Standard of Work Item	Work	Nil	Nil	Nil	Nil							
No.	Name	Unit	1	2	3	4	5	6	7	8	9	10	Comments
OM400	Vegetation		Nil	Nil	Nil	Nil							
	Gross Control		Nil	Nil	Nil	Nil							
OM401	(a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil							
	(b) Clear near Safety signs, Kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							
OM402	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Shrub Management within Stipulated time
	Cutting of Branches of Trees	No	Nil	Nil	Nil	Nil							
	Cutting of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							
	Other Activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil							Trimming of grass within Stipulated time
OM500	Safety Signage and Road		Nil	Nil	Nil	Nil							Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							
OM502	Guard Stones	Lm	Nil	Nil	Nil	Nil							Not Required
OM503	Distance Stones	No	Nil	Nil	Nil	Nil							KM Post/200 mt. Post Not Required
OM504	Road Marking	M2	Nil	Nil	Nil	Nil							Road Marking Not Required
	Other activities												

Jayant Kumar
Bidder

13/08/22
J.E

Appendix

Executive Engineer
RWD, Works Division, Dhaka
