

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, हिलसा

पत्र संख्या1512-अनु० हिलसा/दिनांक 20.8.2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हिलसा

सेवा में,

नोडल पदाधिकारी,
MR 3054,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय:- नई अनुरक्षण निति 2018 शीर्ष के अंतर्गत कराये जा रहे अनुरक्षण कार्य के भुगतान हेतु राशि अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक नई अनुरक्षण निति 2018 शीर्ष के पथ में कराये जा रहे अनुरक्षण कार्य के भुगतान हेतु राशि की अधियाचना विहित प्रपत्र में संलग्न कर समर्पित किया जाता है।

अनु:- यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हिलसा

2008

Sl No	Road Name	Batch No.	Project ID	Actual Completion Date	AA Details		Agreement Details										PREVIOUS MAINTENANCE EXP		LENGTH AS PER REPORT 1st year	1st AS PER BUMP REPORT	CURRENT DEMAND FOR MAINTENANCE AMOUNT					REMARKS
					Main Work Amount	Mainten ance Amount	Main Work Amount	MAINTENANCE AGREEMENT AMOUNT 1ST YEAR	MAINTENANCE AGREEMENT AMOUNT 2ND YEAR	MAINTENANCE AGREEMENT AMOUNT 3RD YEAR	MAINTENANCE AGREEMENT AMOUNT 4TH YEAR	MAINTENANCE AGREEMENT AMOUNT 5TH YEAR	TOTAL MAINTENANCE AMOUNT	Length	1ST QUARTER	TOTAL MAINTENANCE EXP.					1ST QUARTER	2ND QUARTER	3RD QUARTER	4TH QUARTER	5TH QUARTER	TOTAL
1	Cont of Road from Arpa More to Sudampur Via Akbarpur (post-Habbapur) Road.	RM/NA/HIL /20/0003	10200803095	23/06/2021	96,888	23,221	95,031	4,2875	4,2875	4,2875	4,2875	4,2875	21,4375	2.29	0.00	0.00	2.29	2835	1.07188	-	-	-	-	-	1.07188	1ST QUARTER
2	TOL to Barwan Pur via Kamta (TRACK)	RM/NA/HIL /20/0003	10200802082	23/06/2021	84,508	17,854	81,843	3,13729	3,13729	3,13729	3,13729	3,13729	15,68645	1.75	0.00	0.00	1.75	2920	0.78432	-	-	-	-	-	0.78432	1ST QUARTER
3	Chikaura Arant Road To Keshochak	RM/NA/HIL /20/0003	10200813003	18/05/2021	31.06	8,461	31,177	1,84146	1,84146	1,84146	1,84146	1,84146	9,2073	0.845	0.00	0.00	0.845	3006	0.46036	0.46036	-	-	-	-	0.92072	1ST & 2ND QUARTER
4	Labna bhadaul path to Bhadaul gram	RM/NA/HIL /20/0003	1281036170	23/06/2021	38,062	8,483	35,946	1,72216	1,72216	1,72216	1,72216	1,72216	8,6108	0.8	0.00	0.00	0.8	3020	0.43054	-	-	-	-	-	0.43054	1ST QUARTER
5	Indust allipur road to Arpa village	RM/NA/HIL /20/0003	1281036483	30/05/2021	107,88	25,169	40,093	2,24872	2,24872	2,24872	2,24872	2,24872	11,2436	1	0.00	0.00	1	2199	0.56218	0.56218	-	-	-	-	1.12436	1ST & 2ND QUARTER
6	TOL to Nema Tola (TRACK)	RM/NA/HIL /20/0003	10200802117	23/06/2021	18,703	6,004	17,766	1,23291	1,23291	1,23291	1,23291	1,23291	6,16455	0.65	0.00	0.00	0.65	262	0.0823	-	-	-	-	-	0.30823	1ST QUARTER
7	Cont of Road from Village Korawan to Barhi High Road.	RM/NA/HIL /20/0003	10200803093	18/05/2021	69,487	17,349	69,92	2,44903	2,44903	2,44903	2,44903	2,44903	14,24515	1.667	0.00	0.00	1.667	3035	0.71286	0.71286	-	-	-	-	1.42572	1ST & 2ND QUARTER
8	Isamgur-Cara PWD Rd. - Ichhosh	RM/NA/HIL /20/0004	10200802053	18/05/2021	29,817	9,278	27,827	1,95536	1,95536	1,95536	1,95536	1,95536	9,7768	0.825	0.00	0.00	0.825	297	0.0884	0.0884	-	-	-	-	0.1768	1ST & 2ND QUARTER
9	TOL to Mubaddampur (TRACK)	RM/NA/HIL /20/0004	10200802076	23/03/2021	104,55	29,822	96,911	6,37748	6,37748	6,37748	6,37748	6,37748	31,8874	2.785	0.00	0.00	2.785	3003	1.9847	1.9847	-	-	-	-	3.18874	1ST & 2ND QUARTER
10	Cont of Road from Shobha Singh-Sonjama Main Road to Sonjama Main Road Chak Road	RM/NA/HIL /20/0004	10200805092	23/06/2021	55,68	15,361	50,738	3,2549	3,2549	3,2549	3,2549	3,2549	16,2745	1.415	0.00	0.00	1.415	3082	0.81372	-	-	-	-	-	0.81372	1ST QUARTER
11	Meena Bazar sado path ke nahar par road after to south village via south field	RM/NA/HIL /20/0004	1281036278	18/05/2021	53,653	14,857	49,822	3,35763	3,35763	3,35763	3,35763	3,35763	16,78815	1.29	0.00	0.00	1.29	3007	0.83941	0.83941	-	-	-	-	1.67882	1ST & 2ND QUARTER
12	Cont of Road from Amapur Village to Road Pur to Bishampur More.	RM/NA/HIL /20/0004	10200804010	18/05/2021	83,398	24,349	79,118	5,02279	5,02279	5,02279	5,02279	5,02279	25,11395	2.38	0.00	0.00	2.38	3128	1.25370	1.25370	-	-	-	-	2.51140	1ST & 2ND QUARTER
13	Village Kastampur - Sonjama Higha Sonjama Road to Jaitiya	RM/NA/HIL /20/0004	10200901021	18/05/2021	48,101	12,06	41,656	2,6059	2,6059	2,6059	2,6059	2,6059	13,0295	1.165	0.00	0.00	1.165	3009	0.83148	0.83148	-	-	-	-	1.20296	1ST & 2ND QUARTER

DAO
RWD WORKS DIVISION, HILSA

EXECUTIVE ENGINEER
RWD WORKS DIVISION, HILSA

1st Quarter

Form

Government of Bihar

OM01

Rural Work Department

ORDINARY MAINTENANCE INSPECTION REPORT
Form OM01Road From :- Const of Road From Arpa More to Sultanpur Via Akbarpur
(post- Habbipur) Road.

Length of Road : 2.29

Period:- from 24.06.2021 to 23.09.2021

Inspector :J.E., RWD Sub Division

To: ... Executive Engineer
RWD, Works Division Hilsa

Date : ...

Position : ..J.E

No.	Standard work item	Work Units	Unit of work required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed Pavement												
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No. Pothole found.
OM102	Surface Depression and Rut patching	m ²	Nil	Nil	Nil	Nil							No Surface Depression and Rut patching found.
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing found
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding / Flushing Required
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking found
OM105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
OM106	Digouts	m ²	N.A.	N.A.	N.A.	N.A.							
OM107	Concrete Pavement	m ³	N.A.	N.A.	N.A.	N.A.							
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							No Roughness, Scouring or Potholes Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding water Found
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil							No Embankment Repair Required
	Other activities		N.A.	N.A.	N.A.	N.A.							
OM300 Drainage including culverts major and minor													
OM301	Surface Drains & Verge	Lm	N.A.	N.A.	N.A.	N.A.							Not Required
OM302	Culvert Cleaning	No.	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (White Washing)	M ²	Nil	Nil	Nil	Nil							Not Required

Bidder

Appendix

Executive Engineer, Works Division

Standard work item		Work Units	Unit of work required in each kilometre										Comments
No.	Name		1	2	3	4	5	6	7	8	9	10	
OM400 Vegetation													
	Grass Control												
OM401	a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No.	Nil	Nil	Nil	Nil							Not Required
OM402	(Cutting Trees)	No.	Nil	Nil	Nil	Nil							Not Required
	(Cutting shrubs)	No.	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road												Not Required
OM501	Signs Maintenance	No.	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A.	N.A.	N.A.	N.A.							Not Applicable
OM503	Distance Stones	No.	N.A.	N.A.	N.A.	N.A.							Not Applicable
OM504	Road marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

(Signature of Contractor/Authorized representative)

Date

Time

Place

Note:- Enclose photographs with this report

Handwritten signature
12.08.12

Handwritten signature
12/08/12
PC

Handwritten signature
12/08/12

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT (1st Quarter)

1	Name of Road	Const of Road From Arpa More to Sultanpur Via Akbarpur (post-Habbipur) Road.		
2	Batch No.	RM/NA/HIL/20/0003		
3	Project ID	10200803095		
4	Total Length of Road (in km.)	2.290		
5	Length of Road to Meet Required Service Level {Completed Length} (in km) [1]	2.290		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Shedule {Agreement Amount for Maintenance} in lakh	1.07188		
8	Quarterly Payment:1/20 of Ordinary Maintenance Cost as per shedule (in Lakh) [2]	1.07188		
Compliance Criteria	Standard job Description	Non Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	Paved Roads (CARRIAGEWAY)	0%	60%	0.00
II	SHOULDERS AND EMANMENTS	0%	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0%	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0%	10%	0.00
V	VEGATAION	0%	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00
TO BE PAIF FOR THE QUARTER / DEMAND (in Lakh) [6]				1.07188

Date of inspection by E/I or his agent
Prepared by contractor's self control unit

12-08-2022
J.E. 72.08.2022

Adnan
12/08/22
AE

Name and Designation of person inspecting road

Signature

12/08/22

Date
Signature of person inspecting road

Name of work : Construction Of Road Arpa More To Sultanpur Via Akbarpur
Habbipur Road

Name of customer : M/S Kumar Construction

(R)Rural Road

Date	Time	Test No	Distance(m)	Total Distance(m)	Good		Average		Poor		Remarks				
					< 4000		4001 - 5000		> 5000						
					BUM(cm)	Speed(km/hr)	Ull(mm/km)	Corrected Ull (mm/km)	IRI	Status		Latitude	Direction	Longitude	Direction1
07/08/22	15:01:12	76	100	100	21.0 cm	8.1 km/hr	2100.0 mm/km	2254	3.12	Good	25.2370081	N	85.3048334	E	Normal
07/08/22	15:01:28	76	100	200	30.0 cm	21.6 km/hr	3000.0 mm/km	3078	4.12	Good	25.2367277	N	85.3053904	E	Curve
07/08/22	15:01:43	76	100	300	26.0 cm	24.6 km/hr	2600.0 mm/km	2712	3.68	Good	25.2376223	N	85.3058634	E	Normal
07/08/22	15:01:55	76	100	400	23.0 cm	28.5 km/hr	2300.0 mm/km	2437	3.35	Good	25.2365092	N	85.3056650	E	Curve
07/08/22	15:02:09	76	100	500	30.0 cm	26.7 km/hr	3000.0 mm/km	3078	4.12	Good	25.2392988	N	85.3054361	E	Normal
07/08/22	15:02:27	76	100	600	26.0 cm	20.2 km/hr	2600.0 mm/km	2712	3.68	Good	25.2386746	N	85.3054361	E	Normal
07/08/22	15:33:18	76	100	700	19.0 cm	23.9 km/hr	1900.0 mm/km	2071	2.89	Good	25.2531958	N	85.3053369	E	Breaker
07/08/22	15:33:32	76	100	800	26.0 cm	25.4 km/hr	2600.0 mm/km	2712	3.68	Good	25.2531958	N	85.3053369	E	Normal
07/08/22	15:33:48	76	100	900	29.0 cm	22.5 km/hr	2900.0 mm/km	2966	4.01	Good	25.2559462	N	85.3053751	E	Normal
07/08/22	15:34:03	76	100	1000	25.0 cm	24.5 km/hr	2500.0 mm/km	2620	3.57	Good	25.2559462	N	85.3053751	E	Normal
07/08/22	15:34:24	76	100	1100	27.0 cm	16.7 km/hr	2700.0 mm/km	2803	3.79	Good	25.2559462	N	85.3053751	E	Breaker
07/08/22	15:34:39	76	100	1200	34.0 cm	24.6 km/hr	3400.0 mm/km	3444	4.56	Good	25.2559462	N	85.3053751	E	Normal
07/08/22	15:34:54	76	100	1300	22.0 cm	27.2 km/hr	2200.0 mm/km	2346	3.23	Good	25.2559462	N	85.3053751	E	Normal
07/08/22	15:35:04	76	100	1400	30.0 cm	30.3 km/hr	3000.0 mm/km	3078	4.12	Good	25.2559462	N	85.3053751	E	Normal
07/08/22	15:35:15	76	100	1500	26.0 cm	30.9 km/hr	2600.0 mm/km	2712	3.68	Good	25.2559462	N	85.3053751	E	Normal
07/08/22	15:35:35	76	100	1600	32.0 cm	18.1 km/hr	3200.0 mm/km	3261	4.34	Good	25.2559462	N	85.3053751	E	Curve
07/08/22	15:35:51	76	100	1700	34.0 cm	23.1 km/hr	3400.0 mm/km	3444	4.56	Good	25.2559462	N	85.3053751	E	Normal
07/08/22	15:36:11	76	100	1800	28.0 cm	18.1 km/hr	2800.0 mm/km	2895	3.9	Good	25.2559462	N	85.3053751	E	Normal
07/08/22	15:36:51	76	100	1900	27.0 cm	9.0 km/hr	2700.0 mm/km	2803	3.79	Good	25.256012	N	85.3051462	E	Normal
07/08/22	15:37:24	76	100	2000	33.0 cm	10.8 km/hr	3300.0 mm/km	3352	4.45	Good	25.260418	N	85.3056955	E	Breaker
07/08/22	15:37:56	76	100	2100	26.0 cm	10.5 km/hr	2600.0 mm/km	2712	3.68	Good	25.260418	N	85.3056955	E	Normal

12-08-2022
12-08-2022
12-08-2022

12/10/2022
12/10/2022
12/10/2022

12/10/2022
12/10/2022
12/10/2022


Name of work :		Construction Of Road Arpa More To Sultanpur Via Akbarpur													
Name of customer :		Habbipur Road													
		(R) Rural Road													
		Good		Average				Poor							
		< 4000		4001 - 5000				> 5000							
07/08/22	15.58.35	76	100	2200	29.0 cm	9.7 Km/Hr	2900.0 mm/Km	2986	4.01	Good	25.2660418	N	85.3066955	E	Normal
07/08/22	15.59.42	76	90	2290	31.0 cm	5.1 Km/Hr	3100.0 mm/Km	3169	4.23	Good	25.2664633	N	85.3066432	E	Normal

km/s-12-08-22
12-08-22

12/08/22
12/08/22
At

12/08/22

Name of Customer: M/S Kumar Construction, Machine no: 19214, Road: Construction Of Road Arpa More To Sultanpur Via Akbarpur Habbipur Road, Date: 07.08.22, Section No: 76, Equation: $y = 0.915 + 332.7$

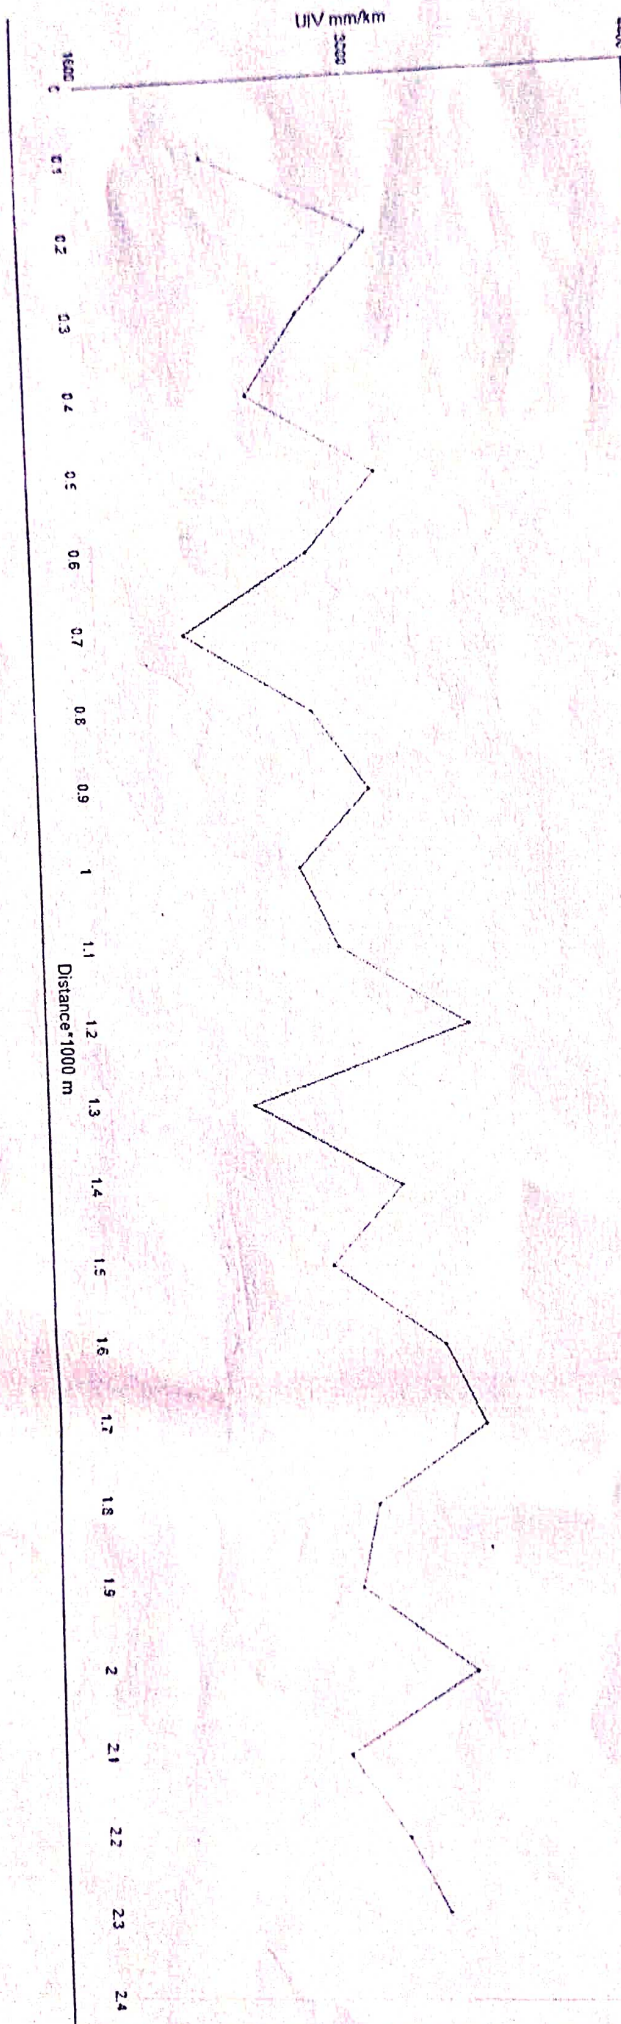

12/08/2022
12.08

12/10/22
12.10
At

12/08/22
