

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, दलसिंहसराय।

पत्रांक:-

1434 (कव)

दिनांक:- 25/8/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, दलसिंहसराय

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
सचिव -सह- प्राधिकृत पदाधिकारी, बिहार
ग्रामीण पथ विकास एजेंसी पटना।

विषय-

MR New Maintenance Policy 2018 योजनान्तर्गत 5 पथों का पॉचवर्षीय अनुरक्षण का आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि MR New Maintenance Policy 2018 योजनान्तर्गत पॉचवर्षीय अनुरक्षण के पथों का पथवार मॉगी जानेवाली आवंटन की सूची Quarter Wise इस पत्र के साथ संलग्न कर आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अतः अनुरोध है कि उक्त पथों में आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०- 1) अधियाचना प्रपत्र।

2) 19ए फॉर्म।

3½ IRI Report की छायाप्रति संलग्न।

विश्वासभाजन

25/8/22

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, दलसिंहसराय

FORM GFR -19 -A

(see Govt. of India's decision (i) below rule 150)

Form of Utilisation Certificate upto the Month of June 2022

New Maintenance Policy -2018

PIO:- R.W.D. Works, Division , Dalsinghsarai

Month : June 2022

Sl. No.	Name of Scheme	Sanction No.& Date with amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	2	3	4	5
1	Maintenance of Rural Road Under New Maintenance Policy - 2018 MR- 3054	14/18.7.2022 (748033)	748033.00	Certified that out of Rs-748033 lacs received during the year's 2022-23 in favour of Ex-Engineer, R.W.D. Works Division, Dalsinghsarai a sum of Rs.0.00 lacs has been utilized for the purpose of New Maintenance Policy -2018 as given in the margine for which it was sanctioned and that the balance of Rs-748033 remaining unutilized at the end of the period under the time of completion.
		0.00	748033.00	

2 Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have


Kind of Checks Exercised :-

- (i) Workers have been supervised by Executive Engineer/ Superintending Engineer
- (ii) Periodical inspection has been conducted by Executive Engineer/Superintending Engineer
- (iii) Construction materials have been tested.
- (iv) Measurments have been recorded in the MB's and test check conducted by the Assistant
- (v) All other codal formalities have overserved

3 Physical Progress Achieved.

- (i) Construction of Road Works
- (ii) Construction of CD Works.

SR. D.A.O
Rural Works Division
Works Division, Dalsinghsarai


Executive Engineer
Rural Works Division
Works Division, Dalsinghsarai

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

TIU Name :-RWD,Works Divisin,Dalsinghsarai

1	Name of the Road	NH-28, Satanpur to REO Road Salampur		
2	Batch No.	RM/SA/DAL/19/0013		
3	Project ID	32010401004		
4	Total Length of Road (in Km)	2.05		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	2.05		
6	No. of Total Quarter (ie 3 Months as a in 5 years)	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	2.20816		
8	Quarterly Payment :3/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.98532		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Paym'nt [6]=[3]/[1]*[2]*[4]
		Length Non- compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS		60%	0
II	SHOULDERS AND		10%	0
III	CROSS DRAINAGE		15%	0
IV	SIGNAGE AND ROAD		10%	0
V	VEGETATION		5%	0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				0.98532

Date of inspection by E/I or his agent

Prepared by Contractor's Self Control Unit

Name and Designation of person inspecting road


Date

Signature of person inspecting road

Certify by E/I [signature] Date:-

Executive Engineer
Rural works Department
Works Division,Dalsinghsarai

Name of Customer: SONA INFRACON PRIVATE LIMITED, Machine no: 19190, Road: NH-28, Salraipur to REO Road Salraipur, Date: 12/08/22, Section No: 20, Equation: $Y=0.909X+125.0$

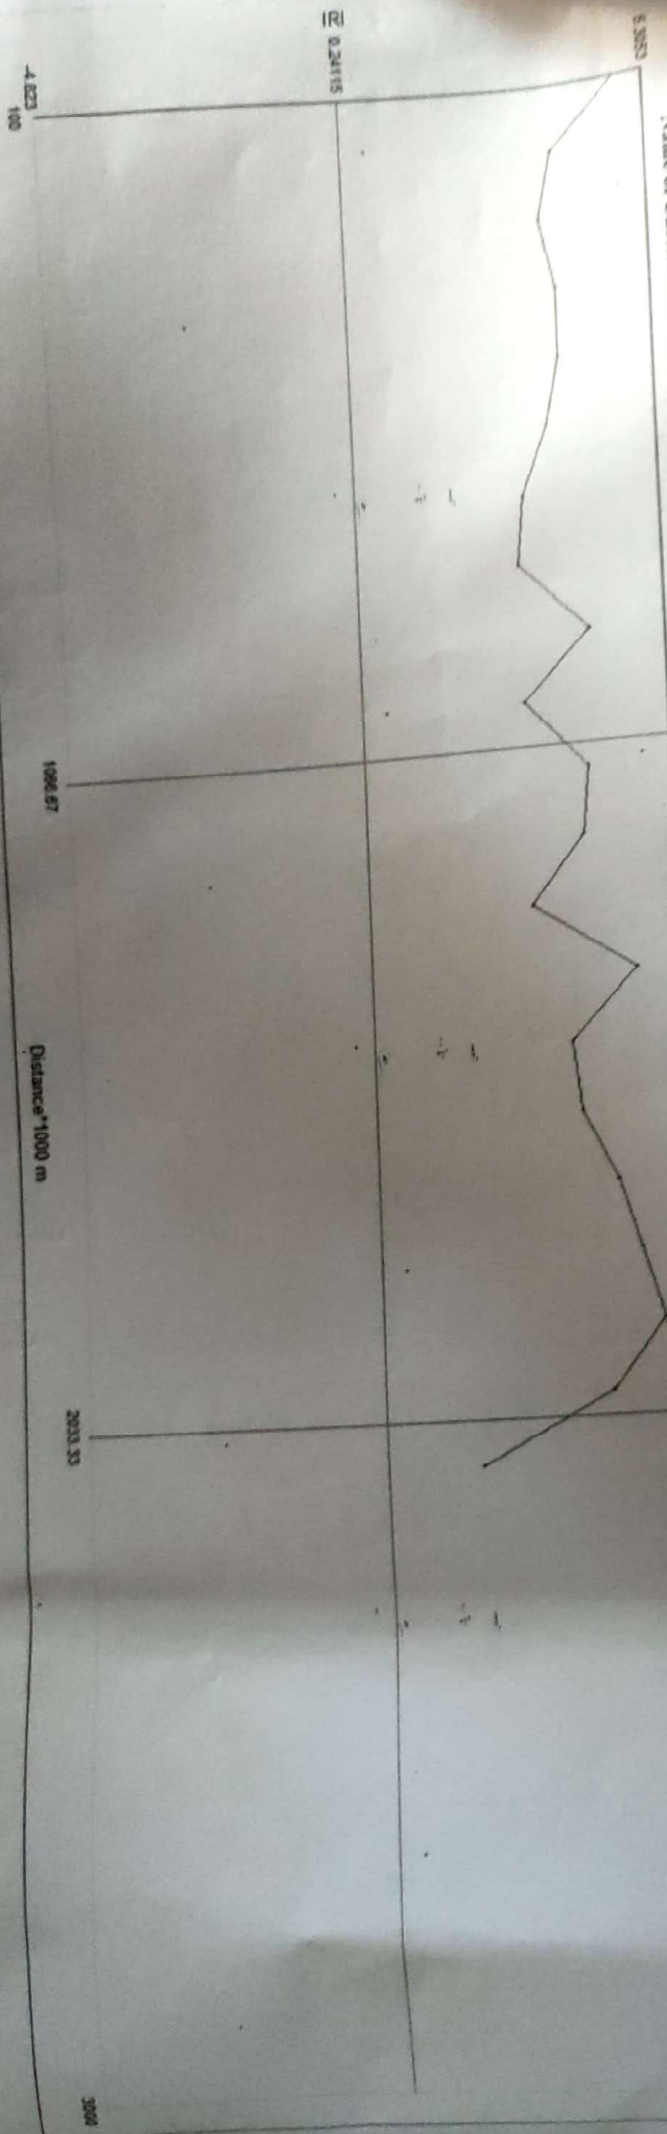

500/AN
1/21/01/2022
SE

1/21/01/2022
1/21/01/2022
1/21/01/2022

7/5/10/8/1/22
E.E.

Name of the work: NH-28, Satapur to REO Road Salampur

Date	Time	Test No	Distance (meter)	Total Distance (meter)	BUMP (cm)	Speed (km/h)	U1 (mm/Km)	Corrected U1 (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
12/8/2022	13:17:07	20	100	100	39.0 cm	15.8 Km/Hr	3900.0 mm/Km	3670.1	3.823	Good	25.75484	N	85.78013	E	Normal
12/8/2022	13:18:27	20	100	200	29.0 cm	17.4 Km/Hr	2900.0 mm/Km	2761.1	3.741	Good	25.7539	N	85.77973	E	Normal
12/8/2022	13:19:48	20	100	300	27.0 cm	17.5 Km/Hr	2700.0 mm/Km	2579.3	3.52	Good	25.75309	N	85.77929	E	Normal
12/8/2022	13:20:08	20	100	400	29.0 cm	17.6 Km/Hr	2900.0 mm/Km	2761.1	3.741	Good	25.75241	N	85.77872	E	Normal
12/8/2022	13:21:46	20	100	500	29.0 cm	12.5 Km/Hr	2900.0 mm/Km	2761.1	3.741	Good	25.75188	N	85.77792	E	Normal
12/8/2022	13:22:14	20	100	600	27.0 cm	12.8 Km/Hr	2700.0 mm/Km	2579.3	3.52	Good	25.75135	N	85.77717	E	Normal
12/8/2022	13:23:41	20	100	700	23.0 cm	13.2 Km/Hr	2300.0 mm/Km	2215.7	3.074	Good	25.75065	N	85.77661	E	Normal
12/8/2022	13:24:15	20	100	800	22.0 cm	10.8 Km/Hr	2200.0 mm/Km	2124.8	2.961	Good	25.74967	N	85.77631	E	Normal
12/8/2022	13:25:42	20	100	900	32.0 cm	22.9 Km/Hr	3200.0 mm/Km	3033.8	4.069	Good	25.74878	N	85.77599	E	Normal
12/8/2022	13:26:42	20	100	1000	22.0 cm	12.9 Km/Hr	2200.0 mm/Km	2124.8	2.961	Good	25.74802	N	85.77528	E	Normal
12/8/2022	13:27:42	20	100	1100	31.0 cm	10.9 Km/Hr	3100.0 mm/Km	2942.9	3.96	Good	25.74741	N	85.77473	E	Normal
12/8/2022	13:28:42	20	100	1200	30.0 cm	12.9 Km/Hr	3000.0 mm/Km	2852	3.851	Good	25.74744	N	85.7738	E	Normal
12/8/2022	13:29:42	20	100	1300	22.0 cm	11.9 Km/Hr	2200.0 mm/Km	2124.8	2.961	Good	25.74648	N	85.77373	E	Normal
12/8/2022	13:30:42	20	100	1400	37.0 cm	16.9 Km/Hr	3700.0 mm/Km	3488.3	3.609	Good	25.74562	N	85.77358	E	Normal
12/8/2022	13:31:42	20	100	1500	27.0 cm	14.9 Km/Hr	2700.0 mm/Km	2579.3	3.52	Good	25.74466	N	85.77323	E	Normal
12/8/2022	13:32:42	20	100	1600	38.0 cm	13.9 Km/Hr	2800.0 mm/Km	2670.2	3.631	Good	25.74382	N	85.77281	E	Normal
12/8/2022	13:33:42	20	100	1700	33.0 cm	22.9 Km/Hr	3300.0 mm/Km	3124.7	3.178	Good	25.74299	N	85.77249	E	Normal
12/8/2022	13:34:42	20	100	1800	36.0 cm	17.9 Km/Hr	3600.0 mm/Km	3397.4	3.502	Good	25.74199	N	85.77195	E	Normal
12/8/2022	13:35:42	20	100	1900	39.0 cm	16.9 Km/Hr	3900.0 mm/Km	3670.1	3.823	Good	25.74113	N	85.77148	E	Normal
12/8/2022	13:36:42	20	100	2000	31.0 cm	22.9 Km/Hr	3100.0 mm/Km	2942.9	3.96	Good	25.7403	N	85.77095	E	Normal
12/8/2022	13:37:42	20	100	2100	12.0 cm	10.9 Km/Hr	1200.0 mm/Km	1215.8	1.799	Good	25.73964	N	85.77097	E	Normal

95108112
S.E

17/11/22
S.E

95108112
S.E

Machine ID 19190
IRI Value 3712
