

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Mobile No- 8986915814

Email ID- eerwdwd2bettiah@gmail.com

पत्रांक- 1494 अड्ड/ नरकटियागंज, दिनांक- 04/8/22

प्रेषक,

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
-सह- सचिव नोडल पदाधिकारी,
ग्रामीण कार्य विभाग,
बिहार पटना।

विषय:-

MR-3054 (New Maint. Policy-2018) योजना अन्तर्गत 5 (पाँच) वर्षीय अनुरक्षण का
आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि MR-3054 (New Maint. Policy-2018) योजना
अन्तर्गत 5 (पाँच) वर्षीय अनुरक्षण का आवंटन उपलब्ध कराने के लिए सूची बनाकर इस पत्र में
संलग्न कर अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अनु०:- 1. उपयोगिता प्रमाण-पत्र From GFR 19A

2. अधियाचना पत्र।

विश्वासभाजन,

कार्यपालक अभियन्ता,

ग्रा०का०वि०, का०प्र०, नरकटियागंज।

04/08/2022

FORM GFR 19-A

(See Government of India's decision (I) below rule- 150)
Form of Utilization certificate up to the month of Aug-2022

PIU:- E.E RWD(W)DIV-NARKATIAGANJ

SL.NO.	Name of Schemes	Sanction No.& Date with Amount (In Lacs)	Amount received (In Lacs)	Particulars
1	2	3	4	5
1	Maintenance Fund of MR(3054) New Maintenance Policy- 2018		NIL	Certified that out of Rs. 0.00 Lacs of grants-in-aid sanctioned during the years 2022-23 in favour of Executive Engineer R. W. D. Works Division, Narkatiaganj a sum of Rs. 0.00 Lacs has been utilized for the purpose of Maintenance Fund of MR(3054) New Maintenance Policy-2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs. NIL Lac remaining unutilized at the end of the period under report.
		TOTAL	NIL	

2. Certified that I have satisfied myself that the conditions on which the grant-in-aid was sanctioned have been duly fulfilled, are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.


SR.DIV ACCOUNTS OFFICER
R.W.D. Works Division, Narkatiaganj

Kinds of checks exercised:-

- Works has been supervised by Executive Engineer / Superintending Engineer.
- Periodic as inspection has been conducted by Executive Engineer / Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer / Executive Engineer.
- All other codal formalities have been observed.

3. Physical Progress achieved:-

- Construction of Road Works.
- Construction of CD Works.


Executive Engineer
R.W.D. Works Division, Narkatiaganj

Requisition Format for Scheme Head - 5 Year Maintenance of MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Rectification and surface Renewal)

Name of Division :- Narkatiaganj

Name of Circle :- Bettiah

Sl. No	Package No.	Name of Road	Project ID as per MIS	Administrative Sanction Letter No & Date.	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Current Maintenance Demand (In Lacs)				Remarks.
					Length (in km)	Amount of (in Lakh)	Initial Rectification with surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)				1st Qtr Maint Demand	2nd Qtr Maint Demand	3rd Qtr Maint Demand	4th Qtr Maint Demand	
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
1	RM/WE/NAR/19/0025	Bakulahr to Fatepur Jitiya	318891031902	3628 27.08.2019	3.86	137.3364	92.845	34.13715	37/MBD/2021-22	06.03.2021	05.05.2021	1.70686	1.70686	-	-	
2	RM/WE/NAR/19/0025	Chanpatiya Lalgaadh Karamaya Tirhuniya Chauk via Lalgaadh from Jami Tola, Jha Tola	318891031903	3628 27.08.2019	6.7	270.8409	189.092	59.63905	37/MBD/2021-22	06.03.2021	18.06.2021	2.98195	-	-	-	
3	RM/WE/NAR/19/0025	Mushari to Bijhaniya Bandobasti	318891032206	3628 27.08.2019	2.3	64.6468	39.872	18.99595	38/MBD/2021-22	08.03.2021	05.05.2021	0.94980	0.94980	-	-	
4	RM/WE/NAR/19/0024	Kuriya Kothi to Mahna Via Chuhri Road	318891032207	3628 27.08.2019	9.55	288.0603	179.977	83.41705	37/MBD/2021-22	06.03.2021	27.05.2021	4.17085	4.17085	-	-	
5	RM/WE/NAR/19/0024	Bettiah Lauriya to Mushari	318891032208	3628 27.08.2019	2.58	95.7343	65.44	20.92335	37/MBD/2021-22	06.03.2021	03.06.2021	1.04617	1.04617	-	-	


 Executive Engineer
 Rural Works Department
 Works Division Narkatiaganj
 Date: 04/08/2021

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD, Works Division, Narkatiaganj

2nd Quarter

Government Of Bihar

OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Bakulahar to Fatepur Jitiya

Length of Road :- 3.860 KM

Inspector :- A.E. RWD WORKS SUB DIVISION, CHANPATIA

To:-

**Executive Engineer
RWD, Works Division Narkatiaganj**

Date:-

Position :- A.E.

No	standard Of Work Item	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												
OM101	Pothole Patching	m ²	NIL	NIL	NIL								No pothole found
OM102	Surface Depression and Rut patching	m ³	NIL	NIL	NIL								No Surface Depression and Rut patching found
OM103	Crack Sealing	Lm	NIL	NIL	NIL								No crack
	Surface Treatment		NIL	NIL	NIL								Not required
OM104	(a) Loss of Aggregate (Surface Raveling)	m ²	NIL	NIL	NIL								No Loss of Aggregate (Surface raveling) found
	(b) Bleeding / Flushing	m ²	NIL	NIL	NIL								No bleeding / furnishing found
	© Crocodile Cracking	m ²	NIL	NIL	NIL								No Crocodile cracking found
OM105	Edge Repair	m ²	NIL	NIL	NIL								Notified & repaired
OM106	Digouts	m ²	N.A.	N.A.	N.A.								
OM107	Concrete pavement	m ³	N.A.	N.A.	N.A.								
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	NIL	NIL	NIL								No Edge Drop off found
	(b) Roughness, Scouring or Potholes	Lm	NIL	NIL	NIL								No Roughness, Scouring or Potholes found
	(c) Holding water	Lm	NIL	NIL	NIL								No Holding Water Found
OM202	Embankment Repair	M ³	NIL	NIL	NIL								Notified & repaired
	Other activities (Rain Cuts)		N.A.	N.A.	N.A.								
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N.A.	N.A.	N.A.								NA
OM302	Culvert Cleaning	No	NIL	NIL	NIL								DONE
OM303	Culvert and pit Repair	M ³	NIL	NIL	NIL								DONE
	Other activities (Whitewashing)	M ²	NIL	NIL	NIL								Not required

Handwritten signature

Handwritten signature



STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :- RWD, Works Division, Narkatiaganj

2nd Quarter

1	Name of the Road	Bakulahar to Fatepur Jitiya		
2	Batch No.	RM/WE/NAR/19/0025		
3	Project ID	318891031902		
4	Total Lenth of Road (in KM)	3.860		
5	Length of Road to Meet Required Service Level [Completed length](in Km) [1]	3.860		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	34.13715		
8	Quarterly Payment : 4/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.7068575		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00
II	SHOULDERS AND EMBANMENTS	0	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00
V	VEGATION	0	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (IN Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.7068575

Date of inspection by E/I or his agent
Prepare by Contractor's self Control unit

[Signature]

[Signature]
Name and Designation of person inspecting road

Date

(Signature)

[Signature]

Signature of person inspecting road

Certify by E/I [signature] Date:-
Executive Engineer
Rural Works Department
Works Division, Narkatiaganj

Name of Road - Bakulahar to Fatepur Jitiya [Sec-75]

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY	Latitude	Longitude	Event
21/4/22	10:26:4	75	0.1	140	20.2	1400	1397	ROAD	26.931505	84.589865	Normal
21/4/22	10:26:4	75	0.1	130	20.2	1300	1295	G	26.931762	84.588905	Normal
21/4/22	10:26:39	75	0.1	210	20.2	2100	2112	G	26.932135	84.58803	Normal
21/4/22	10:26:39	75	0.1	200	20.2	2000	2010	G	26.932275	84.587373	Normal
21/4/22	10:27:0	75	0.1	130	10.1	1300	1295	G	26.933132	84.58648	Normal
21/4/22	10:27:14	75	0.1	170	20.2	1700	1703	G	26.93292	84.585505	Normal
21/4/22	10:27:14	75	0.1	190	20.2	1900	1908	G	26.933187	84.584578	Normal
21/4/22	10:28:0	75	0.1	290	10.1	2900	2929	G	26.93356	84.58367	Normal
21/4/22	10:28:0	75	0.1	320	10.1	3200	3235	G	26.933635	84.58271	Normal
21/4/22	10:28:25	75	0.1	330	20.2	3300	3337	G	26.933868	84.58173	Normal
21/4/22	10:28:25	75	0.1	370	10.1	3700	3745	G	26.934078	84.580858	Normal
21/4/22	10:28:25	75	0.1	360	20.2	3600	3643	G	26.934218	84.579813	Normal
21/4/22	10:29:0	75	0.1	350	20.1	3600	3604	G	26.934305	84.57882	Normal
21/4/22	10:29:0	75	0.1	340	20.1	3400	3439	G	26.934362	84.577895	Normal
21/4/22	10:29:0	75	0.1	310	20.1	3100	3133	G	26.934248	84.576852	Normal
21/4/22	10:29:0	75	0.1	270	20.1	2700	2724	G	26.934065	84.575892	Culvert
21/4/22	10:29:35	75	0.1	250	20.3	2500	2562	G	26.934558	84.57513	Normal
21/4/22	10:29:35	75	0.1	280	20.2	2800	2835	G	26.934895	84.574225	Normal
21/4/22	10:30:0	75	0.1	260	20.2	2600	2662	G	26.935107	84.573232	Normal
21/4/22	10:30:10	75	0.1	310	20.2	3100	3133	G	26.935342	84.572238	Normal
21/4/22	10:30:10	75	0.1	290	20.2	2900	2929	G	26.935635	84.571312	Normal
21/4/22	10:30:45	75	0.1	310	20.2	3100	3133	G	26.935873	84.570387	Normal
21/4/22	10:31:0	75	0.1	230	10.1	2300	2316	G	26.93587	84.56941	Normal
21/4/22	10:31:0	75	0.1	300	10.1	3000	3031	G	26.935927	84.56843	Normal
21/4/22	10:31:20	75	0.1	240	20.2	2400	2418	G	26.93607	84.56744	Normal
21/4/22	10:31:20	75	0.1	250	20.2	2500	2520	G	26.936187	84.566413	Normal

4.8.22
GB



Name of Road - Bakulahar to Fatepur Jitiya [Sec-75]

Date	Time	Section	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY	Latitude	Longitude	Event
		No.						ROAD			
21/4/22	10:31:20	75	0.1	260	20.2	2600	2622	G	26.93624	84.565453	Normal
21/4/22	10:31:20	75	0.1	200	20.2	2000	2010	G	26.936162	84.564443	Normal
21/4/22	10:32:0	75	0.1	210	20.2	2100	2112	G	26.935922	84.563502	Normal
21/4/22	10:32:0	75	0.1	260	10.1	2600	2622	G	26.935855	84.562457	Curve
21/4/22	10:32:31	75	0.1	380	10.1	3800	3848	G	26.936027	84.561515	Normal
21/4/22	10:32:31	75	0.1	330	10.1	3300	3358	G	26.936207	84.560538	Normal
21/4/22	10:32:31	75	0.1	330	10.1	3300	3337	G	26.936532	84.559562	Normal
21/4/22	10:33:0	75	0.1	270	10.1	2700	2792	G	26.936762	84.558585	Curve
21/4/22	10:33:6	75	0.1	220	20.2	2200	2247	G	26.937512	84.558248	Curve
21/4/22	10:33:6	75	0.1	170	20.2	1700	1702	G	26.938008	84.557592	Normal
21/4/22	10:33:41	75	0.1	210	20.2	2100	2157	G	26.938328	84.556598	Normal
21/4/22	10:33:41	75	0.1	250	20.2	2500	2512	G	26.938612	84.555655	Normal
21/4/22	10:33:41	75	0	280	20.2	2800	2854	G	26.938628	84.555655	Normal

Average IRI Value=2647

AK/4.8.22
OK


Executive Engineer
Rural Works Department
Works Division, Narkatyaganj

Name of Customer :	ARBIND KUMAR SINGH
Name of Work/ Road :	Bakulohar to Fatepur Jitiya
Lab Job number :	
Date :	21-Apr-22
Section No. :	75

Test Date :	21-Apr-22	Road Name :	Bakulohar to Fatepur Jitiya
Machine No. :		Road Type :	(R) RURAL ROAD
Start S No. :		Side :	
Start E No. :		UIV Range :	295 To 5000 Interval 1000 mm/km
Weather :		Dist Range :	0 To 4 ~ 1000 m
Start Location :		Equation :	$Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$
End Location :			


Print Generate Report and Graph

Redraw Graph

Map View

File : F:\21041406.Xls, Section No. : 75, Eqn : $Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$

Name of Customer : ARBIND KUMAR SINGH, Name of Work/ Road : Bakulohar to Fatepur Jitiya, Lab Job number :

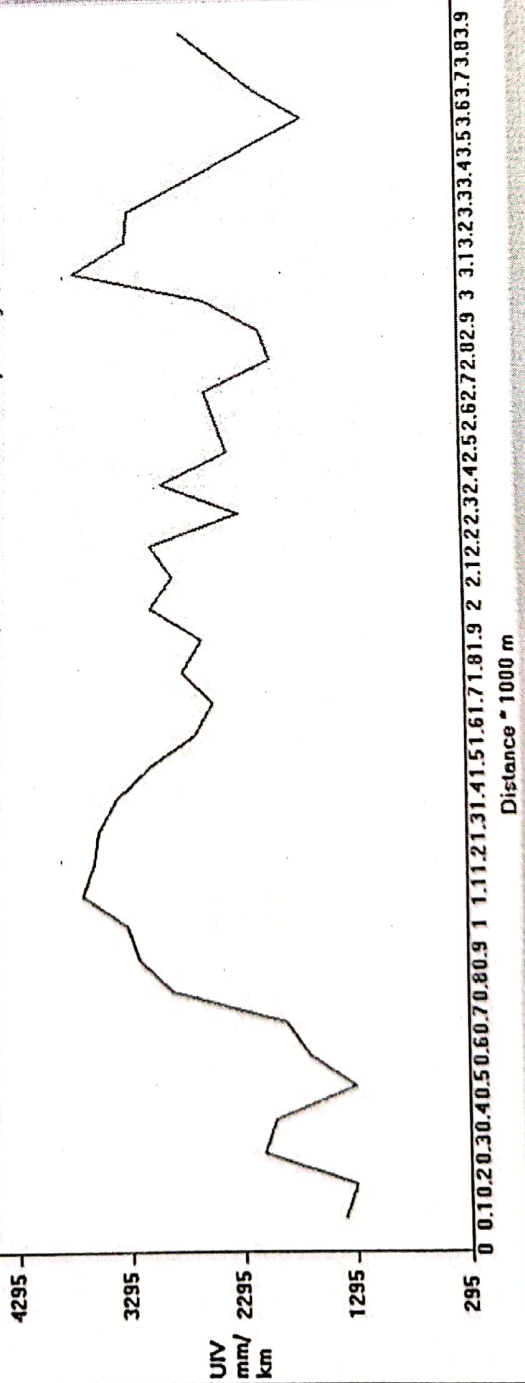

[Signature]

Executive Engineer
Rural Works Department
Works Division, Narkatiyaganj

[Signature] 4.8.22
OR
