

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रगण्डल, धमदाहा,**

पत्रांक- ...1213

/ दिनांक 25/7/22

प्रेषक :- कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रगण्डल धमदाहा।

सेवा में,
अपर मुख्य कार्यपालक भदाउ-राहठ-रासिच,
बिहार परा विकास अभिकरण, पटना।

विषय:- MR(3054) New Maintenance Policy-2018 योजनान्तर्गत अनुरक्षण हेतु राशि की अधियाचना के संबंध में।

प्रसंग:- अभियंता प्रमुख, ग्रामीण कार्य विभाग, बिहार, पटना के पत्रांक-
मु0अ0-4(मु0)3054-04-229/2021 - 1135 (अनु0) / पटना, दिनांक- 09.03.2022

महोदय,

उपरोक्त विषयक प्रासंगिक पत्र में दिये निर्देश के आलोक में नई अनुरक्षण नीति-2018 अन्तर्गत पथों का अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में अंकित कर आवश्यक कार्रवाई हेतु तैयार किया जाता है।

अतः MR(3054) New Maintenance Policy-2018 (Package No. MR-N/19-20 Dhamdaha/-10) योजनान्तर्गत अनुरक्षण हेतु अधियाचना प्रपत्र में दर्शाये गये अधियाचित राशि उपलब्ध कराने की कृपा की जाय। कार्य का निरीक्षण किया गया कार्य संतोषप्रद है। उक्त पथ में ए0टी0आर0 लंबित नहीं है।

अनु0- 1) अधियाचना प्रपत्र।

2) 19 ए प्रपत्र।

3) Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed

4) Standard Formate For Roads Quarterly Statement

विरक्तगणन,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रगण्डल धमदाहा।

25/07/22

STANDARD FORMATE FOR ROADS QUARTERLY STATEMENT (2nd Quarter)

PIU NAME - Rural Works Department Works Division Dhamdaha

Improvement of Road Form Jamalpur Chowk Rangpura to Utna
RM/PU/DHA/19/0010

1	Name Of Road			
2	Batch No.	21105301001		
3	Project ID	4.240		
4	Total Length Of Road(in Km)	4.240		
5	Length Of Road To Meet Required Service Level [Completed Length] (in Km) [1]	20		
6	NO. of Total Quarter (ie 3 Months as a unit) in 5 year	50.42395		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount For Maintenance] (in Lakh)	2.52120		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]			
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment [60]=[3]/[1]*[2]*[4]
		Length Non- Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS AND (CARRIAGEWAY)	0	60%	0
II	SHOULDERS AND EMBANMENTS	0	10%	0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGE	0	15%	0
IV	SIGNAGE AND ROAD SAFETY	0	10%	0
V	VEGETATION	0	5%	0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				2.52120

date of Inpection by E/I Or His Agent
Prepared by Contractor's Self Control Unit

Name and Designation of person inspecting road

date

[Signature]
15/07/22

Signature of person inspecting road

[Signature]
15/07/22
(AE)

[Signature]
25-7-22
(Signature)
Executive Engineer
Rural Works Department
Dhamdaha (Purnea)

Government Of Bihar
 OM01
 Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From: Improvement of Road Form Jamalpur Chowk Rangpura to Uma
 (Package- MR-N/19-20 Dhamdaha/10)

Length of Road : 4.240 Km
 Period :- From:- 14-12-2020 To 13-03-2021
 Inspector :- A.E RWD Sub Division :Dhamdaha

To:-
 Executive Engineer
 RWD, Works Division Dhamdaha
 Position :- A.E

Date:-

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												Comments
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM102	Surface Depression and Rut Patching	m ³	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	© Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	N.A	N.A	N.A	N.A							
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							Not Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							Not Required
OM202	Embankment Repair	m ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Rain Cuts)												
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and Pit Repair	m ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Whirl washing)	m ²	Nil	Nil	Nil	Nil							Not Required

11-07-22
 (J.E)

Executive Engineer
 Rural Works Department
 Dhamdaha (Purwa)

Executive Engineer
 Rural Works Department
 Dhamdaha (Purwa)

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												
OM401	(a) Roadside- General Tidy												
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	No	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road	M ²	Nil	Nil	Nil	Nil							Not Required
OM501	Signs Maintenance												Not Required
OM502	Guard Stones	No	Nil	Nil	Nil	N/A	N/A						Not Required
OM503	Distance Stones	Lm	N/A	N/A	N/A	N/A							Not Required
OM504	Road Marking	No	N/A	N/A	N/A	N/A							Not Required
	Other activities	M ²	Nil	Nil	Nil	Nil							Not Required

Bidder

24 24 43

Appendix

Executive Engineer
Rural Works Division, District
Works Division Dhara: 2 (Area)

11-09-22
11-09-22

25/09/2012
075

11

Date Time Section Length Dumps Speed OR IRI CATEGORY Latitude Longitude Event
 No. Inkm Inmm Rate mm/km mm/km ROAD
 Road Name: Improvement of Road from Jamulpur Chowk Rangpura to Utra, Contractor Name: Parasnathi Construction P/rop
 Y=0° X=7° 06'3" X=73° 22'

23/7/22	14:26:0	42	0.1	150	0	1500	1536 G	25 75695	87 27708	Normal	X = 2111
23/7/22	14:26:26	42	0.1	160	20.2	1600	1797 G	25 75703	87 27806	Normal	Y = 2067
23/7/22	14:26:56	42	0.1	220	30.3	2200	2144 G	25 75697	87 27907	Normal	
23/7/22	14:27:1	42	0.1	250	20.2	2500	2492 G	25 75697	87 28079	Normal	
23/7/22	14:27:1	42	0.1	240	30.3	2400	2918 G	25 75707	87 28118	Normal	(M) RURAL ROAD
23/7/22	14:27:35	42	0.1	220	20.2	2200	2144 G	25 75679	87 28274	Normal	Good Average Poor
23/7/22	14:27:36	42	0.1	150	20.2	1500	1536 G	25 75655	87 28356	Normal	4000 4001-5000 >5001
23/7/22	14:28:0	42	0.1	160	30.3	1600	1621 G	25 75642	87 28458	Normal	
23/7/22	14:28:12	42	0.1	190	20.2	1900	1683 G	25 75612	87 28544	Normal	
23/7/22	14:28:47	42	0.1	290	30.1	2900	2752 G	25 75583	87 28636	Normal	
23/7/22	14:29:0	42	0.1	240	20.2	2400	2318 G	25 75591	87 28734	Normal	
23/7/22	14:29:0	42	0.1	250	20.2	2500	2405 G	25 75631	87 28828	Normal	
23/7/22	14:29:22	42	0.1	220	20.2	2200	2144 G	25 75648	87 28918	Normal	
23/7/22	14:29:22	42	0.1	220	30.3	2200	2144 G	25 757	87 29013	Normal	
23/7/22	14:29:22	42	0.1	220	20.2	2200	2144 G	25 75643	87 29113	Normal	
23/7/22	14:29:22	42	0.1	200	20.2	2000	1970 G	25 75721	87 29216	Normal	
23/7/22	14:30:0	42	0.1	270	20.2	2700	2579 G	25 7561	87 29312	Normal	
23/7/22	14:30:0	42	0.1	160	20.2	1600	1623 G	25 75647	87 29334	Normal	
23/7/22	14:30:32	42	0.1	210	30.3	2100	2057 G	25 75696	87 29333	Normal	
23/7/22	14:30:33	42	0.1	230	30.1	2300	2231 G	25 75955	87 29384	Normal	
23/7/22	14:31:43	42	0.1	190	30.1	1900	1831 G	25 76009	87 29457	Normal	
23/7/22	14:32:0	42	0.1	230	20.2	2300	2231 G	25 75987	87 29751	Normal	
23/7/22	14:32:19	42	0.1	160	30.3	1600	1623 G	25 75995	87 29847	Normal	
23/7/22	14:32:19	42	0.1	330	30.3	3300	3100 G	25 76015	87 29941	Normal	
23/7/22	14:32:19	42	0.1	240	30.3	2400	2318 G	25 76077	87 30005	Normal	
23/7/22	14:32:54	42	0.1	190	30.3	1900	1683 G	25 7612	87 30082	Normal	
23/7/22	14:33:0	42	0.1	220	30.3	2200	2144 G	25 76129	87 30178	Normal	
23/7/22	14:33:0	42	0.1	200	30.3	2000	1970 G	25 76173	87 30268	Normal	
23/7/22	14:33:29	42	0.1	280	30.3	2800	2666 G	25 76198	87 30335	Normal	
23/7/22	14:33:29	42	0.1	90	30.3	900	1015 G	25 76222	87 30451	Normal	
23/7/22	14:33:29	42	0.1	160	30.3	1600	1623 G	25 76242	87 30542	Normal	
23/7/22	14:33:29	42	0.1	140	30.3	1400	1449 G	25 76244	87 30643	Normal	
23/7/22	14:33:4	42	0.1	80	30.3	800	928 G	25 76262	87 30732	Normal	
23/7/22	14:33:4	42	0.1	60	30.3	600	754 G	25 76293	87 30823	Normal	
23/7/22	14:33:39	42	0.1	100	30.3	1000	1101 G	25 76299	87 30924	Normal	
23/7/22	14:34:39	42	0.1	110	30.3	1100	1108 G	25 76301	87 3102	Normal	
23/7/22	14:35:0	42	0.1	160	20.2	1600	1623 G	25 76266	87 31095	Normal	
23/7/22	14:35:14	42	0.1	120	20.2	1200	1275 G	25 76194	87 31138	Normal	

24/07/2022

Executive Engineer
 Rural Works Department
 Purnea Division, Bihar

23/7/22 14:35:14
 23/7/22 14:35:14
 23/7/22 14:35:00
 23/7/22 14:35:00
 23/7/22 14:35:25
 23/7/22 14:37:00
 23/7/22 14:37:00
 23/7/22 14:37:00
 23/7/22 14:37:35
 23/7/22 14:38:00
 23/7/22 14:38:10
 23/7/22 14:38:10

42
 42
 42
 42
 42
 42
 42
 42
 42
 42
 42

0.1
 0.1
 0.1
 0.1
 0.1
 0.1
 0.1
 0.1
 0.1
 0.1
 0.1
 0.1

330
 240
 190
 220
 200
 260
 130
 170
 160
 100
 220
 160

30.3
 30.3
 30.3
 30.3
 30.3
 30.3
 30.3
 20.2
 20.2
 20.2
 20.2
 20.2

3300
 2400
 1900
 2200
 2000
 2600
 1300
 1700
 1600
 1000
 2200
 1600

3100 G
 2318 G
 1883 G
 2144 G
 1970 G
 2645 G
 1362 G
 1710 G
 1623 G
 1101 G
 2144 G
 1623 G

Total
 96258
 1623 G

Average 1925.16


25.7613 47.31715 Normal
 25.7611 47.31795 Normal
 25.76091 47.31895 Normal
 25.76097 47.31403 Normal
 25.7601 47.31554 Normal
 25.75997 47.31548 Normal
 25.75989 47.31739 Normal
 25.76005 47.31835 Normal
 25.76014 47.31921 Normal
 25.76086 47.32001 Normal
 25.76144 47.32082 Normal
 25.76194 47.32163 Normal

25/04/22

Executive Engineer
 Rural Works Department
 Works Division Dnandaha (Pune)
25.07.22

File :\\12020931.Xls. Section No. 17, Egn test

Name of Customer : PARASNATH CONSTRUCTION, Name of Work/ Road : JAMALPUR CHOWK RANGPURA TO

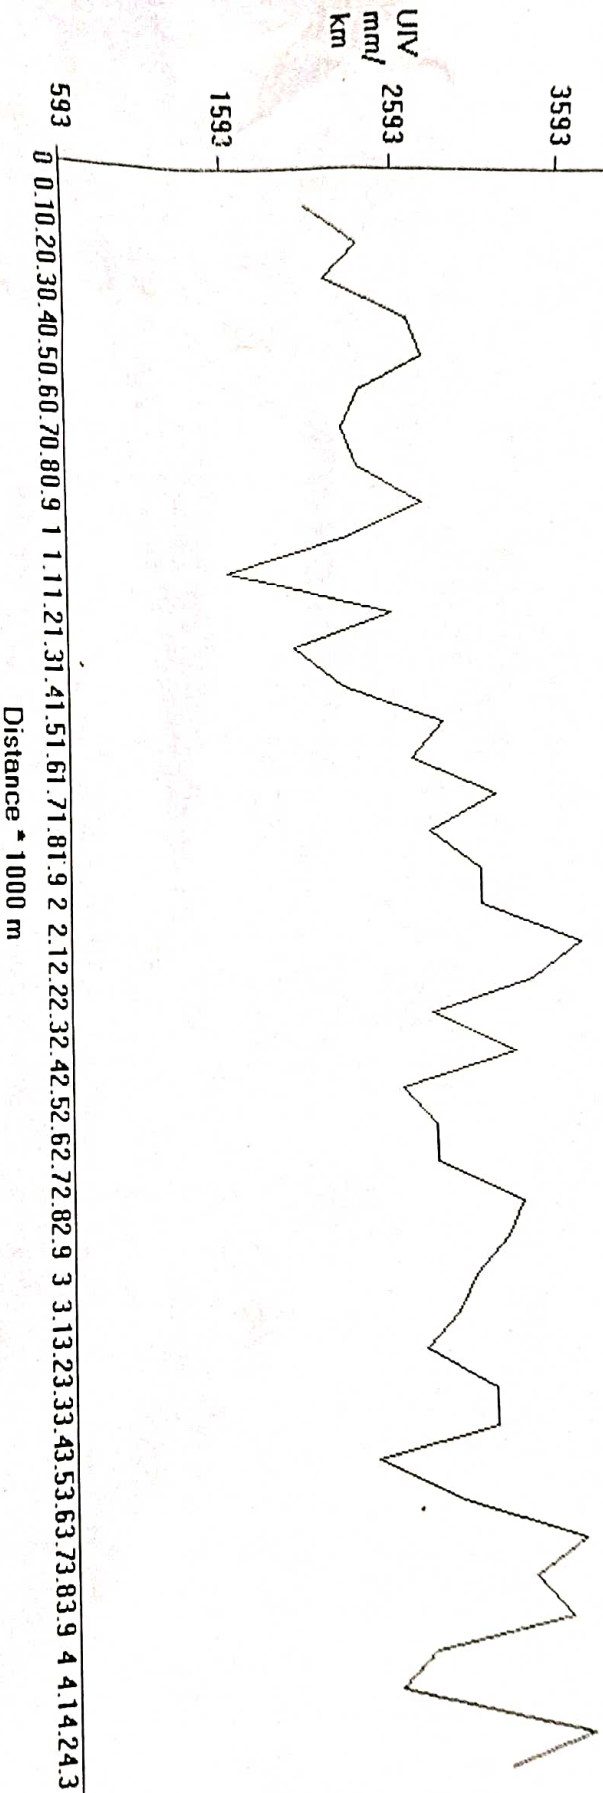

11-07-22
C.B.

27/07/2022

28-7-22

Executive Engineer

Rural Works Department

Works Division Dharmdaha (Pune)
