

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Mobile No- 8986915814

Email ID- eerwdwd2bettiah@gmail.com

पत्रांक- 1498अड6 नरकटियागंज, दिनांक- 05-8-2022

प्रेषक,

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
—सह— सचिव नोडल पदाधिकारी,
ग्रामीण कार्य विभाग,
बिहार पटना।

विषय:- MR-3054 (New Maint. Policy-2018) योजना अन्तर्गत 5 (पाँच) वर्षीय अनुरक्षण का आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि MR-3054 (New Maint. Policy-2018) योजना अन्तर्गत 5 (पाँच) वर्षीय अनुरक्षण का आवंटन उपलब्ध कराने के लिए सूची बनाकर इस पत्र में संलग्न कर अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अनु0:- 1. उपयोगिता प्रमाण-पत्र From GFR 19A

2. अधियाचना पत्र।

विश्वासभाजन,

कार्यपालक अभियन्ता,
ग्रा0का0वि0, का0प्र0, नरकटियागंज।

05/08/22

FORM GFR 19-A
(See Government of India's decision (I) below rule- 150)
Form of Utilization certificate up to the month of Aug-2022
PIU:- E.E RWD(W)DIV-NARKATIAGANJ

SL.NO.	Name of Schemes	Sanction No.& Date with Amount (In Lacs)	Amount received (In Lacs)	Particulars
1	2	3	4	5
1	Maintenance Fund of MR(3054) New Maintenance Policy- 2018		NIL	Certified that out of Rs. 0.00 Lacs of grants-in-aid sanctioned during the years 2022-23 in favour of Executive Engineer R. W. D. Works Division, Narkatiaganj a sum of Rs. 0.00 Lacs has been utilized for the purpose of Maintenance Fund of MR(3054) New Maintenance Policy-2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs. NIL Lac remaining unutilized at the end of the period under report.
		TOTAL	NIL	

2. Certified that I have satisfied myself that the conditions on which the grant-in-aid was sanctioned have been duly fulfilled, are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.


SR.DIV ACCOUNTS OFFICER
R.W.D. Works Division, Narkatiaganj

Kinds of checks exercised:-

- Works has been supervised by Executive Engineer / Superintending Engineer.
- Periodic as inspection has been conducted by Executive Engineer / Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer / Executive Engineer.
- All other codal formalities have been observed.

3. Physical Progress achieved:-

- Construction of Road Works.
- Construction of CD Works.


Executive Engineer
R.W.D. Works Division, Narkatiaganj

Requisition Form for Scheme Head - 5 Year Maintenance of MRC(054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Rectification and surface Renewal)

Name of Division :- Narkatiaganj

Name of Circle :- Bettiah

Sl. No	Package No.	Name of Road	Project ID as per MIS	Administrative Sanction Letter No & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Current Maintenance Demand (in Lacs)				Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)				1st Qtr Maint Demand	2nd Qtr Maint Demand	3rd Qtr Maint Demand	4th Qtr Maint Demand	
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
1	RM/WE/NAR/19/0020	Singhasini MARGSY Road to Jhumla Road	31808801017	3628 27.08.2019	2.3	91.821	64.96	19.82435	80/2020-21 07.03.2020	16.03.2021	03.01.2021	0.99122	0.99122	0.99122	0.00000	
2	RM/WE/NAR/19/0020	BASHITA - SANTPUR PARSA	31808902016	3628 27.08.2019	2.185	84.604	58.635	19.22295	80/2020-21 07.03.2020	16.03.2021	03.01.2021	0.96115	0.96115	0.96115	0.00000	
3	RM/WE/NAR/19/0001	Maintar to Pakubhawa	NEA20002765	539 08.02.2019	3.53	145.982	99.908	35.86275	29/2019-20 18.10.2019	17.10.2021	03.01.2021	1.79314	1.79314	1.79314	0.00000	
4	RM/WE/NAR/19/0001	Triveni Main Canal se Baudharwa	NEA20002766	539 08.02.2019	2.85	115.075	75.568	28.8359	29/2019-20 18.10.2019	17.10.2021	28.03.2021	1.44180	1.44180	0.00000	0.00000	

Executive Engineer
Rural Works Department
Works Division Narkatiaganj

05/08/2022

2nd Quarter

RWD, Works Division, Narkatiaganj

Government Of Bihar

OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:-Triveni Main Canal se Baudhbarwa				To:-		Executive Engineer RWD, Works Division Narkatiaganj		Date:-					
Length of Road : 2.850KM				Inspector :- A.E. RWD WORKS SUB DIVISION, Mainatanr		Position :- A.E.							
No	standard Of Work Item Name	Work Unit	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed paymnet												
OM101	Pothole Patching	m ²	NIL	NIL	NIL								No pothole found
OM102	Surface Depression and Rut patching	m3	NIL	NIL	NIL								No Surface Depression and Rut patching found
OM103	Crack Sealing	Lm	NIL	NIL	NIL								No crack
OM103	Surface Treatment		NIL	NIL	NIL								Not required
OM104	(a) Loss of Aggregate (SurfaceRavelling)	m ²	NIL	NIL	NIL								No Loss of Agreegate (Surface ravelling) found
OM104	(b) Bleeding / Flushing	m ²	NIL	NIL	NIL								No bleeding / furnishing found
OM104	© Crocodile Cracking	m ²	NIL	NIL	NIL								No Crocodile cracking found
OM105	Edge Repair	m ²	N.A.	N.A.	N.A.								Notified & repaired
OM106	Digouts	m ²	N.A.	N.A.	N.A.								
OM107	Concrete pavement	m ³	N.A.	N.A.	N.A.								
OM107	Other activities												
OM200	Shoulder												
OM200	Unsealed Shoulder												No Edge Drop off found
OM201	(a) Edge Drop-off	Lm	NIL	NIL	NIL								No Roughness, Scouring or Potholes found
OM201	(b) Roughness, Scouring or Potholes	Lm	NIL	NIL	NIL								No Holding Water Found
OM201	(c) Holding water	Lm	NIL	NIL	NIL								Notified & repaired
OM202	Embankment Repair	M ³	NIL	NIL	NIL								
OM202	Other activities (Rain Cuts)		N.A.	N.A.	N.A.								
OM300	Drainage including culverts major												NA
OM301	Surface Drains & Verge	Lm	N.A.	N.A.	N.A.								DONE
OM302	Culvert Cleaning	No	NIL	NIL	NIL								DONE
OM303	Culvert and pit Repair	M ³	NIL	NIL	NIL								Not required
OM303	Other activities(Whilw washing)	M ²	NIL	NIL	NIL								

Contractor

J.E.

A.E.

E.E.

No	standard Of Work Item Name	Work Unit	Unit OF Required in each Kilometere										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												
OM401	(a) Roadside- General Tidy	Ha	NIL	NIL	NIL								Done
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	NIL	NIL	NIL								Done
OM402	Tree and Shrub Management	No	NIL	NIL	NIL								Done
	Cutting Of Branches Of Trees	No	NIL	NIL	NIL								Done
	Cutting Of Shrubs From Road Way	No	NIL	NIL	NIL								Done
	Other activities (Trimming of Grass)	M ²	NIL	NIL	NIL								Not Required
	Safety Signage and Road	No	NIL	NIL	NIL								Not Required
OM500	Signs Maintenance	Lm	NA	NA	NA								N.A.
OM501	Guard Stones	No	NA	NA	NA								N.A.
OM502	Distance Stones	No	NA	NA	NA								Not Required
OM503	Road Marking	M ²	NIL	NIL	NIL								Not Required
OM504	Other activities												

05/08/22
A.E

05/08/22
J.E

Contractor

Executive Engineer
Rural works Department
Works Division, Narkatiaganj

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :- RWD, Works Division, Narkatiaganj

2nd Quarter

1	Name of the Road	Triveni Main Canal se Baudhbarwa		
2	Batch No.	RM/WE/NAR/19/0001		
3	Project ID	NEA20002766		
4	Total Lenth of Road (in KM)	2.850		
5	Length of Road to Meet Required Service Level [Completed length](in Km) [1]	2.850		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	28.8359		
8	Quarterly Payment : 4/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.4417950		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00
II	SHOULDERS AND EMBANMENTS	0	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00
V	VEGATION	0	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (IN Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.4417950


Date of inspection by E/I or his agent
Prepare by Contractor's self Control unit

Name and Designation of person inspecting road


Date


Signature of person inspecting road


05/08/22

(Signature)

Certify by E/I [Signature] Date:-
Executive Engineer
Rural Works Department
Works Division, Narkatiaganj

Name of Road - Triveni Main Canal se Baudhbarwa (Sec-68)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
25/4/22	15:4:2	68	0.1	280	21.5	2800	2830	G	27.133815	84.628988	Normal
25/4/22	15:4:2	68	0.1	290	26.4	2900	2867	G	27.132938	84.62867	Normal
25/4/22	15:4:37	68	0.1	310	26.4	3100	3099	G	27.132127	84.62838	Normal
25/4/22	15:4:37	68	0.1	290	26.4	2900	2920	G	27.131277	84.628248	Curve
25/4/22	15:4:37	68	0.1	360	30.3	3600	3638	G	27.13043	84.628635	Normal
25/4/22	15:5:12	68	0.1	300	20.2	3000	3010	G	27.130212	84.62803	Normal
25/4/22	15:5:12	68	0.1	300	30.3	3000	2951	G	27.13039	84.627037	Normal
25/4/22	15:5:12	68	0.1	340	10.1	3400	3368	G	27.130537	84.626093	Normal
25/4/22	15:6:0	68	0.1	320	20.2	3200	3189	G	27.130425	84.625185	Curve
25/4/22	15:6:0	68	0.1	330	20.2	3300	3289	G	27.129645	84.624713	Normal
25/4/22	15:6:23	68	0.1	330	20.2	3300	3279	G	27.129115	84.623988	Normal
25/4/22	15:6:23	68	0.1	310	20.2	3100	3099	G	27.128513	84.623315	Normal
25/4/22	15:7:0	68	0.1	350	20.2	3500	3458	G	27.127742	84.622978	Normal
25/4/22	15:7:0	68	0.1	330	20.2	3300	3279	G	27.126962	84.622777	Normal
25/4/22	15:7:33	68	0.1	320	10.1	3200	3189	G	27.126902	84.622037	Normal
25/4/22	15:8:0	68	0.1	340	10.1	3400	3368	G	27.127345	84.621212	Normal
25/4/22	15:8:9	68	0.1	310	20.2	3100	3120	G	27.12741	84.620387	Normal
25/4/22	15:8:9	68	0.1	290	20.2	2900	2920	G	27.126712	84.62002	Normal
25/4/22	15:8:44	68	0.1	310	20.2	3100	3051	G	27.125845	84.619865	Normal
25/4/22	15:9:0	68	0.1	290	10.1	2900	2891	G	27.125103	84.619578	Normal
25/4/22	15:9:19	68	0.1	300	20.2	3000	3010	G	27.124302	84.619225	Curve
25/4/22	15:9:19	68	0.1	340	20.2	3400	3368	G	27.123685	84.618568	Normal
25/4/22	15:9:19	68	0.1	330	30.3	3300	3279	G	27.122835	84.618535	Normal
25/4/22	15:10:0	68	0.1	320	30.3	3200	3189	G	27.121972	84.618502	Normal
25/4/22	15:10:0	68	0.1	290	20.2	2900	2920	G	27.121285	84.619157	Normal
25/4/22	15:10:30	68	0.1	300	20.2	3000	3010	G	27.120675	84.619848	Normal
25/4/22	15:10:30	68	0.1	320	20.2	3200	3189	G	27.119822	84.619763	Normal
25/4/22	15:11:5	68	0.1	340	10.1	3400	3368	G	27.119002	84.619948	Normal
25/4/22	15:11:5	68	0.05	290	10.1	2900	2920	G	27.11812	84.619898	Normal
Average IRI Value=							3140				

Executive Engineer
Rural Works Department
Works Division, Marikayaganj

Analyzer


Name of Customer : KHURSHID ALAM
 Name of Work/Road : Triveni Main Canal se Baudhbarwa
 Lab Job number :
 Date : 25-Apr-22
 Section No. : 18

Test Date : 25-Apr-22
 Machine No : 402
 Start S No :
 Start E No :
 Weather :
 Start Location :
 End Location :
 Road Name : Triveni Main Canal se Baudhbarwa
 Road Type : (R) RURAL ROAD
 Side :
 Interval :
 UV Range : 1830 To 5000 mm/km
 Dist Range : 0 To 3
 Equation : $Y = 0 \cdot X^2 + 1.021 \cdot X - 31.77$

Print Generate Report and Graph

Redraw Graph

Map View

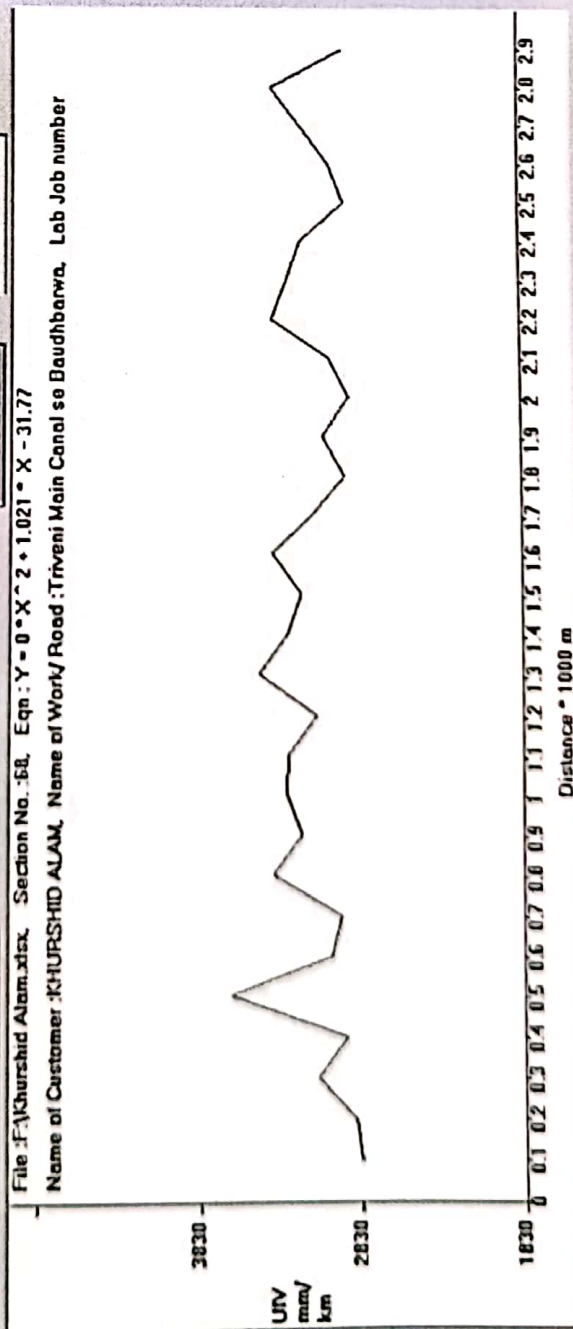

[Signature]
 Executive Engineer
 Rural Works Department
 Works Division, Nartatyaganj
 05/06/22
