

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, महुआ।

पत्रांक.....1734 /

महुआ/दिनांक.....18 / 08 / 2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, महुआ।

सेवा में,


नोडल पदाधिकारी,
एम0आर0 3054 नई अनुरक्षण नीति 2018,
विश्वेश्वरैया भवन,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय : शीर्ष एम0आर0 3054 नई अनुरक्षण नीति 2018 अन्तर्गत पथ में कराये गए कार्य के विरुद्ध अधियाचना भेजने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष एम0आर0 3054 नई अनुरक्षण नीति 2018 अन्तर्गत पथ में कराये गए कार्य के विरुद्ध अधियाचना इस पत्र के साथ समर्पित की जा रही है।


विश्वासभाजन,



18-08-22

कार्यपालक अभियंता

ग्रामीण कार्य विभाग, कार्य प्रमंडल,
महुआ।



Requisition Formate for Scheme Head- MR-3054 Under Bihar Rural Road Maintenance Policy 2018 (In Rectification and Surface Renewal)

Division Name:- Rural Works Department, Works Division, Mahua

S.No	Package No	Name of Road	Project ID as per MIS	Administ ative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lacs)		Agreement No & Date		Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (In Km)	Thickness of Bitumen Layer (In mm)	Value of Bitumen Content in %	Previous Total Alloted Amount (In Lacs)	Upto date Expenditure as per MIS (In Lacs)	Requisition against Work Done (In Lacs)	Remarks
1	MR-N/19-20 Mahua/23	Mustafapur Chowk to PMGSY Road via raj kumar baida house(Chehrakata)	31507601013	3610/26.08.2019	2.150	59.928	34.07100	14.96967	04/MBD/MR/2020-21	10.05.2021			1999	25.00	5.00	0	0	31.54379	Work Completed
2		BHOREHA - KAILA KALAYAN	31507502048		4.300	136.472	75.59000	39.08352					3041	25.00	5.00	0	0	75.58320	Work Completed
3		CHEHRA KALA - KAMALPUR	31507502057		3.700	96.590	56.71100	27.80813					1930	25.00	5.00	0	0	56.70387	Work Completed
4		Construction of road from Vashali Jila antargat chehrakata prakhand me geam sehan tola mohammadpur se Munial thakur ke ghur ke nikal se sehan Babahapur mein road ke pass Lakshman paswan ke ghar tak PCC nirman karya	31507603070		1.340	35.738	18.23800	11.9993					2212	25.00	5.00	0	0	18.23705	Work Completed
																		182.06791	

[Signature]
Executive Engineer
R.W.D. Works Division, Mahua
18-08-22
18.08.22

[Signature]
18.08.22

Form GFR 19-A

(See Government of India's Decision (1) below Rule-150)

Form of Utilisation Certificate upto the month- 17.08.2022

STATE- BIHAR

SL. No	Name of Scheme	Sanction No. & Date With Amount (In Rs. Lacs)	Amount Received (In Rs.Lacs)	Particulars
1	Construction of Rural Roads under MR New Maintenance Policy 2018	Lt-22 Dated-08-08-2022 Amount- 81.96533	5598.06236	Certified that out of Rs. 5598.06236 Lacs of grants-in-aid sanctioned upto 12/2017 in favour of E-in-C, REO Bihar, Patna a sum of Rs.5496.89816 lacs has been utilized for the purpose of MR New Maintenance Policy 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs- 1.16420 lacs remaining unutilized at the end of the period under.
	Total:		5598.06236	


2 Certified that I have satisfied myself that the conditions on which the gram-in-aid was sanctioned have


Kind of Checks exercised:-

- Works has been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the
- All other codal formalities have been observed.

3 **Physical Progress achived:-**

- Construction of Road Works.
- Construction of CD Works.


Divisional Account Officer
RWD. Works Division, Mahua



18-08-22
Executive Engineer
RWD. Works Division, Mahua
RWD 18/8/22

प्रमाण-पत्र


पथ का नाम — BHORHA - KAILA KALAYAN
योजना — एम0आर0 (3054) नई अनुरक्षण नीति 2018
कार्य प्रमंडल — महुआ।
प्रखंड — चेहराकला।

उक्त पथ में कराये गये सभी अवयवों के अवयववार कार्य निम्नलिखित पदाधिकारी द्वारा मापी पुस्तिका से सत्यापन किया गया।


क्र0	पदनाम	कराये गये कार्य के मापी पुस्तिका से सत्यापन की प्रतिशत	अभ्युक्ति
1	कनीय अभियंता	100 प्रतिशत	
2	सहायक अभियंता	50 प्रतिशत	
3	कार्यपालक अभियंता	10 प्रतिशत	


20/07/22

कनीय अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रशाखा-चेहराकला।


20/07/22

सहायक अभियंता,
ग्रामीण कार्य विभाग,
कार्य अवर प्रमंडल, चेहराकला।


20.07.22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, महुआ।

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
	First and Final Bill				
	N/W:- Bhosha to Kailu, Malayon				
	Agency:- Rom Nareesh Singh				
	Agreement No:- 04/MBD/2020-21				
	Date of Start:- 11/05/2020				
	Date of Completion:- 10/05/2021				
	Pokaye No :- 23				
	Actual Date of Completion:- 20/07/2022				

Abstract of Cost

1. Clearing and Grubbing road land...

Vide T.M.B. P.N. (1) item (1)

Qty- 0.850 Hect.

② Rs 49496.70/Hect.

= Rs 42567.16

2. Construction of Sub-grade and Formation Shoulder...

Vide T.M.B. P.N. (2) item (1/2)

Qty- 1806.00 m³

③ Rs 176.75/m³

= Rs 319210.50

Sch. XLV-Form No. 134

Particulars	Details of actual measurement			Contents of area
	No.	L.	B.	
20. 600 mm Circular				
Vide T.M.B. P.N. (17) item (6)				
Qty = 4 Nos.				
Rs 3699.37/Each				
= Rs 14,797.96				
21. 600 mm x 450 mm Rectangular				
Vide T.M.B. P.N. (17) item (7)				
Qty = 7 Nos.				
Rs 3570.37/Each				
= Rs 24,992.59				
22. Plantation of Tree and their Maintenance for				
One Year				
Vide T.M.B. P.N. (17) item (1)				
Qty = 215 Nos				
Rs 800.30/Each = Rs 1,72,064.50				
Total = Rs 74,31,975.93				
Add 12% GST Rs 8,91,837.11				
Add 1% L.C. = Rs 74,319.76				
Total = Rs 83,98,132.80				
Less 10% Below RA = Rs 8,39,813.28				
Total = Rs 75,58,319.52				
Say Rs 75,58,320.00				
20/07/2022 J.E.				
20-07-22				
20/07/22				

Name of the work: Borba to Kayla Kalyan

Date	Time	Test No	Distance(meter)	Total Distance (metre)	EUM(cm)	Speed(km/ Hr)	Ull(mm/Km)	Corrected Ull(mm/K m)	IRI	Status	Latitude	Direction	Longitude	Direction	Remarks
03-07-2022	10:03:20	4	0	0	0.0 cm	2.0 Km/Hr	0.0 mm/Km	125	0.236	Good	25.8942347 N		85.4346552 E		Normal
03-07-2022	10:19:32	4	100	100	20.0 cm	13.2 Km/Hr	2000.0 mm/Km	1943	2.734	Good	25.8960505 N		85.436283 E		Normal
03-07-2022	10:19:50	4	100	200	22.0 cm	19.8 Km/Hr	2200.0 mm/Km	2124.8	2.961	Good	25.8960505 N		85.436283 E		Normal
03-07-2022	10:20:11	4	100	300	22.0 cm	18.0 Km/Hr	2200.0 mm/Km	2124.8	2.961	Good	25.8676119 N		85.4316274 E		Normal
03-07-2022	10:20:40	4	100	400	27.0 cm	12.4 Km/Hr	2700.0 mm/Km	2579.3	3.52	Good	25.8673354 N		85.4328328 E		Normal
03-07-2022	10:21:11	4	100	500	34.0 cm	11.5 Km/Hr	3400.0 mm/Km	3215.6	4.286	Good	25.8662013 N		85.4337244 E		Normal
03-07-2022	10:21:39	4	100	600	29.0 cm	12.7 Km/Hr	2900.0 mm/Km	2761.1	3.741	Good	25.8662081 N		85.4344415 E		Normal
03-07-2022	10:22:06	4	100	700	18.0 cm	13.5 Km/Hr	1800.0 mm/Km	1761.2	2.504	Good	25.8653246 N		85.434701 E		Normal
03-07-2022	10:22:31	4	100	800	23.0 cm	14.4 Km/Hr	2300.0 mm/Km	2215.7	3.074	Good	25.8645754 N		85.4352732 E		Normal
03-07-2022	10:23:01	4	100	900	15.0 cm	11.7 Km/Hr	1500.0 mm/Km	1488.5	2.155	Good	25.8645754 N		85.4357767 E		Normal
03-07-2022	10:23:24	4	100	1000	21.0 cm	15.7 Km/Hr	2100.0 mm/Km	2033.9	2.847	Good	25.8655901 N		85.435647 E		Normal
03-07-2022	10:23:45	4	100	1100	26.0 cm	17.1 Km/Hr	2600.0 mm/Km	2488.4	3.409	Good	25.8665457 N		85.435647 E		Normal
03-07-2022	10:24:07	4	100	1200	27.0 cm	16.3 Km/Hr	2700.0 mm/Km	2579.3	3.52	Good	25.8674441 N		85.4353342 E		Normal
03-07-2022	10:24:26	4	100	1300	25.0 cm	16.6 Km/Hr	2500.0 mm/Km	2397.5	3.298	Good	25.8683196 N		85.4352579 E		Normal
03-07-2022	10:24:50	4	100	1400	32.0 cm	17.0 Km/Hr	3200.0 mm/Km	3033.8	4.069	Good	25.8691245 N		85.4350595 E		Normal
03-07-2022	10:25:10	4	100	1500	24.0 cm	17.2 Km/Hr	2400.0 mm/Km	2306.6	3.186	Good	25.8701106 N		85.4345026 E		Normal
03-07-2022	10:25:33	4	100	1600	34.0 cm	16.0 Km/Hr	3400.0 mm/Km	3215.6	4.286	Good	25.8707858 N		85.4342966 E		Normal
03-07-2022	10:26:15	4	100	1700	27.0 cm	17.6 Km/Hr	2700.0 mm/Km	2579.3	3.52	Good	25.872613 N		85.4341974 E		Normal
03-07-2022	10:26:36	4	100	1800	34.0 cm	16.5 Km/Hr	3400.0 mm/Km	3215.6	4.286	Good	25.8734255 N		85.4342813 E		Normal
03-07-2022	10:26:57	4	100	1900	12.0 cm	17.0 Km/Hr	1200.0 mm/Km	1215.8	1.799	Good	25.8745127 N		85.4344568 E		Normal
03-07-2022	10:27:24	4	100	2000	23.0 cm	13.5 Km/Hr	2300.0 mm/Km	2215.7	3.074	Good	25.8753844 N		85.4341974 E		Normal
03-07-2022	10:27:46	4	100	2100	23.0 cm	16.7 Km/Hr	2200.0 mm/Km	2124.8	2.961	Good	25.8756609 N		85.4337244 E		Normal
03-07-2022	10:28:06	4	100	2200	22.0 cm	17.5 Km/Hr	1100.0 mm/Km	1124.9	1.678	Good	25.8765059 N		85.4332209 E		Normal
03-07-2022	10:28:27	4	100	2300	11.0 cm	17.4 Km/Hr	2200.0 mm/Km	2124.8	2.961	Good	25.8777762 N		85.4329081 E		Normal
03-07-2022	10:33:19	4	100	2400	22.0 cm	1.2 Km/Hr	1100.0 mm/Km	1124.9	1.678	Good	25.8771582 N		85.4330378 E		Normal
03-07-2022	10:33:41	4	100	2500	11.0 cm	16.3 Km/Hr	800.0 mm/Km	852.2	1.31	Good	25.8769217 N		85.4330912 E		Normal
03-07-2022	10:34:02	4	100	2600	8.0 cm	16.8 Km/Hr	2300.0 mm/Km	2215.7	3.074	Good	25.8755675 N		85.4338236 E		Normal
03-07-2022	10:34:30	4	100	2700	23.0 cm	12.6 Km/Hr	2000.0 mm/Km	1943	2.734	Good	25.875062 N		85.4339358 E		Normal
03-07-2022	10:34:54	4	100	2800	20.0 cm	15.1 Km/Hr	1900.0 mm/Km	1852.1	2.619	Good	25.8741427 N		85.4343424 E		Normal
03-07-2022	10:35:15	4	100	2900	17.0 cm	17.2 Km/Hr	1700.0 mm/Km	1670.3	2.388	Good	25.8731204 N		85.4342127 E		Normal
03-07-2022	10:35:35	4	100	3000	26.0 cm	15.9 Km/Hr	2600.0 mm/Km	2488.4	3.409	Good	25.8721114 N		85.4342279 E		Normal
03-07-2022	10:35:58	4	100	3200	26.0 cm		2600.0 mm/Km	2488.4	3.409	Good	25.8712244 N		85.4343958 E		Normal

04/07/22
J.E.

04/07/22
J.E.

04.07.22
J.E.

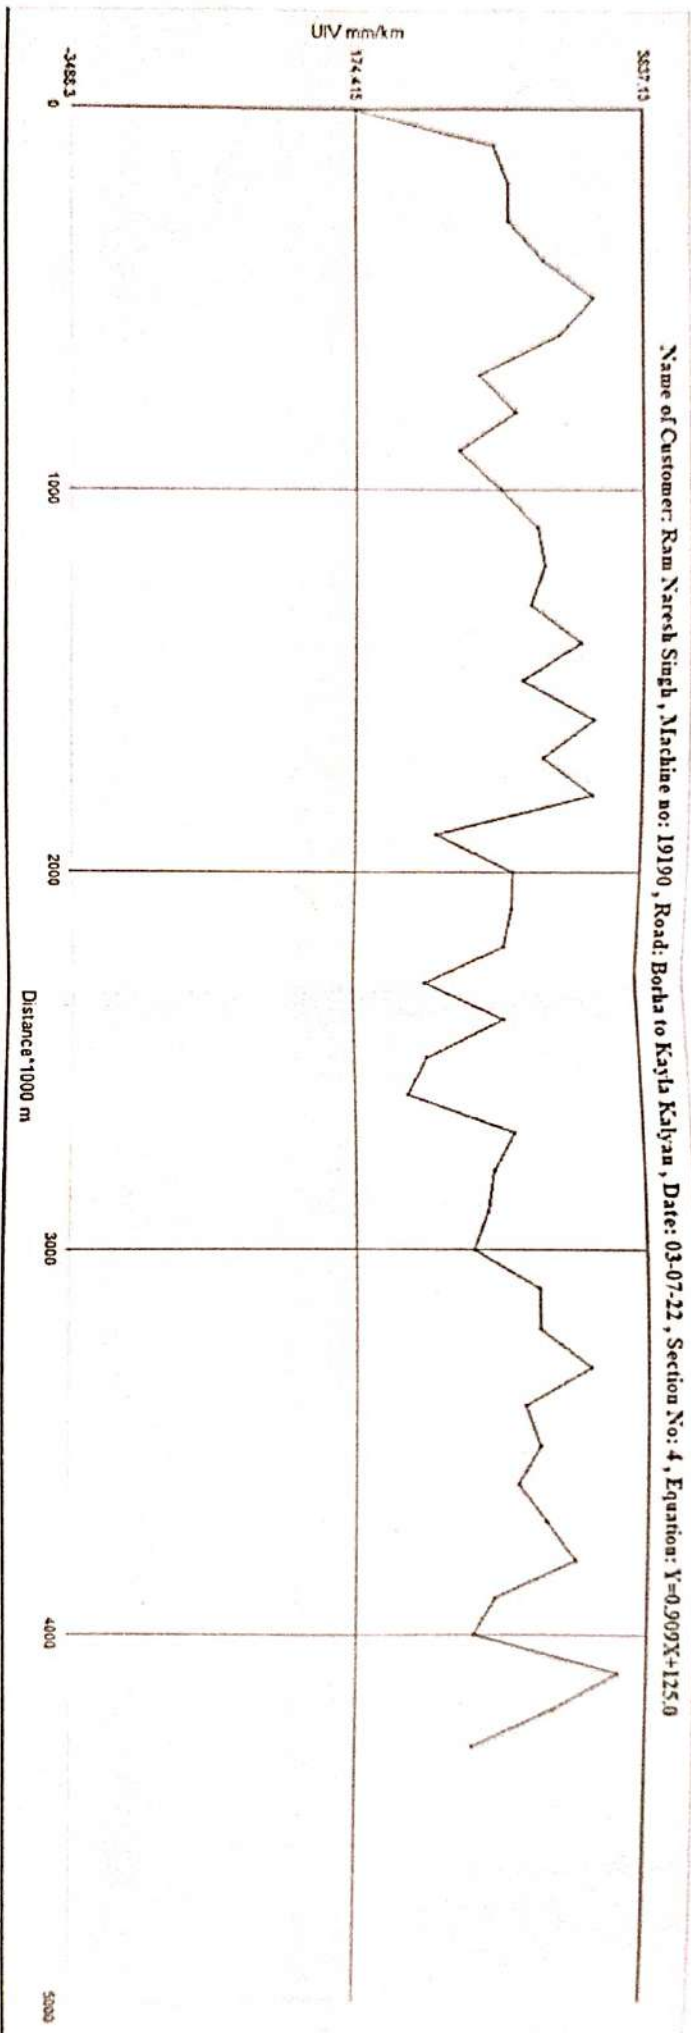
Date	Time	Test No	Distance(meter)	TotalDistance (m)	BUMP/cm	Speed(Km/ Hr)	U1(mm/Km)	Corrected U1(mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction	Remarks
03-07-2022	10:36:21	4	100	3300	33.0 cm	15.7 Km/Hr	3300.0 mm/Km	3124.7	4.178	Good	25.8703261 N		85.4346399 E	1	Normal
03-07-2022	10:36:43	4	100	3400	24.0 cm	16.2 Km/Hr	2400.0 mm/Km	2306.6	3.186	Good	25.8701106 N		85.4347315 E		Normal
03-07-2022	10:37:05	4	100	3500	26.0 cm	16.2 Km/Hr	2600.0 mm/Km	2488.4	3.409	Good	25.8686533 N		85.4351435 E		Normal
03-07-2022	10:37:28	4	100	3600	23.0 cm	15.7 Km/Hr	2300.0 mm/Km	2215.7	3.074	Good	25.8677092 N		85.4352579 E		Normal
03-07-2022	10:37:52	4	100	3700	27.0 cm	15.2 Km/Hr	2700.0 mm/Km	2579.3	3.52	Good	25.8668051 N		85.4354639 E		Normal
03-07-2022	10:38:12	4	100	3800	31.0 cm	17.5 Km/Hr	3100.0 mm/Km	2942.9	3.96	Good	25.866025 N		85.435708 E		Normal
03-07-2022	10:38:34	4	100	3900	20.0 cm	16.9 Km/Hr	2000.0 mm/Km	1943	2.734	Good	25.8651915 N		85.435708 E		Normal
03-07-2022	10:38:57	4	100	4000	17.0 cm	15.7 Km/Hr	1700.0 mm/Km	1670.3	2.388	Good	25.8640547 N		85.435708 E		Normal
03-07-2022	10:41:12	4	100	4100	37.0 cm	2.6 Km/Hr	3700.0 mm/Km	3488.3	4.609	Good	25.8637267 N		85.4361963 E		Normal
03-07-2022	10:41:45	4	100	4200	28.0 cm	10.4 Km/Hr	2800.0 mm/Km	2670.2	3.631	Good	25.8643599 N		85.4355326 E		Normal
03-07-2022	10:43:10	4	100	4300	17.0 cm	4.2 Km/Hr	1700.0 mm/Km	1670.3	2.388	Good	25.8644248 N		85.4354486 E		Normal

IRI Value 3041
Machine ID 19190


04/07/22
J.E.


04/07/22
AE


04-07-22



[Signature]
04/07/22
J.E.

[Signature]
04/07/22
A.E.

[Signature]
04-07-22
