

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

पत्रांक 1727 अ/अ

दिनांक 23/08/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।

विषय: नई अनुरक्षण नीति 2018 अंतर्गत वित्तीय वर्ष 2022-23 में अनुरक्षण मद में व्यय हेतु आवंटन की मांग।

महाशय,

उपर्युक्त विषय के संबंध में नई अनुरक्षण नीति 2018 अंतर्गत वित्तीय वर्ष 2022-23 में अनुरक्षण मद में व्यय हेतु संलग्न विवरणी के अनुसार 13.35861 (तेरह लाख पैंतीस हजार आठ सौ एकसठ) रुपये का आवंटन उपलब्ध कराने की कृपा की जाये ताकि किये गये कार्यों का भुगतान किया जा सके।


अनुलग्नक:- यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

23/08/2022



Name of Works Division:- Muzaffarpur East-1

Road Details				AA Details		Agreement					Actual Maintenance Expenditure										Current Maintenance Demand		Remarks			
Sl. No.	Name of Roads	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh)	Maintenance Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	Length (in KM)	1st. Year Maintenance	2nd. Year Maintenance	3rd. Year Maintenance	4th. Year Maintenance	5th. Year Maintenance	Total Maintenance Expenditure	Length as per Bump Report	IRI As per Bump Report		1st QTR Maintenance	2nd QTR Maintenance	Total
1	Improvement of Chakhalad Community Building to Rly. Crossing Via - Raghunathpur Middle School	RM/MU/MUZ/20/0004	31507201005	04/06/2021	33.92100	17.83000	33.19700	0.94447	1.88774	5.46735	2.41178	6.11455	16.82589	2.100	0.000	0.000	0.000	0.000	0.000	0.000	2.100	2687.00		0.84129	0.84129	1.68259
2	Improvement of Ramjivan Prasad Deputy Mukhia house to Bishanpur (Maa Bhagwati Asthan) Via - Sivan Paswan house Road	RM/MU/MUZ/20/0004	31507201024	20/05/2021	38.10400	19.05800	37.28800	1.00526	2.01460	5.84859	2.57343	6.53968	17.98156	2.250	0.000	0.000	0.000	0.000	0.000	0.000	2.250	2566.000		0.89908	0.89908	1.79816
3	Muzaffarpur jila anatargat pusa road musahri block se gangapur pahladpur sadhari chakhalad railway gunti hote hue N.H 28 tak path.	RM/MU/MUZ/20/0004	31507204011	27/05/2021	116.60000	50.76000	113.52400	2.65156	5.34824	15.59317	6.84871	17.44574	47.88742	6.010	0.000	0.000	0.000	0.000	0.000	0.000	6.010	2623.000		2.39437	2.39437	4.78874

Road Details				AA Details		Agreement										Actual Maintenance Expenditure										Current Maintenance Demand					Remarks
Sl. No.	Name of Roads	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh)	Maintenance Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	Length (in KM)	1st. Year Maintenance	2nd. Year Maintenance	3rd. Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintenance Expenditure	Length as per Bump Report	IRI As per bump Report	1st QTR Maintenance	2nd QTR Maintenance	Total						
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	30	31					
1	Muzaffarpur jila antargat musabiri kalbhut sri ramsakal ojha ke ghar se baranhipur bodhi chaul tak bhaya anusuchit jati mahadalit tola ewn khabra pokhar hote hue path nirman	RM/MU/MUZ/20/0004	31507205003	22/05/2021	41.83600	18.30900	40.90200	0.96803	1.93409	5.61512	2.47126	6.27849	17.26699	2.160	0.000	0.000	0.000	0.000	0.000	0.000	2.160	2642.000	0.86335	0.86335	1.72670						
5	Baikunthpur - Madhopur	RM/MU/MUZ/20/0004	NEA220002 670	18/04/2021	34.77000	16.54300	33.74200	0.87800	1.75190	5.07387	2.23455	5.67051	15.60883	1.950	0.000	0.000	0.000	0.000	0.000	0.000	1.950	2687.000	0.78044	0.78044	1.56088						
6	Manika Harkishna - Bindra patha	RM/MU/MUZ/20/0002	NEA220000 2676	12/06/2021	59.59000	26.14000	37.61800	1.09725	1.94316	5.62608	2.80628	6.54263	18.01540	3.050	0.000	0.000	0.000	0.000	0.000	0.000	3.050	2366.000	0.90077	0.90077	1.80154						
Total																									13.35861						

10000
2008.12
2008.12


22/18/22
A.C

22/18/22
Executive Engineer
R.W.D. Works Division
Muzaffarpur East-1

Name of Road - Pusa Road Mushari Block se Gangapur Pahladpur Sagahri Chakahlad railway Gumti Hote Hue NH-28 Tak										Latitude Longitude		Event	
Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI CATEGORY						
						UIV	ROAD						
14/ 8/ 22	13: 40: 20	9	0.1	300	0	3000	2953 G	3.97	26.58553	85.43247	Normal	$Y = 0 * X^2 + 0.989 * X - 13.58$	
14/ 8/ 22	13: 41: 0	9	0.1	200	10.1	2000	1964 G	2.76	26.58202	85.43322	Normal	$X = 1800$	
14/ 8/ 22	13: 41: 0	9	0.1	230	20.2	2300	2261 G	3.13	26.57377	85.43365	Normal	$Y = 1766$	
14/ 8/ 22	13: 41: 31	9	0.1	280	20.2	2800	2755 G	3.73	26.56613	85.43411	Normal		
14/ 8/ 22	13: 41: 31	9	0.1	270	20.2	2700	2656 G	3.61	26.55762	85.43461	Normal	(R) RURAL ROAD	
14/ 8/ 22	13: 42: 6	9	0.1	220	10.1	2200	2162 G	3	26.54987	85.43505	Normal	Good	Average Poor
14/ 8/ 22	13: 43: 0	9	0.1	250	0	2500	2458 G	3.37	26.54763	85.4352	Normal	<4000	4001-5000 >5001
14/ 8/ 22	13: 44: 0	9	0.1	200	0	2000	1964 G	2.76	26.57305	85.43434	Normal		
14/ 8/ 22	13: 44: 0	9	0.1	200	30.3	2000	1964 G	2.76	26.57497	85.43539	Normal		
14/ 8/ 22	13: 44: 27	9	0.1	370	10.1	3700	3645 G	4.79	26.57727	85.43663	Normal		
14/ 8/ 22	13: 44: 27	9	0.1	270	20.2	2700	2656 G	3.61	26.58005	85.43758	Normal		
14/ 8/ 22	13: 45: 2	9	0.1	330	10.1	3300	3250 G	4.32	26.5886	85.43788	Normal		
14/ 8/ 22	13: 45: 2	9	0.1	340	20.2	3400	3349 G	4.44	26.59757	85.43813	Normal		
14/ 8/ 22	13: 46: 13	9	0.1	230	0	2300	2261 G	3.13	26.60447	85.4383	Normal		
14/ 8/ 22	13: 46: 48	9	0.1	230	20.2	2300	2261 G	3.13	26.6108	85.43754	Normal		
14/ 8/ 22	13: 47: 0	9	0.1	220	20.2	2200	2162 G	3	26.61815	85.43694	Curve		
14/ 8/ 22	13: 47: 22	9	0.1	310	20.2	3100	3052 G	4.09	26.6267	85.43736	Normal		
14/ 8/ 22	13: 47: 22	9	0.1	290	20.2	2900	2854 G	3.85	26.6349	85.43779	Normal		
14/ 8/ 22	13: 48: 0	9	0.1	240	10.1	2400	2360 G	3.25	26.64432	85.43776	Normal		
14/ 8/ 22	13: 48: 0	9	0.1	290	20.2	2900	2854 G	3.85	26.65305	85.43774	Normal		
14/ 8/ 22	13: 48: 33	9	0.1	280	20.2	2800	2755 G	3.73	26.66142	85.43793	Normal		
14/ 8/ 22	13: 48: 33	9	0.1	220	30.3	2200	2162 G	3	26.67013	85.43822	Normal		
14/ 8/ 22	13: 48: 33	9	0.1	190	30.3	1900	1865 G	2.63	26.6797	85.43848	Normal		
14/ 8/ 22	13: 49: 8	9	0.1	290	20.2	2900	2854 G	3.85	26.688	85.43875	Normal		
14/ 8/ 22	13: 49: 8	9	0.1	370	10.1	3700	3645 G	4.79	26.69273	85.43944	Normal		
14/ 8/ 22	13: 49: 43	9	0.1	350	20.2	3500	3447 G	4.55	26.69282	85.44044	Normal		
14/ 8/ 22	13: 50: 0	9	0.1	330	10.1	3300	3250 G	4.32	26.69152	85.44145	Normal		
14/ 8/ 22	13: 50: 19	9	0.1	330	10.1	3300	3250 G	4.32	26.69823	85.44204	Normal		
14/ 8/ 22	13: 50: 54	9	0.1	230	20.2	2300	2261 G	3.13	26.70762	85.44229	Normal		
14/ 8/ 22	13: 51: 0	9	0.1	320	10.1	3200	3151 G	4.2	26.71707	85.44246	Normal		
14/ 8/ 22	13: 51: 29	9	0.1	320	10.1	3200	3151 G	4.2	26.71875	85.443	Normal		
14/ 8/ 22	13: 51: 29	9	0.1	250	10.1	2500	2458 G	3.37	26.7255	85.44401	Normal		
14/ 8/ 22	13: 52: 5	9	0.1	370	20.2	3700	3645 G	4.79	26.73443	85.44426	Normal		
14/ 8/ 22	13: 52: 5	9	0.1	300	20.2	3000	2953 G	3.97	26.74327	85.44458	Normal		
14/ 8/ 22	13: 52: 40	9	0.1	260	20.2	2600	2557 G	3.49	26.75153	85.44495	Normal		
14/ 8/ 22	13: 53: 0	9	0.1	320	10.1	3200	3151 G	4.2	26.75927	85.44556	Normal		
14/ 8/ 22	13: 53: 15	9	0.1	210	10.1	2100	2063 G	2.88	26.76787	85.44618	Normal		
14/ 8/ 22	13: 53: 15	9	0.1	290	20.2	2900	2854 G	3.85	26.77543	85.44673	Normal		

Shree 22 vish
Construction Pvt. Ltd.
Misra
Director

Scanned with CamScanner

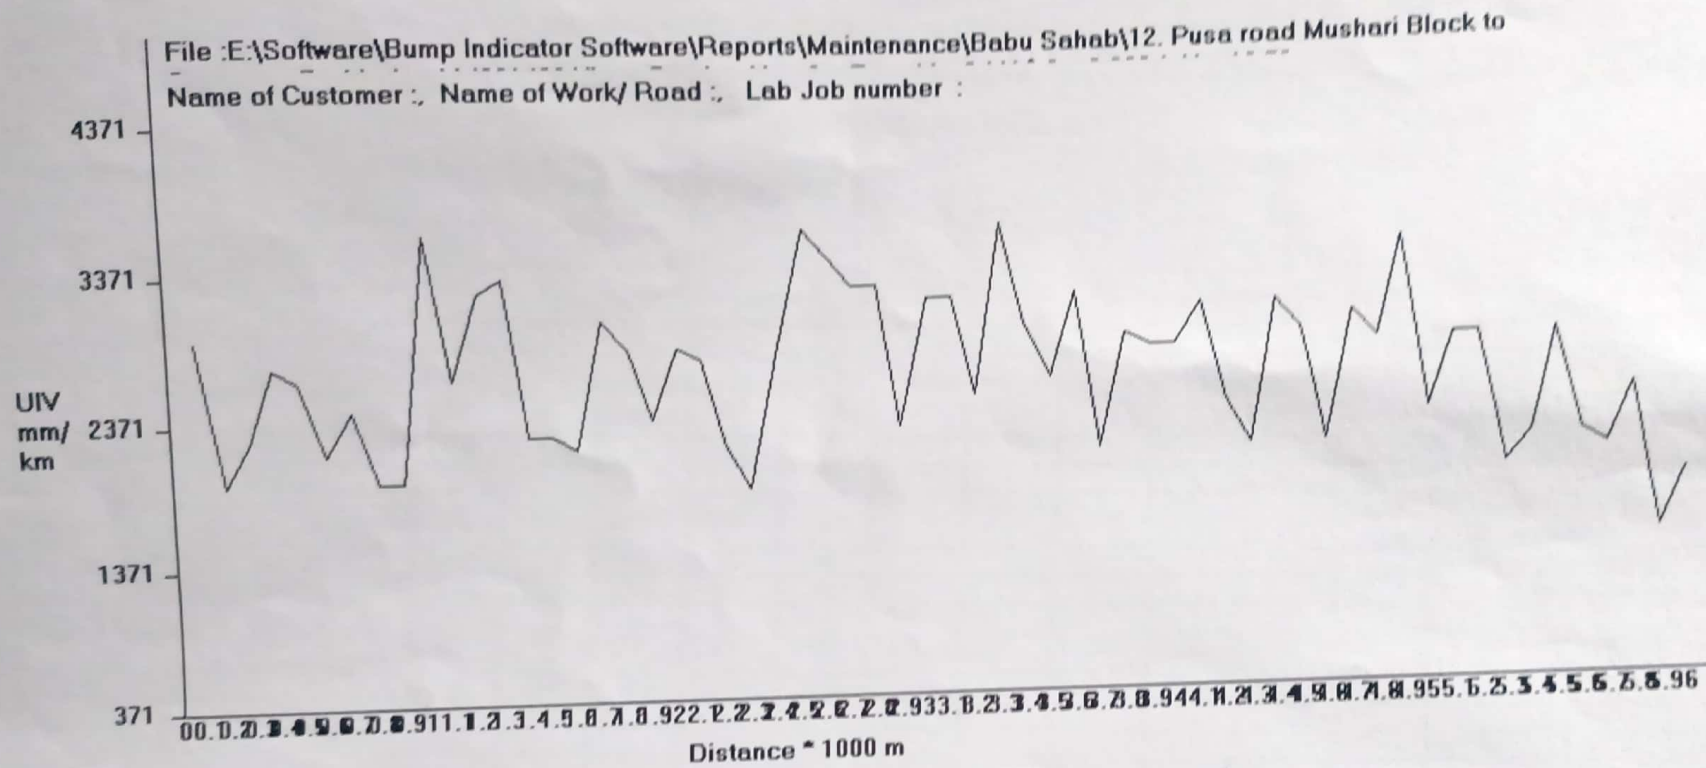

Shree Aashish Mittal
Construction Pvt Ltd,
Director

Smil
22/8/22
A.C

22/8/22

Inspection Form for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Muzaffarpur East-1

Government of Bihar

OMM1

Rural works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From- Muzaffarpur jila anantnagar pura road munshani block

To: Executive Engineer

se gangapur patilashpur sadbhari chakshelad railway gunni hote

RWD Works Division Muzaffarpur East-1

Date:

near N.H 28 tak path.

Length of Road: 6.01 KM

Position: A.E

Period : From.....

Inspector: A.E RWD Sub Division, Munshani

Standard Work item			Work	Units of work required in each kilometre										
S No	Name	Units	1	2	3	4	5	6	7	8	9	10		
OMM100 Sealed Pavement														
OMM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							No. Pothole found.	
OMM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching found	
OMM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing found	
Surface Treatment														
OMM104	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface Ravelling) found	
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							No Bleeding/Flushing Required	
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil							No Crocodile Cracking found	
OMM105	Edge Repair	m2	Nil	Nil	Nil	Nil							No Edge Repair Required	
OMM106	Dips/rips	m2	N/A	N/A	N/A	N/A								
OMM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A								
Other activities														
OMM200 Shoulder														
OMM201	Unsealed Shoulder	No											No Edge Drop off Required	
	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil							Defects rectified within stipulated time.	
	(b) Roughness, Scouring or Potholes	Lm	Nil	3%	2%	Nil							No Holding water found	
OMM202	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							No Embankment Repair Required	
	Embankment Repair	No	Nil	Nil	Nil	Nil							Defects rectified within stipulated time.	
Other Activities (Ratons)														
OMA 500 Drainage including culverts major														
OMA501	Surface Drains & Verges	Lm	N/A	N/A	N/A	N/A							Not Required	
OMA502	Culvert Cleaning	Lm											Culvert maintain within stipulated time	
OMA503	Culvert and Pits repair	m2	Nil	Nil	Nil	Nil							Not Required	

Other activities (White Washing)	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
OM 400 Vegetation																			
Grass Control																			
OM401																			
a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
Tree and shrub management	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
Cutting trees	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
Cutting Shrubs	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
Other activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
OM500	Safety Signage and Road																		Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	Not Applicable
OM503	Distance Stones	No	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	Not Applicable
OM504	Road Marking	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
Other activities																			

Shree P. W. S. J. N. Mittal
Construction Pvt. Ltd.
Bidding Director

22/08/22
Appendix

22/09/22
A.C.

Executive Engineer, Rural Work Department, Work
Division, Muzaffarpur East I

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	Muzaffarpur jila anatarat pusa road musahri block se gangapur pahladpur sadhhari chakhalad railway gumti hote hue N.H 28 tak path.		
2	Batch No.	RM/MU/MUZ/20/0004		
3	Project ID	31507204011		
4	Total Length of Road (in Km)	6.01		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	6.01		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	47.88742		
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	2.39437		

Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				2.39437

Date of inspection by E/1 or his agent Prepared by
Contractor's self Control unit

Name and Designation of person inspecting road
(Signature)

Date

Signature of person inspecting road

Certify by E/T (signature) Date
