

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

पत्रांक 1727 अ/अ

दिनांक 23/08/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।

विषय: नई अनुरक्षण नीति 2018 अंतर्गत वित्तीय वर्ष 2022-23 में अनुरक्षण मद में व्यय हेतु आवंटन की मांग।

महाशय,

उपर्युक्त विषय के संबंध में नई अनुरक्षण नीति 2018 अंतर्गत वित्तीय वर्ष 2022-23 में अनुरक्षण मद में व्यय हेतु संलग्न विवरणी के अनुसार 13.35861 (तेरह लाख पैंतीस हजार आठ सौ एकसठ) रुपये का आवंटन उपलब्ध कराने की कृपा की जाये ताकि किये गये कार्यों का भुगतान किया जा सके।

अनुलग्नक:- यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1


23/08/2022

23/8/2022

Maintenance Requisition Formate for Scheme Head- MIR (3054) Under Bihar Rural Road Maintenance Policy-2018

[illegible]

Road Details				AA Details		Agreement										Actual Maintenance Expenditure										Current Maintenance Demand					Remarks
Sl. No.	Name of Roads	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh)	Maintenance Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	Length (in KM)	1st. Year Maintenance	2nd. Year Maintenance	3rd. Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintenance Expenditure	Length as per Bump Report	IRI As per bump Report	1st QTR Maintenance	2nd QTR Maintenance	Total						
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	30	31					
1	Muzaffarpur jila antargat musabiri kalbhut sri ramsakal ojha ke ghar se baranhipur bodhi chaul tak bhaya anusuchit jati mahadalit tola ewn khabra pokhar hote hue path nirman	RM/MU/MUZ/20/0004	31507205003	22/05/2021	41.83600	18.30900	40.90200	0.96803	1.93409	5.61512	2.47126	6.27849	17.26699	2.160	0.000	0.000	0.000	0.000	0.000	0.000	2.160	2642.000	0.86335	0.86335	1.72670						
5	Baikunthpur - Madhopur	RM/MU/MUZ/20/0004	NEA220002 670	18/04/2021	34.77000	16.54300	33.74200	0.87800	1.75190	5.07387	2.23455	5.67051	15.60883	1.950	0.000	0.000	0.000	0.000	0.000	0.000	1.950	2687.000	0.78044	0.78044	1.56088						
6	Manika Harkishna - Bindra patha	RM/MU/MUZ/20/0002	NEA220000 2676	12/06/2021	59.59000	26.14000	37.61800	1.09725	1.94316	5.62608	2.80628	6.54263	18.01540	3.050	0.000	0.000	0.000	0.000	0.000	0.000	3.050	2366.000	0.90077	0.90077	1.80154						
Total																									13.35861						


 22/08/22
 A.C.


 Executive Engineer
 R.W.D. Works Division
 Muzaffarpur East-1

Name of Road - Marjauliya Culvert Ramsakal Ojha Ke ghar se Barmaipur Boudhi Chawik tak via Anusuchit Jati Mahadali Tola Evm Bakira Polkhari Hote Hise

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI	IRI CATEGORY	Latitude	Longitude	Event
14/8/22	13: 9: 37	6	0.1	220	0	2200	2162 G	3	26.98798	85.37259	Normal
14/8/22	13: 10: 15	6	0.1	270	10.1	2700	2656 G	3.61	26.9908	85.37167	Normal
14/8/22	13: 10: 15	6	0.1	230	10.1	2300	2261 G	3.13	26.99248	85.37069	Curve
14/8/22	13: 11: 0	6	0.1	370	10.1	3700	3645 G	4.79	26.9902	85.36983	Normal
14/8/22	13: 11: 26	6	0.1	260	20.2	2600	2557 G	3.49	26.99002	85.36882	Normal
14/8/22	13: 11: 26	6	0.1	350	20.2	3500	3447 G	4.55	26.98557	85.36813	Curve
14/8/22	13: 12: 0	6	0.1	300	20.2	3000	2953 G	3.97	26.98742	85.3671	Normal
14/8/22	13: 12: 1	6	0.1	220	20.2	2200	2162 G	3	26.98062	85.36646	Normal
14/8/22	13: 12: 11	6	0.1	220	20.2	2200	2162 G	3	26.97728	85.36608	Normal
14/8/22	13: 12: 36	6	0.1	260	20.2	2600	2557 G	3.49	26.96407	85.36579	Normal
14/8/22	13: 13: 0	6	0.1	310	10.1	3100	3052 G	4.09	26.95515	85.36545	Normal
14/8/22	13: 13: 11	6	0.1	300	10.1	3000	2953 G	3.97	26.94912	85.3648	Normal
14/8/22	13: 13: 47	6	0.1	310	10.1	3100	3052 G	4.09	26.94475	85.36409	Curve
14/8/22	13: 14: 0	6	0.1	240	20.2	2400	2360 G	3.25	26.9426	85.36313	Normal
14/8/22	13: 14: 10	6	0.1	240	20.2	2400	2360 G	3.25	26.94428	85.36214	Normal
14/8/22	13: 14: 22	6	0.1	220	10.1	2200	2162 G	3	26.9501	85.36136	Normal
14/8/22	13: 14: 29	6	0.1	280	20.2	2800	2755 G	3.73	26.95462	85.36051	Normal
14/8/22	13: 15: 0	6	0.1	300	20.2	3000	2953 G	3.97	26.95853	85.35963	Normal
14/8/22	13: 15: 10	6	0.1	250	20.2	2500	2458 G	3.37	26.96343	85.35875	Normal
14/8/22	13: 15: 33	6	0.1	240	20.2	2400	2360 G	3.25	26.97263	85.35862	Normal
14/8/22	13: 15: 8	6	0.1	250	0	2500	2458 G	3.37	26.98175	85.35886	Normal
AVG:-							2642				

$$Y = 0 * X^2 + 0.989 * X - 13.58$$

$$X = 2500$$

$$Y = 2458$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001


SPRUE & WASTE MATERIALS
CONSTRUCTION
DIRECTOR

Said
22/8/22
A.C

22/8/22

File : E:\Software\Bump Indicator Software\Reports\Maintenance\Babu Sahab\11. Manjhauliya Culvert Ramsakal

Name of Customer : Name of Work/ Road : Lab Job number :

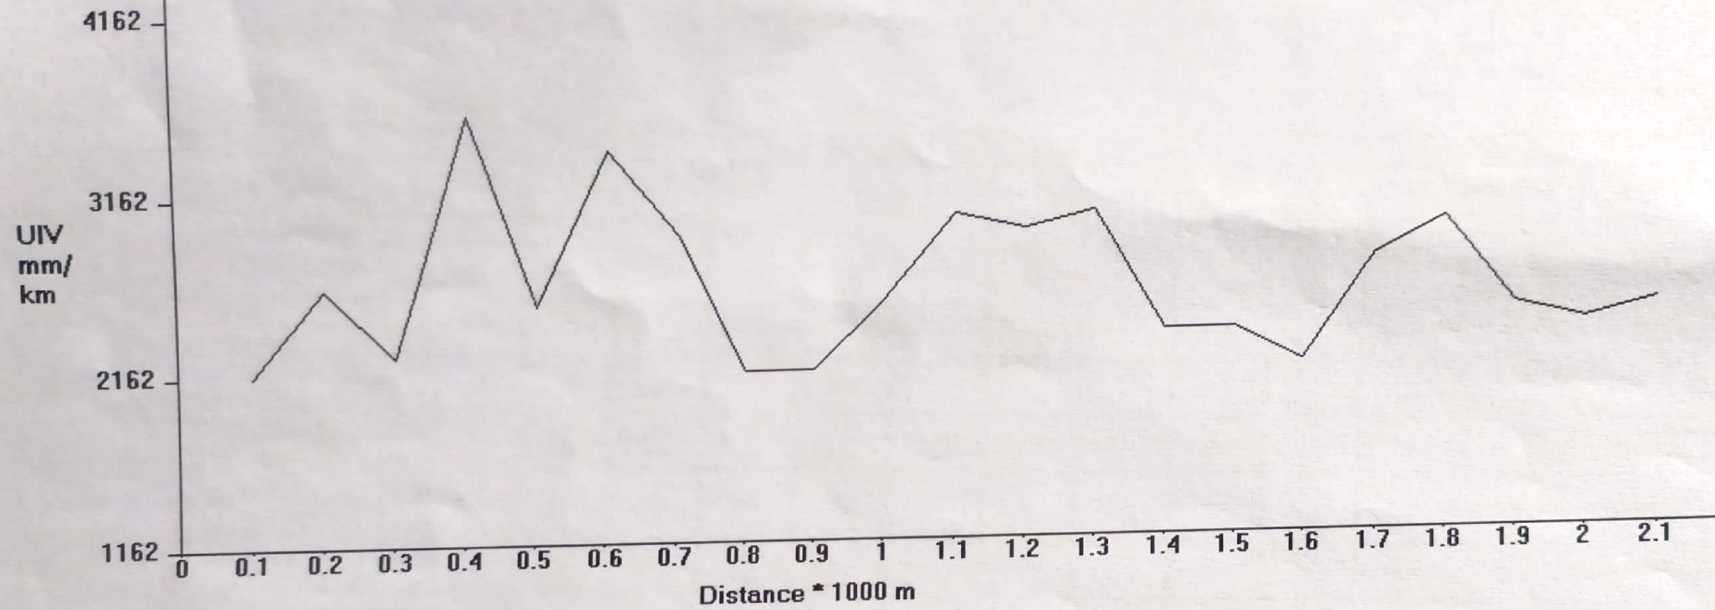

Com
20-8-22
S.E.

Shree Aash Mishra
Construction Pvt. Ltd.
Director

Smriti
22/8/22
A.C.

19/8/22

Acquisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Muzaffarpur East-1

Government of Bihar
OM01
Rural works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From- Muzaffarpur jila antargat musahri kalbhat sri
ramsakal oja ke ghar se baramthpur bodhi chauk tak bhaya
anusuchit jati mahadalit tola ewn khabra pokhar hote hue path
nimmaan.

To: Executive Engineer
RWD Works Division Muzaffarpur East-1

Date:

Length of Road: 2.16 KM

Position: A.E

Periode : From.....

Inspector: A.E RWD Sub Division, Mushari

Standard Work item		Work	Units of work required in each kilometre										Comments
S No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM100 Sealed Pavement													
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							No. Pothole found.
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing found
Surface Treatment													
OM104	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil							No Loss of Agregate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil							No Crocodile Cracking found
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil							No Edge Repair Required
OM106	Digouts	m2	N/A	N/A	N/A	N/A							
OM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A							
Other activities			Lm										
OM200 Shoulder													
OM201	Unsealed Shoulder	No											
	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil							No Edge Drop off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	3%	2%	Nil							Defects rectified within stipulated time.
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							No Holding water found
OM202	Embankment Repair	No	Nil	Nil	Nil	Nil							No Embankment Repair Required
	Other Activite (Raincut)		3%	1%	2%								Defects rectified within stipulated time.
OM 300 Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A							Not Required
OM302	Culvert Cleaning	Lm											Culvert maintain within stipulated time

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	Muzaffarpur jila antargat musahri kalbhat sri ramsakal ojha ke ghar se baramthpur bodhi chauk tak bhaya anusuchit jati mahadalit tola ewn khabra pokhar hote hue path nirmaan.		
2	Batch No.	RM/MU/MUZ/20/0004		
3	Project ID	31507204011		
4	Total Length of Road (in Km)	2.16		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	2.16		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	17.26699		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	0.86335		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.86335

Date of inspection by E/I or his agent Prepared by
Contractor's self Control unit

Name and Designation of person inspecting road
(Signature)

Date

Signature of person inspecting road

Certify by E/I (Signature) Date
