

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, मोहनियाँ।

Email ID:- ee.rwdworkmohania@gmail.com

Mob:- 8986915825

पत्रांक...2014.....

मोहनियाँ / दिनांक...25.11.2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मोहनियाँ।

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :- नई अनुरक्षण नीति-2018MR (3054) योजना के अंतर्गत पथ में कराये गये
त्रैमासिक अनुरक्षण कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये त्रैमासिक अनुरक्षण कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मोहनियाँ।
25.11.22

FORM GFR 19-A

(See Government of India's Decision (I) below Rule-150)

Form of Utilization Certificate up to 16 July 2022

Sl.No	Name of Scheme	Sanction No.&Date With Amount (In lace Rs.)	Amount Received (In lace Rs.)	Particulars
1	Maintenance of Rural roads Under MR (New Maintenance Policy-2018 MR (3054) BRRDA PATNA)	New Maintenance Policy-2018 MR (3054) BRRDA PATNA	205.01908	Certified that out of Rs.205.01908 lakh of grants-in-aid sanctioned during the years 2022-23 In favor of EE,RWD works division mohania a sum of Rs. 41.74158 lakh has been utilized for the purpose of MR (3054) Schemes as given in the margin for which it was sanctioned and that the balance of Rs.163.27750 lakh remaining unutilized at the end of the period under report.
	Total:		205.01908	

2. Certified that I have satisfied my self that the cosnditions on which the grant-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was utilized for the purpose for which it was sanctioned.-

Kind of Checks exercised:-

- Works have been supervised by Executive Engineer/ Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/ Executive Engineer.
- All other caudal formalities have been observed.

3. Physical Progress achieved:-

- Construction of Road Works.
- Construction of CD works.


Divisional Accounts Officer
R.W.D, works Division
Mohania.


Executive Engineer
R.W.D, works Division
Mohania.

Name of Road-BarwarCanalRoad - Aatdih

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
14/ 10/ 22	13: 44: 40	59	0.1	370	0	3700	3426	G	25.343253	83.658972	Normal
14/ 10/ 22	13: 45: 0	59	0.1	340	30.3	3400	3163	G	25.344003	83.65968	Normal
14/ 10/ 22	13: 45: 16	59	0.1	370	30.3	3700	3426	G	25.344712	83.660337	Normal
14/ 10/ 22	13: 45: 16	59	0.1	320	30.3	3200	2987	G	25.34518	83.660875	Normal
14/ 10/ 22	13: 45: 16	59	0.1	240	30.3	2400	2286	G	25.346035	83.6617	Normal
14/ 10/ 22	13: 45: 16	59	0.1	340	20.2	3400	3163	G	25.346685	83.662423	Normal
14/ 10/ 22	13: 45: 52	59	0.1	360	20.2	3600	3338	G	25.347368	83.663063	Normal
14/ 10/ 22	13: 46: 0	59	0.1	300	10.1	3000	2812	G	25.348202	83.66335	Normal
14/ 10/ 22	13: 46: 0	59	0.1	270	10.1	2700	2549	G	25.349182	83.6634	Normal
14/ 10/ 22	13: 46: 27	59	0.1	360	10.1	3600	3338	G	25.350055	83.66348	Normal
14/ 10/ 22	13: 46: 27	59	0.1	320	40.4	3200	2987	G	25.350985	83.663552	Normal
14/ 10/ 22	13: 46: 27	59	0.1	270	20.2	2700	2549	G	25.351765	83.663618	Normal
14/ 10/ 22	13: 46: 27	59	0.1	380	20.2	3800	3513	G	25.352693	83.663703	Normal
14/ 10/ 22	13: 47: 0	59	0.1	380	10.1	3800	3513	G	25.35358	83.66377	Normal
14/ 10/ 22	13: 47: 1	59	0.1	300	20.2	3000	2812	G	25.354452	83.663838	Normal
14/ 10/ 22	13: 47: 1	59	0.1	280	20.2	2800	2636	G	25.355355	83.663888	Normal
14/ 10/ 22	13: 47: 1	59	0.1	260	20.2	2600	2461	G	25.356315	83.663938	Normal
14/ 10/ 22	13: 47: 36	59	0.1	360	20.2	3600	3338	G	25.357162	83.663988	Normal
14/ 10/ 22	13: 47: 36	59	0.1	290	20.2	2900	2724	G	25.35817	83.664057	Normal
14/ 10/ 22	13: 48: 0	59	0.1	350	20.2	3500	3250	G	25.359038	83.664123	Normal
14/ 10/ 22	13: 48: 12	59	0.1	280	30.3	2800	2636	G	25.359918	83.664192	Normal
14/ 10/ 22	13: 48: 12	59	0.1	270	20.2	2700	2549	G	25.36089	83.664275	Normal
14/ 10/ 22	13: 48: 47	59	0.1	310	10.1	3100	2900	G	25.360975	83.66508	Normal
14/ 10/ 22	13: 49: 0	59	0.1	380	20.2	3800	3513	G	25.360855	83.665992	Normal
14/ 10/ 22	13: 49: 0	59	0.1	360	30.3	3600	3338	G	25.36087	83.666968	Normal
14/ 10/ 22	13: 49: 22	59	0.1	330	10.1	3300	3075	G	25.361403	83.667658	Normal
14/ 10/ 22	13: 49: 22	59	0.1	390	20.2	3900	3601	G	25.361895	83.6684	Normal
14/ 10/ 22	13: 50: 0	59	0.1	320	30.3	3200	2987	G	25.361768	83.669258	Normal
14/ 10/ 22	13: 50: 0	59	0.1	380	20.2	3800	3513	G	25.361972	83.670168	Normal
14/ 10/ 22	13: 50: 33	59	0.1	300	30.3	3000	2812	G	25.36194	83.671178	Normal
14/ 10/ 22	13: 50: 33	59	0.1	340	10.1	3400	3163	G	25.36228	83.672238	Normal
14/ 10/ 22	13: 53: 29	59	0.1	350	10.1	3500	3250	G	25.362198	83.672003	Normal
			3.2								

S. Bal
19/10/2022 R-E

Executive Engineer
R.W.D. Work Div. Mohania

Name of Customer : M/S Saraswati Construction,Pr
 Name of Work/ Road : BarwarCanalRoad - Aaldin
 Lab Job number :
 Date : 14-10-2022
 Section No. : 59


Test Date : 14-10-2022 Road Name : BarwarCanalRoad - Aaldin
 Machine No : 405 Road Type : (R) RURAL ROAD
 Start S No : 59 Side :
 Start E No : Interval
 Weather : UIV Range : 1286 To 5000 1000 mm/km
 Start Location : Dist Range : 0 To 3.3 0.1 * 1000 m
 End Location : Equation : $Y = 0 * X^2 + 0.877 * X + 181.3$

Print

Generate Report and Graph

Redraw Graph

Map View

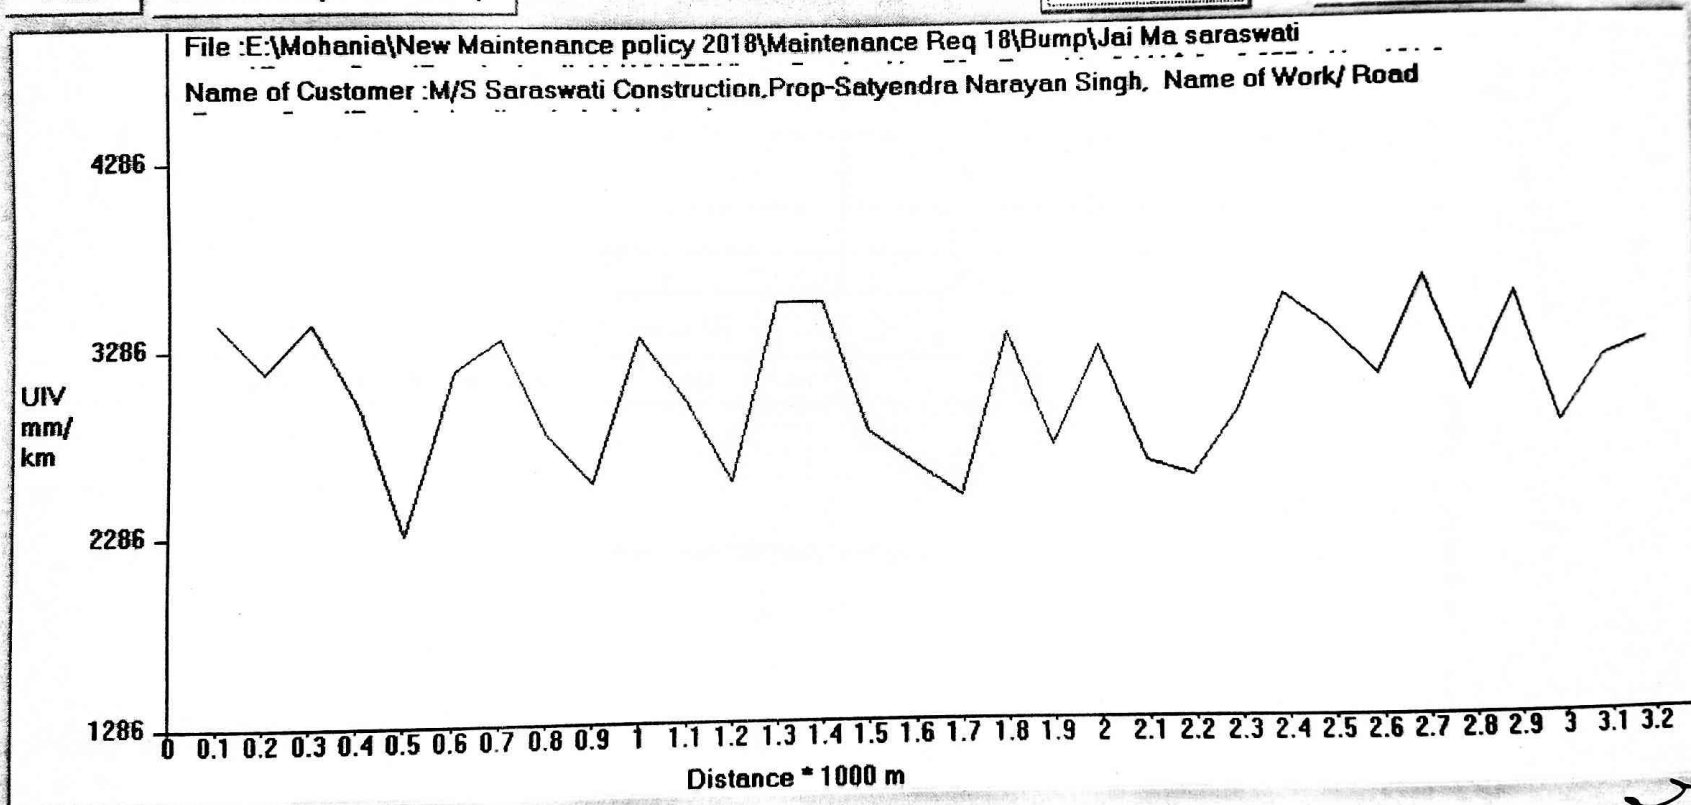

Steele,
 19/10/2022
 R.B

Executive Engineer
 R.W.D. Work Div. Mohania
 19/10/22

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PU Name :- RWD, Works Division, Mohania

Quarter:- 2

Period- 18-04-2021
17-07-2021

1	Name of the Road	BarwarCanalRoad - Aatdin		
2	Batch No./Package No.	RM/KA/MOH/19/0011		
3	Project ID	NEA220002366		
4	Total Lenth of Road (in KM)	3.200		
5	Length of Road to Meet Required Service Level [Completed length](in Km) [1]	3.200		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	28.81837		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.44092		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	-	60%	0.00000
II	SHOULDERS AND EMBANMENTS	-	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	-	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	-	10%	0.00000
V	VEGATION	-	5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (IN Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.44092

Date of inspection by E/I or his agent

Prepare by Contractor's self Control unit

Name and Designation of person inspecting road

Date

S. Bala.
14/11/2022
(Signature) R.E.

Signature of person inspecting road

Certify by E/I [signature] Date:-

14/11/2022
O.E.

Executive Engineer
Rural Works Department
Works Division, Mohania

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rurak Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD, Works Division:- Mohania

Quarter:- 2

Government Of Bihar OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:-**BarwarCanalRoad - Aatdin**
(Package No.-RM/KA/MOH/19/0011)
ength of Road:-3.200 KM

To,

Executive Engineer
RWD (w) Div. Mohania

Date:-10.11.2022

Inspector :- JE RWD Sub Division Ramgarh

Position :-J.E.

No	standard Of Work Item	Work Unit	Unit OF Required in each Kilometere										Comments
	Name		1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Pot Hole found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching found.
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealling found
OM104	Surface Treatment												
	(a) Loss of Agreegate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No Loss of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Loss of Aggregates (Surface Ravelling) Found
	© Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Bleeding / Flushing found.
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
106	Digouts	m ²	NA	NA	NA	NA							No Edge Repair Required
107	Concrete pavement	m ³	NA	NA	NA	NA							
	Other activities												
OM200	Shoulder												
OM201	Unsealed Shoulder												
	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding water Found.
OM202	Embankment Repair	m ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil							Not Required
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	NA	NA	NA	NA							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	m ³	Nil	Nil	Nil	Nil							Not Required
	Other activities(Whilw washing)	m ²	Nil	Nil	Nil	Nil							Not Required

No	standard Of Work Item Name	Work Unit	Unit OF Required in each Kilometere										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil								Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil								Not Required
OM402	Tree and Shrub Management	Ha	Nil	Nil	Nil								Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil								Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil								Not Required
	Other activities (Trimming of Grass)	m ²	Nil	Nil	Nil								Not Required
OM500	Safety Signage and Road												
OM501	Signs Maintanence	No	NIL	NIL	NIL								Not Required
OM502	Guard Stones	Lm	NA	NA	NA								Not Required
OM503	Distance Stones	No	NA	NA	NA								Not Required
OM504	Road Marking	No	Nil	Nil	Nil								Not Required
	Other activities												Not Required

Bidder

Appendix

14/11/2022
O.E

S.Bale.
14/11/2022
A.E.

Executive Engineer
Rural works Department
Works Division, Mohania
