

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग
कार्य प्रमण्डल गोपालगंज-2

पत्रांक 843 खनु

दिनांक 09/05/2022

प्रेषक,

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल गोपालगंज-2

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी -सह-
सचिव,
ब्राडा,
बिहार, पटना।

विषय:- **MR-3054 (New Maintenance policy 2018)** के अन्तर्गत 5 (पांच) वर्षीय
अनुरक्षण हेतु अधियाचना के संबंध में।

प्रसंग :- अभियन्ता प्रमुख, ग्रामीण कार्य विभाग, बिहार, पटना के पत्रांक-मु0अ0-4 (मु0) 3054
- 04-229/2021-1135 अनु0 पटना, दिनांक-09.03.22।


महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र में दिये गये निर्देश के आलोक में नई अनुरक्षण नीति -
2018 अन्तर्गत पथों के अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में तैयार कर आवश्यक
कार्रवाई हेतु समर्पित की जा रही है।

अतः MR-3054 (New Maintenance policy 2018) के अन्तर्गत (MR-N/2019-20
Gopalganj-2/12) 1. झझवा से शाहपुर, 2. कटेया टोला से काशी टेंगराही, 3. विशुनपुरा से
जलालपुर पथ के अनुरक्षण हेतु अधियाचित प्रपत्र में दर्शाये गए राशि उपलब्ध कराने की कृपा
की जाय। कार्य का निरीक्षण किया गया एवं कराया गया कार्य संतोषप्रद है। उक्त पथों में
ए0टी0आर0 लंबित नहीं है।

अनु0- यथोक्त।

विश्वासभाजन



कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग

कार्य प्रमण्डल, गोपालगंज-2
03.5.22

Standrad Format For Roads Quarterly Statement (5th Quarter)

PIU Name:- R.W.D.(W)Division Gopalganj-2

1	Name of the Road	Vishunpura to Jalalpur		
2	Batch No.			
3	Project ID	314701036977		
4	Total Length of Road(in K.M.)	3.70		
5	Length of Road to Meet Required Service Level (Completed Length)(in K.M.)	3.70		
6	No of Total Quarter(ie 3 Months as a Unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount For Maintenance(in Lakh)	375021620		
8	Quarterly Payment: 1/20 of Ordinary Maintennance Cost as per Schedule (in Lakh)	18751020		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment (6) = (3) / (1)*(2)*(4)
		Length Non Compliant	Weightred Value for Payment Reduction (%)	
	Paved Roads(Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Total Payment Reduction for the Quarter (in Lakh)				18751020
To be Paid for the Quarter/ Demand (in Lakh)				

Date of Inspection by E/I or his agent

Prepared by Contractor's self Control unit

Name and Designation of Person inspecting road

Date:-

30-4-22
J.E.

30-4-22
AK

(Signature)

30/4/22

Signature of Person inspecting road

Certify by E/I (Signature) Date

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

1 Year (1st Quarter)

RWD, Works Division Gopalganj-2

Government Of Bihar

OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Vishunpura to Jalalpur
(Package No.MR-N/2019-20 Gopalganj-2/12)

Length of Road :- 3.70 Km

Period :- From:- 12.02.20 to 11.05.20

Inspector :- A.E RWD Sub Division : Sidhawalia

To:-


Executive Engineer
RWD, Works Division Gopalganj-2

Date:-

Position :- A.E

No	Standard Of Work Item Name	Work Unit	Unit OF Required in each Kilometere										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil	Nil						No Pot Hole Found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil	Nil						Not Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil	Nil						No Crack sealing Found
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil	Nil						No Loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil	Nil						No Bleeding/ Flushing Required
	© Crocodile Cracking	m ²	Nil	Nil	Nil	Nil	Nil						No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil	Nil						No Edge Repair Required
106	Digouts	m ²	N.A	N.A	N.A	N.A	N.A						
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A	N.A						
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil	Nil						No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil	Nil						Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil	Nil						No Holding Water Found
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil	Nil						Not Required
	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil	Nil						Not Required
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A	N.A						Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil	Nil						Not Required

Name of Customer: M/s Nandani construction , Machine no: 19193 , Road: Vishnupura se jalapur , Date: 05/05/22 , Section No: 28 , Equation: $Y=0.936X+245.3$

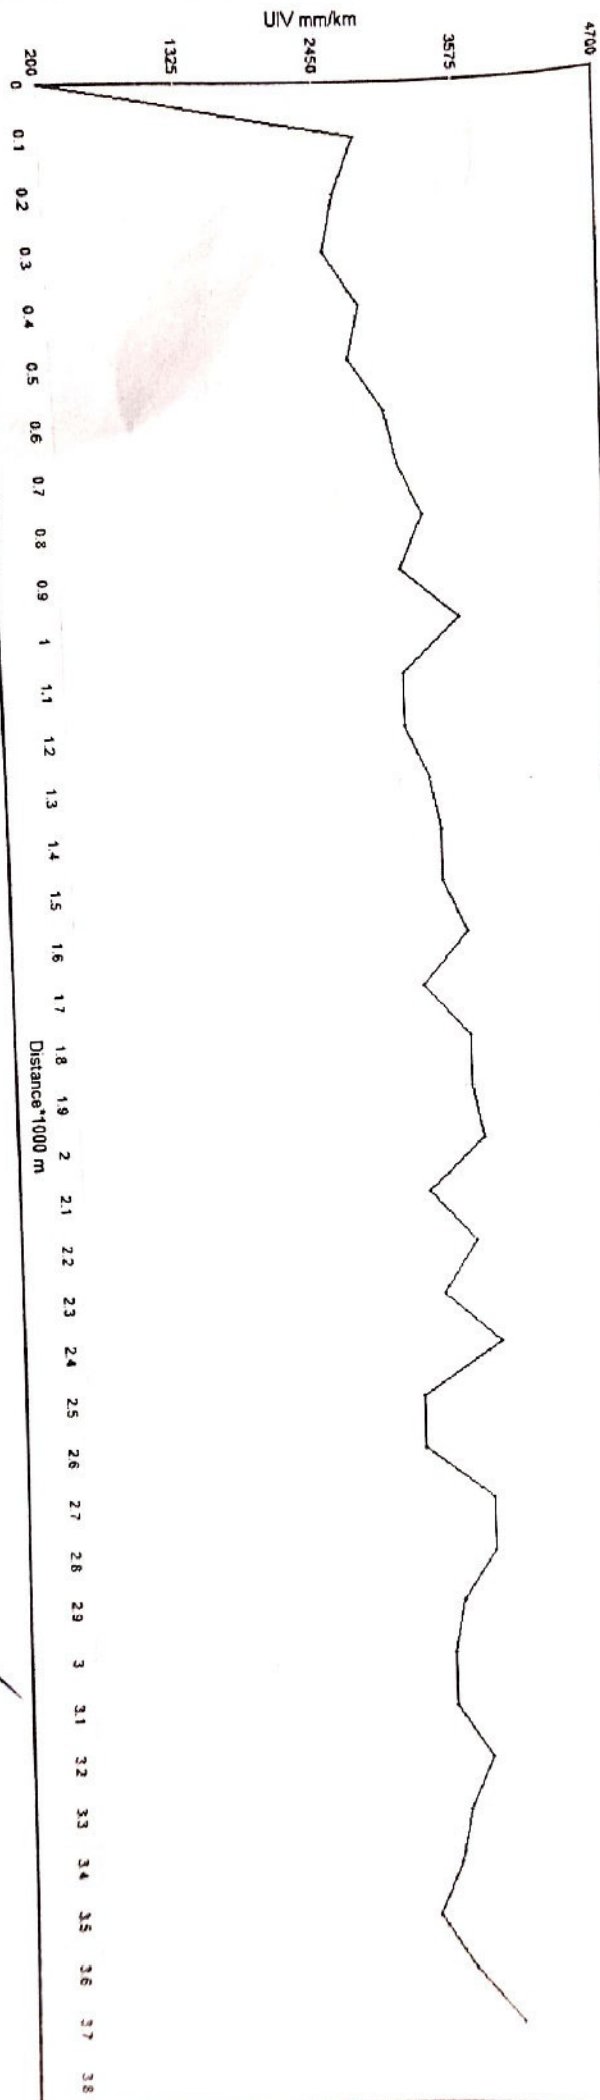

~~30-04-22~~
30-04-22

30-04-22
AE

30/4/22

Name of work : Vishunpura se Jalajpur

Name of customer : M/s Nandani construction

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUM(Per)	Speed(Km/Hr)	Ultim(Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
30/04/22	10:32:32	28	0	0	0.0 cm	13.3 Km/Hr	0.0 mm/Km	245	0.43	Good	26.4977541	N	83.9338847	E	Normal
30/04/22	12:02:08	28	100	100	27.0 cm	20.1 Km/Hr	2700.0 mm/Km	2773	3.75	Good	26.5001764	N	84.0826654	E	Normal
30/04/22	12:02:19	28	100	200	25.0 cm	25.2 Km/Hr	2500.0 mm/Km	2585	3.53	Good	26.4936558	N	84.0824366	E	Normal
30/04/22	12:02:30	28	100	300	24.0 cm	31.2 Km/Hr	2400.0 mm/Km	2452	3.41	Good	26.4984465	N	84.0821924	E	Normal
30/04/22	12:02:41	28	100	400	27.0 cm	32.4 Km/Hr	2700.0 mm/Km	2773	3.75	Good	26.4975195	N	84.0823069	E	Normal
30/04/22	12:02:52	28	100	500	26.0 cm	34.5 Km/Hr	2600.0 mm/Km	2679	3.64	Good	26.4966478	N	84.0822077	E	Normal
30/04/22	12:03:02	28	100	600	29.0 cm	33.4 Km/Hr	2900.0 mm/Km	2960	3.98	Good	26.4959040	N	84.0820322	E	Normal
30/04/22	12:03:14	28	100	700	30.0 cm	32.0 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4952078	N	84.0818338	E	Normal
30/04/22	12:03:27	28	100	800	32.0 cm	27.9 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4938574	N	84.0812006	E	Normal
30/04/22	12:03:40	28	100	900	30.0 cm	27.3 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4934912	N	84.0810251	E	Normal
30/04/22	12:03:51	28	100	1000	35.0 cm	31.2 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4927015	N	84.0804224	E	Normal
30/04/22	12:04:04	28	100	1100	30.0 cm	28.5 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4915457	N	84.0801935	E	Normal
30/04/22	12:04:40	28	100	1200	30.0 cm	10.0 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4905043	N	84.0802240	E	Normal
30/04/22	12:05:02	28	100	1300	32.0 cm	16.5 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4898767	N	84.0799036	E	Normal
30/04/22	12:05:15	28	100	1400	33.0 cm	27.6 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4891157	N	84.0798655	E	Normal
30/04/22	12:05:27	28	100	1500	33.0 cm	29.1 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4880915	N	84.0798189	E	Normal
30/04/22	12:05:40	28	100	1600	35.0 cm	27.2 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4870939	N	84.0799341	E	Normal
30/04/22	12:05:57	28	100	1700	31.0 cm	22.9 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4861574	N	84.0799799	E	Normal
30/04/22	12:06:58	28	100	1800	35.0 cm	25.9 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4854250	N	84.0802927	E	Normal
30/04/22	12:07:11	28	100	1900	35.0 cm	27.0 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4854250	N	84.0802927	E	Normal
30/04/22	12:07:23	28	100	2000	36.0 cm	29.1 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4854250	N	84.0802927	E	Normal

30-04-22
S-E

30-04-22
S-E

30/04/22

Name of work : Vishunpura se Jalajpur
 Name of customer : M/s Nandani construction

(R)Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

30/04/22	12 07 33	28	100	2100	31.0 cm	34.9 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4827394	N	84.0804224	E	Normal
30/04/22	12 07 44	28	100	2200	35.0 cm	35.2 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4816504	N	84.0803080	E	Normal
30/04/22	12 07 53	28	100	2300	32.0 cm	37.0 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4813504	N	84.0802927	E	Normal
30/04/22	12 08 04	28	100	2400	37.0 cm	33.5 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4805307	N	84.0802240	E	Normal
30/04/22	12 08 21	28	100	2500	30.0 cm	21.3 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4790687	N	84.0803690	E	Normal
30/04/22	12 08 40	28	100	2600	30.0 cm	19.6 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4786024	N	84.0802774	E	Normal
30/04/22	12 08 56	28	100	2700	36.0 cm	22.0 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4774542	N	84.0802774	E	Normal
30/04/22	12 09 17	28	100	2800	36.0 cm	17.4 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4767637	N	84.0802776	E	Normal
30/04/22	12 09 37	28	100	2900	33.0 cm	17.4 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4759455	N	84.0812996	E	Normal
30/04/22	12 09 55	28	100	3000	32.0 cm	20.6 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4752207	N	84.0811014	E	Normal
30/04/22	12 10 28	28	100	3100	32.0 cm	10.6 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4743289	N	84.0809412	E	Normal
30/04/22	12 10 41	28	100	3200	35.0 cm	27.3 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4733973	N	84.0804377	E	Normal
30/04/22	12 11 03	28	100	3300	33.0 cm	17.6 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4725027	N	84.0803537	E	Normal
30/04/22	12 11 17	28	100	3400	32.0 cm	23.9 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4719458	N	84.0803537	E	Normal
30/04/22	12 11 34	28	100	3500	30.0 cm	21.8 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4712419	N	84.0801783	E	Normal
30/04/22	12 11 46	28	100	3600	33.0 cm	29.7 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4705469	N	84.0799494	E	Normal
30/04/22	12 11 57	28	100	3700	37.0 cm	32.7 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4690576	N	84.0794611	E	Normal

30-04-22
 S-E

30-04-22
 SK

8/2/14/12
