

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल गोपालगंज-1

पत्रांक:- 1925अनु / गोपालगंज दिनांक 21/11/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल गोपालगंज-1

सेवा में,

सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।


विषय:- राशि उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत पंचवर्षीय अनुरक्षण अवधि के अधीन पथों में कराये गये त्रैमासिक अनुरक्षण कार्य हेतु राशि की अधियाचना उपलब्ध कराये गये प्रपत्र में सभी सुचनाओं के साथ अंकित कर समर्पित किया जाता है।

अनु0-यथोक्त।

विश्वासभाजन


21/11/22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, गोपालगंज-1
21.11.22

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PJT Name : Rural Works Department, Works Division, Gorpalganj I

Forth Quarter

1	Name of Road	SEMARA - BANIYA CHAPPAR		
2	Batch No.	RM/GO/GOP/19/0007		
3	Project ID	31406902098		
4	Total Length of Road (in Km)	1.490		
5	Length of Road to Meet Required Service Level [Completed Length] (in km) [1]	1.490		
6	No. of Total Quarte (ie 3 Months as a Unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	15.854		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.79271		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment [6] = [3]/[1]*[2]*[4]
		Length Non - Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGE WAY)	0	60%	0
II	SHOULDERS AND EMBANKEMENTS	0	10%	0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0
IV	SIGNAGE AND ROAD SAFETY	0	10%	0
V	VEGETATION	0	5%	0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]		0		0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]		0.792		lae

Date of inspection by E/I or his agent
Prepared by Contractor's self Control Unit

Name and Designation of Executive Engineer

Executive Engineer
Rural Works Department
Works Div. Gorpalganj I

Date

Signature of person inspecting road

Certify by E/I [signature] Date

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												Not Required
	Grass Control												Not Required
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road												Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Not Required
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												


 V. N. S. S.
 15/10/22


 R. S. S.
 15/10/22


 R. S. S.
 15/10/22

Executive Engineer,
 Rural Works Department
 Works Div Gopalganj-1

Name Of Road :-Semra Baniya Chappar

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	CATEGORY ROAD	IRI	Latitude	Longitude	Event
27/8/22	16:46:9	87	0.1	380	20.2	3800	G	3724	26.54866	84.23961	Normal
27/8/22	16:46:9	87	0.1	320	20.2	3200	G	3206	26.54885	84.23865	Normal
27/8/22	16:46:44	87	0.1	340	20.2	3400	G	3379	26.549	84.23766	Normal
27/8/22	16:47:0	87	0.1	290	30.3	2900	G	2948	26.54899	84.2366	Normal
27/8/22	16:47:20	87	0.1	360	10.1	3600	G	3551	26.54901	84.23557	Normal
27/8/22	16:47:20	87	0.1	350	10.1	3500	G	3465	26.54855	84.2348	Normal
27/8/22	16:47:55	87	0.1	250	20.2	2500	G	2603	26.54856	84.2338	Normal
27/8/22	16:48:0	87	0.1	280	20.2	2800	G	2862	26.54875	84.23283	Normal
27/8/22	16:48:0	87	0.1	240	20.2	2400	G	2517	26.54909	84.23182	Normal
27/8/22	16:48:30	87	0.1	330	20.2	3300	G	3293	26.54952	84.23096	Normal
27/8/22	16:48:30	87	0.1	270	20.2	2700	G	2775	26.54961	84.22997	Normal
27/8/22	16:49:5	87	0.1	300	20.2	3000	G	3034	26.5497	84.22892	Normal
27/8/22	16:49:5	87	0.1	340	10.1	3400	G	3379	26.55021	84.22806	Normal
27/8/22	16:49:41	87	0.1	370	10.1	3700	G	3637	26.55058	84.22712	Normal
IRI AVERAGE								3169.5			

$$Y = 0 * X^2 + 0.862 * X + 448.5$$

$$X = 3700$$

$$Y = 3637$$


(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

15/10/22
15/10/22

15/10/22

Executive Engineer
Rural Works Department
Works Div Gopetgaon

File :E:\STECO-USB-GPS V1_1\27081858.Xls, Section No. :87, Eqn : $Y = 0 * X^2 + 0.862 * X + 448.5$
 Name of Customer :M/S Sri Krishna Construction Company, Name of Work/ Road :Semra Baniya Chappar, Lab Job

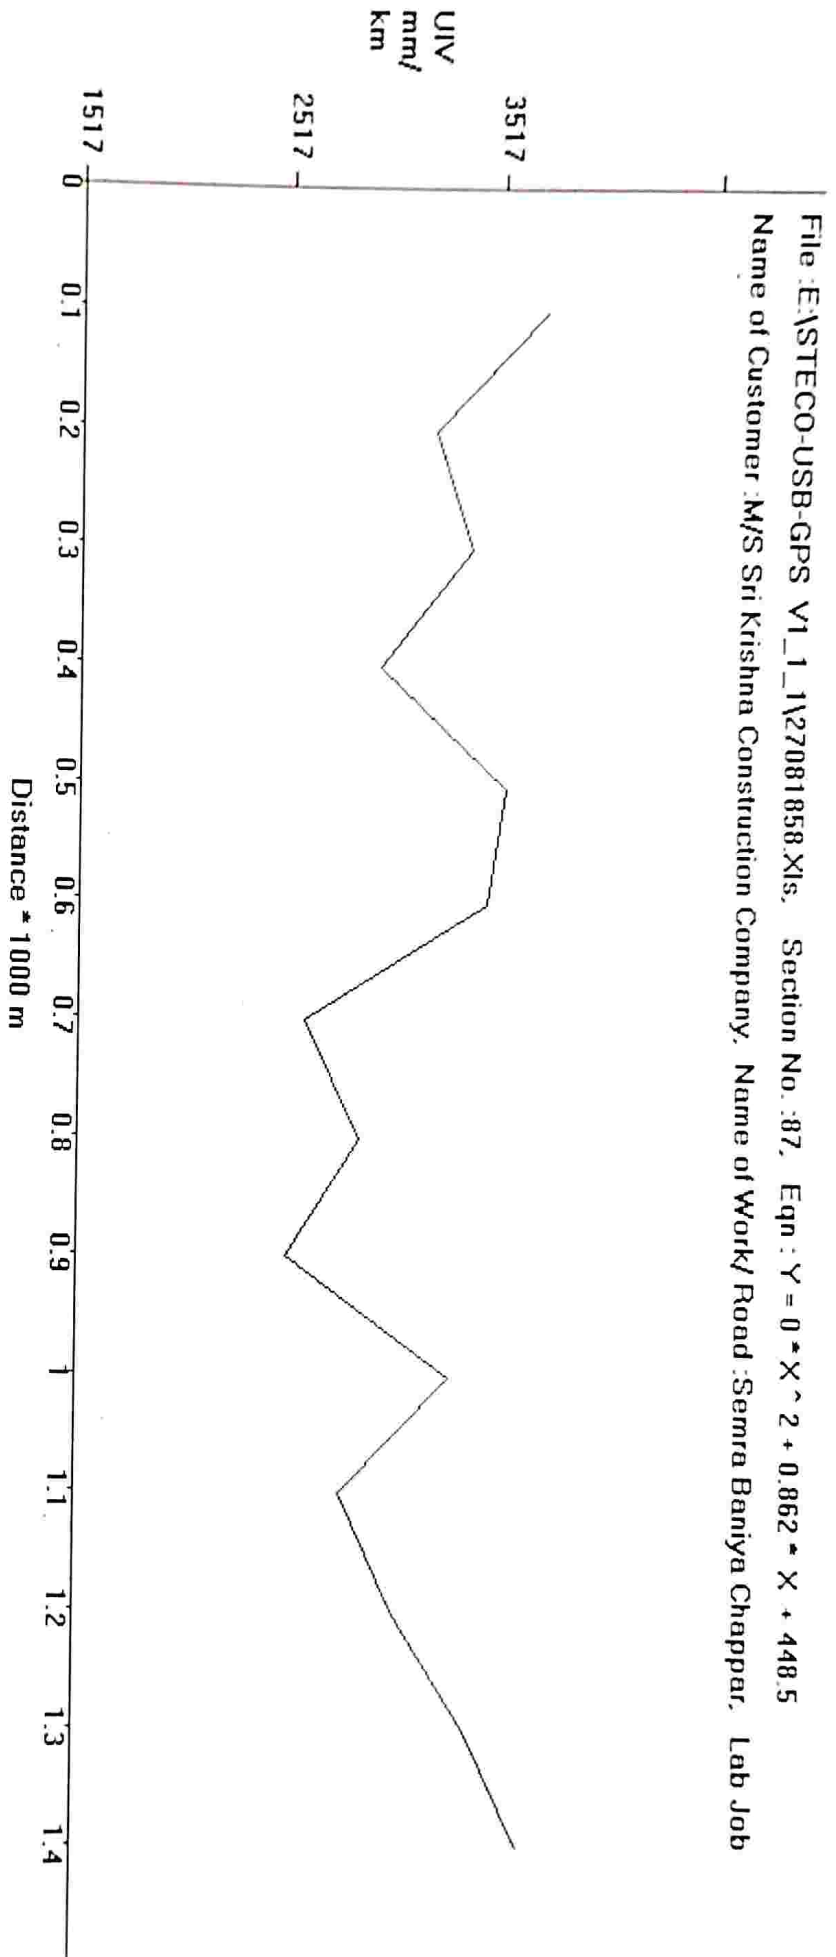

[Signature]
 15.11.37
 15.37

[Signature]
 15.11.37

[Signature]
 15.10.22
 Executive Engineer
 Rural Works Department
 VV.M.K. Div Goraiyaur-1
