

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सिमरी बख्तियारपुर।

पत्रांक— 2537 अ/प्र

दिनांक— 24/11/2022

प्रेषक:—

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल सिमरी बख्तियारपुर।

सेवा में,

नोडल पदाधिकारी,
MR 3054,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय:—


नई अनुरक्षण नीति 2018 शीर्ष अंतर्गत वित्तीय वर्ष 2020-21 एवं 2021-22 में व्यय हेतु
अनुरक्षण मद में आवंटन की मांग।

महाशय,

उपर्युक्त विषयक नई अनुरक्षण नीति 2018 शीर्ष अंतर्गत वित्तीय वर्ष 2020-21 एवं
2021-22 में व्यय हेतु अनुरक्षण मद में संलग्न विवरणी के अनुसार रुपये 12,74,871.00 (बारह लाख
चौहत्तर हजार आठ सौ एकहत्तर रुपये) मात्र का आवंटन उपलब्ध कराने की कृपा की जाय, ताकि किये
गये कार्यों का भुगतान किया जा सके।

अनुलग्नक:— यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, सिमरी बख्तियारपुर।

24/11/22

Maintenance Requisition for Scheme Head MR(3054) Under Bihar Rural Road Maintenance Policy- 2018
Name of Work Division:- Siarti Bakharyarpur

Road Details		Road Name		Batch No	Project ID	Actual Date of Completion	A. A. Details		Agreement Details					Legenth	Actual Maintenance Expenditure					Length as Per Bump Report 1st Year	IRI As per Bump Report	Current Demand for Maintenance Amount (in Lac)						Remarks																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
							Main wok Amount	Maintenance Amount	Maintenance of Agreement Amount 1st Year	Agreement 2	Agreement 3	Agreement 4	Agreement 5		Total Maint. Amount	1st Year Maint. Exp.	2nd Year Maint. Exp.	3rd Year Maint. Exp.	4th Year Maint. Exp.			5th Year Maint. Exp.	Total Maint. Exp.	1st Quarter	2nd Quarter	3rd Quarter	4th Quarter		5th Quarter	6th Quarter	Total																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
1		Amoja - Durgapur	RM/SA/SIM /19/0011	20904302013		30/05/2021	116.73000	60.25000	116.65300	11.83341	11.83341	11.83341	11.83341	11.83341	59.16705	6.125	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0</


 Executive Engineer
 RWD Work Division
 Siarti Bakharyarpur

STANDARD FORMAT FOR QUARTERLY STATEMENT

PIU NAME- RWD Simri Bakhtiyarpur 2nd Quarter (31-08-2021 to 30-11-2021)

1	Name of the Road	Amoja - Durgapur		
2	Batch No / Package no	RM/SA/sim/19/0011		
3	Project ID	20904302013		
4	Total Length of Road (in Km)	6.125		
5	Length of Road to Meet Required Service Level [Completed Length] (in KM) [1]	6.125		
6	No of Total Quarter (ie 3 Months as a unit) in 5 years.	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	59.16705 Lakh		
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	2.95835 Lakh		

Compliance criteria	Standard job Description	Non- Compliance		Reduction Payment [6] = [3] / [1] * [2] * [4]
		Length Non- Compliance [3]	Weighted Value for Payment Reduction (%) [4]	
1	PAVED ROADS (CARRIAGEWAY)	0.00	60%	0.00
2	SHOULDERS AND EMBANMENTS	0.00	10%	0.00
3	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00	15%	0.00
4	SIGNAGE AND ROAD SAFETY	0.00	10%	0.00
5	VEGETATION	0.00	5%	0.00
TOTAL PAYMENT REDUCATION FOR THE QUARTER (in Lakh) [5]				0.00
TOTAL PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				2.95835

Bijay Kumar Singh
 Date of inspection by E / I his agent prepared by Contractor's self Control unit

RAM KUMAR.
 Name and Designation of person inspecting road

[Signature]
 08/11/2021
 Signature of person inspecting road

[Signature]
 29/11/21
 Certify by E / I [signature] Date:-

STANDARD FORMAT FOR QUARTERLY STATEMENT

PIU NAME- RWD Simri Bakhtiyarpur 1st Quarter (31-05-21 to 30-08-21)

1	Name of the Road	Amoza - Durgapur		
2	Batch No / Package no	RM/SA/Sim/19/0011		
3	Project ID	20904302013		
4	Total Length of Road (in Km)	6.125 Km		
5	Length of Road to Meet Required Service Level [Completed Length] (in KM) [1]	6.125 Km		
6	No of Total Quarter (ie 3 Months as a unit) in 5 years.	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	59.16705 Lakh		
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	2.95835 Lakh		
Compliance criteria	Standard job Description	Non- Compliance		Reduction Payment [6] = [3] / [1] * [2] * [4]
		Length Non- Compliance [3]	Weighted Value for Payment Reduction (%) [4]	
1	PAVED ROADS (CARRIAGEWAY)	0.00	60%	0.00
2	SHOULDERS AND EMBANKMENTS	0.00	10%	0.00
3	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00	15%	0.00
4	SIGNAGE AND ROAD SAFETY	0.00	10%	0.00
5	VEGETATION	0.00	5%	0.00
TOTAL PAYMENT REDUCATION FOR THE QUARTER (in Lakh) [5]				0.00
TOTAL PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				2.95835

Signature of E/I

Date of inspection by E / I his agent prepared by Contractor's self Control unit

RAM KUMAR.
Name and Designation of person inspecting road

Signature of person inspecting road
08/11/2022
Signature of person inspecting road

Signature of E/I
23/11/22
Certify by E / I [signature] Date:-

Government of Bihar
OM01
Rural Works Department

ORDINARY MAINTENANCE INSPECTION REPORT
Form OM01

Date:

Road From: Amoia - Durgapur
Length of Road: 6.125 km
Period: 1st Quarter (31-05-2021 to 30-08-2021)
Inspector: J.E. RWD, Sub Division Sonbhadra

To: **EXECUTIVE ENGINEER,**
RWD, Works Division, Simr Bakhtiyarpur
Position: J.E.

No.	Name	Work Units	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed Pavement												
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Pothole found.
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Surface Depression and Rut Patching found.
OM 103	Crack Sealing	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Crack Sealing found
	Surface Treatment												
OM104	(a) Loss of Aggregate	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Loss of Aggregate (Surface)
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Bleeding/Flushing required.
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Crocodile cracking found.
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Edge Repair required.
OM106	Digouts	m2	N/A	N/A	N/A	N/A	N/A	N/A	N/A				
OM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A	N/A	N/A	N/A				
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-Off	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Edge Drop-Off required.
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Roughness, Scouring or Potholes required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Holding Water Found.
OM202	Embankment Repair	m3	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Embankment Repair required.
	Other activities												
OM 300	Drainage including culverts major and minor br												
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A	N/A	N/A	N/A				Not required.
OM302	Culvert Cleaning	No.	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not required.
OM303	Culvert and Pit Repair	m3	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not required.
	Other activities	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				

Bidder

Executive Engineer, Work Division

Standard work item		Work Units	Units of work required in each kilometre										Comments
No.	Name		1	2	3	4	5	6	7	8	9	10	
OM400 Vegetation	Grass Control												
	a) Roadside - General Tidy	Ha	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not required
	b) Clear near safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not required
OM402	Tree and Shrub Management												
	Cutting Tree	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not required
	Cutting Shrubs	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not required
	Other activities												
OM500 Safety Signage and Road													
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not required
OM502	Guard stones	Lm	N.A	N.A	N.A	N.A	N.A	N.A	N.A				Not required
OM503	Distance stones	No	N.A	N.A	N.A	N.A	N.A	N.A	N.A				Not required
OM504	Road markings	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not required
	Other activities												

Bigdeli Koo Singh

[Signature of Contractor/ Authorized representative]

Date

Time

Place

08/11/2022
S

08/11/22
A.E.

Government of Bihar
OM01
Rural Works Department

ORDINARY MAINTENANCE INSPECTION REPORT
Form OM01

Road From: Am03a - Durgapur

Length of Road: 6.125 km

Period: 2nd Quarter (31-08-2021 to 30-11-2021)

Inspector: J.E. RWD, Sub Division Sonbadga

Date:

To: **EXECUTIVE ENGINEER,**
RWD, Works Division, Simr Bakhtyarpur
Position: **J.E.**

No.	Name	Work	Unit of work required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed Pavement												
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Pothole found.
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Surface Depression and Rut Patching found.
OM 103	Crack Sealing	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Crack Sealing found
OM104	Surface Treatment												
	(a) Loss of Aggregate	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Loss of Aggregate (Surface
	(b) Bleeding/ Flushing	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Bleeding/Flushing required.
OM105	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Crocodile cracking found.
	Edge Repair	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Edge Repair required.
OM106	Digouts	m2	N.A	N.A	N.A	N.A	N.A	N.A	N.A				
OM107	Concrete Pavement	m3	N.A	N.A	N.A	N.A	N.A	N.A	N.A				
Other activities													
OM200 Shoulder													
OM201	Unsealed Shoulder												
	(a) Edge Drop-Off	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Edge Drop-Off required.
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Roughness, Scouring or Potholes required
OM202	(c) Holding water	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Holding Water Found.
	Embankment Repair	m3	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Embankment Repair required.
Other activities													
OM 300 Drainage including culverts major and minor br													
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A	N.A	N.A	N.A				Not required.
OM302	Culvert Cleaning	No.	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not required.
OM303	Culvert and Pit Repair	m3	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not required.
Other activities		m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				

Bidder

Executive Engineer, Work Division

Standard work item		Work	Units of work required in each kilometre										Comments
No.	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM400 Vegetation													
OM401	Grass Control												Not required
	a) Roadside - General Tidy	Ha	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not required
	b) Clear near safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil	Nil	Nil	Nil				
	Tree and Shrub Management												Not required
	Cutting Tree	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil			Not required
OM402	Cutting Shrubs	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil				
	Other activities												
OM500 Safety Signage and Road													
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil			Not required
OM502	Guard stones	Lm	N.A	N.A	N.A	N.A	N.A	N.A	N.A	N.A			Not required
OM503	Distance stones	No	N.A	N.A	N.A	N.A	N.A	N.A	N.A	N.A			Not required
OM504	Road markings	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil			Not required
	Other activities												

Signature of Contracted Authority representative

Signature

Date

Time

Place

Signature of Contractor/ Authorized representative

Date

Time

Place

Signature
08/11/2022
JG

Signature
08/11/22
A.E

Name of work : Amoja - Durgapur

Name of customer : Ms Bijay Kumar Singh

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

14/08/22	15:45:03	34	100	4400	24.0 cm	27.6 Km/Hr	2400.0 mm/Km	2330	3.21	Good	25.7613211	N	86.8269053	E	Normal
14/08/22	15:45:17	34	100	4500	18.0 cm	27.2 Km/Hr	1800.0 mm/Km	1770	2.51	Good	25.7613211	N	86.8269053	E	Normal
14/08/22	15:45:31	34	100	4600	17.0 cm	24.6 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.7613211	N	86.8269053	E	Normal
14/08/22	15:45:45	34	100	4700	20.0 cm	25.9 Km/Hr	2000.0 mm/Km	1956	2.75	Good	25.7613211	N	86.8269053	E	Normal
14/08/22	15:45:57	34	100	4800	24.0 cm	29.1 Km/Hr	2400.0 mm/Km	2330	3.21	Good	25.7613211	N	86.8269053	E	Normal
14/08/22	15:46:16	34	100	4900	20.0 cm	19.9 Km/Hr	2000.0 mm/Km	1956	2.75	Good	25.7613211	N	86.8269053	E	Normal
14/08/22	15:45:45	34	100	5000	20.0 cm	25.9 Km/Hr	2000.0 mm/Km	1956	2.75	Good	25.7613211	N	86.8269053	E	Normal
14/08/22	15:46:36	34	100	5100	17.0 cm	18.0 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.7613211	N	86.8269053	E	Normal
14/08/22	15:46:52	34	100	5200	15.0 cm	22.2 Km/Hr	1500.0 mm/Km	1489	2.16	Good	25.7615805	N	86.8403635	E	Normal
14/08/22	15:47:05	34	100	5300	19.0 cm	27.0 Km/Hr	1900.0 mm/Km	1863	2.63	Good	25.7614965	N	86.8408061	E	Normal
14/08/22	15:47:28	34	100	5400	19.0 cm	16.9 Km/Hr	1900.0 mm/Km	1863	2.63	Good	25.7614965	N	86.8408061	E	Normal
14/08/22	15:47:45	34	100	5500	12.0 cm	20.9 Km/Hr	1200.0 mm/Km	1209	1.79	Good	25.7614965	N	86.8408061	E	Normal
14/08/22	15:47:56	34	100	5600	16.0 cm	31.5 Km/Hr	1600.0 mm/Km	1563	2.28	Good	25.7614965	N	86.8408061	E	Normal
14/08/22	15:47:45	34	100	5700	12.0 cm	20.9 Km/Hr	1200.0 mm/Km	1209	1.79	Good	25.7614965	N	86.8408061	E	Normal
14/08/22	15:48:18	34	100	5800	17.0 cm	16.0 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.7614965	N	86.8408061	E	Normal
14/08/22	15:48:39	34	100	5900	24.0 cm	17.8 Km/Hr	2400.0 mm/Km	2330	3.21	Good	25.7614965	N	86.8408061	E	Normal
14/08/22	15:48:53	34	100	6000	15.0 cm	24.9 Km/Hr	1500.0 mm/Km	1489	2.16	Good	25.7614965	N	86.8408061	E	Normal
14/08/22	15:49:07	34	100	6100	12.0 cm	26.2 Km/Hr	1200.0 mm/Km	1209	1.79	Good	25.7614965	N	86.8408061	E	Normal

Name of work : Amoja - Durgapur

Name of customer : Ms Bijay Kumar Singh

(R) Rural Road

Good

Average

Poor

< 4000

4001 - 5000

> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMPI(m)	Speed(Km/Hr)	Ull(m/Km)	Corrected Ull (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
14/08/22	15:34:42	34	100	100	17.0 cm	2.3 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.7459116	N	86.8074732	E	Normal
14/08/22	15:34:58	34	100	200	19.0 cm	21.6 Km/Hr	1900.0 mm/Km	1863	2.63	Good	25.7459116	N	86.8074732	E	Normal
14/08/22	15:35:11	34	100	300	15.0 cm	27.9 Km/Hr	1500.0 mm/Km	1489	2.16	Good	25.7459116	N	86.8074732	E	Normal
14/08/22	15:35:26	34	100	400	12.0 cm	25.6 Km/Hr	1200.0 mm/Km	1209	1.79	Good	25.7486143	N	86.8094569	E	Normal
14/08/22	15:35:41	34	100	500	15.0 cm	23.1 Km/Hr	1500.0 mm/Km	1489	2.16	Good	25.7487516	N	86.8094721	E	Normal
14/08/22	15:35:54	34	100	600	19.0 cm	27.2 Km/Hr	1900.0 mm/Km	1863	2.63	Good	25.7487516	N	86.8094721	E	Normal
14/08/22	15:36:06	34	100	700	10.0 cm	29.7 Km/Hr	1000.0 mm/Km	1022	1.54	Good	25.7487516	N	86.8094721	E	Normal
14/08/22	15:36:17	34	100	800	17.0 cm	34.5 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.7518320	N	86.8094721	E	Normal
14/08/22	15:36:27	34	100	900	28.0 cm	32.7 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.7530489	N	86.8095255	E	Normal
14/08/22	15:36:38	34	100	1000	19.0 cm	35.0 Km/Hr	1900.0 mm/Km	1863	2.63	Good	25.7530489	N	86.8095255	E	Normal
14/08/22	15:36:59	34	100	1100	28.0 cm	17.4 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.7530489	N	86.8095255	E	Normal
14/08/22	15:37:34	34	100	1200	33.0 cm	10.4 Km/Hr	3300.0 mm/Km	3171	4.23	Good	25.7552996	N	86.8098612	E	Normal
14/08/22	15:37:56	34	100	1300	22.0 cm	16.3 Km/Hr	2200.0 mm/Km	2143	2.98	Good	25.7564344	N	86.8103190	E	Normal
14/08/22	15:38:14	34	100	1400	36.0 cm	19.4 Km/Hr	3600.0 mm/Km	3451	4.57	Good	25.7574759	N	86.8111964	E	Normal
14/08/22	15:38:34	34	100	1500	20.0 cm	18.1 Km/Hr	2000.0 mm/Km	1956	2.75	Good	25.7582293	N	86.8117991	E	Normal
14/08/22	15:38:58	34	100	1600	23.0 cm	15.3 Km/Hr	2300.0 mm/Km	2237	3.1	Good	25.7589941	N	86.8124018	E	Normal
14/08/22	15:39:23	34	100	1700	31.0 cm	14.4 Km/Hr	3100.0 mm/Km	2984	4.01	Good	25.7596006	N	86.8127909	E	Normal
14/08/22	15:39:36	34	100	1800	13.0 cm	26.4 Km/Hr	1300.0 mm/Km	1303	1.91	Good	25.7599336	N	86.8130198	E	Normal
14/08/22	15:39:23	34	100	1900	31.0 cm	14.4 Km/Hr	3100.0 mm/Km	2984	4.01	Good	25.7596006	N	86.8127909	E	Normal
14/08/22	15:39:48	34	100	2000	18.0 cm	29.4 Km/Hr	1800.0 mm/Km	1770	2.51	Good	25.7607508	N	86.8132487	E	Normal
14/08/22	15:40:04	34	100	2100	21.0 cm	23.4 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.7615805	N	86.8144846	E	Normal


Name of work : Anjoia - Durgapur		
Name of customer : Ms Bijay Kumar Singh		
(R)Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

14/08/22	15.40.27	34	100	2200	16.0 cm	15.7 Km/Hr	1600.0 mm/Km	1583	2.28	Good	25.7620573	N	86.8149424	E	Normal
14/08/22	15.40.54	34	100	2300	23.0 cm	13.7 Km/Hr	2300.0 mm/Km	2237	3.1	Good	25.7625990	N	86.8153315	E	Normal
14/08/22	15.41.18	34	100	2400	23.0 cm	14.7 Km/Hr	2300.0 mm/Km	2237	3.1	Good	25.7624769	N	86.8166666	E	Normal
14/08/22	15.41.33	34	100	2500	16.0 cm	23.4 Km/Hr	1600.0 mm/Km	1583	2.28	Good	25.7624273	N	86.8172999	E	Normal
14/08/22	15.41.47	34	100	2600	16.0 cm	26.7 Km/Hr	1600.0 mm/Km	1583	2.28	Good	25.7624598	N	86.8179713	E	Normal
14/08/22	15.42.00	34	100	2700	16.0 cm	27.0 Km/Hr	1600.0 mm/Km	1583	2.28	Good	25.7625170	N	86.8197260	E	Normal
14/08/22	15.42.13	34	100	2800	34.0 cm	27.0 Km/Hr	3400.0 mm/Km	3264	4.34	Good	25.7625341	N	86.8204890	E	Normal
14/08/22	15.42.25	34	100	2900	20.0 cm	30.9 Km/Hr	2000.0 mm/Km	1956	2.75	Good	25.7624769	N	86.8212748	E	Normal
14/08/22	15.42.36	34	100	3000	18.0 cm	32.7 Km/Hr	1800.0 mm/Km	1770	2.51	Good	25.7622805	N	86.8221674	E	Normal
14/08/22	15.42.50	34	100	3100	28.0 cm	26.5 Km/Hr	2800.0 mm/Km	2704	3.67	Good	25.7620783	N	86.8230143	E	Normal
14/08/22	15.43.01	34	100	3200	21.0 cm	33.1 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.7616949	N	86.8239909	E	Normal
14/08/22	15.43.10	34	100	3300	11.0 cm	36.3 Km/Hr	1100.0 mm/Km	1116	1.67	Good	25.7615805	N	86.8249522	E	Normal
14/08/22	15.43.21	34	100	3400	14.0 cm	33.4 Km/Hr	1400.0 mm/Km	1386	2.03	Good	25.7614794	N	86.8259593	E	Normal
14/08/22	15.43.31	34	100	3500	16.0 cm	36.7 Km/Hr	1600.0 mm/Km	1583	2.28	Good	25.7613211	N	86.8269053	E	Normal
14/08/22	15.43.41	34	100	3600	11.0 cm	34.5 Km/Hr	1100.0 mm/Km	1116	1.67	Good	25.7613211	N	86.8269053	E	Normal
14/08/22	15.43.21	34	100	3700	14.0 cm	33.4 Km/Hr	1400.0 mm/Km	1386	2.03	Good	25.7614794	N	86.8259593	E	Normal
14/08/22	15.44.02	34	100	3800	12.0 cm	18.8 Km/Hr	1200.0 mm/Km	1209	1.79	Good	25.7613211	N	86.8269053	E	Normal
14/08/22	15.44.15	34	100	3900	14.0 cm	27.0 Km/Hr	1400.0 mm/Km	1386	2.03	Good	25.7613211	N	86.8269053	E	Normal
14/08/22	15.44.28	34	100	4000	14.0 cm	28.5 Km/Hr	1400.0 mm/Km	1386	2.03	Good	25.7613211	N	86.8269053	E	Normal
14/08/22	15.44.40	34	100	4100	21.0 cm	29.4 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.7613211	N	86.8269053	E	Normal
14/08/22	15.44.40	34	100	4200	21.0 cm	29.4 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.7613211	N	86.8269053	E	Normal
14/08/22	15.44.50	34	100	4300	18.0 cm	34.9 Km/Hr	1800.0 mm/Km	1770	2.51	Good	25.7613211	N	86.8269053	E	Normal

08/11/2022
J E

08/11/22
J E

NTGraph ActiveX Control
 mer: Ms. Bijay Kumar Singh , Machine no: 19215 , Road: Amoja - Durgapur , Date: 25/08/22 , Section No: 34 , Equation: $Y=0.934$

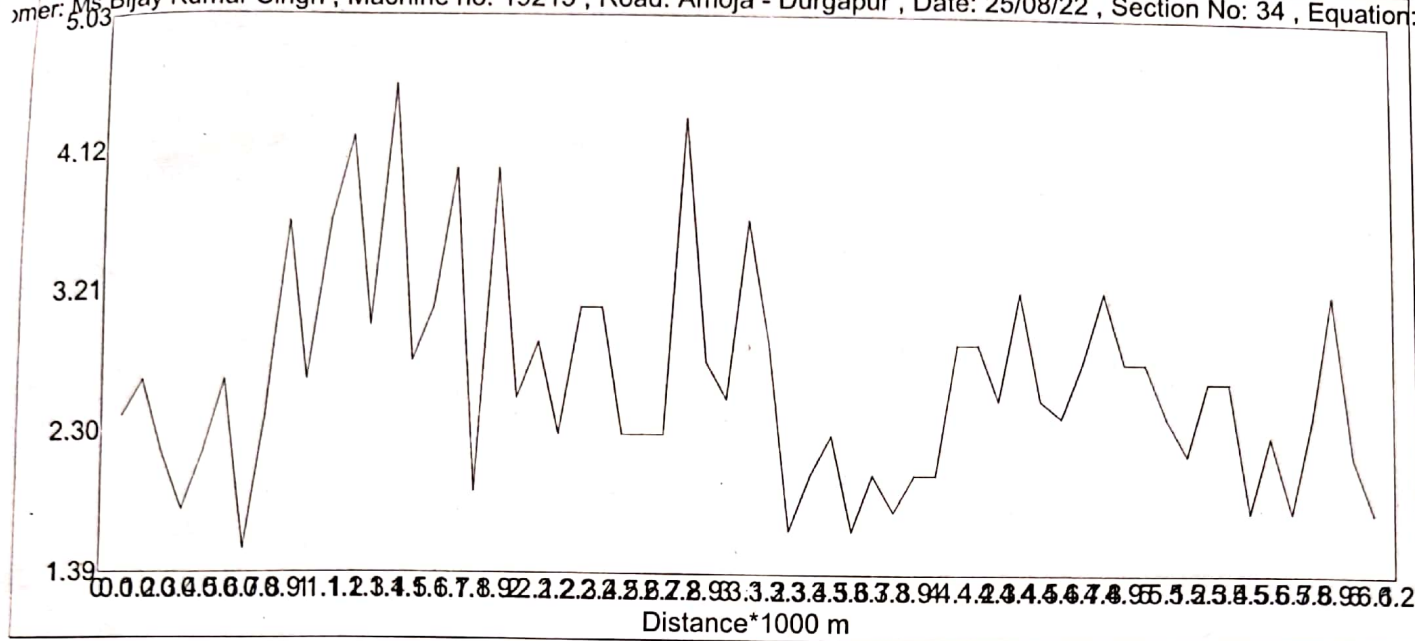

Handwritten signature
 08/11/2022
 JE

Handwritten signature
 08/11/22
 A.E.

Handwritten signature
 23/11/22
 BA
