

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पालीगंज।

पत्रांक:- 1609 (अभियंता)

पालीगंज/दिनांक:- 13/12/22

प्रेषक :

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
-सह-सचिव,
बिहार ग्रामीण पथ विकास, अभिकरण
ग्रामीण कार्य विभाग, पटना।

विषय:- शीर्ष-MR, 3054 Under-Bihar Rural Road Maintenance Policy-2018 योजना अन्तर्गत आवंटन का
अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष-MR, 3054 Under-Bihar Rural Road
Maintenance Policy-2018 योजना अन्तर्गत पथों का अधियाचना का माँग विहित प्रपत्र में तैयार कर
Signed Hard Copy of Recorded IRI के साथ अधियाचना हेतु भेजी जा रही है।

अतः अनुरोध है कि उक्त योजना का आवंटन उपलब्ध करने की कृपा की जाय, ताकि संवेदक
का भुगतान हो सके।

अनु:- यथोक्त।

विश्वासभाजन



13/12/22

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल पालीगंज।


13/12/2022

Requisition Format for Scheme Head -Mm (3054) Under Bihar Rural Road Maintenance Policy 2018(Initial Rectification and surface Renewal)
Name Of Work division- Paliganj

Requisition Format for Scheme Head -MR (3054) Under Bihar Rural Road Maintenance Policy 2018(Initial Rectification and Surface Rectification)																		
Name Of Work Division- Paliganj																		
Sl	Package No	Name Of Road	Project ID as per MIS	Administra the Approval (AA) Letter No & Date	Administrative		Agreement Amount		Date of completion as per Agreement	Actual Date of completion	Value of Irr(in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to - date expenditure as per MIS (in Lakh)	Requisito n against work done (in Lakh)	Remarks	
					Length (in km)	Amount of (in lakh)	Initial Rectificati on with Surface Renewal (in lakh)	5 Year Maintena nee (in lakh)										Agremen t no & Date
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
MR-N/19-20	MASS/ID- SARDA	SAIDABAD	NEA22000897	lt no 6459 dt 13.12.2019	1.0	40.58600	30.95700	10.67190	05/MBD/ 2020-21 & 18.06.202	17.03.2021	24.06.2022	2.57800 (SDBC)	25 mm	5.01%	17.32894	17.32894	3.75749	Work is Completed as per specification & Verification of Surface by a bump indicator machine 100% Measurement decided by AE & 50% by EE
MR-N/19-20	Sahranpur - Mahaspura via Aachouli		NEA220001592	lt no 6459 dt 13.12.2019	2.83	80.28300	77.10000	29.80626	05/MBD/ 2020-21 & 18.06.202	17.03.2021	28.08.2022	4.565185 (SDBC)	25 mm	5.11%	66.81393	66.81393	0.70744	Work is Completed as per specification & Verification of Surface by a bump indicator machine 100% Measurement decided by AE & 50% by EE
MR-N/19-20	Palma jila antargat nauksipur prastand ke antargat nauksipur P.W.D path se mahadali total tak path himsaan.		101005059001	lt no 6459 dt 13.12.2019	1.574	33.03300	39.89900	16.71981	05/MBD/ 2020-21 & 18.06.202	17.03.2021	26.08.2022	4.11 (SDBC)	25 mm	5.07%	32.77399	32.77399	3.22657	Work is Completed as per specification & Verification of Surface by a bump indicator machine 100% Measurement decided by AE & 50% by EE

27/12/22
Divisional Accounts Officer
Rural Work Department
Works Division Paliganj

27/12/22
Executive Engineer
Rural Works Deptt.
Work Division Paliganj

01/12/2022

FORM GFR 19-A


(See Government of India's Decision (1) below Rule-150)
Form of utilisation Certificate up to the end of 5th December 2022

PIU: RWD Works Division , Paliganj

Sl No.	Name of Scheme	Sanction No. & Date with Amount	Amount Received (In Rs.)	Particulars
1	Construction of Rural roads under MR New maintenance policy		236259347.00	Certified that out of Rs 236259347.00 received upto the year 2022-23 in favour of Ex. Engineer, RWD, Works Div. Paliganj Bihar a sum of Rs 232311988.00 has been utilized for the purpose of const of road under Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 3947359.00 remaining unutilized at the end to the period under
Total			236259347.00	

2. Certified that I have satisfied myself that the conditions of which the grants sanction Sanctioned have been duly fulfilled/are being fulfilled and I have exercised the checks to see the money was actually utilised for the purpose for which it was sanctioned.


07/12/22
Divisional Accounts Officer
Rural Work Department
Works Division Paliganj


07/12/22
Executive Engineer
Rural works Deptt.
Works Division, Paliganj


NAME OF THE ROAD : SAHAR RAMPUR TO MAHAJ, JBA VIA ANCHALI

LENGTH OF THE ROAD : 2.230 KM

PACKAGE NO. : MR-N/19-20/PALGAH/08

DIVISION : PALGAH

BLOCK : KALUPATPUR

CONTRACTOR : SANTOSH KUMAR

Date	Time	Section	Length in km	Bumps in mm	Speed km/hr	OR mm/hr	UVI mm/hr	CATEGORY	IRI	Latitude	Longitude	Event		
10/1/21	10:13:16	43	0.1	330	0.1	3300	3367	G	4.6	25.448727	84.916178	Speed Breaker	X = 3100	
10/1/21	10:13:38	43	0.1	310	20.2	3100	3180	G	4.74	25.448942	84.915335	Normal	Y = 3180	
10/1/21	10:14:0	43	0.1	350	30.1	3500	3535	G	5.01	25.449145	84.914258	Normal		
10/1/21	10:14:10	43	0.1	370	30.3	3700	3741	G	4.9	25.449235	84.913167	Normal	(R) RUWA ROAD	
10/1/21	10:14:20	43	0.1	290	20.2	2900	2937	G	4.01	25.449442	84.912355	Normal	UVI 5	Average
10/1/21	10:14:34	43	0.1	360	20.2	3600	3640	G	4.73	25.449595	84.911326	Normal	UVI 5	5001-5000-5001
10/1/21	10:14:48	43	0.1	330	30.3	3300	3367	G	4.6	25.449799	84.910187	Normal		
10/1/21	10:15:4	43	0.1	340	30.3	3400	3450	G	4.57	25.450135	84.916435	Normal		
10/1/21	10:15:19	43	0.1	300	30.3	3000	3086	G	4.13	25.451175	84.918096	Normal		
10/1/21	10:15:24	43	0.1	280	30.3	2800	2835	G	4.03	25.451515	84.918535	Normal		
10/1/21	10:15:34	43	0.1	360	20.2	3600	3648	G	4.79	25.451647	84.917928	Normal		
10/1/21	10:15:48	43	0.1	320	20.3	3200	3273	G	4.15	25.45311	84.917772	Normal		
10/1/21	10:16:0	43	0.1	360	30.2	3600	3643	G	4.79	25.453753	84.916347	Normal		
10/1/21	10:16:14	43	0.1	340	30.3	3400	3460	G	4.7	25.454102	84.915522	Normal		
10/1/21	10:16:24	43	0.1	320	30.2	3200	3241	G	4.5	25.454703	84.914662	Normal		
10/1/21	10:16:34	43	0.1	320	30.3	3200	3273	G	4.75	25.455165	84.91317	Normal		
10/1/21	10:16:50	43	0.1	290	30.3	2900	2997	G	4.01	25.455595	84.912962	Normal		
10/1/21	10:17:0	43	0.1	270	30.3	2700	2741	G	4.9	25.455873	84.911968	Normal		
10/1/21	10:17:10	43	0.1	300	20.2	3000	3086	G	4.13	25.456348	84.911497	Curve		

R-72007

10/1/19

8.8 km

10/01/21

A.E.

Dr. Executive Engineer

Date	Time	Section	Length	Bumps	Speed	OR	UIV	CATEGORY	IRI	Latitude	Longitude	Event				
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD								
10/1/21	10:17:25	43	0.1	320	30.3	3200	3273	G	4.35	25.457272	84.91182	Normal				
10/1/21	10:17:35	43	0.1	340	30.3	3400	3460	G	4.57	25.45822	84.91178	Normal				
10/1/21	10:17:45	43	0.1	330	20.2	3300	3367	G	4.46	25.45863	84.91195	Normal				
10/1/21	10:18:0	43	0.1	380	20.2	3800	3835	G	5.01	25.458777	84.910202	Normal				
10/1/21	10:18:25	43	0.1	320	30.3	3200	3273	G	4.35	25.459287	84.908298	Normal				
10/1/21	10:18:45	43	0.02	250	30.3	3100	3180	G	4.24	25.45939	84.907895	Normal				
TOTAL			2.62	9110	696.9	91700	93337		123.26	687.24908	2292.74967					
AVERAGE						3396.295	3456.926		4.565185							

R. T. 10/1/21
J.E.

8.5 km
10/6/21
A.E.

10-02-21
Engineer
NOTE

Name of Customer :	SANTOSH KR
Name of Work/	SAHAR RAMPUR TO MAHAUF
Road :	
Lab Job number :	
Date :	10/01/2021
Section No.	43

Test Date :	10-01-2021	Road Name :	MAHAUF RAMPUR VIA ANCHIMULU
Machine No :		Road Type :	R9 RURAL ROAD
Start S No :		Side :	
Start E No :		Interval	
Weather :		UIV Range :	1992 To 5000 mm/Km
Start Location :		Dist Range :	0 To 7.8 0.1 1000 m
End Location :		Equation :	


Print Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\SHAZID\Desktop\13 DEC 2020\10 JAN 2021\13.Xls, Section No. : 43, Eqd :

Name of Customer : SANTOSH KR, Name of Work/ Road : SAHAR RAMPUR TO MAHAUF RAMPUR VIA ANCHIMULU, Lab

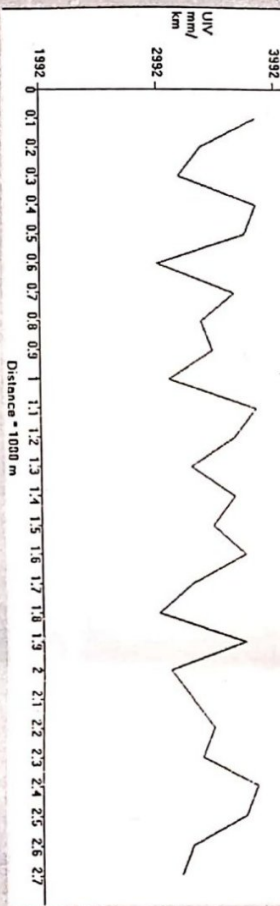

8/12/2021
10/01/21
T.E.

8.5 km
10/01/21
A.E.

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, क्षेत्रीय प्रयोगशाला, गुलजारबाग
पटना-800007

पत्रांक - १४/म.प्र.

पटना/दिनांक - 15.1.2021

प्रेषक,

कार्यपालक अभियंता

ग्रामीण कार्य विभाग

क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना -7

सेवा में,

कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रणालि ..सा.प्र.रा.ज......।

विषय :- जाँचफल प्रतिवेदन के संबंध में ।

प्रसंग :- AE, Nawabpur vide letter no - 38 dt 5.1.2021

महोदय,

उपर्युक्त विषयक के संबंध में जाँचफल प्रतिवेदन इस पत्र के साथ संलग्न कर आवश्यक कारवाई हेतु भेजा जा रहा है जो निम्न प्रकार है:-

Sahar Rampur to Mahaupura via Aulandh

MSS - Type B

SDR

Return to Central for SDR

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R.W.D. GULJARIBAGH, PATNA - 7

38

PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

15/01/2024

Name of Project/Road : Sahar Rampur to Mahajpura via Achanlli

Name of Scheme : M.R. 3551

Name of Agency : Sri Sanjesh Kumar

Nature of sample : Mix seal (13.2 mm to 0.075 mm)

Location : 1375 m

Date of Collection/Received : 7.1.2024

Ref : Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division - Neubabur

Date of Test : 12.1.2024

vide letter No : 38 Dt : 5.1.2024

Agreement No / Package No : 05 / M 20 / 0020 - 21

Sl No	A.I.V.
Average Test Value	Required Value(Max)
1	40%

Sl. No	Sieve Size in (mm)	Weight of Sample Taken Kgs 15.280				Required Value		Remarks
		Weight Retd.	% of Wt. Retained	% of Cumm. Retained	% of Passing	Type A	Type B	
1	13.2	0.00	0.00	0.00	100	-----	100	
2	11.2	0.359	2.35	2.35	97.65	100	88-100	
3	5.6	2.847	57.90	60.25	39.75	52-88	31-52	
4	2.8	2.529	16.55	76.80	23.20	14-38	5-25	
5	0.09	3.247	21.25	98.05	1.95	0-5	0-5	

[Signature]
12/1/2024
A.D.

[Signature]
12-10/2024
A.E.

[Signature]
12/1/2024
E.E.

Regional Laboratory
R.W.D. Guljaribagh patna - 7

Regional Laboratory
R.W.D. Guljaribagh patna - 7

Regional Laboratory
R.W.D. Guljaribagh patna - 7

Regional Laboratory
R.W.D. Guljaribagh patna - 7

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D. GULJARIBAGH, PATNA - 7
91 PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

Name of Project/Road :- Sahar Rampur to Mahatpura via Achanli
 Name of Scheme :- MR 354
 Name of Agency :- Sri Sanjesh Kumar
 Nature of sample : Semi Dense Bituminous Concrete Date of Collection/Received :- 7.1.2021
 Location :- 137507 Date of Test :- 12.1.2021
 Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division Maubattour
 vide letter No. 38 Dt. 5.1.2021
 Agreement No / Package No. : 85 / MRD / 2020-21

A.I.V.		Remarks
Average Test Value	Required Value max (%)	
<u> </u>	30 %	

Sl. No	Sieve Size in (mm)	Weight of Sample Taken kgs				Required Value	Remarks
		Weight Retd.	% of Wt. Retained	% of Cumm. Retained	% of Passing		
1	13.2	0.00	0.00	0.00	100	100	
2	9.5	0.620	3.80	3.80	96.20	90-100	
3	4.75	8.320	47.50	51.30	48.70	35-51	
4	2.36	3.251	18.45	69.75	30.25	24-39	
5	1.18	1.947	11.55	80.80	19.20	15-30	
6	0.300	1.313	7.45	88.25	11.75	9-19	
7	.075	1.436	8.15	96.40	3.60	3-8	

Patel 12/1/2021
 12/1/2021
Patel 12/1/2021
 12/1/2021

Lab. Regional Laboratory Regional Laboratory Regional Laboratory
 Guljaribagh Patna - 7 R.W.D. Guljaribagh Patna - 7 R.W.D. Guljaribagh Patna - 7 R.W.D. Guljaribagh Patna - 7

98

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D. GULZARRAH, PATNA.

Name of Project/Road :- Sahar Rampur to Mahajpura via G. S. M. S.
 Name of Scheme :- M. R. 3034
 Name of Agency :- Govt. Samarth Kumar
 Nature of sample :- Bitumen Content for S. S. C.
 Location :- 1275 M

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division Naubatta vide letter NO 38 Dt 5.1.2021
 Agreement No / Package No. :- 05/mao/2020-21

Date of Collection Received 5.1.2021
 Date of Test 5.1.2021

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	515.00	506.00	501.00	
2	Wt. of Dry chips after extraction (b)	488.46	480.00	473.00	
3	Percentage of bitumen (in the mix) $[(a-b) \times 100] / a$ (%)	515	500	501	
4	Average % bitumen		501		

[Signature]
 Regional Laboratory
 R. W. D. Gulzarrah, Patna

[Signature]
 Regional Laboratory
 R. W. D. Gulzarrah, Patna

[Signature]
 Regional Laboratory
 R. W. D. Gulzarrah, Patna

Date 15/11/2021

Name of Project/Road :- Sahar Road Roorpur to Mahabubnagar via Akaltit

Name of Scheme :- MR-3054 Bituminous mix

Name of Agency :- S&P Sandesh Kumar

Nature of sample :- Bituminous Content for S.M.C

Location :- 1375 M Date of Collection/Received :- 11.11.2021

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division. Mahabubnagar vide letter No. 38 Dt. 11.11.2021

Agreement No / Package No. :- 65/MSB/2020-21

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)				
2	Wt. of Dry chips after extraction (b)	515.00	506.00	509.00	
3	Percentage of bitumen (in the mix) [(a-b)*100]/a (%)	48.46	48.90	48.20	
4	Average % bitumen	S-15	S-0	S-13	

Regional Laboratory R.W.D. Guljarbogh patna - 7
A.D. 15/11/2021
Regional Laboratory R.W.D. Guljarbogh patna - 7
A.E. 15/11/2021
Regional Laboratory R.W.D. Guljarbogh patna - 7
