

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

पत्रांक—...2500...2022

दिनांक—22-12-2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
“नई अनुरक्षण नीति 2018” (3054-MR)
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(3054) “नई अनुरक्षण नीति 2018” योजनान्तर्गत पथ के निर्माण में संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) “नई अनुरक्षण नीति 2018” योजनान्तर्गत पथ:-

L040 Dhankutwa Mandir Chowk To Jagiriya Tola (VR52).

का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:-यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता

ग्रा०का०वि०, का०प्र०, नरकटियागंज।

Signature
21/12/2022

**Office Of The Executive Engineer
Rural Works Department, Works Division, Narkataganj**

Requisition Form for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2020 (Initial Rectification and Surface Renewal)

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Letter No. & Date	Administrative		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer in mm	Value of Bitumen content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	RM/WE/NAR22/0032	L040 Dhankurwa Mandir Chowk To Jagdiga Tola (VRSJ).	31808902180	105 03.06.2022	2.630	126.39000	119.93125	22.49110	17/22-23(MBD) 12.09.2022	13.06.2022		2664	SDBC-25mm	SDBC-5%	0.000000	0.000000	119.930000	Surface Complete

Executive Engineer
Rural Works Department
Work(s) Division Narkataganj

Name of Road - L040 Dhankutwa Mandir Chowk to Jagiriya tola (VR52) (Sec-29)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
20/12/22	14:22:15	29	0.1	220	0	2200	2189	G	26.985895	84.578670	Normal
20/12/22	14:22:15	29	0.1	260	20.2	2600	2631	G	26.985980	84.577693	Normal
20/12/22	14:23:0	29	0.1	270	20.2	2700	2705	G	26.986698	84.577305	Normal
20/12/22	14:23:26	29	0.1	270	30.3	2700	2721	G	26.987582	84.577070	Curve
20/12/22	14:23:26	29	0.1	280	20.2	2800	2770	G	26.988468	84.576835	Normal
20/12/22	14:24:1	29	0.1	280	20.2	2800	2758	G	26.989290	84.576532	Normal
20/12/22	14:26:0	29	0.1	270	20.2	2700	2666	G	26.989823	84.576328	Normal
20/12/22	14:26:22	29	0.1	270	10.1	2700	2694	G	26.990560	84.576127	Curve
20/12/22	14:27:33	29	0.1	290	20.2	2900	2875	G	26.991205	84.576615	Normal
20/12/22	14:28:8	29	0.1	280	20.2	2800	2770	G	26.992125	84.576598	Normal
20/12/22	14:28:43	29	0.1	260	20.2	2600	2634	G	26.993008	84.576665	Normal
20/12/22	14:29:0	29	0.1	270	10.1	2700	2735	G	26.993898	84.576700	Normal
20/12/22	14:29:18	29	0.1	290	20.2	2900	2875	G	26.994768	84.576730	Curve
20/12/22	14:30:0	29	0.1	250	23.2	2500	2503	G	26.995620	84.576935	Normal
20/12/22	14:30:0	29	0.1	260	25.1	2600	2689	G	26.997458	84.577172	Normal
20/12/22	14:30:29	29	0.1	250	23.4	2500	2496	G	26.998340	84.577357	Normal
20/12/22	14:30:29	29	0.1	290	23.6	2900	2868	G	26.999210	84.577558	Curve
20/12/22	14:31:4	29	0.1	260	23.1	2600	2601	G	27.130000	84.577743	Normal
20/12/22	14:32:14	29	0.1	240	23.1	2400	2463	G	27.103700	84.578030	Normal
20/12/22	14:33:24	29	0.1	250	30.3	2500	2541	G	27.126200	84.578430	Normal
20/12/22	14:33:25	29	0.068	260	30.3	2600	2643	G	27.148700	84.578830	Normal
Average IRI Value=							2664				

[Signature]
20/12/22
JE

[Signature]
22/12/2022
AE

[Signature]
Executive Engineer
Rural Works Department
Works Division, Narasipatnam
20/12/2022

Name of Customer: Kharshid Alam
 Name of Work/ Road: LD40 Dhankulwa Mandir Chowk
 Lab Job number:
 Date: 20-12-2022
 Section No: 29

Test Date:	<u>20-12-2022</u>	Road Name:	<u>LD40 Dhankulwa Mandir Chowk</u>
Machine No:	<u>402</u>	Road Type:	<u>(R) RURAL ROAD</u>
Start S No:	<u> </u>	Side:	<u> </u>
Start E No:	<u> </u>	Interval:	<u> </u>
Weather:	<u> </u>	UV Range:	<u>1189</u> To <u>4000</u> <u>1000</u> mm/km
Start Location:	<u> </u>	Dist Range:	<u>0</u> To <u>23</u> <u>01</u> *1000 m
End Location:	<u> </u>	Equation:	$Y = 0 \cdot X^2 + 1136 \cdot X + 1325$


Print Generate Report and Graph

Redraw Graph

Map View

File: G:\20121450.Xls, Section No: 29, Egn: $Y = 0 \cdot X^2 + 1136 \cdot X + 1325$

Name of Customer: Kharshid Alam, Name of Work/ Road: LD40 Dhankulwa Mandir Chowk to Jagirya tola (VR52).

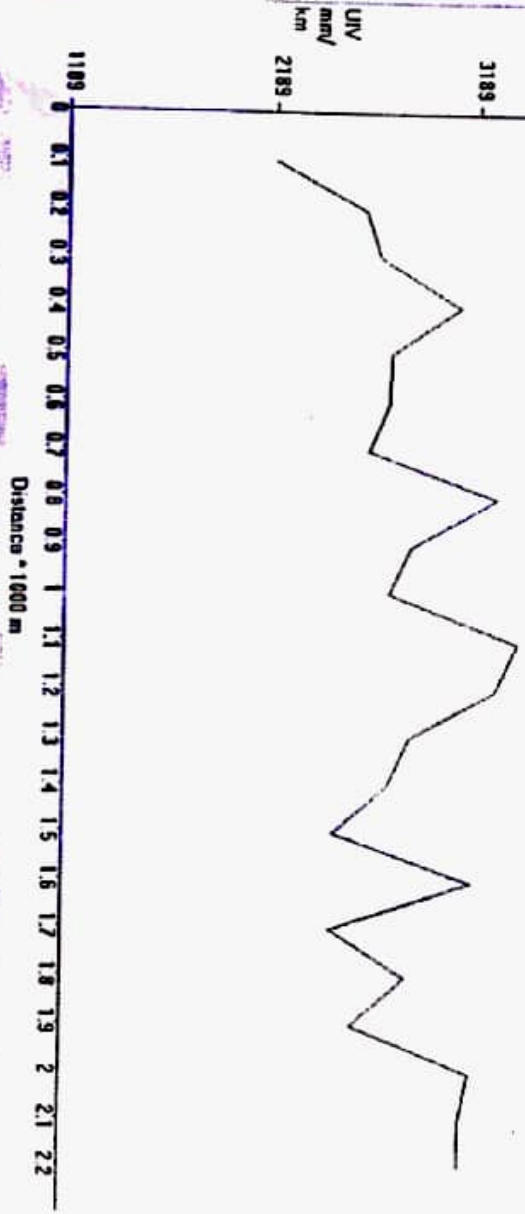

[Signature]
 20/12/22
 JE

[Signature]
 24/12/2022
 HE

[Signature]
 Executive Engineer
 Rural Works Department
 Works Division, Narsimharajpur
 20/12/2022

Office of the Executive Engineer RWD Works Division, Narkatiaganj

Name of Road :- L040 Dhankutwa Mandir Chowk To Jagirya Tola (VR52).
Name of Scheme :- MR 3054 New Maintenance Policy 2018
Name of Contractor :- Khurshid Alam
Length of Road :- 2.630 Km
Project ID :- 31808902180
Package No :- RM/WE/NAR/22/0032
Name of Block :- Sikta

Certified that all item wise 100% measurement has been taken by me


24/12/22

Certified that all item wise 50% measurement has been Verified by me


22/12/2022
AE

Certified that all item wise 10% measurement has been taken by me


Executive Engineer
Rural Works Department
Works Division, Narkatiaganj
