

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, चकिया, (पूर्वी चम्पारण)।

पत्रांक: 1974/अनु0 / चकिया, दिनांक: 23/12/2022

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, चकिया।

सेवामे,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास एजेंसी,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय- विभाग के नई निति रख-रखाव 2018 M.R (3054) योजना के अन्तर्गत निर्माणाधीन कार्य के लिए निधि उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में विभाग के नई निति रख-रखाव 2018 M.R (3054) योजना के अन्तर्गत निर्माणाधीन कार्य के लिए पथवार मांगी जाने वाली आवंटन की सूची पत्र के साथ भवदीय के अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः संलग्न सूची के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय।

अनु0:- 1. आवंटन की सूची।

2. Bump Test Integrator Machine

विश्वासभाजन,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल-चकिया।
23.12.22

ज्ञापांक- 1974 दिनांक- 23-12-2022

प्रतिलिपि-नोडल पदाधिकारी (3054), ग्रामीण कार्य विभाग, बिहार, पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।

अनु0:- 1. आवंटन की सूची

2. Bump Test Integrator Machine

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल-चकिया।
23.12.22

**OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, Chakia.**

Requisition Form for Scheme Head- M8(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division : Chakia

SI No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval ((AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)			Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done. (in Lakh)	Remarks
					Length (In Km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (in lakh)	5 Years Routine Maintenance (In Lakh)											
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	
1	RM/EA/CHA/22/0013	Vankat PMGSY Path to Bathna Ahlyapur	31708413016	Letter No.106 Date-03.06.2022	2.476	144.25	109.64575	23.51252	12MBD/2022-23 Date-30.09.2022	29.06.2023	In Progress	2772	25	05.00	0.00000	0.00000	107.25000	Work in Progress	
					2.476	144.25	109.64575	23.51252									107.25000		

1 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.

2 Up-to-date Physical Progress has been uploaded in MIS.

Executive Engineer,
Rural Works Department,
Works Division, Chakia.



Name of work :	Vankat PMGSY Path to Bathna Ahiyapur
Name of customer :	Vijay Kumar Jaiswal
(R)Rural Road	
Good	Average
Poor	
< 4000	4001 - 5000
	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
16/12/22	11:52:04	38	0	0	0.0 cm	14.2 Km/Hr	0.0 mm/Km	205	0.37	Good	26.3190641	N	84.9010783	E	Normal
16/12/22	11:56:27	38	100	100	20.0 cm	10.0 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.3199968	N	84.8968592	E	Normal
16/12/22	11:56:43	38	100	200	23.0 cm	22.2 Km/Hr	2300.0 mm/Km	2337	3.22	Good	26.3206835	N	84.8970576	E	Normal
16/12/22	11:56:59	38	100	300	20.0 cm	22.2 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.3214769	N	84.8973628	E	Normal
16/12/22	11:57:15	38	100	400	22.0 cm	23.4 Km/Hr	2200.0 mm/Km	2244	3.11	Good	26.3214293	N	84.8984690	E	Normal
16/12/22	11:57:40	38	100	500	37.0 cm	14.9 Km/Hr	3700.0 mm/Km	3635	4.78	Good	26.3214617	N	84.8997050	E	Normal
16/12/22	11:58:16	38	100	600	36.0 cm	19.9 Km/Hr	3600.0 mm/Km	3542	4.67	Good	26.3219080	N	84.9005518	E	Normal
16/12/22	11:58:41	38	100	700	34.0 cm	14.4 Km/Hr	3400.0 mm/Km	3357	4.45	Good	26.3219614	N	84.9012690	E	Normal
16/12/22	11:58:57	38	100	800	33.0 cm	21.1 Km/Hr	3300.0 mm/Km	3264	4.34	Good	26.3223810	N	84.9010554	E	Normal
16/12/22	11:59:10	38	100	900	30.0 cm	27.2 Km/Hr	3000.0 mm/Km	2986	4.01	Good	26.3234091	N	84.9004908	E	Normal
16/12/22	11:59:24	38	100	1000	19.0 cm	25.9 Km/Hr	1900.0 mm/Km	1966	2.76	Good	26.3243418	N	84.9000330	E	Normal
16/12/22	11:59:42	38	100	1100	20.0 cm	20.4 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.3250341	N	84.8996439	E	Normal
16/12/22	12:00:07	38	100	1200	25.0 cm	24.8 Km/Hr	2500.0 mm/Km	2522	3.45	Good	26.3259459	N	84.8989726	E	Normal
16/12/22	12:00:36	38	100	1300	27.0 cm	22.2 Km/Hr	2700.0 mm/Km	2708	3.68	Good	26.3267794	N	84.8985072	E	Normal
16/12/22	12:01:04	38	100	1400	27.0 cm	22.9 Km/Hr	2700.0 mm/Km	2708	3.68	Good	26.3275938	N	84.8983393	E	Normal
16/12/22	12:01:31	38	100	1500	31.0 cm	23.0 Km/Hr	3100.0 mm/Km	3079	4.12	Good	26.3283949	N	84.8981638	E	Normal
16/12/22	12:01:49	38	100	1600	33.0 cm	19.0 Km/Hr	3300.0 mm/Km	3264	4.34	Good	26.3292456	N	84.8978816	E	Normal
16/12/22	12:02:03	38	100	1700	39.0 cm	25.9 Km/Hr	3900.0 mm/Km	3820	5	Good	26.3299456	N	84.8975306	E	Normal
16/12/22	12:02:16	38	100	1800	32.0 cm	27.7 Km/Hr	3200.0 mm/Km	3171	4.23	Good	26.3308363	N	84.8969584	E	Normal
16/12/22	12:02:30	38	100	1900	31.0 cm	25.7 Km/Hr	3100.0 mm/Km	3079	4.12	Good	26.3316412	N	84.8963709	E	Normal
16/12/22	12:02:42	38	100	2000	32.0 cm	29.4 Km/Hr	3200.0 mm/Km	3171	4.23	Good	26.3322477	N	84.8958979	E	Normal

Name of work : Vankat PMGSY Path to Bathua Ahiyapur	
Name of customer : Vijay Kumar Jaiswal	
(R) Rural Road	
Good	Average
< 4000	4001 - 5000
	> 5000

16/12/22	12:02:54	38	100	2100	31.0 cm	29.7 Km/Hr	3100.0 mm/Km	3079	4.12	Good	26.3332453	N	84.8953104	E	Normal
16/12/22	12:03:08	38	100	2200	33.0 cm	27.9 Km/Hr	3300.0 mm/Km	3264	4.34	Good	26.3340254	N	84.8949366	E	Normal
16/12/22	12:03:22	38	100	2300	33.0 cm	25.4 Km/Hr	3300.0 mm/Km	3264	4.34	Good	26.3348646	N	84.8944483	E	Normal
16/12/22	12:03:37	38	100	2400	30.0 cm	23.8 Km/Hr	3000.0 mm/Km	2986	4.01	Good	26.3357153	N	84.8941431	E	Normal
16/12/22	12:03:52	38	100	2500	22.0 cm	23.6 Km/Hr	2200.0 mm/Km	2244	3.11	Good	26.3365927	N	84.8939753	E	Normal
1			0	2500				205	0.37	Good					


Average :- 2572

16/12/22
12:03:37
38
100
2400
30.0 cm
23.8 Km/Hr
3000.0 mm/Km
2986
4.01
Good
26.3357153
N
84.8941431
E
Normal

कायपादक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, चकीया



Name of Customer: Vijay Kumar Jaiswal , Machine no: 19191 , Road: Vankat PMGSY Path to Bathna Ahirapur , Date: 16-12-22 , Section No: 38 , Equation: $Y = 0.927 X + 204.8$

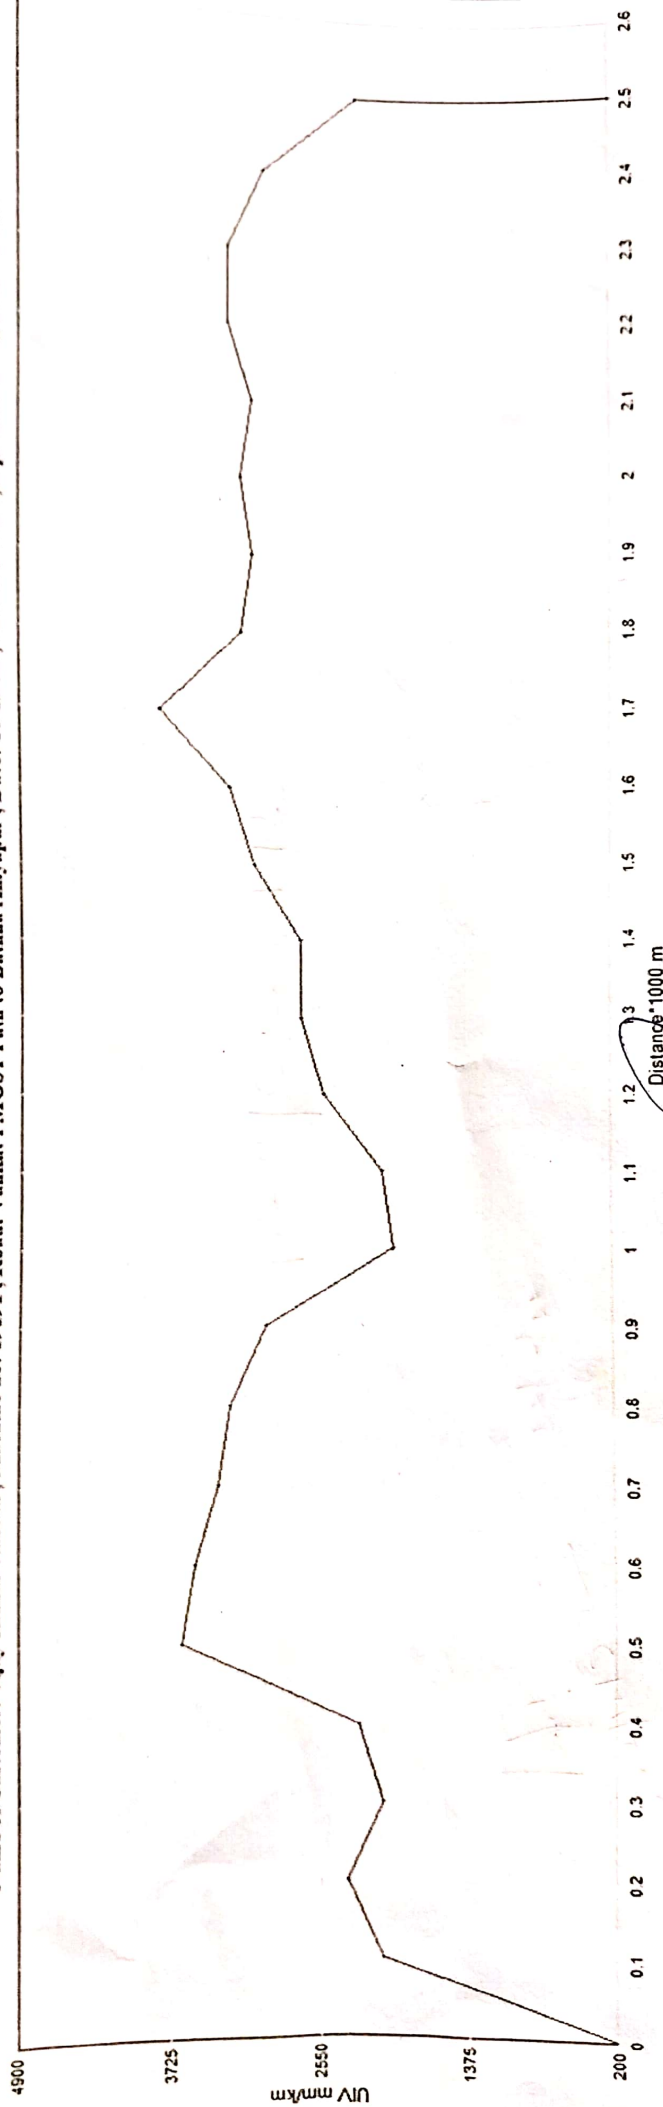

Distance*1000 m

22/12/22
22/12/22
22/12/22

कायप्रलक अभियता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, चकीय
