

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पालीगंज।

पत्रांक : 302(अनुब)

पालीगंज / दिनांक : 18/2/22

प्रेषक :

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल पालीगंज।

सेवा में,

विशेष सचिव,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:—शीर्ष—MR (3054) Under Bihar Rural Road Maintenance Policy-2018 योजना अन्तर्गत आवंटन का अध्याचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष—MR (3054) Under Bihar Rural Road Maintenance Policy-2018 योजना अन्तर्गत पथों का आवंटन का अध्याचना का मॉग विहित—प्रपत्र में तैयार कर Signed Hard Copy of recorded IRI के साथ अध्याचना हेतु भेजी जा रही है।

अतः आपसे अनुरोध है कि उक्त योजना का आवंटन उपलब्ध कराने की कृपा की जाये, ताकि संवेदक का भुगतान किया जा सके।

अनु०:—यथोक्त।

विश्वासभाजन

9
17/2/22

17/2/22
कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल पालीगंज।
17/2/22

Requisition Format For Scheme Head -MR (3054) Under Bihar Rural Road Maintenance Policy 2018 (Initial Rectification and surface Renewal)
Name Of Work division- Paliganj

Sl	Package No	Name Of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Length (in KM)	Administrative Amount of (in Lakh)	Agreement Amount Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)	Agreement Date	Date of completion as per Agreement	Actual Date of completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
	MR-N/19-20	Khanpura - Mera Patauna	NEA220001619	Lt no 6459 dt 13.12.2019	5.4	216.20400	169.15700	56.22972	03/MBD/2020-21 & 08.06.202	07.03.2021	04.06.2021	4.45360	25 mm (SDBC)	5.18%	134.85276	137.84767	11.36575	Work has been completed as per specification and verification of fifty percent measurement by assistant engineer and ten percent by Executive Engineer has been done.
2	MR-N/19-20	Pali Kinjar road Bela Khranti khanda Kutubey Dhokhara	10100102360	Lt no 6459 dt 13.12.2019	2.1	80.03800	54.14800	22.30005	03/MBD/2020-21 & 08.06.202	07.03.2021	05.06.2021	4.6955	25 mm (SDBC)	5.16%	42.4468	42.4468	6.17715	Work has been completed as per specification and verification of fifty percent measurement by assistant engineer and ten percent by Executive Engineer has been done.

17/12/22
Sr. Divisional Accounts Officer
Rural Work Department
Works Division Paliganj

17/12/2022
Executive Engineer
Rural Works Deptt.
Work Division Paliganj

FORM GFR 19-A

(See Government of India's Decision (1) below Rule-150)
Form of utilisation Certificate up to the end of January.2022

PIU: RWD Works Division , Paliganj				
Sl No.	Name of Scheme	Sanction No. & Date with Amount	Amount Received (In Rs.)	Particulars
1	Construction of Bihar Rural road Maintenance Policy -2018 under MR 3054	64we dt 06.12.2021	158574627.00	Certified that out of Rs 158574627.00 received during the years January 2022 in favour of Ex. Engineer, RWD, Works Div. Paliganj Bihar a sum of Rs 157585023.00 has been utilized for the purpose of PMGSY II Program Fund Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 989604.00 remaining unutilized at the end to the period under
Total			158574627.00	

2. Certified that I have satisfied myself that the conditions of which the grants sanction Sanctioned have been duly fulfilled/are being fulfilled and I have exercised the checks to see the money was actually utilised for the purpose for which it was sanctioned.

Kishor 17/1/22
Sr. Divisional Accounts Officer
Rural Work Department
Works Division Paliganj

17.2.22
Executive Engineer
Rural works Deptt.
Works Division, Paliganj

NAME OF THE ROAD : PAU KIN/AR ROAD TO BELA KHARATI KHURD KUTBI DHOKHARA

LENGTH OF THE ROAD : 2.10 KM

PACKAGE NO. : MR-N/19-20/PALIGANI/09

DIVISION : PALIGANI

BLOCK : PALIGANI

AGENCY : KRISHABH NIRMAN PVT LTD

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV mm/km	CATEGORY ROAD	IRI	Latitude	Longitude	Event				
22/3/21	13:15:36	48	0.1	370	0	3700	3741	G	4.9	25.258178	84.85303	Normal	$Y = 0 * X + 2 + 0.936 * X + 278.4$			
22/3/21	13:16:0	48	0.1	360	30.3	3600	3648	G	4.79	25.25787	84.853938	Normal	$X = 3600$			
22/3/21	13:16:12	48	0.1	390	10.1	3900	3928	G	5.12	25.25766	84.854948	Speed Breaker	$Y = 3648$			
22/3/21	13:16:32	48	0.1	300	30.3	3000	3086	G	4.13	25.25739	84.855892	Normal				
22/3/21	13:16:47	48	0.1	340	30.3	3400	3460	G	4.57	25.257263	84.856902	Normal	(R) RURAL ROAD			
22/3/21	13:17:0	48	0.1	320	30.3	3200	3273	G	4.35	25.257018	84.857845	Normal	Good	Average	Poor	
22/3/21	13:17:10	48	0.1	380	30.3	3800	3835	G	5.01	25.256953	84.858855	Normal	<4000 4001-5000 >5001			
22/3/21	13:17:23	48	0.1	390	30.3	3900	3928	G	5.12	25.256955	84.859865	Normal				
22/3/21	13:17:33	48	0.1	350	20.2	3500	3554	G	4.68	25.257253	84.860807	Curve				
22/3/21	13:17:43	48	0.1	320	30.3	3200	3273	G	4.35	25.257465	84.862	Normal				
22/3/21	13:18:0	48	0.1	330	20.2	3300	3367	G	4.46	25.257013	84.862137	Curve				
22/3/21	13:18:10	48	0.1	350	30.3	3500	3554	G	4.68	25.25628	84.861598	Normal				
22/3/21	13:18:20	48	0.1	390	30.3	3900	3928	G	5.12	25.25542	84.86116	Normal				
22/3/21	13:18:33	48	0.1	320	20.2	3200	3273	G	4.35	25.254613	84.860892	Culvert				
22/3/21	13:19:0	48	0.1	320	30.3	3200	3273	G	4.35	25.25375	84.860555	Normal				
22/3/21	13:19:17	48	0.1	330	20.2	3300	3367	G	4.46	25.253195	84.860842	Curve				
22/3/21	13:19:37	48	0.1	370	30.3	3700	3741	G	4.9	25.253177	84.861868	Normal				

Nisuper
 22/3/21
 13:19:37
 48

22.03.2021
 5 L

8/

W

Name of Customer: KRISHABH NIRMAN PVT LTD
Name of Work: PALU KINJAR RD TO BELA KH
Road:
Lab Job number:
Date: 22-03-2021
Section No. 48


Test Date: 22-03-2021
Road Name: PHURDAKUTBI DHOKHAPPA
Machine No:
Road Type: (0) RURAL ROAD
Start S No:
Side:
Start E No:
Interval:
Weather:
U/V Range: 2086 To 5060 mm/km
Dist Range: 0 To 21 0.1 * 1000 m
Start Location:
End Location:
Equation: $Y = 0.0 * X^2 + 0.936 * X + 278.4$

Print Generate Report and Graph

Redraw Graph

Map View

File C:\Users\SHAZN\Desktop\48 Xs. Section No.: 48. Eqn: $Y = 0.0 * X^2 + 0.936 * X + 278.4$
Name of Customer: KRISHABH NIRMAN PVT LTD, Name of Work/Road: PALU KINJAR RD TO BELA KHARATI

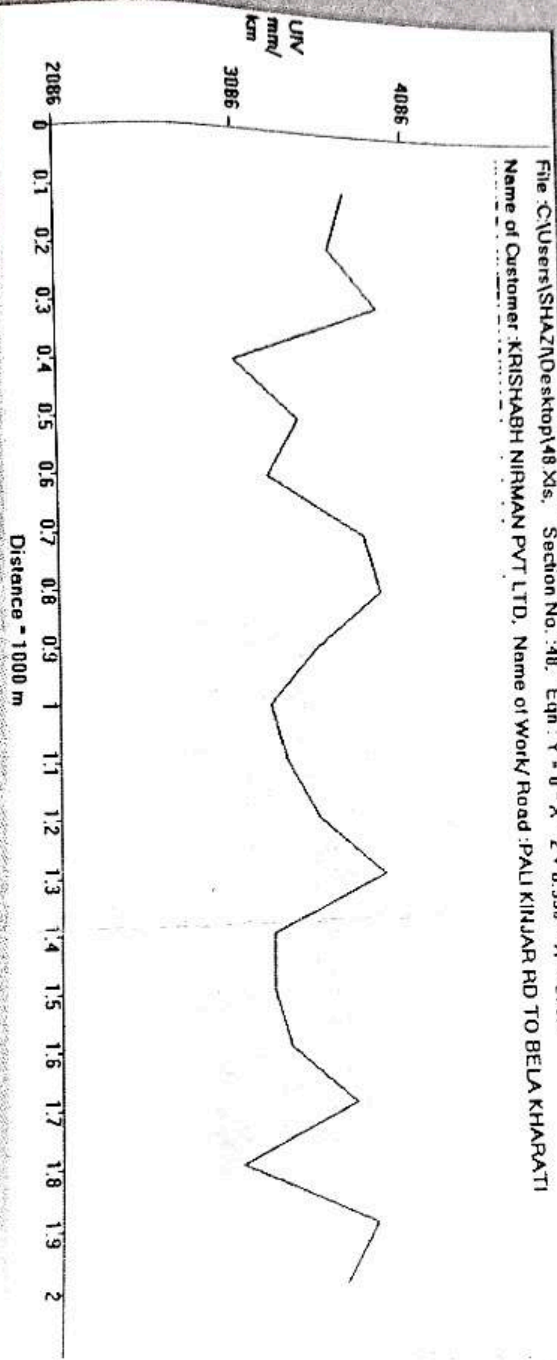

Handwritten: 22/3/2021, 1558 IT mmpm

Handwritten: 22.03.2021, 59

Handwritten: 22/03/2021, A.R.

Handwritten: 05/11

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, क्षेत्रीय प्रयोगशाला, गुलजारबाग
पटना-800007

पत्रांक - 331/अड

पटना/दिनांक 06-03-2021

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना -7

सेवा में,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल ... Palikumar.

विषय :- जाँचफल प्रतिवेदन के संबंध में।

प्रसंग :-

A.E, Palikumar vide letter NO-07 dated
Date - 15/2/21

महाशय,

उपर्युक्त विषयक के संबंध में जाँचफल प्रतिवेदन इस पत्र के साथ संलग्न कर आवश्यक
कारवाई हेतु भेजा जा रहा है जो निम्न प्रकार है:-

y Pali Kumar Pool to Bela Kharamthi Khari
Kubey Shokhara.

Mix Seal

(13.2mm to 0.5mm)

अनु:-यथोक्त

विश्वासभाजन

331/अड

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना -7

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R.W.D. GULJARBAGH, PATNA - 7
PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

336

06/03/24

Name of Project/Road :- Pali Kinsar Road to Bela
 Name of Scheme :- Kharuli Kut Bay Sholehara
 Name of Agency :- M.A. 359
 Nature of sample :- Semi Dense Bituminous Concrete Date of Collection/Received :- 11/03/24
 Location :- 1500 mt Date of Test :- 5/3/24
 Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division Patna
 vide letter No. 1028 Dt. 22.02.2024
 Agreement No / Package No. :- 03/M33/2020-21

Sl. No.	A.I.V.	
	Average Test Value	Required Value(Max)
1.		30%

Sl. No.	Sieve Size in (mm)	Weight of Sample Taken Kgs					Remarks
		Weight Retd.	% of Wt. Retained	% of Cumm. Retained	% of Passing	Required value	
1	13.2	0.000	0.00	0.00	100	100	
2	9.5	0.745	3.85	3.85	96.15	90-100	
3	4.75	8.969	46.35	50.20	49.80	35-51	
4	2.36	3.164	16.35	66.55	33.45	24-39	
5	1.18	1.277	6.60	73.15	26.85	15-30	
6	0.300	2.245	11.60	84.75	15.25	9-19	
7	0.075	1.858	9.60	94.35	5.65	3-8	

Copy Submitted to/forwarded to:
 E.E. R.W.D. Works Division :-

Rains
 L.A. 5/3/24

5/3/24
 A.E.

Rakesh Kumar
 A.E. 05/03/2024

18
 E.E. 05/03/2024

Regional Laboratory V.D. Guljarbagh patna - 7 Regional Laboratory R.W.D Guljarbagh patna - 7 Regional Laboratory R.W.D Guljarbagh patna - 7 Regional Laboratory R.W.D. Guljarbagh patna - 7

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, क्षेत्रीय प्रयोगशाला, गुलजारबाग
पटना-800007

पत्रांक : 336/अड

पटना/दिनांक : 6.03.2021

प्रेषक :

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना -7

सेवा में,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल Paliganj.

विषय :- जॉचफल प्रतिवेदन के संबंध में।

प्रसंग :- AE, Paliganj vide letter no-10 (3157)
Date - 22.02.21.

महाशय,

उपर्युक्त विषयक के संबंध में जॉचफल प्रतिवेदन इस पत्र के साथ संलग्न कर आवश्यक कारवाई हेतु भेजा जा रहा है जो निम्न प्रकार है:-

1) Pali Kinsar road to Bela Kharaanthi Kuth
- Sholchana.

1) SBC

अनु:- यथोक्त

विश्वासभाजन

5/3/21

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना -7

Date 09/03/2021

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D., GULZARBAGH, PATNA - 7

Bituminous mix

Name of Project/Road :- Pali Kingar Road to Bela Kheranthi Khurd Kumbhey Dhokhara

Name of Scheme :- MR-3054

Name of Agency :- Krishabh Nirman Pvt. Ltd

Nature of sample :- Bitumen Content for S.D.B.C.

Location :- S.O.M

Date of Collection/Received :- 01/03/2021

Date of Test :- 09/03/2021

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division Paliganj vide letter No. 14/45 Dt. 24.02.2021

Agreement No / Package No. : 03/MAD/2020-21

SL NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	508.00	506.00	505.00	
2	Wt. of Dry chips after extraction (b)	481.35	480.10	479.20	
3	Percentage of bitumen (in the mix) $[(a-b)*100] / a$ (%)	5.25	5.12	5.11	
4	Average % bitumen	5.16			

R. W. D. 21/3/21

Regional Laboratory
R.W.D. Guljarbagh patna - 7

A.D. 23/3/21

Regional Laboratory
R.W.D Guljarbagh patna - 7

A.E. 09/03/2021

Regional Laboratory
R.W.D Guljarbagh patna - 7

E.E. 09/03/2021

Regional Laboratory
R.W.D. Guljarbagh patna - 7

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D. GULJARIBAGH, PATNA - 7

337

PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

06/03/2021

Name of Project/Road :- Pali Kimsen Road to Bela Phara.

Name of Scheme :- Mr. Hurd Kuntabay Shokhara.

Name of Agency :- Krishabh Nirmam Pvt Ltd.

Nature of sample : Mix seal (13.2mm to 0.075mm)

Location :-

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division

vide letter No. 07/08/21 - 15/2/21

Agreement No / Package No. : 03/MBD/2000-21

Sl. No.	A.I.V.	
	Average Test Value	Required Value(Max)
1.		40%

Sl. No.	Sieve Size in (mm)	Weight of Sample Taken Kgs 14.725				Required Value		Remarks
		Weight Retd.	% of Wt. Retained	% of Cum. Retained	% of Passing	Type A	Type B	
1	13.2	0.000	0.00	100	100	---	100	/
2	11.2	0.648	4.40	4.40	95.60	100	88-100	
3	5.6	6.921	47.00	51.40	48.60	52-88	31-52	
4	2.8	3.954	26.85	78.25	21.75	14-38	5-25	
5	0.09	2.754	18.70	96.95	3.05	0-5	0-5	

Rainy
5/3/21
LA

Regional Laboratory

R.W.D. Guljaribagh patna - 7

5/3/21
A.D.

Regional Laboratory

R.W.D. Guljaribagh patna - 7

Rainy
05/03/2021
A.E.

Regional Laboratory

R.W.D. Guljaribagh patna - 7

05/03/21
E.E.

Regional Laboratory

R.W.D. Guljaribagh patna - 7

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, क्षेत्रीय प्रयोगशाला, गुलजारबाग
पटना-800007

पत्रांक 367/358

पटना/दिनांक 09-03-2021

प्रेषक

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना -7

सेवा में

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल पालिगंज

विषय :- जॉचफल प्रतिवेदन के संबंध में।

प्रसंग :- A.E. R. & D. (W) Sub-Division: Paligunj vide letter No-14(डा.गु), Dt-24/02/2021

महाराज

उपर्युक्त विषयक के संबंध में जॉचफल प्रतिवेदन इस पत्र के साथ संलग्न कर आवश्यक कारवाई हेतु भेजा जा रहा है जो निम्न प्रकार है:-

N/R - Pali Kington Road to B.E. Kheranathi Khurd Kurbey Dhotkhar

Ag. No. - 03/MBD/2020-21

1- S.D.B.C.
2) Bitumen Content

अनु:-यथोक्त

विश्वासभाजन

प्रमाण

कार्यपालक अभियंता
ग्रामीण कार्य विभाग

क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना -7

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R.W.D. GULZARBAGH, PATNA
PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

362
Name of Project/Road : Pali Kingar Road to Bela (Charamthi Khurd Kuthay
Name of Scheme : Dhokhara
Name of Agency : MR-1054
Name of Agency : Krishabh Nirman Pvt. Ltd.
Nature of sample : Semi Dense Bituminous Concrete Date of Collection/Received : 01/03/2021
Location : 500 m Date of Test : 05/03/2021
Ref : Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division : Pali Kingar
vide letter No. 143130 Dt. 24/02/2021
Agreement No / Package No. : 01/MBD/2020-21

Sl. No.	A.I.V.	
	Average Test Value	Required Value(Max)
1.	—	30%

Sl. No.	Sieve Size in (mm)	Weight of Sample Taken Kgs 18.260					Remarks
		Weight Retd.	% of Wt. Retained	% of Cumm. Retained	% of Passing	Required value	
1	13.2	0.000	0.00	0.00	100	100	
2	9.5	0.703	3.85	3.85	96.15	90-100	
3	4.75	8.500	46.55	50.40	49.60	35-51	
4	2.36	3.150	17.25	67.65	32.35	24-39	
5	1.18	1.023	5.60	73.25	26.75	15-30	
6	0.300	2.657	14.55	87.80	12.20	9-19	
7	0.075	1.570	8.60	96.40	3.60	3-8	

Copy Submitted to/forwarded to:

E.E. R.W.D. Works Division :- Masaurhi

RAI
5/3/21

RAI
5/3/21
A.D.

RAI
05/03/2021
A.E.

RAI
05/03/2021
E.E.
