

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पटना ।

दिनांक 21/02/2022

पत्रांक 296 (अ/उ)

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पटना।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बी.आर.आर.डी.ए.,
ग्रामीण कार्य विभाग,
बिहार, पटना ।

विषय :- शीर्ष-MR(3054) under Bihar Rural Road Maintenance Policy-2018 योजना अन्तर्गत आवंटन का अधियाचना के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि शीर्ष-MR(3054) under Bihar Rural Road Maintenance Policy-2018 योजना अन्तर्गत पथों का आवंटन का अधियाचना का मांग विहित-प्रपत्र में तैयार कर अधियाचना हेतु भेजी जा रही है। पथों का कार्य विशिष्टियों के अनुरूप किया जा चुका है।

अतः आपसे अनुरोध है कि उक्त योजना का आवंटन उपलब्ध कराने की कृपा की जाये ताकि संवेदक का भुगतान किया जा सके।

अनु० :- यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता

ग्रामीण कार्य विभाग,

कार्य प्रमंडल, पटना।

21/02/2022



21/02/22

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division : Patna

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (In Lakh)	Up-to-date expenditure as per MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks
					Length (in km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	7	Baikatpur Mandir to Ganga Nadi Path	10103573	Lett No.-3024 dated 16.07.2019	2.65000	74.82600	44.82500	24.12186	04-MBD/2020-2021 Dated 12.05.2020	11.02.2021	-	3036.74	25 mm	5%	0.00000	0.00000	34.98682	अगरले गले कार्व सुपवासापूर्ण एवं विभिन्नियो ले अनुकूप है एवं सहायक अमिलता द्वारा 50 प्रतिशत एवं अपोहसमारी द्वारा 10 प्रतिशत मापी का सत्यापन कर लिया गया है।
2	7	Khushirapur Nagarnosha Road to Madwa Road	10100101040	Lett No.-3024 dated 16.07.2019	2.00000	88.46540	60.94500	20.48786	04-MBD/2020-2021 Dated 12.05.2020	11.02.2021	-	3049.92	20 mm	4.57%	0.00000	0.00000	41.15579	
Total																	76.14261	

- Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
- Up-to-Date Physical Progress has been uploaded in MIS.


 Executive Engineer
 RWD Works Division, Patna

 21/02/2022

Packege No. : MR-N/2019-2020/PATNA/07

Length : 1.835

Contractor Name : AJAY KUMAR

Name of The Road : Baikatpur Mandir to Ganga nadi path

Block : Khushrupur

Division : Patna

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event			
No.	in km	in mm	Rate	mm/km	mm/km	ROAD								
											$Y = 0 * X^2 + 0.936 * X + 278.4$			
											Normal			
											Normal	X = 2600		
											Normal	Y = 2712		
											Normal			
19/02/2022	14: 35: 42	18	0.1	310	30.3	3100	3180	G	25.496409	85.376303	Normal			
19/02/2022	14: 35: 42	18	0.1	340	30.3	3400	3460	G	25.497375	85.376727	Normal			
19/02/2022	14: 36: 0	18	0.1	280	30.3	2800	2899	G	25.498218	85.377129	Normal			
19/02/2022	14: 36: 17	18	0.1	290	30.3	2900	2992	G	25.498991	85.377503	Normal			
19/02/2022	14: 36: 17	18	0.1	370	10.1	3700	3741	G	25.499855	85.377904	Speed Breaker	(R)RURAL ROAD		
19/02/2022	14: 36: 17	18	0.1	220	30.3	2200	2337	G	25.500679	85.378268	Normal	Good	Average	Poor
19/02/2022	14: 36: 17	18	0.1	260	30.3	2600	2712	G	25.501595	85.0378745	Normal	<4000	4001-5000	>5001
19/02/2022	14: 36: 52	18	0.1	340	30.3	3400	3460	G	25.502363	85.379069	Normal			
19/02/2022	14: 36: 52	18	0.1	260	30.3	2600	2899	G	25.503172	85.379393	Normal			
19/02/2022	14: 37: 0	18	0.1	280	30.3	2800	2618	G	25.504018	85.379759	Normal			
19/02/2022	14: 37: 0	18	0.1	250	30.3	2500	2618	G	25.504948	85.380169	Speed Breaker			
19/02/2022	14: 37: 28	18	0.1	380	20.2	3800	3835	G	25.505799	85.380395	Normal			
19/02/2022	14: 37: 28	18	0.1	330	30.3	3300	3367	G	25.506612	85.380532	Normal			
19/02/2022	14: 37: 28	18	0.1	220	30.3	2200	2337	G	25.507343	85.38069	Normal			
19/02/2022	14: 38: 3	18	0.1	220	30.3	2900	2992	G	25.507343	85.38069	Normal			
19/02/2022	14: 38: 38	18	0.1	290	30.3	3200	3273	G	25.508416	85.380942	Normal			
19/02/2022	14: 38: 38	18	0.1	320	30.3	3200	2712	G	25.50933	85.381063	Normal			
19/02/2022	14: 39: 0	18	0.1	260	30.3	2600	2712	G	25.510264	85.381162	Speed Breaker			
19/02/2022	14: 39: 13	18	0.1	350	20.2	3500	3554	G	25.510907	85.3812	Normal			
19/02/2022	14: 39: 13	18	0.1	250	30.3	2500	2618	G	25.511411	85.381226	Normal			
19/02/2022	14: 39: 13	18	0.035	260	30.2	2600	2712	G	484.577705	1621.86731				
19/02/2022	14: 39: 49	18	1.835	5600	535.2	56000	57698							
Total						2947.3684	3036.7368							
Average														

19.02.22
27 Manager

Singh
19/2/22
AE

Executive Engineer
Rural Work Department
Work Division, Patna

Name of Customer : Ajay Kumar
 Name of Work/ Road : Baikatpur Mandir to Ganga nadi
 Lab Job number :
 Date : 19/02/2022
 Section No. : 18

Test Date : 19/02/2022 Road Name : Baikatpur Mandir to Ganga nec
 Machine No : 374 Road Type : (R) RURAL ROAD
 Start S No : Side : Interval
 Start E No : Weather : UIV Range : 1337 To 5000 1000 mm/km
 Start Location : Dist Range : 0 To 2 0.1 * 1000 m
 End Location : Equation : $Y = 0 * X^2 + 0.936 * X + 278.4$

Print

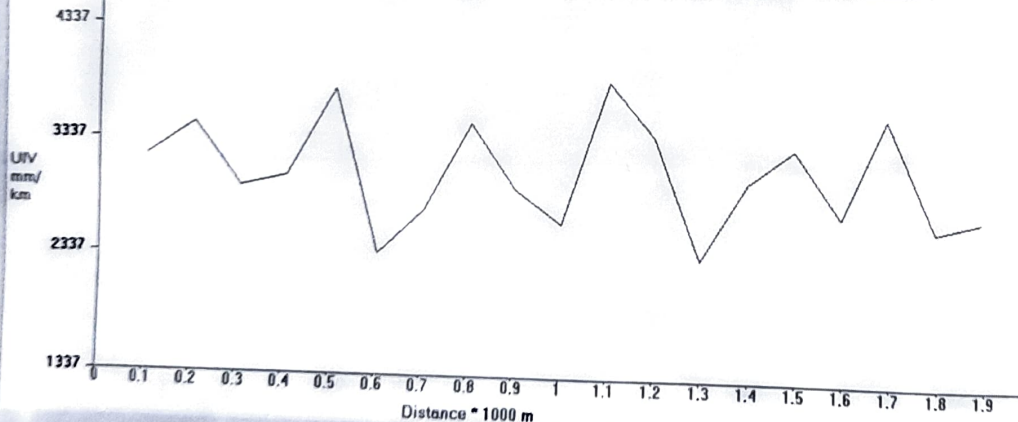
Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\BRDA23\OneDrive\Desktop\14011322.Xls. Section No. : 18. Eqn : $Y = 0 * X^2 + 0.936 * X + 278.4$

Name of Customer : Ajay Kumar, Name of Work/ Road : Baikatpur Mandir to Ganga nadi path, Lab Job number :



Signature
 19.02.22
 ST Manager

Signature
 19/2/22
 AR

Signature
 21.2.22
 Executive Engineer
 Rural Work Department
 Work Division, Patna

Name of Work—
 Situation of Work—
 Agency by which work is executed—
 Date of Measurement—
 No. and date of agreement

(These four lines should be repeated at the commencement of the measurement relating to each work)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
	<u>Record Entry</u>				
Name of Road	Ganga Nadi Path				Construction & Maintenance
Agency:-	Ajay Kumar, Malan				
No and date of Agreement:-	04 M.B.D. of 2020-21				
W.O. No. vide B.B. letter No 636 dt. 12.5.20					
Date of Measurement:-	12.10.20				
Entry:-	12.10.20				
Item No ① clearing and grubbing the Road Land	as per sp. and dir. of B.I.L.				
	$2 \text{ Nos} \times 1835 \text{ M} \times 1.42 \text{ M} = 3670 \text{ M}^2 \text{ or } 0.367 \text{ Hec}$				
Item No ② surfacing Existing Bituminous	$20 \text{ M} \times 3.75 \text{ M} = 75 \text{ M}^2$				
Item No ③ construction of sub grade	as per sp. and dir. of B.I.L.				
	$2 \text{ Nos} \times 1450 \text{ M} \times 1.42 \text{ M} \times 0.30 \text{ M} = 870.00 \text{ M}^3$				
Item No ④ Providing & fixing logs and for Maintenance base	03 Nos.				
12.10.20	S.B.				
	Original 12/10/20				

Continuation

Continuation
