

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पालीगंज।

पत्रांक : 302(अनुब)

पालीगंज/दिनांक : 18/2/22

प्रेषक :

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल पालीगंज।

सेवा में,

विशेष सचिव,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:—शीर्ष—MR (3054) Under Bihar Rural Road Maintenance Policy-2018 योजना अन्तर्गत आवंटन का अध्याचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष—MR (3054) Under Bihar Rural Road Maintenance Policy-2018 योजना अन्तर्गत पथों का आवंटन का अध्याचना का मॉग विहित—प्रपत्र में तैयार कर Signed Hard Copy of recorded IRI के साथ अध्याचना हेतु भेजी जा रही है।

अतः आपसे अनुरोध है कि उक्त योजना का आवंटन उपलब्ध कराने की कृपा की जाये, ताकि संवेदक का भुगतान किया जा सके।

अनु०:—यथोक्त।

विश्वासभाजन

9
17/2/22

17/2/22
कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल पालीगंज
17/2/22

Requisition Format For Scheme Head -MR (3054) Under Bihar Rural Road Maintenance Policy 2018 (Initial Rectification and surface Renewal)
Name Of Work division- Paliganj

Sl	Package No	Name Of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Length (in KM)	Administrative Amount of (in Lakh)	Agreement Amount Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)	Agreement Date	Date of completion as per Agreement	Actual Date of completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
	MR-N/19-20	Khanpura - Mera Patauna	NEA220001619	Lt no 6459 dt 13.12.2019	5.4	216.20400	169.15700	56.22972	03/MBD/2020-21 & 08.06.202	07.03.2021	04.06.2021	4.45360	25 mm (SDBC)	5.18%	134.85276	137.84767	11.36575	Work has been completed as per specification and verification of fifty percent measurement by assistant engineer and ten percent by Executive Engineer has been done.
2	MR-N/19-20	Pali Kinjar road Bela Khranti khanda Kutubey Dhokhara	10100102360	Lt no 6459 dt 13.12.2019	2.1	80.03800	54.14800	22.30005	03/MBD/2020-21 & 08.06.202	07.03.2021	05.06.2021	4.6955	25 mm (SDBC)	5.16%	42.4468	42.4468	6.17715	Work has been completed as per specification and verification of fifty percent measurement by assistant engineer and ten percent by Executive Engineer has been done.

17/12/22
Sr. Divisional Accounts Officer
Rural Work Department
Works Division Paliganj

17/12/2022
Executive Engineer
Rural Works Deptt.
Work Division Paliganj

FORM GFR 19-A

(See Government of India's Decision (1) below Rule-150)
Form of utilisation Certificate up to the end of January.2022

PIU: RWD Works Division , Paliganj				
Sl No.	Name of Scheme	Sanction No. & Date with Amount	Amount Received (In Rs.)	Particulars
1	Construction of Bihar Rural road Maintenance Policy -2018 under MR 3054	64we dt 06.12.2021	158574627.00	Certified that out of Rs 158574627.00 received during the years January 2022 in favour of Ex. Engineer, RWD, Works Div. Paliganj Bihar a sum of Rs 157585023.00 has been utilized for the purpose of PMGSY II Program Fund Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 989604.00 remaining unutilized at the end to the period under
Total			158574627.00	

2. Certified that I have satisfied myself that the conditions of which the grants sanction Sanctioned have been duly fulfilled/are being fulfilled and I have exercised the checks to see the money was actually utilised for the purpose for which it was sanctioned.

Kishor 17/1/22
Sr. Divisional Accounts Officer
Rural Work Department
Works Division Paliganj

17.2.22
Executive Engineer
Rural works Deptt.
Works Division, Paliganj

NAME OF THE ROAD : KHANPURA TO MERA PATAUNA

LENGTH OF THE ROAD : 5.40 KM

PACKAGE NO. : MR-N/19-20/PALIGANJ/09

DIVISION : PALIGANJ

BLOCK : PALIGANJ

AGENCY : KRISHABH NIRMAN PVT LTD

Date	Time	Section	Length	Bumps	Speed	OR	UIV	CATEGORY	IRI	Latitude	Longitude	Event			
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD							
22/3/21	12:18:0	46	0.1	380	0	3800	3835	G	5.01	25.275622	84.786245	Normal	$y = 0 \cdot x^2 + 0.936 \cdot x + 278.4$		
22/3/21	12:18:16	46	0.1	280	30.3	2800	2899	G	3.9	25.27543	84.787222	Normal	$x = 3000$		
22/3/21	12:18:26	46	0.1	270	30.3	2700	2805	G	3.79	25.27525	84.788282	Normal	$y = 3086$		
22/3/21	12:18:36	46	0.1	280	30.3	2800	2899	G	3.9	25.275458	84.789192	Normal			
22/3/21	12:18:51	46	0.1	300	30.3	3000	3086	G	4.13	25.275578	84.790218	Normal			
22/3/21	12:19:0	46	0.1	280	20.2	2800	2899	G	3.9	25.2758	84.790958	Curve	Good	Average	Poor
22/3/21	12:19:10	46	0.1	270	30.3	2700	2805	G	3.79	25.276722	84.790858	Normal	<4000	4001-5000	>5001
22/3/21	12:19:27	46	0.1	240	30.3	2400	2524	G	3.45	25.277623	84.79079	Normal			
22/3/21	12:19:37	46	0.1	380	30.3	3800	3835	G	5.01	25.27854	84.790757	Normal			
22/3/21	12:19:47	46	0.1	370	30.3	3700	3741	G	4.9	25.279512	84.790605	Normal			
22/3/21	12:20:2	46	0.1	300	30.3	3000	3086	G	4.13	25.280412	84.790505	Normal			
22/3/21	12:20:12	46	0.1	280	30.3	2800	2899	G	3.9	25.281343	84.790387	Normal			
22/3/21	12:20:22	46	0.1	340	30.3	3400	3460	G	4.57	25.28222	84.790258	Normal			
22/3/21	12:20:37	46	0.1	380	20.2	3800	3835	G	5.01	25.283037	84.790673	Curve			
22/3/21	12:21:0	46	0.1	330	10.1	3300	3367	G	4.46	25.283572	84.791295	Speed Breaker			
22/3/21	12:21:13	46	0.1	300	30.3	3000	3086	G	4.13	25.283725	84.792272	Normal			
22/3/21	12:21:33	46	0.1	350	30.3	3500	3554	G	4.68	25.283745	84.793232	Normal			
22/3/21	12:21:48	46	0.1	270	30.3	2700	2805	G	3.79	25.283792	84.794275	Normal			

Abhinav
22/3/21
12:21:48

22/3/21
12:21:48

✓

✓

Date	Time	Section	Length	Bumps	Speed	OR	UIV	CATEGORY	IRI	Latitude	Longitude	Event
22/3/21	12: 22: 0	No. 46	0.1	330	10.1	3300	3367	ROAD	4.46	25.28384	84.795252	Speed Breaker
22/3/21	12: 22: 23	46	0.1	320	30.3	3200	3273	G	4.35	25.28385	84.796295	Normal
22/3/21	12: 23: 0	46	0.1	360	30.3	3600	3648	G	4.79	25.284157	84.797222	Normal
22/3/21	12: 23: 10	46	0.1	350	30.3	3500	3554	G	4.68	25.2848	84.797962	Normal
22/3/21	12: 23: 20	46	0.1	280	30.3	2800	2899	G	3.9	25.285103	84.798888	Normal
22/3/21	12: 23: 34	46	0.1	300	30.3	3000	3086	G	4.13	25.284993	84.799898	Normal
22/3/21	12: 23: 44	46	0.1	340	30.3	3400	3460	G	4.57	25.284888	84.800875	Normal
22/3/21	12: 23: 54	46	0.1	270	30.3	2700	2805	G	3.79	25.284563	84.801885	Normal
22/3/21	12: 24: 10	46	0.1	310	30.3	3100	3180	G	4.24	25.28427	84.802862	Normal
22/3/21	12: 24: 29	46	0.1	350	30.3	3500	3554	G	4.68	25.28399	84.803737	Normal
22/3/21	12: 24: 39	46	0.1	370	30.3	3700	3741	G	4.9	25.283693	84.804763	Normal
22/3/21	12: 24: 49	46	0.1	340	30.3	3400	3460	G	4.57	25.28363	84.80574	Normal
22/3/21	12: 25: 4	46	0.1	350	30.3	3500	3554	G	4.68	25.283593	84.8068	Normal
22/3/21	12: 25: 20	46	0.1	340	10.1	3400	3460	G	4.57	25.283527	84.807793	Speed Breaker
22/3/21	12: 25: 30	46	0.1	300	30.3	3000	3086	G	4.13	25.283458	84.808753	Normal
22/3/21	12: 25: 40	46	0.1	390	30.3	3900	3928	G	5.12	25.283395	84.80978	Normal
22/3/21	12: 25: 50	46	0.1	380	30.3	3800	3835	G	5.01	25.283345	84.810773	Normal
22/3/21	12: 26: 0	46	0.1	360	30.3	3600	3648	G	4.79	25.283282	84.81182	Normal
22/3/21	12: 26: 10	46	0.1	360	30.3	3600	3648	G	4.79	25.283225	84.812793	Normal
22/3/21	12: 26: 30	46	0.1	370	10.1	3700	3741	G	4.9	25.283158	84.813855	Speed Breaker
22/3/21	12: 26: 40	46	0.1	310	30.3	3100	3180	G	4.24	25.283108	84.814882	Normal
22/3/21	12: 27: 0	46	0.1	340	30.3	3400	3460	G	4.57	25.283182	84.815875	Normal

22/3/21
22.05.2021
22

22.05.2021
22

22

22

Date	Time	Section	Length	Bumps	Speed	OR	UIV	CATEGORY	IRI	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD				
22/3/21	12:27:16	46	0.1	360	30.3	3600	3648	G	4.79	25.283237	84.816858	Normal
22/3/21	12:27:26	46	0.1	360	30.3	3600	3648	G	4.79	25.283308	84.817945	Normal
22/3/21	12:27:41	46	0.1	310	30.3	3100	3180	G	4.24	25.283263	84.818905	Normal
22/3/21	12:28:16	46	0.1	390	10.1	3900	3928	G	5.12	25.283303	84.819848	Speed Breaker
22/3/21	12:28:26	46	0.1	370	30.3	3700	3741	G	4.9	25.2828	84.820892	Normal
22/3/21	12:28:36	46	0.1	350	30.3	3500	3554	G	4.68	25.282577	84.821868	Normal
22/3/21	12:29:0	46	0.1	300	30.3	3000	3086	G	4.13	25.282347	84.82281	Normal
22/3/21	12:29:10	46	0.1	370	30.3	3700	3741	G	4.9	25.282122	84.82377	Normal
22/3/21	12:29:26	46	0.1	360	30.3	3600	3648	G	4.79	25.281888	84.82478	Normal
22/3/21	12:29:36	46	0.1	310	30.3	3100	3180	G	4.24	25.28166	84.825757	Normal
22/3/21	12:29:46	46	0.1	340	10.1	3400	3460	G	4.57	25.281412	84.82675	Speed Breaker
22/3/21	12:30:11	46	0.065	300	30.3	3000	3086	G	4.13	25.28125	84.82744	Normal
TOTAL			5.165	17140	1403.9	171400	174887		231.59	1314.66136	4409.81417	
AVERAGE						3296.154	3363.212		4.453654			

Almudena
25/3/21
24060717

22.03.2021
5.8

28/03/2021
K.C.

8314

Name of Customer : KRISHABH NIRMAN PVT LTD
Name of Work/ Road : KHANPURA TO MERA PATAL
Lab Job number :
Date : 22-03-2021
Section No. : 46


Test Date : 22-03-2021
Machine No :
Start S No :
Start E No :
Weather :
Start Location :
End Location :
Road Name : KHANPURA TO MERA PATAL
Road Type : (H) RURAL ROAD
Side :
U/V Range : 324 To 5000 Interval :
Dist Range : 0 To 53 01 1000 m/km
Equation : 1000 m

Print Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\SHAZ\Desktop\46.xls. Section No. : 46. Egn :
Name of Customer : KRISHABH NIRMAN PVT LTD. Name of Work/ Road : KHANPURA TO MERA PATAL. Lab

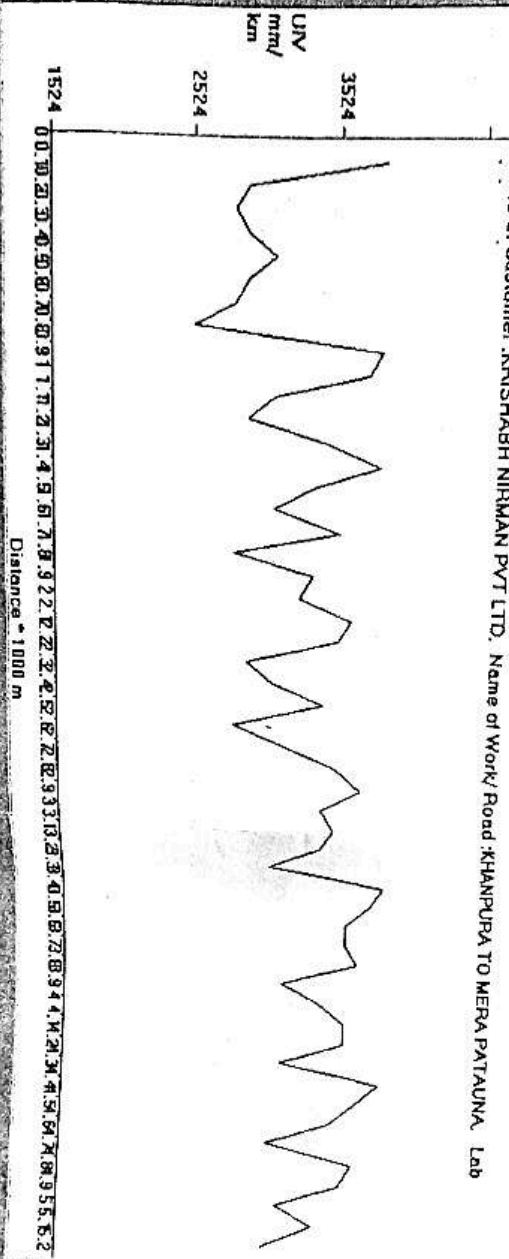

Moisture
92.3/91
Add 11% moisture

22.03.2021
JS

22/03/21
A.E

M 0574

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, क्षेत्रीय प्रयोगशाला, गुलजारबाग
पटना-800007

पत्रांक - 338/1150

पटना/दिनांक 06-03-2021

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना -7

सेवा में,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल Paliganj.

विषय :- जाँचफल प्रतिवेदन के संबंध में।

प्रसंग :- AE, Paliganj, vide letter NO-15 3380

महाशय, Date - 24/2/21

उपर्युक्त विषयक के संबंध में जाँचफल प्रतिवेदन इस पत्र के साथ संलग्न कर आवश्यक कारवाई हेतु भेजा जा रहा है जो निम्न प्रकार है:-

1) Kharbura to Mera Patanona

1) 3380

अनु:-यथोक्त

विश्वासभाजन

११/३/२१

कार्यपालक अभियंता
ग्रामीण कार्य विभाग

क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना -7

OFFICE OF THE EXECUTIVE ENGINEER

03/03/2021

366

REGIONAL LABORATORY, R. W. D., GULZARBAGH, PATNA - 7

PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

Name of Project/Road : Khanpura to Mera Patana

Name of Scheme : MR - 3054

Name of Agency : Krishabh Nirmal Pvt Ltd.

Nature of sample:- Semi Dense Bituminous Concrete Date of Collection/Received :- 01/03/2021

Location : 2200 M

Date of Test : 05/03/2021

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division Paligarh

vide letter No. 19415 Dt. 26/02/2021

Agreement No / Package No. : 03/M&D/2020-21

Sl. No.	A.I.V.	
	Average Test Value	Required Value(Max)
1.	—	30%

Sl. No.	Sieve Size in (mm)	Weight of Sample Taken Kgs 17.320					Remarks
		Weight Retd.	% of Wt. Retained	% of Cum. Retained	% of Passing	Required value	
1	13.2	0.000	0.00	0.00	100	100	
2	9.5	0.831	4.80	4.80	95.20	90-100	
3	4.75	8.392	48.45	53.25	46.75	35-51	
4	2.36	3.022	17.45	70.70	29.30	24-39	
5	1.18	1.368	7.90	78.60	21.40	15-30	
6	0.300	1.412	8.15	86.75	13.25	9-19	
7	0.075	1.637	9.45	96.20	3.80	3-8	

Copy Submitted to/forwarded to:

E.E. R.W.D. Works Division :- Masgaurhi

Ranish
05/03/21

5/3/21
A.D.

Ranish Kumar
05/03/2021
A.E.

05/03/21
E.E.

Regional Laboratory

Regional Laboratory

Regional Laboratory

Regional Laboratory

R. W. D. Guljarbagh patna - 7

R. W. D. Guljarbagh patna - 7

R. W. D. Guljarbagh patna - 7

R. W. D. Guljarbagh patna - 7

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D., GULZARBAGH, PATNA - 7

PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

06/03/2021

Name of Project/Road :- Khanpura to Mera Patana

Name of Scheme :- MLR-3054

Name of Agency :- Krishabh Nirman Pvt Ltd.

Nature of sample :- Semi Dense Bituminous Concrete Date of Collection/Received :- 1/3/21

Location :- 950m

Date of Test :- 5/3/21

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division

vide letter No. 15288 Dt. 29/2/21

Agreement No / Package No. : 03/MBD/2020-21

Sl. No.	A.I.V	
	Average Test Value	Required Value(Max)
1.	<u>/</u>	30%

Sl. No.	Sieve Size in (mm)	Weight of Sample Taken Kgs					Remarks
		Weight Retd.	% of Wt. Retained	% of Cum. Retained	% of Passing	Required value	
1	13.2	0.000	0.00	0.00	100	100	
2	9.5	0.514	2.80	2.80	97.20	90-100	
3	4.75	8.725	47.55	50.35	49.65	35-51	
4	2.36	3.202	17.45	67.80	32.20	24-39	
5	1.18	1.395	7.60	75.40	24.60	15-30	
6	0.300	1.798	9.80	85.20	14.80	9-19	
7	0.075	1.789	9.75	94.95	5.05	3-8	

Copy Submitted to/forwarded to:

E.E. R.W.D. Works Division:-

Raias
5/3/2021

Regional Laboratory
R. W. D. Guljarbagh patna - 7

Krishabh
5/3/21

A.D.
Regional Laboratory
R. W. D. Guljarbagh patna - 7

Ramesh
05/03/2021

A.E.
Regional Laboratory
R. W. D. Guljarbagh patna - 7

Ramesh
05/03/2021

E.E.
Regional Laboratory
R. W. D. Guljarbagh patna - 7

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D. GULJARBAUGH, PATNA - 7

PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

Name of Project/Road

1. Ramba. An. N. S. 8/10/2020

Name of Scheme

MR/3054

Name of Agency

Prashant Kumar Pvt Ltd.

Nature of sample

Mix seal (13.2mm to 0.075mm)

Date of Collection/Received

1/3/21

Location

Date of Test

5/3/21

Ref: Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division

vide letter No.

03/10/22.2.21.

8/10/2020

Agreement No / Package No. :

03/10/2020-21

Sl. No.	A.I.V.	
	Average Test Value	Required Value(Max)
1.		40%

Sl. No.	Sieve Size in (mm)	Weight of Sample Taken Kgs 16.785				Required Value		Remarks
		Weight Retd.	% of Wt. Retained	% of Cum. Retained	% of Passing	Type A	Type B	
1	13.2	0.000	0.00	0.00	100		100	✓
2	11.2	0.297	1.75	1.75	98.25	100	88-100	
3	5.6	2.662	15.85	17.60	82.40	52-88	31-52	
4	2.8	4.431	26.40	28.15	71.85	14-38	5-25	
5	0.075	3.449	20.55	28.15	71.85	0.5	0.5	

Ratish
LA
3/3/21

3/3/21
A.D.

Ratish Kumar
A.E.
05/03/2021

05/03/2021
E.E.

Regional Laboratory
R.W.D. Guljarbagh patna - 7

Regional Laboratory
R.W.D. Guljarbagh patna - 7

Regional Laboratory
R.W.D. Guljarbagh patna - 7

Regional Laboratory
R.W.D. Guljarbagh patna - 7

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, क्षेत्रीय प्रयोगशाला, गुलजारबाग
पटना-800007

पत्रांक 366/अड

पटना/दिनांक 02-03-2021

प्रेषक

कार्यपालक अभियंता

ग्रामीण कार्य विभाग

क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना -7

सेवा में

कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रमाण्डल पालीग्राम

विषय :- जॉचफल प्रतिवेदन के संबंध में।

प्रसंग :- A.E. Road (w) Sub-Division : Paligrama vide letter No. 19 अड, Dt-26/02/2021

महाशय,

उपर्युक्त विषयक के संबंध में जॉचफल प्रतिवेदन इस पत्र के साथ संलग्न कर आवश्यक कारवाई हेतु भेजा जा रहा है जो निम्न प्रकार है:-

N/R- Khajurpur to Bhera Bittamra

Ag. No.- 03/08 D/2020-21

- 1) S.D.B.C.
- 2) Bitumen Content

अनु:- यथोक्त

विश्वासभाजन

9/3/21

कार्यपालक अभियंता

ग्रामीण कार्य विभाग

क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना -7

Date 09/03/2021

366

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D., GULZARBAGH, PATNA - 7

Bituminous mix

Name of Project/Road :- Khanpura to Mera Patana

Name of Scheme :- MR-3054

Name of Agency :- Krishabh Nirman Pvt Ltd.

Nature of sample :- Bitumen content for S.D.B.C.

Location :- 2200mtr

Date of Collection/Received :- 01/03/2021

Date of Test :- 09/03/2021

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division Paliganj vide letter No. 19430 Dt. 26.02.2021

Agreement No / Package No. : 03/M&D/2020-2021

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	504.00	501.00	509.00	
2	Wt. of Dry chips after extraction (b)	477.74	474.85	482.92	
3	Percentage of bitumen (in the mix) $[(a-b)*100]/a$ (%)	5.21	5.22	5.12	
4	Average % bitumen	5.18			

RAVISH
LA 9/3/2021
Regional Laboratory
R.W.D. Guljarbagh patna - 7

A.D.
Regional Laboratory
R.W.D. Guljarbagh patna - 7

RAVISH KUMAR
A.E.
Regional Laboratory
R.W.D. Guljarbagh patna - 7

E.E.
Regional Laboratory
R.W.D. Guljarbagh patna - 7

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, क्षेत्रीय प्रयोगशाला, गुलजारबाग
पटना-800007

पत्रांक 339/अनु

पटना/दिनांक 06-03-2021

प्रेषक

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना -7

सेवा में

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल Paligami.

विषय :- जॉचफल प्रतिवेदन के संबंध में।

प्रसंग :- A.E., Paligami vide letter NO-09 dated
Date-22.2.21.

महोदय,

उपर्युक्त विषयक के संबंध में जॉचफल प्रतिवेदन इस पत्र के साथ संलग्न कर आवश्यक कारवाई हेतु भेजा जा रहा है जो निम्न प्रकार है:-

Hampura to Mera Patanna

Mix Seed

(13.2 mm to 0.9 mm)

अनु:-यथोक्त

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना -7
