

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, महुआ।

पत्रांक 81 /

महुआ / दिनांक 08 / 01 / 2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, महुआ।

सेवा में,

नोडल पदाधिकारी,
एम0आर0 3054 नई अनुरक्षण नीति 2018,
विश्वेश्वरैया भवन,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय : शीर्ष एम0आर0 3054 नई अनुरक्षण नीति 2018 अन्तर्गत पथ में कराये गए कार्य के विरुद्ध अधियाचना भेजने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष एम0आर0 3054 नई अनुरक्षण नीति 2018 अन्तर्गत पथ में कराये गए कार्य के विरुद्ध अधियाचना इस पत्र के साथ समर्पित की जा रही है।

विश्वासभाजन,



08.01.22

कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
महुआ।

Requisition Formate for Scheme Head- MR-3054 Under Bihar Rural Road Maintenance Policy 2018 (In Rectification and Surface Renewal)

Division Name:- Rural Works Department, Works Division, Mahua

S.No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lacs)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (In Km)	Thickness of Bitumen Layer (In mm)	Value of Bitumen Content in %	Previous Total Allocated Amount (In Lacs)	Upto date Expenditure as per MIS (In Lacs)	Requisition Done (In Lacs)	Remarks
					Length (In Km.)	Amount (In Lacs)	Initial Rectification on surface Renewal (In Lacs)	5 Years Routine Maintenance (In Lacs)										
1	MR-N/19-20 Mahua/10	Chhiwara Kapur - Jahangirpur Salhani	NEA220002397	3610/26.08.2019	6.85	216.400	119.40810	62.51609	32/MBD/MR-3054/2020-21	25.08.2021		2504	25.00	5.00	0	0	119.40810	Work Completed
2	MR-N/19-20 Mahua/17	Bikanpur - Rampur Diliwar	31507502049	3610/26.08.2019	3.170	104.486	58.09023	29.54091	76/MBD/MR-3054/2020-21	13.12.2021		1644	25.00	5.00	0	0	58.09023	Work Completed
															0	0	177.49833	

Executive Engineer
R.W.D, Works Division, Mahua

[Signature]
08.01.22

Form GFR 19-A

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate upto the month- 08 .01.2022

STATE- BIHAR

SL. No	Name of Scheme	Sanction No. & Date With Amount (In Rs. Lacs)	Amount Received (In Rs.Lacs)	Particulars
1	Construction of Rural Roads under MR New Maintenance Policy 2018	Lt-02 Dated-03-01-2022 Amount- 2469.06493	2469.06493	Certified that out of Rs. 2469.06493 Lacs of grants-in-aid sanctioned upto 12/2017 in favour of E-in-C, REO Bihar, Patna a sum of Rs.2007.39253 lacs has been utilized for the purpose of MR New Maintenance Policy 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs- 461.67240 lacs remaining unutilized at the end of the period under.
	Total:		2469.06493	

Certified that I have satisfied myself that the conditions on which the gram-in-aid was sanctioned have

- 2 been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.


Kind of Checks exercised:-

- i Works has been supervised by Executive Engineer/Superintending Engineer.
- ii Periodical inspection has been conducted by Executive Engineer/Superintending
- iii Construction materials have been tested.
- iv Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/ Executive Engineer
- v All other codal formalities have been observed.

3 Physical Progress achieved:-

- i Construction of Road Works.
- ii Construction of CD Works.

Divisional Account Officer
RWD. Works Division, Mahua


08.01.22
Executive Engineer
RWD. Works Division, Mahua

Name of the work: Bikanpur - Rampur Dilwar

Date	Time	Test No	Distance (meter)	Total Distance (meter)	BUMP (cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
07-01-2022	14:53:38	5	100	100	7.0 cm	6.5 Km/Hr	700.0 mm/Km	761.3	1.184	Good	25.8342123	N	85.4774256	E	Normal
07-01-2022	14:54:10	5	100	200	8.0 cm	11.1 Km/Hr	800.0 mm/Km	852.2	1.31	Good	25.8342123	N	85.4774256	E	Normal
07-01-2022	14:54:36	5	100	300	5.0 cm	13.4 Km/Hr	500.0 mm/Km	579.5	0.928	Good	25.8342123	N	85.4774256	E	Normal
07-01-2022	14:54:57	5	100	400	12.0 cm	17.5 Km/Hr	1200.0 mm/Km	1215.8	1.799	Good	25.8342123	N	85.4774256	E	Normal
07-01-2022	14:55:17	5	100	500	11.0 cm	18.3 Km/Hr	1100.0 mm/Km	1124.9	1.678	Good	25.8342123	N	85.4774256	E	Normal
07-01-2022	14:55:38	5	100	600	14.0 cm	16.9 Km/Hr	1400.0 mm/Km	1397.6	2.037	Good	25.8342123	N	85.4774256	E	Normal
07-01-2022	14:55:59	5	100	700	16.0 cm	17.1 Km/Hr	1600.0 mm/Km	1579.4	2.272	Good	25.8342123	N	85.3528299	E	Normal
07-01-2022	14:56:19	5	100	800	9.0 cm	17.4 Km/Hr	900.0 mm/Km	943.1	1.434	Good	25.716876	N	85.3528299	E	Normal
07-01-2022	14:56:41	5	100	900	18.0 cm	16.6 Km/Hr	1800.0 mm/Km	1761.2	2.504	Good	25.716876	N	85.3528299	E	Normal
07-01-2022	14:57:04	5	100	1000	12.0 cm	15.8 Km/Hr	1200.0 mm/Km	1215.8	1.799	Good	25.716876	N	85.3528299	E	Normal
07-01-2022	14:57:27	5	100	1100	14.0 cm	15.7 Km/Hr	1400.0 mm/Km	1397.6	2.037	Good	25.716876	N	85.3528299	E	Normal
07-01-2022	14:58:40	5	100	1200	8.0 cm	4.7 Km/Hr	800.0 mm/Km	852.2	1.31	Good	25.7151422	N	85.3552408	E	Normal
07-01-2022	14:59:13	5	100	1300	22.0 cm	11.0 Km/Hr	2200.0 mm/Km	2124.8	2.961	Good	25.7135019	N	85.3553095	E	Normal
07-01-2022	14:59:40	5	100	1400	14.0 cm	13.5 Km/Hr	1400.0 mm/Km	1397.6	2.037	Good	25.7128019	N	85.3559427	E	Normal
07-01-2022	15:00:03	5	100	1500	29.0 cm	15.4 Km/Hr	2900.0 mm/Km	2761.1	3.741	Good	25.7121763	N	85.3562174	E	Normal
07-01-2022	15:00:39	5	100	1600	16.0 cm	10.0 Km/Hr	1600.0 mm/Km	1579.4	2.272	Good	25.7112932	N	85.355958	E	Normal
07-01-2022	15:01:09	5	100	1700	12.0 cm	12.1 Km/Hr	1200.0 mm/Km	1215.8	1.799	Good	25.7107553	N	85.3557825	E	Normal
07-01-2022	15:01:37	5	100	1800	10.0 cm	12.4 Km/Hr	1000.0 mm/Km	1034	1.556	Good	25.7096128	N	85.3553705	E	Normal
07-01-2022	15:01:59	5	100	1900	8.0 cm	16.8 Km/Hr	800.0 mm/Km	852.2	1.31	Good	25.708827	N	85.3551111	E	Normal
07-01-2022	15:02:18	5	100	2000	5.0 cm	18.0 Km/Hr	500.0 mm/Km	579.5	0.928	Good	25.7078428	N	85.3546381	E	Normal
07-01-2022	15:02:40	5	100	2100	3.0 cm	17.0 Km/Hr	300.0 mm/Km	397.7	0.663	Good	25.7074957	N	85.3538065	E	Normal
07-01-2022	15:02:56	5	100	2200	10.0 cm	21.6 Km/Hr	1000.0 mm/Km	1034	1.556	Good	25.7074881	N	85.3528986	E	Normal
07-01-2022	15:03:21	5	100	2300	2.0 cm	15.2 Km/Hr	200.0 mm/Km	306.8	0.526	Good	25.7078257	N	85.3517389	E	Normal
07-01-2022	15:03:39	5	100	2400	6.0 cm	19.8 Km/Hr	600.0 mm/Km	670.4	1.057	Good	25.7080812	N	85.3510065	E	Normal

07/01/22
AE

07/01/22
AE

07.01.22
E.E

07-01-2022	15:03:59	5	100	2500	16.0 cm	18.0 Km/Hr	1600.0 mm/Km	1579.4	2.272	Good	25.7084932	N	85.3500299	E	Normal
07-01-2022	15:04:20	5	100	2600	10.0 cm	16.5 Km/Hr	1000.0 mm/Km	1034	1.556	Good	25.7090712	N	85.3497705	E	Normal
07-01-2022	15:04:38	5	100	2700	11.0 cm	20.4 Km/Hr	1100.0 mm/Km	1124.9	1.678	Good	25.7099943	N	85.350358	E	Normal
07-01-2022	15:04:59	5	100	2800	6.0 cm	17.0 Km/Hr	600.0 mm/Km	670.4	1.057	Good	25.7108088	N	85.350831	E	Normal
07-01-2022	15:05:18	5	100	2900	7.0 cm	18.8 Km/Hr	700.0 mm/Km	761.3	1.184	Good	25.7114763	N	85.3514338	E	Normal
07-01-2022	15:05:40	5	100	3000	7.0 cm	16.8 Km/Hr	700.0 mm/Km	761.3	1.184	Good	25.7121668	N	85.3520823	E	Normal
07-01-2022	15:11:02	5	100	3100	7.0 cm	1.1 Km/Hr	700.0 mm/Km	761.3	1.184	Good	25.7128916	N	85.3524713	E	Normal
07-01-2022	15:11:26	5	100	3200	12.0 cm	14.7 Km/Hr	1200.0 mm/Km	1215.8	1.799	Good	25.7128916	N	85.3524713	E	Normal

IRI Value 1644
Machine ID 19190

7/1/2022
JE

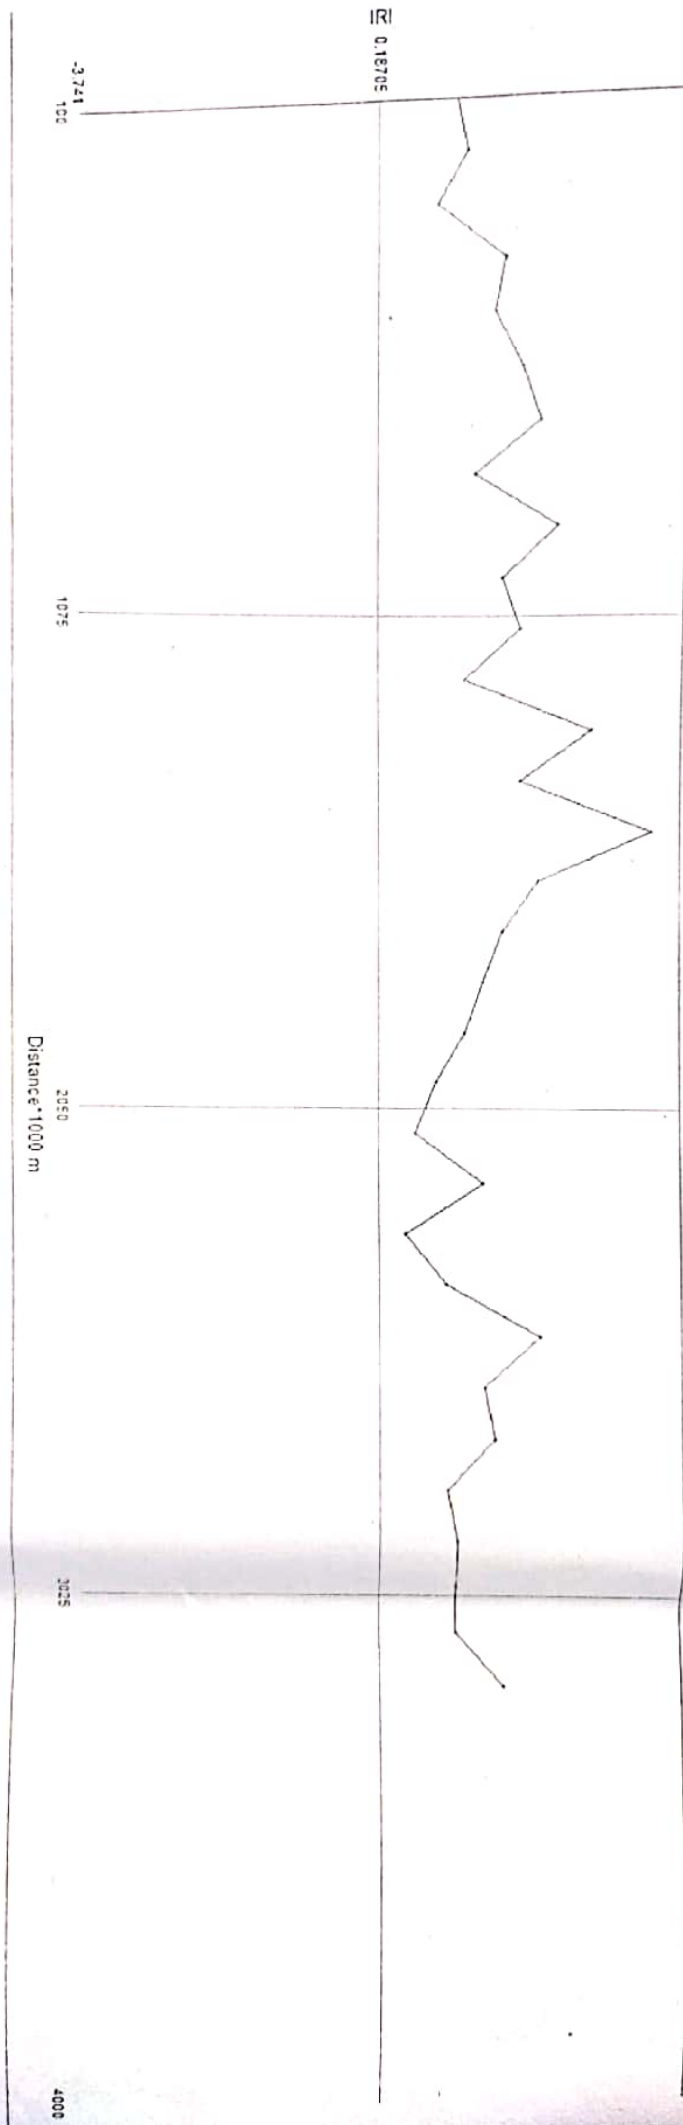
07/01/22
AE

07-01-22
EE

4.1151

Name of Customer: M/S MARUTI ENTERPRISES, Machine no: 19190, Road: Bilkaurpur - Rampur Dilwar, Date: 08-01-22, Section No: 5, Equation: $Y=0.909X+125.0$

E 0.18705



9/11/2022
JC

18/01/22
AE

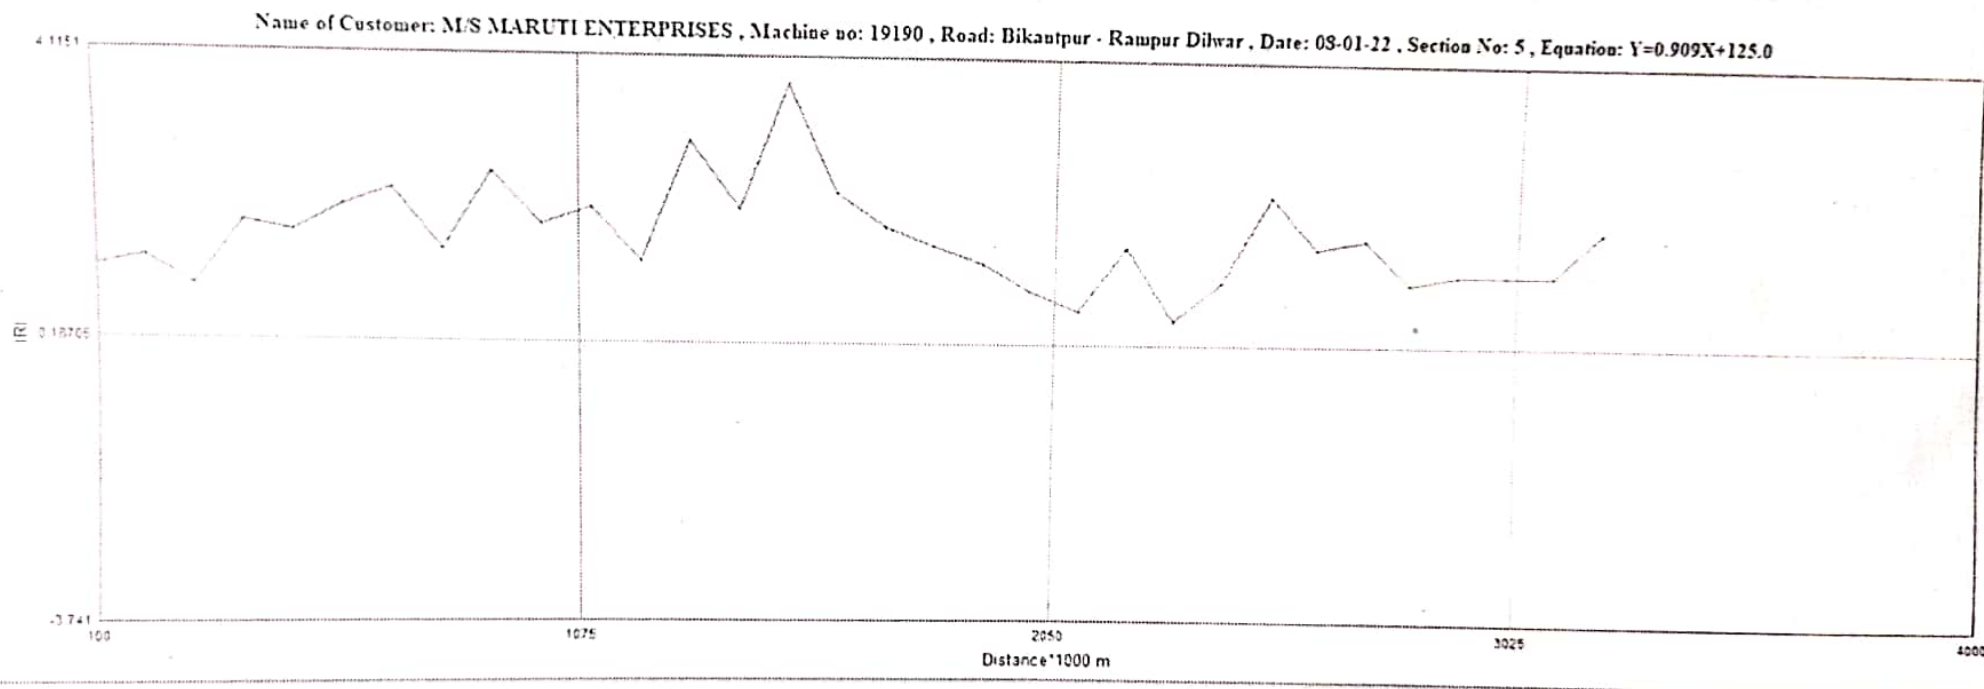
Shanghi
07.01.22
EE

Name of Customer: M/S MARUTI ENTERPRISES
 Name of Work/Road: Bikantpur - Rampur Dilwar
 Lab Job Number: 5
 Date: 08 January 2022
 Section No: 5
 m: 0.909 c: 125.0

Test Date: 05 January 2022
 Machine no: 19190
 Start S No:
 Start E No:
 Weather:
 Start Location:
 End Location:

Road Name: Bikantpur - Rampur Dilwar
 Road Type:
 Side:
 UIV Range:
 Dist Range:
 Equations: $Y=0.909X+125.0$
 To: Interval: mm/km
 To: 1000m

Graph Corrected IRI v/s Distance: Corrected IRI v/s distance: Data
 Graph:



7/1/2022
 Jor

07/01/22
 AE


67.01.22


प्रमाण-पत्र

पथ का नाम - Baikantpur - Rampur Dilwar.
योजना - एम0आर0 (3054) नई अनुरक्षण नीति 2018
कार्य प्रमंडल - महुआ।
प्रखंड - राजापाकर।

उक्त पथ में कराये गये सभी अवयवों के अवयववार कार्य निम्नलिखित पदाधिकारी द्वारा मापी पुस्तिका से सत्यापन किया गया।

क्र0	पदनाम	कराये गये कार्य के मापी पुस्तिका से सत्यापन की प्रतिशत	अभ्युक्ति
1	कनीय अभियंता	100 प्रतिशत	
2	सहायक अभियंता	50 प्रतिशत	
3	कार्यपालक अभियंता	10 प्रतिशत	


कनीय अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रशाखा-राजापाकर।


सहायक अभियंता,
ग्रामीण कार्य विभाग,
कार्य अवर प्रमंडल, राजापाकर।


08.01.22
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, महुआ।

1st A/c Bill

Name of work—

1

Situation of work—

Agency by which work is executed—

Date of measurement—

No. and date of agreement.

(These four lines should be repeated at the commencement of the measurements relating to each work.)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work - Backwater pur to Rampur Dehwar Block Raja Pagar.					
Name of contractor - M/s Maruti Enterprises.					
Agreement No - 3.170 km.					

Length - 3.170

Estimated cost -

Work done.

1) Cleaning and grubbing
Road land - E13

$$105 \text{ Nos} \times 30 \text{ m} \times 1.00 = 3150 \text{ m}^2$$

$$31 \times 20 \text{ m} \times 1.00 = 20 \text{ m}^2$$

$$3170 \text{ m}^2$$

$$2 \times 3170 \text{ m}^2 = 0.63 \text{ Hec}$$

