

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सिकहरना, ढाका।

पत्रांक - ९१९ / सिकहरना, ढाका, दिनांक- ३०.०६.२०२२

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिकहरना, ढाका।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
ग्रामीण कार्य विभाग,
विश्वसरैया भवन, पाच्चा तल्ला, बिहार, पटना।



विषय :- M/R (3054) New Maintenance Police 2018 योजना हेतु आवंटन अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि इस प्रमंडलान्तर्गत M/R (3054) New Maintenance Police 2018 योजना के अधीन कराये गये कार्य के विरुद्ध भुगतान हेतु आवंटन अधियाचना विहित-प्रपत्र में संलग्न कर समर्पित किया जाता है।

अनुलग्नक :- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता, २३.६.२२
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
सिकहरना, ढाका।

२३/०६/२२

Requisition Formate for Scheme Head- 5 Year Maintenance of MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and surface Renewal)

Name of Division :- Dhaka

Name of Circle :- Motihari

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Sanction Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Current Maintenance Demand (In Lacs)			Remarks
					Length (In km)	Amount of (in lakh)	Initial Rectification with surface Renewal (in lakh)	5 Year Routine Maintenance (In lakh)				1st Qtr Maint. Demand	2nd Qtr Maint. Demand	3rd Qtr Maint. Demand	
1	RM/EA/SIK/19/0008	Purnahiya jharokhar Road to Nagarwa Tola	31708602127	3034/ 16.07.2019	2.53	97.12100	56.78044	26.44934	45MBD/2019-20 Dt-21.30.2020	20.12.2020	16.02.2021	1.31981	1.31981	1.31981	
2		Purnahiya jharokhar Road to Jagiraha	31708602125		3.20	127.77500	76.32295	32.46997			20.02.2021	1.62269	1.62269	1.62269	
3		East Champaran jila antargat ghorasahan prkhand me purandea jharokhar path me baswariya se len hote hua ghorasahan pani tanki tak path ka nirman	31708603015		2.10	83.75600	41.20436	19.78813			20.02.2021	0.91895	0.91895	0.91895	
					83.75600			19.78813				0.91895	0.91895	0.91895	

Divisional Accounts Officer
Rural Works Div, Dhaka

- 1 उपरोक्त पथों का मूल कार्य विशिष्टियों के अनुरूप पूर्ण कराया जा चुका है।
2 सर्वेदकों के द्वारा किये गये अनुरक्षण कार्य का मासिक विपत्र प्रमंडल में प्राप्त है।

Executive Engineer
RWD (W) Div. Dhaka


FORM GFR 19-A

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate Upto the Month of upto.....
MR 3054 New Maintenance Policy-2018

PIU :- EE RWD (W) DIVISION DHAKA

Sl.	Name of the Scheme	Sanction No. & Date with Amount (Rs. In Lakh)	Amount Received (Rs. In Lakh)	Particulars
1	Construction of Rural Roads Under MR-3054 New Maintenance Policy-2018			Certified that out of Rs. Nil Lacs received the year 2022-23 in favor of Executive Engineer, R.W.D. (W), Division Dhaka a sum of Rs. Nil lacks has been utilized for the purpose of MR 3054 New Maintenance Policy-2018 Schemes as given in the margin for which it was sanctioned of Rs. Nil Remaining unutilized at the end of the period under.
Total :-				

Certified that I have satisfied my self that the condition on which the grants-in-aid was sanctioned have been duly fulfilled are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.



Divisional Account Officer
R.W.D. (W) Div., Dhaka

Kind of Checks Exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conduct by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurement have been recorded in the MBs and test check conducted by the Assistant.
- All other codal Formalities have been observed.

Physical Progress achieved :-

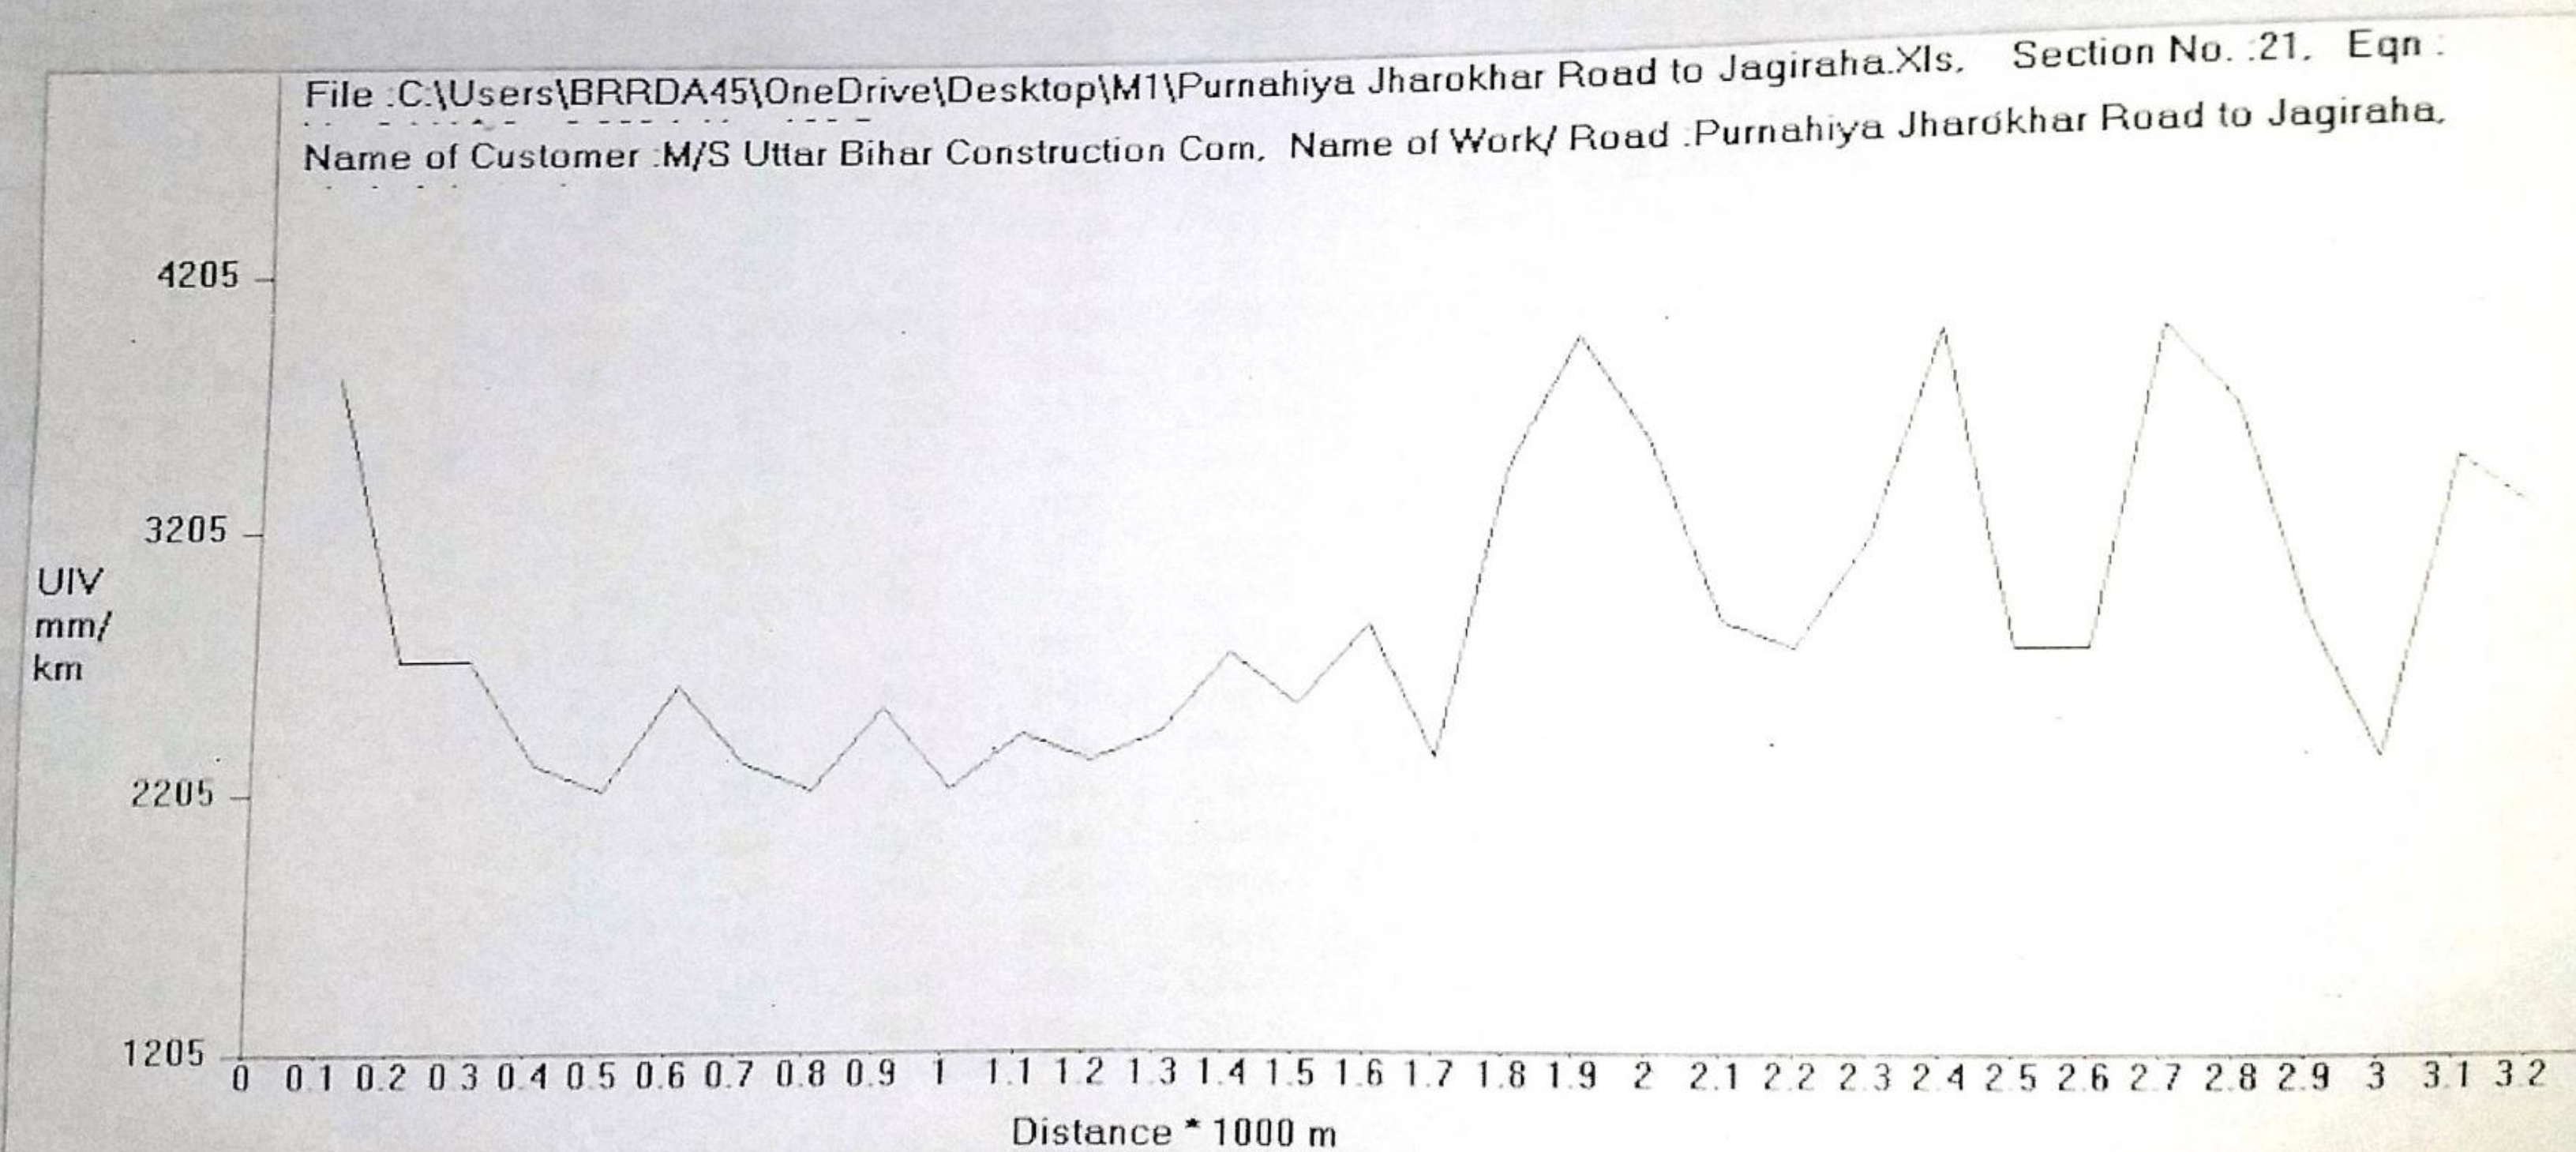
- Construction of Road Works.
- Construction of CD Works.


Executive Engineer 23.6.22
R.W.D.(W) Div., Dhaka

Steco Analyze

Name of Customer : M/S Uttar Bihar Construction Com
 Name of Work/ Road : Purnahiya Jharokhar Road to Jagiraha
 Lab Job number :
 Date : 28-02-2022
 Section No. : 21

Test Date : 28-02-2022	Road Name : Purnahiya Jharokhar Road to Jagiraha
Machine No : 378	Road Type : (R) RURAL ROAD
Start S No : 0.00 KM	Side : Interval
Start E No : 3.202 KM	UIV Range : 1205 To 5000 1000 mm/km
Weather :	Dist Range : 0 To 3.3 0.1 * 1000 m
Start Location : 26.80067	Equation : $Y = 0 \cdot X^2 + 0.998 \cdot X + 109.5$
End Location : 85.15581	



Subendrapr
 28.02.22
 J.E

[Signature]
 28.02.22

Road Name- Purnahiya Jharokhar Road to Jagiraha, Contractor-M/S Uttar Bihar Construction Com

Date	Time	Section	Length	Bumps	Speed	OR	IRI in	CATEGO	Latitude	Longitu	Event	Y = 0 * X ^ 2 + 0.998 * X + 109.5
No.		in km	in mm	Rate	mm/km	UIV	mm/km	RY		de		
28/ 2/ 22	12: 44: 39	21	0.1	250	0	3700	3802	G	26.80067	85.13658	Normal	X = 2100
28/ 2/ 22	12: 44: 39	21	0.1	250	20.2	2600	2704	G	26.80101	85.13746	Normal	Y = 2205
28/ 2/ 22	12: 45: 0	21	0.1	200	20.2	2600	2704	G	26.80099	85.13837	Normal	
28/ 2/ 22	12: 45: 0	21	0.1	230	20.2	2200	2305	G	26.80125	85.13936	Normal	
28/ 2/ 22	12: 45: 14	21	0.1	190	20.2	2100	2205	G	26.80173	85.14015	Normal	(R) RURAL ROAD
28/ 2/ 22	12: 45: 14	21	0.1	200	20.2	2500	2604	G	26.80125	85.14103	Normal	Good Average Poor
28/ 2/ 22	12: 45: 14	21	0.1	180	30.3	2200	2305	G	26.80083	85.14192	Normal	<4000 4001-5000 >5001
28/ 2/ 22	12: 46: 0	21	0.1	210	20.2	2100	2205	G	26.80067	85.1429	Normal	
28/ 2/ 22	12: 46: 0	21	0.1	220	20.2	2400	2504	G	26.801	85.1438	Normal	
28/ 2/ 22	12: 46: 25	21	0.1	240	20.2	2100	2205	G	26.80119	85.14478	Normal	
28/ 2/ 22	12: 46: 25	21	0.1	230	10.1	2300	2404	G	26.801	85.14572	Normal	
28/ 2/ 22	12: 46: 25	21	0.1	220	20.2	2200	2305	G	26.80071	85.14663	Normal	
28/ 2/ 22	12: 47: 0	21	0.1	290	10.1	2300	2404	G	26.80043	85.14758	Normal	
28/ 2/ 22	12: 47: 0	21	0.1	270	20.2	2600	2704	G	26.80026	85.14848	Normal	
28/ 2/ 22	12: 47: 35	21	0.1	190	20.2	2400	2504	G	26.80012	85.14956	Normal	
28/ 2/ 22	12: 47: 35	21	0.1	200	20.2	2700	2804	G	26.79968	85.15035	Normal	
28/ 2/ 22	12: 49: 0	21	0.1	210	30.3	2200	2305	G	26.79918	85.15111	Normal	
28/ 2/ 22	12: 49: 21	21	0.1	210	30.3	3300	3402	G	26.79876	85.15202	Normal	
28/ 2/ 22	12: 50: 0	21	0.1	210	30.3	3800	3901	G	26.79816	85.15276	Normal	
28/ 2/ 22	12: 51: 7	21	0.1	210	30.3	3400	3502	G	26.79755	85.15352	Normal	
28/ 2/ 22	12: 51: 42	21	0.1	210	30.3	2700	2804	G	26.79696	85.15426	Normal	
28/ 2/ 22	12: 52: 0	21	0.1	210	20.2	2600	2704	G	26.79625	85.15423	Normal	
28/ 2/ 22	12: 52: 18	21	0.1	190	30.3	3000	3103	G	26.79567	85.15354	Normal	
28/ 2/ 22	12: 52: 18	21	0.1	210	30.3	3800	3901	G	26.79489	85.15305	Normal	
28/ 2/ 22	12: 53: 0	21	0.1	210	30.3	2600	2704	G	26.79404	85.15298	Normal	
28/ 2/ 22	12: 53: 0	21	0.1	210	20.2	2600	2704	G	26.7931	85.1531	Normal	
28/ 2/ 22	12: 53: 28	21	0.1	240	20.2	3800	3901	G	26.79246	85.15367	Normal	
28/ 2/ 22	12: 53: 28	21	0.1	190	20.2	3500	3602	G	26.79249	85.15463	Normal	
28/ 2/ 22	12: 54: 39	21	0.1	210	30.3	2700	2804	G	26.7918	85.15522	Normal	
28/ 2/ 22	12: 54: 39	21	0.1	210	30.3	2200	2305	G	26.7911	85.15589	Normal	

Subendrakr
28.02.22
J.E

Subendrakr
28.02.22
J.E

28/2/22 12:55:0	21	0.1	200	30.3	3300	3402 G	26.79032	85.15616	Normal
28/2/22 12:55:14	21	0.1	210	20.2	3100	3203 G	26.78938	85.15581	Normal
Total IRI						90915			
Average IRI						2841.094			

Subendrakr
28.02.22
JE

AE

~~Normal~~ 28/2/22
Excutive Engineer
Rural Works Department
Works Division, Dhaka

Standard Format For Roads Quarterly Statement

3rd Quarter

PIU Name :- R.W.D., Works Div. Dhaka

1	Name of Road	Purnahiya Jharokhar road to jagiraha		
2	Batch No.	31708602125		
3	Project ID	RM/EA/SIK/19/0008		
4	Total Length of road (in K.M)	3.202		
5	Length of road to Meet Required Service Level (Completed Length) (In K.M.)	3.202		
6	No. of Total Quarter (ie 3 months as a unit) in 5 Year	20		
7	Ordinary Maintenance Cost as per Schedule {Agreement Amount For maintenance (In Lakh)}	32.46997		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (In Lakh)	1.62350		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment (6) = (3)/(1)*(2)*(4)
		Length Non Compliant	Weighted Value for Payment Reduction (%)	
	Paved Roads (Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Quarterly Payment as per Agreement				1.62350
Total Payment Reduction for the Quarter (in Lakh) (As per work done length)				0.00000
Agreement Below 0.05%				0.00081
To be paid for the Quarter/Demand (In Lakh)				1.62269

Date of Inspection by E/I or his agent
Prepared by Contractor's self Control unit

Name of Designation of Person inspecting

(Signature)

[Signature]

21.6.22
CE

Subendrak
21.06.22

Signature of Person inspecting road

Certified by E/I (Signature) Date

Requisition Formate for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)
RWD, Works Division, Dhaka (3rd Quarter)

Government of Bihar OM01 Rural Works Department			Summary of Ordinary Maintenance Inspection Report										
Road From :- Purnahiya Jharokhar road to jagiraha (Package No. - MR-N/19-20 Dhaka/08)			To		Date :-								
Length of Road :- 3.202 Km Period From :- 20.08.2021 to 19.11.2021 Inspector :- AE, RWD, Sub Division, Dhaka			Executive Engineer RWD, Works Division, Dhaka		Position :- A.E								
No.	Standard of Works Item	Work	Unit of Required in each Kilometer										Comments
No.	Name	Unit	1	2	3	4	5	6	7	8	9	10	
OM100	Seales Payment												
OM101	Pot hole Patching	m2	8.82	13.88	12.3	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Defects Rectified within Stipulated time
OM102	Surface Depression and Rut Patching	m3	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
OM103	Crack Sealing	Lm	225	575	600	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Defects Rectified within Stipulated time
OM104	Surface Treatment			Nil	Nil								
	(a) Loss of Agreegate (Surface Ravelling)	m2	5.25	9.66	20.09	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Defects Rectified within Stipulated time
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							Not Required
	© Crocodile Cracking	m2	Nil	Nil	Nil	Nil							Not Required
105	Edge Repair	m2	Nil	Nil	Nil	Nil							
106	Digouts	m2	Nil	Nil	Nil	Nil							Defects Rectified within Stipulated time
107	Concrete pavement	m3	Nil	Nil	Nil	Nil							
	Other Activities		Nil	Nil	Nil	Nil							
OM200	Shoulder		Nil	Nil	Nil	Nil							
	Unsealed Shoulder		Nil	Nil	Nil	Nil							
OM201	(a) Edge Drop-off	Lm	49	85	187	Nil	Nil	Nil	Nil				Defects Rectified within Stipulated time
	(b) Roughness Scouring or potholes	Lm	Nil	Nil	Nil	Nil							
	© Holding Water	Lm	Nil	Nil	Nil	Nil							
OM202	Embankment Repair	Lm	14.78	15.88	19.34	Nil	Nil	Nil	Nil				Defects Rectified within Stipulated time
	Other activities (Rain Cuts)	M3	Nil	Nil	Nil	Nil							
OM300	Drainage including culverts major		Nil	Nil	Nil	Nil							
OM301	Surface Drains & Verge	Lm	Nil	Nil	Nil	Nil							
OM302	Culvert Cleanning	No	Nil	Nil	Nil	Nil							Culvert Cleaning within stipulated time
OM303	Culvert and Pit Repair	M3	Nil	Nil	Nil	Nil							Not Required
	Other activities (Whilw Washing)	M2	Nil	Nil	Nil	Nil							
	Standard of Work Item	Work	Nil	Nil	Nil	Nil							
No.	Name	Unit	1	2	3	4	5	6	7	8	9	10	Comments
OM400	Vegetation		Nil	Nil	Nil	Nil							
	Gross Control		Nil	Nil	Nil	Nil							
OM401	(a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil							
	(b) Clear near Safety signs, Kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							
OM402	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Shrub Management within Stipulated time
	Cutting of Branches of Trees	No	Nil	Nil	Nil	Nil							
	Cutting of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							
	Other Activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil							Trimming of grass within Stipulated time
OM500	Safety Signage and Road	No	Nil	Nil	Nil	Nil							Not Required
OM501	Signs Maintenance	Lm	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	No	Nil	Nil	Nil	Nil							KM Post/200 mt. Post Not Required
OM503	Distance Stones	No	Nil	Nil	Nil	Nil							Road Marking Not Required
OM504	Road Marking	M2	Nil	Nil	Nil	Nil							
	Other activities												

Subendrar
21.06.22

Appendix

Executive Engineer
RWD, Works Division, Dhaka

21.6.22

Bidder
