

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, रक्सौल।

पत्रांक :- ११४ मसु

रक्सौल, / दिनांक :- ०६/०५/२२

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग, बिहार, पटना।


विषय :- बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत पाँच वर्षीय रूटीन अनुरक्षण कार्य मद योजना अन्तर्गत आवंटन निर्गत करने हेतु अधियाचना के संबंध में।
महाशय,

उपर्युक्त विषयक बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत पाँच वर्षीय रूटीन अनुरक्षण कार्य मद में संलग्न सूची के अनुसार आवंटन अधियाचना संबंधित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

अनुलग्नक :- संलग्न सूची

1. पथों का आवंटन अधियाचना प्रपत्र।
2. Bump Integrator Report

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

Standard Format For Roads Quarterly Statement (1st Quarter)

PIU Name:- Rural Works Department, (Works) Division, Raxaul

1	Name of the Road	NH-28 A to Senuariya		
2	Batch No.	RM/EA/RAX/20/0013		
3	Project ID	31708502012		
4	Total Length of Road (In Km)	1.102		
5	Length of Road to Meet Required Service Level [Completed Length] (In Km) [1]	1.102		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	10.95364		
8	Quarterly Payment: 1/20 of ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.54768		
Compliance Criteria	Standard Job Description	Non Compliance		Reduction Payment [6] = [3]/[1]*[2]*[4]
		Length Non Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	Paved Roads (Carriageway)	0	60%	0.00000
II	Shoulders and Embanments	0	10%	0.00000
III	Cross Drainage Including Culverts and Bridge	0	15%	0.00000
IV	Signage and Road Safety	0	10%	0.00000
V	Vegataion	1	5%	0.02485
Total Payment Reduction For the Quarterly (In Lakh) [5]				0.02485
To be Paid for the Quarter / Demand (In Lakh) [6]				0.52283

Date of Inspection by E/I or his agent 14/06/22

Prepared by Contractor's self Control Unit

Shyam Sunder Rai (A.E.)

Name and Designation of person inspecting road

Date: 14/06/2022

(Signature)

Signature of person inspecting road

Certify by E/I [Signature] Date

1st Quarter Summary of Ordinary Maintenance Inspection Report

To: Senuariya

Length of Road. 1.102 Km
Period: From 16.06.2021 to 15.09.2021

Inspector: A.E., RWD, Works Sub District: 10.06.2021 to 15.09.2021

Standard World-Wide
Sub Division, Raxaul

Position: Good

Date ..14/06/22

[illegible]

Standard Work Item		Work	Unit of work required in each Kilometre										Comments
No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM300 Drainage including culverts major and minor bridges													
OM301	Surface Drains & Verge												
OM302	Culvert Cleaning	Lm	NA	NA									Not Required
OM303	Culvert and Pit Repair	Lm	Nil	Nil									Not Required
	Other activities	m ³	Nil	Nil									Not Required
OM400 Vegetation													
	Grass Control												Not Required
OM401	(a) Roadside General Tidy	Ha	Nil	Nil									Not Required
	(b) Clear near safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil									Not Required
OM402	Tree and Shrub Management	Ha	Nil	Nil									Not Required
	Other activities												Not Required
OM500 Signage and Road Safety													
OM501	Signs Maintenance	No	Nil	Nil									Not Required
OM502	Guard stones	Lm	NA	NA									Not Required
OM503	Distance Stones	No	NA	NA									Not Required
OM504	Road Markings	No	Nil	Nil									Not Required
	Other activities												Not Required

2108922216122

2816122

Executive Engineer,
RWD, Works Division, Raichur

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate mm/km	OR mm/km	IRI, TEGORY ROAD	Latitude	ongitude	Event
12/6/22	17:10:0	50	0.1	310	0	3100	2926 G	26.94496	84.8347	Normal
12/6/22	17:10:12	50	0.1	360	10.1	3600	3361 G	26.94522	84.83557	Normal
12/6/22	17:11:0	50	0.1	240	10.1	2400	2318 G	26.94598	84.83609	Normal
12/6/22	17:11:23	50	0.1	280	10.1	2800	2666 G	26.94682	84.83648	Normal
12/6/22	17:12:0	50	0.1	220	10.1	2200	2144 G	26.94756	84.83685	Normal
12/6/22	17:12:0	50	0.1	290	10.1	2900	2752 G	26.94806	84.83746	Normal
12/6/22	17:12:34	50	0.1	360	10.1	3600	3361 G	26.94753	84.83823	Normal
12/6/22	17:12:34	50	0.1	240	10.1	2400	2318 G	26.94698	84.83904	Normal
12/6/22	17:13:9	50	0.1	280	10.1	2800	2666 G	26.94723	84.83966	Normal
12/6/22	17:13:44	50	0.1	220	10.1	2200	2144 G	26.94813	84.83998	Normal
		TOTAL					26656			
		AVERAGE					2665.6			

ROAD NAME-NH 28A SE SENUARIYA

$$Y = 0 * X^2 + 0.869 * X + 232.9$$

X = 3000
Y = 2839
(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

[Signature]
14/12/22

[Signature]
12/16/22
A. C.

[Signature]
6/12/22

GANPATI CONSTRUCTION

NH 28 A SE SENUAWARIYA

12-06-2022

50

Generate Report and Graph

Test Date : 12-06-2022

Road Name : NH 28 A SE SENUAWARIYA

Machine No : 406

Road Type : (A) ASPHALTIC

Start S No :

Side :

Start E No :

Interval

Weather :

UV Range : 11.44 To 4000 1000 mm/km

Start Location : NH 28 SE

Dist Range : 0 To 11 0.1 1000 m

End Location : SENUAWARIYA


Equation : Test

Redraw Graph

Map View

File : C:\Users\BRDDA126\Desktop\BUMP INTEGRATOR REPORT\axaul\NH 28 SE SENUARIYA\19.xlsx Section

Name of Customer : M/S GANPATI CONSTRUCTION. Name of Work/ Road : NH 28 A SE SENUAWARIYA. Lab Job

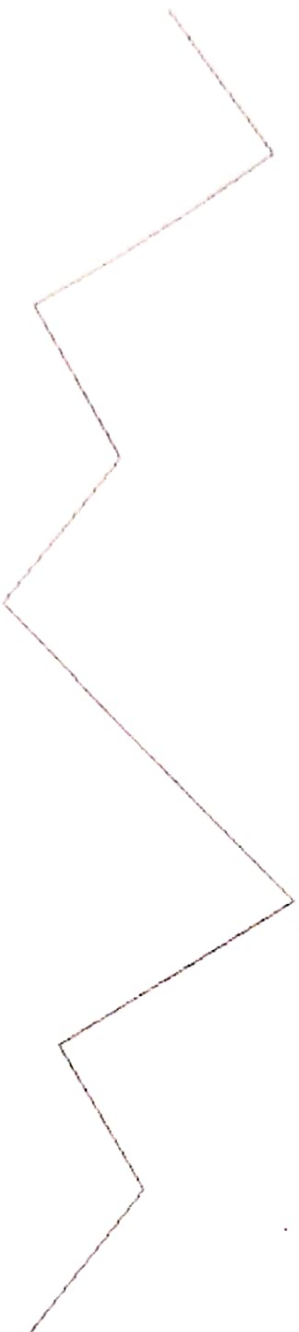

0.1 0.2 0.3 0.4 0.5 0.6 0.7 0.8 0.9 1

Distance - 1000 m

19/6/22

12/6/22
A-C

16/8/22



Latitude: 26.948434
Longitude: 84.840384
Elevation: 124.14±38 m
Accuracy: 3.1 m
Time: 07-04-2022 15:06
Note: NH28A to Senuariya



Latitude: 26.947837
Longitude: 84.837663
Elevation: 118.64±25 m
Accuracy: 1.8 m
Time: 07-04-2022 15:07
Note: NH28A to Senuariya



Latitude: 26.94745
Longitude: 84.836779
Elevation: 121.54±25 m
Accuracy: 1.8 m
Time: 07-04-2022 15:08
Note: NH28A to Senuariya

Powered by NGS



Latitude: 26.947944
Longitude: 84.837045
Elevation: 124.14±25 m
Accuracy: 2.1 m
Time: 07-04-2022 15:08
Note: NH28A to Senuanya



Latitude: 26.948537
Longitude: 84.8415
Elevation: 121.14±96 m
Accuracy: 2.5 m
Time: 07-04-2022 15:04
Note: NH28A to Senuariya
