

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम - 1

पत्रांक:- 915 3130

सासाराम/दिनांक:-01.06.2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
3054 एम0आर0 नई अनुरक्षण नीति-2018
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :- शीर्ष 3054 एम0आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।

प्रसंग :- विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुरक्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।
सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:-Sasaram-1

2nd Quarter From(30/06/2021 - 29/09/2021)

1	Name of the Road	Darigaon - Konki		
2	Batch No.	RM/RO/SAS/19/0023		
3	Project ID	10301002158		
4	Total Length of Road (In Km)	4.000 Km		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	4.000Km		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	32.03957		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.60198		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0.00000	60%	0.00000
II	SHOULDERS AND EMBANKMENTS	0.00000	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00000	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0.000000	10%	0.000000
V	VEGETATION	0.00000	5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.60198

Date of inspection by E/I of his agent

Prepared by Contractor's self Control unit

Puneshwar - 40200
Name and Designation of person inspection road

28.05.22
(Signature)

Date

Signature of person inspection road

28/5/22
Certify by E/I [signature] Date:-

Name of Road : DARIGAON -Konki

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
27/5/22	15:33:14	13	0.1	300	10.1	3000	3540 G		24.884397	83.928248	Speed Breaker
27/5/22	15:34:0	13	0.1	280	10.1	2800	3313 G		24.8853	83.928332	Normal
27/5/22	15:34:0	13	0.1	330	20.2	3300	3881 G		24.88612	83.928618	Normal
27/5/22	15:34:25	13	0.1	300	20.2	3000	3540 G		24.886553	83.929175	Normal
27/5/22	15:35:0	13	0.1	280	30.3	2800	3313 G		24.886747	83.93015	Normal
27/5/22	15:35:0	13	0.1	310	10.1	3100	3654 G		24.88683	83.931093	Normal
27/5/22	15:35:35	13	0.1	320	20.2	3200	3767 G		24.887622	83.931262	Normal
27/5/22	15:35:35	13	0.1	300	20.2	3000	3540 G		24.888288	83.93172	Normal
27/5/22	15:36:10	13	0.1	340	20.2	3400	3994 G		24.888437	83.932625	Normal
27/5/22	15:36:10	13	0.1	330	20.2	3300	3881 G		24.8889022	83.933163	Normal
27/5/22	15:36:10	13	0.1	330	20.2	3300	3881 G		24.888912	83.934175	Normal
27/5/22	15:36:46	13	0.1	340	30.3	3400	3994 G		24.889065	83.934998	Normal
27/5/22	15:37:0	13	0.1	290	20.2	2900	3426 G		24.889932	83.93505	Normal
27/5/22	15:37:21	13	0.1	280	20.2	2800	3313 G		24.89162	83.93515	Normal
27/5/22	15:37:21	13	0.1	330	20.2	3300	3881 G		24.89252	83.934697	Normal
27/5/22	15:38:0	13	0.1	310	20.2	3100	3654 G		24.892773	83.933838	Normal
27/5/22	15:38:31	13	0.1	340	10.1	3400	3994 G		24.893342	83.93313	Normal
27/5/22	15:39:0	13	0.1	340	10.1	3400	3994 G		24.894125	83.932777	Normal
27/5/22	15:39:6	13	0.1	320	20.2	3200	3767 G		24.895027	83.932642	Normal
27/5/22	15:39:6	13	0.1	260	20.2	2600	3086 G		24.895903	83.932508	Normal
27/5/22	15:39:41	13	0.1	320	30.3	3200	3767 G		24.896658	83.932373	Curve
27/5/22	15:40:0	13	0.1	260	30.3	2600	3086 G		24.89678	83.931397	Normal
27/5/22	15:40:0	13	0.1	210	40.4	2100	2518 G		24.896737	83.930387	Normal
27/5/22	15:40:16	13	0.1	270	40.4	2700	3199 G		24.896835	83.92941	Normal
27/5/22	15:40:16	13	0.1	230	40.4	2300	2745 G		24.896963	83.92843	Normal
27/5/22	15:40:16	13	0.1	270	30.3	2700	3199 G		24.897175	83.92749	Normal
27/5/22	15:40:52	13	0.1	320	30.3	3200	3767 G		24.897305	83.926515	Normal
27/5/22	15:41:0	13	0.1	280	30.3	2800	3313 G		24.897668	83.92574	Normal
27/5/22	15:41:0	13	0.1	270	30.3	2700	3199 G		24.89859	83.925925	Normal
27/5/22	15:41:0	13	0.1	270	40.4	2700	3199 G		24.899525	83.925942	Normal
27/5/22	15:41:0	13	0.1	280	40.4	2800	3313 G		24.900342	83.925992	Normal
27/5/22	15:41:0	13	0.1	280	40.4	2800	3313 G		24.901282	83.926093	Normal

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$* = 3000$$

$$Y = 3540$$

(R) RURAL ROAD


Good

<4000

Average Poor
4001-5000 >5001

48

27/5/22	15:41:27	13	0.1	220	40.4	2200	2631	G	24.902215	83.926127	Normal
27/5/22	15:41:27	13	0.1	290	40.4	2900	3426	G	24.903045	83.926195	Normal
27/5/22	15:42:0	13	0.1	280	10.1	2800	3313	G	24.90366	83.925992	Normal
27/5/22	15:42:2	13	0.1	150	10.1	1923	2317	G	24.903423	83.925168	Normal
27/5/22	15:54:22	13	0.1	270	10.1	2700	3199	G	24.891335	83.89338	Normal
27/5/22	15:54:22	13	0.1	270	30.3	2700	3199	G	24.890445	83.893113	Normal
27/5/22	15:54:57	13	0.1	230	30.3	2300	2745	G	24.889562	83.892978	Normal
Average IRI								3433			


 18.05.22
 J. C. A. E.


 Executive Engineer
 Rural Work's Department
 Work Division, Sasaram-1


Name of Customer : SHIVSHANKAR KAUSHIK INF
Name of Work : Daingaon - Konki
Road :
Lab Job number : 13
Date : 5/27/2022
Section No. : 13

Test Date : 5/27/2022
Machine No. : 391
Start S No. : 471
Start E No. : 510
Weather : Normal
Start Location : 24.884397, 83.5
End Location : 24.889562, 83.5
Road Name : Daingaon - Konki
Road Type : (R) RURAL ROAD
Side : Shoulder
Interval :
UVI Range : 1317 To 5000 mm/km
Dist Range : 0 To 1.148 0.028 * 1000 m
Equation : $Y = 0 * X^2 + 1.136 * X + 132.5$

Print Generate Report and Graph

Redraw Graph

Map View

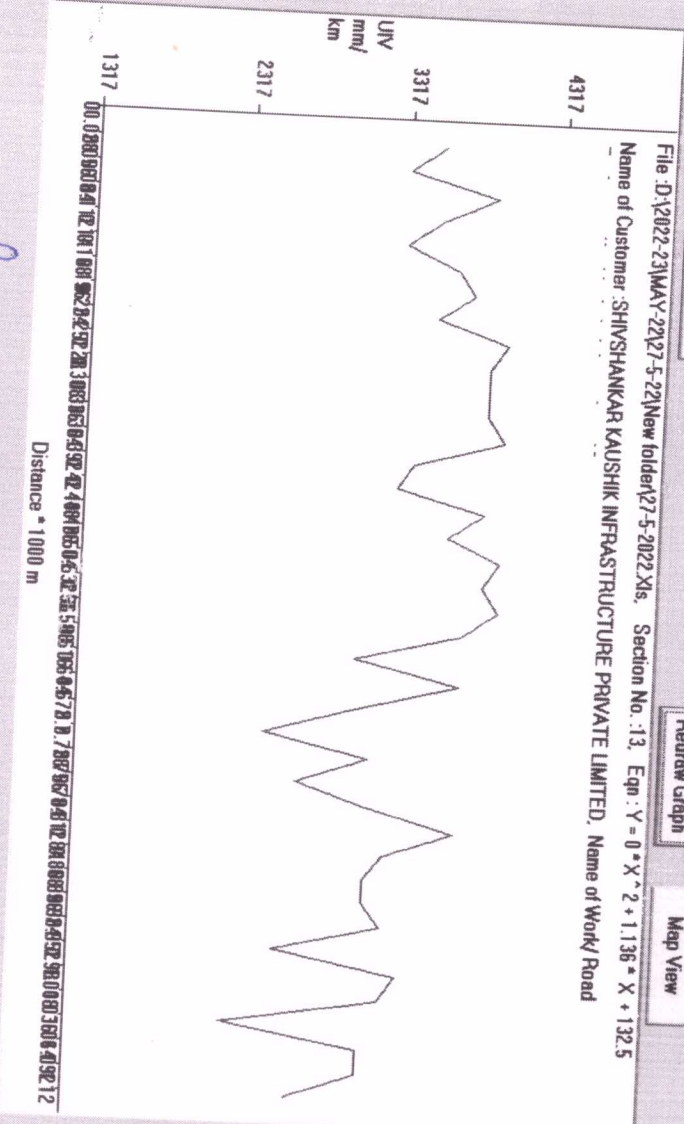

28/05/22
Jc

28/5/2022

28/5/22
