

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम - 1

पत्रांक:- 1108 3130

सासाराम/दिनांक:- 11.07.2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
3054 एम0आर0 नई अनुरक्षण नीति-2018
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :- शीर्ष 3054 एम0आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।

प्रसंग :- विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुरक्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।

सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन

NKumar
11.07.22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

Sasaram-2

4th Quarter

	Name of the Road	SONHAR TO RAIPUR CHOWK		
	Batch No.	PMIR0/SAS/191006		
3	Project ID	2301002342		
4	Total Length of Road (In Km)	0.60 Km		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	—		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	4.83279		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.2416395		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction [6] = [3]/[1]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	—	60%	—
II	SHOULDERS AND EMBANKMENTS	—	10%	—
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	—	15%	—
IV	SIGNAGE AND ROAD SAFETY	—	10%	—
V	VEGETATION	—	5%	—
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)			[5]	—
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)			[6]	0.242

Date of inspection by E/I of his agent

Prepared by Contractor's self Control unit

Purneshwar Yadav,
Name and Designation of person inspection road

(Signature)

Date

Signature of person inspection road

Certify by E/I [signature] Date:-

Name of Road : SONHAR SE RAYPUR CHOR

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
25/5/22	10:19:4	81	0.1	300	30.3	3000	3540	G	24.934228	83.899512	Normal
25/5/22	10:19:4	81	0.1	250	30.3	2500	2972	G	24.935048	83.899697	Normal
25/5/22	10:19:39	81	0.1	340	30.3	3400	3994	G	24.935407	83.898905	Normal
25/5/22	10:19:39	81	0.1	290	20.2	2900	3426	G	24.936052	83.898737	Normal
25/5/22	10:20:0	81	0.1	210	40.4	2100	2518	G	24.936857	83.899057	Normal
25/5/22	10:20:0	81	0.1	230	40.4	2300	2745	G	24.937737	83.899393	Normal
Average IRI							3199				

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 3000$$

$$Y = 3540$$

(R) RURAL ROAD

Good

<4000

Average Poor
4001-5000 >5001

16.05.22
16

05/07/22

11.07.22

Executive Engineer
Rural Work's Department
Work Division, Sasaram-1

Name of Customer : Bhole Shankar Construction
 Name of Work/ Road : SONHAR SE RAYPUR CHOR
 Lab Job number : 81
 Date : 25.05.2022
 Section No. : 81


Test Date : 25-05-2022
 Road Name : SONHAR SE RAYPUR CHOR
 Machine No : 391
 Road Type : (P) RURAL ROAD
 Start S No : 925
 Side : SHEOSAGAR
 Start E No : 930
 Interval :
 Weather : NORMAL
 UIV Range : 1518 To 5000 mm/km
 Dist Range : 0 To 0.252 0.028 = 1000 m
 Start Location : 24.934228
 End Location : 24.937737
 Equation : test

Print Generate Report and Graph

Redraw Graph

Map View

File : D:\BROM INDICATOR REPORT\25-5-22\DATA\XLS. Section No. : 81. Egn : test
 Name of Customer : Bhole Shankar Construction. Name of Work/ Road : SONHAR SE RAYPUR CHOR. Lab

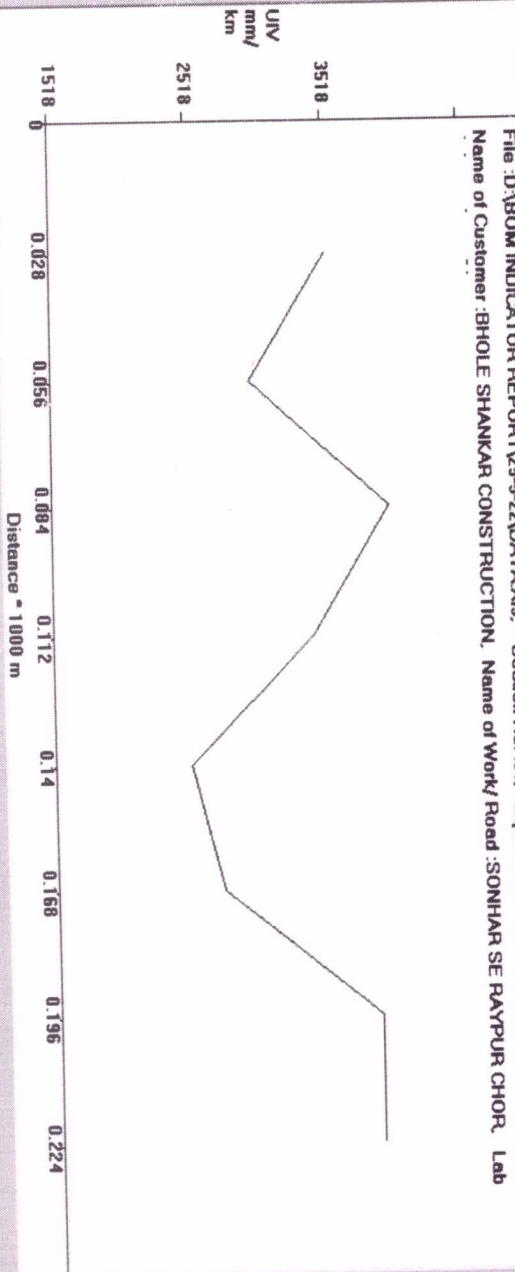

26.05.22
 JE

05/07/22

NEERAN
 11.07.22
 EE
