

5

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम — 1

पत्रांक:- 1111 3-130

सासाराम/दिनांक:- 11.07.2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
3054 एम0आर0 नई अनुरक्षण नीति-2018
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :- शीर्ष 3054 एम0आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।

प्रसंग :- विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुरक्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।
सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन

N. Kumar
11.07.22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:- Sasaram - I

3rd Quarter

1	Name of the Road	SHIBSAGAR CHENARI ROAD - CHANDWAN		
2	Batch No.	RM/RO/SAS/119/0006		
3	Project ID	10301002213		
4	Total Length of Road (In Km)	0.8 km		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	0.8 km		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	6.40300 lacs		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.32015 lacs		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0.00	60%	0.00
II	SHOULDERS AND EMBANKMENTS	0.00	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0.00	10%	0.00
V	VEGETATION	0.00	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)			[5]	
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)			[6]	0.32015 lacs

Date of inspection by E/I of his agent

Prepared by Contractor's self Control unit

Puneshwar Yadav

Name and Designation of person inspection road

[Signature]
26.05.22
(Signature) JE

Date

26/07/22

Signature of person inspection road

[Signature]
11.07.22

Certify by E/I [signature] Date:-

Name of Road : SHEOSAGAR CHENARI ROAD SE CHANDWA

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
25/5/22	10:33:29	82	0.1	300	20.2	3000	3540	G	24.967097	83.901648	Normal
25/5/22	10:34:4	82	0.1	250	10.1	2500	2972	G	24.966252	83.901515	Normal
25/5/22	10:34:4	82	0.1	190	30.3	1900	2290	G	24.965387	83.901413	Normal
25/5/22	10:34:4	82	0.1	200	40.4	2000	2404	G	24.96449	83.901397	Normal
25/5/22	10:34:4	82	0.1	190	40.4	1900	2290	G	24.963537	83.901312	Normal
25/5/22	10:34:39	82	0.1	240	30.3	2400	2858	G	24.962698	83.901143	Normal
25/5/22	10:35:0	82	0.1	300	20.2	3000	3540	G	24.961732	83.900823	Normal
25/5/22	10:35:14	82	0.1	250	20.2	2500	2972	G	24.962192	83.900942	Normal
Average IRI							2858				

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 3000$$

$$Y = 3540$$

(R) RURAL ROAD

Good

<4000

Average Poor
4001-5000 >5001

26.05.22

26/07/22

11.07.22

Executive Engineer
Rural Work's Department
Work Division, Sasaram-1

Name of Customer : BHOLE SHANKAR CONSTRU
Name of Work/ Road : SHEOSAGAR CHENARI ROAD
Lab Job number : 82
Date : 25-05-2022
Section No. : 82


Test Date : 25-05-2022
Road Name : SHEOSAGAR CHENARI ROAD
Machine No. : 391
Road Type : (R) RURAL ROAD
Start S No. : 931
Side : SHEOSAGAR
Start E No. : 938
Interval :
Weather : NORMAL
U/V Range : 1177 To 5000
Dist Range : 0 To 0.364
Equation : test
End Location : 24.962192
Interval : 1000 m

Print Generate Report and Graph

Redraw Graph

Map View

File : D:\BOM INDICATOR REPORT\25-5-22\DATA.Xls, Section No. : 82, Eqn : test
 Name of Customer : BHOLE SHANKAR CONSTRUCTION, Name of Work/ Road : SHEOSAGAR CHENARI ROAD SE

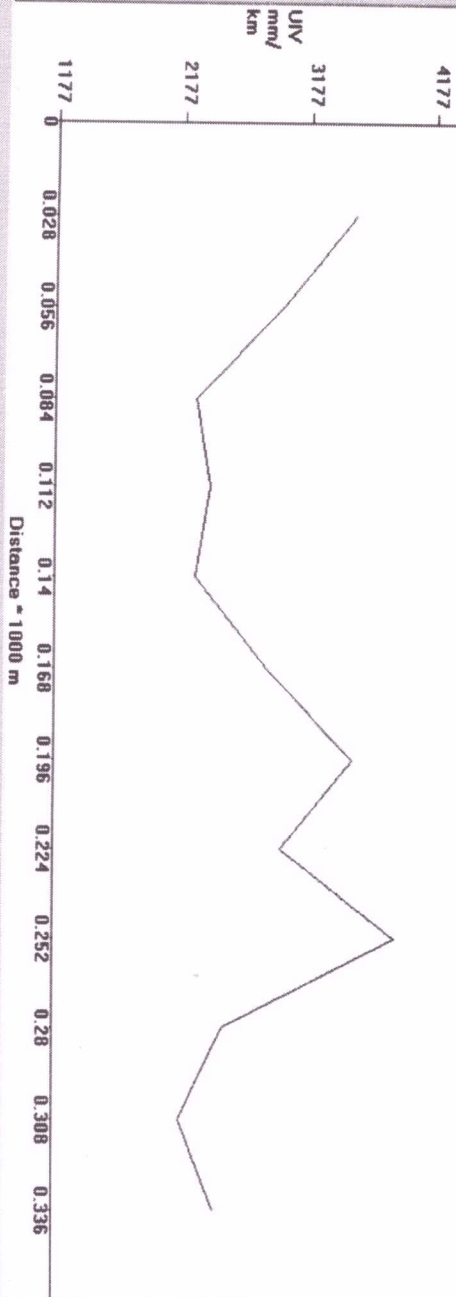

16.05.22
 16/07/22
 11.07.22
