

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम — 1

पत्रांक:- 1114 3190

सासाराम/दिनांक:- 11.07.2022

प्रेषक,

कार्यपालक अभियंता,
 ग्रामीण कार्य विभाग,
 कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
 3054 एम0आर0 नई अनुरक्षण नीति-2018
 ग्रामीण कार्य विभाग
 बिहार, पटना।

विषय :- शीर्ष 3054 एम0आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।

प्रसंग :- विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुरक्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।
 सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन

Signature
 11.07.22

कार्यपालक अभियंता,
 ग्रामीण कार्य विभाग,
 कार्य प्रमण्डल, सासाराम-1

1st Quarter

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:-

Sasaram-I

CONS. OF ROAD FROM KONAR - TORN
ROAD TO GARA CHAUBEY CANAL VIA

~~CONS. OF ROAD FROM CHANDAN PURA~~

RM/20/SAS/19/006

10301101034

0.85 km

0.85 km

1	Name of the Road	Conts. of Road from CHANDAN PURA		
2	Batch No.	PM/20/SAS/19/006		
3	Project ID	10301101034		
4	Total Length of Road (In Km)	0.85 km		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	0.85 km		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	6.89814 lacs		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.344907 lacs		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non- Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0.00	60%	0.00
II	SHOULDERS AND EMBANKMENTS	0.00	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0.00	10%	0.00
V	VEGETATION	0.00	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)			[5]	0.00
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)			[6]	0.344907 lacs

Date of inspection by E/I of his agent

Prepared by Contractor's self Control unit

Puneshwar Yadav
Name and Designation of person inspection road

(Signature)

Date

Signature of person inspection road

Certify by E/I [signature] Date:-

Name of Road : KONAR TONARI ROAD SE JARA CHAUBEY CANAL VIA CHANDANPURA

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
24/5/22	12:40:0	71	0.1	340	0	3400	3994	G	25.22168	83.944275	Normal
24/5/22	12:40:0	71	0.1	260	20.2	2600	3086	G	25.21382	83.94404	Normal
24/5/22	12:40:20	71	0.1	290	10.1	2900	3426	G	25.20512	83.94347	Speed Breaker
24/5/22	12:41:0	71	0.1	260	10.1	2600	3086	G	25.19697	83.94313	Normal
24/5/22	12:41:30	71	0.1	300	0	3000	3540	G	25.18828	83.943097	Normal
24/5/22	12:41:30	71	0.1	330	20.2	3300	3881	G	25.17995	83.942945	Normal
24/5/22	12:42:6	71	0.1	320	30.3	3200	3767	G	25.1711	83.942693	Normal
24/5/22	12:42:6	71	0.1	340	30.3	3400	3994	G	25.16223	83.942608	Normal
		Average IRI					3597	G			

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 3000$$

$$Y = 3540$$

(R) RURAL ROAD

Good
Average
4001-5000
Poor
>5001

Shy S. S. 22
NS JC

NSJC
05/07/22

NSJC
11.07.22

Executive Engineer
Rural Work's Department
Work Division, Sasaram-1

Name of Customer: BHOLESHANKAR CONSTRUCT
Name of Work/Road: KONAR TONARI ROAD SE JA
Lab Job number: 71
Date: 24-05-2022
Section No.: 71


Print Generate Report and Graph

Test Date: 24-05-2022
Machine No: 391
Start S No: 218
Start E No: 225
Weather: NORMAL
Start Location: 25.22168
End Location: 25.16223
Road Name: KONAR TONARI ROAD SE JA
Road Type: (R) RURAL ROAD
Side: SHEOSAGAR
Interval: 1000
UV Range: 1745 To 5000
Dist Range: 0 To 0.308
Equation: test

Redraw Graph

Map View

File: D:\BOM INDICATOR REPORT\24-5-22\MAIN.Xls. Section No.: 71. Egn: test
 Name of Customer: BHOLESHANKAR CONSTRUCTION PVT. LTD. Name of Work/Road: KONAR TONARI ROAD

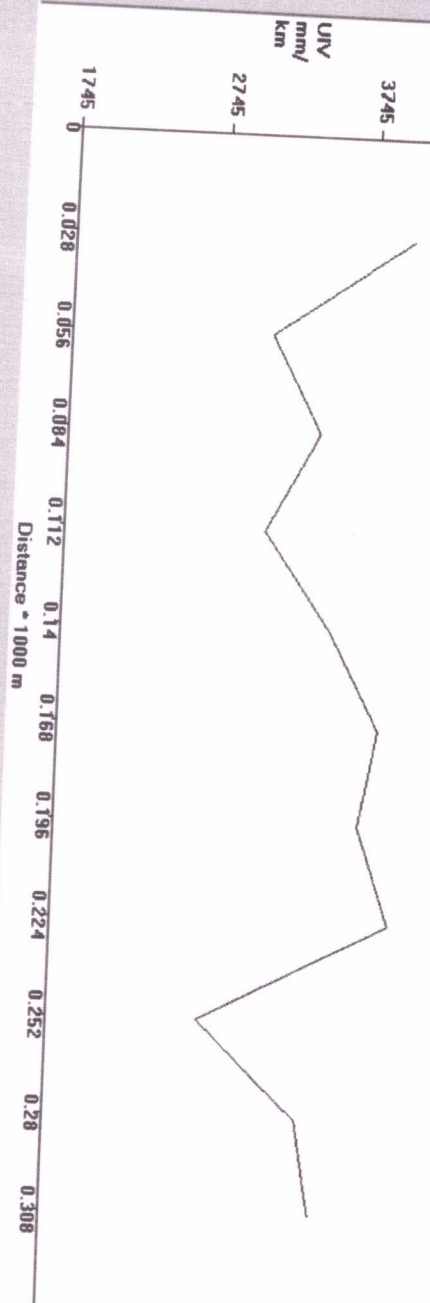

24.05.22

05/06/22

MEENAR
11.07.22
EE
