

(6)

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम - 1

पत्रांक:- 1112 3130

सासाराम/दिनांक:- 11.07.2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
3054 एम0आर0 नई अनुरक्षण नीति-2018
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :- शीर्ष 3054 एम0आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।

प्रसंग :- विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुरक्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।

सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन

N. Kumar
11.07.22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:- Sasaram-1

3rd Quarter

1	Name of the Road	PMGSY ROAD - ANANDPURACANANTPOK		
2	Batch No.	RM / Ro / SAS / B / 006		
3	Project ID	1030100 2207		
4	Total Length of Road (In Km)	0.6 km		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	0.6 km		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	4		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	4.92024 lacs		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0.00	60%	0.00
II	SHOULDERS AND EMBANKMENTS	0.00	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0.00	10%	0.00
V	VEGETATION	0.00	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)		[5]		
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)		[6]		0.246012 lacs

Date of inspection by E/I of his agent

Prepared by Contractor's self Control unit

Puneshwar Yadav

Name and Designation of person inspection road

(Signature)

Date

Signature of person inspection road

Certify by E/I [signature] Date:-

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
24/5/22	12:16:21	70	0.1	290	20.2	2900	3426	G	25.26193	83.932305	Normal
24/5/22	12:16:21	70	0.1	250	20.2	2500	2972	G	25.2711	83.932542	Normal
24/5/22	12:17:0	70	0.1	250	30.3	2500	2972	G	25.2793	83.932693	Normal
24/5/22	12:17:0	70	0.1	260	30.3	2600	3086	G	25.28823	83.932945	Normal
24/5/22	12:17:32	70	0.1	270	10.1	2700	3199	G	25.2979	83.93313	Normal
24/5/22	12:18:0	70	0.1	250	10.1	2500	2972	G	25.30657	83.933332	Normal
Average IRI								3105			

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 3000$$

$$Y = 3540$$

(R) RURAL ROAD
Good
<4000

Average Poor
4001-5000 >5001

Executive Engineer
Rural Work's Department
Work Division, Sasaram-1

Signature
11.07.22
05/07/22

Name of Client : BHOLESHANKAR CONSTRUCT
 Name of Work : PMGSY ROAD SE ANANTPUR
 Road :
 Lab Job number : 70
 Date : 24-05-2022
 Section No. : 70


Test Date : 24-05-2022
 Machine No : 391
 Start S No : 212
 Start E No : 217
 Weather : NORMAL
 Start Location : 25.26193
 End Location : 25.30657
 Road Name : PMGSY ROAD SE ANANTPUR
 Road Type : (R) RURAL ROAD
 Side : SHERSAGAR
 UIV Range : 1972 To 5000
 Dist Range : 0 To 0.224
 Equation : test
 Interval : 1000 mm/km
 * 1000 m

Print
 Generate Report and Graph

Redraw Graph

Map View

File : D:\BOM INDICATOR REPORT\24-5-22\MAIN.Xls Section No. : 70. Egn test
 Name of Customer : BHOLESHANKAR CONSTRUCTION PVT. LTD. Name of Work/ Road : PMGSY ROAD SE

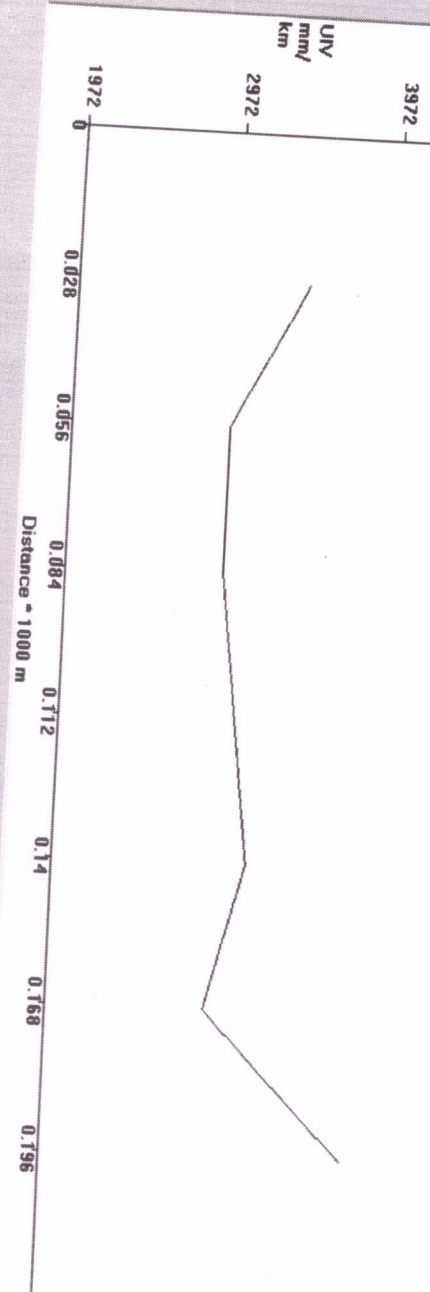

11.7.22
 05/07/22
 11.07.22

05/07/22
 11.07.22

11.07.22
