

9

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम — 1

पत्रांक:- 1115 3190

सासाराम/दिनांक:- 11.07.2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
3054 एम0आर0 नई अनुरक्षण नीति-2018
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :- शीर्ष 3054 एम0आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।

प्रसंग :- विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुरक्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।

सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन

N. Kumar
11.07.22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :- Sasaram-1

Cons. of ROAD FROM SHIVSAGAR - 4th Quarter

1	Name of the Road	XXX RAIPUR GHOR ROAD TO MARKAN		
2	Batch No.	XXX RM/RO/SAS/19/006		
3	Project ID	XXX 103011 01052		
4	Total Length of Road (in Km)	0.00	0.5km	
5	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	0	0.5km	
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20	9	
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	0	3.963231ay	
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0	0.198161ay	
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment [6] = [3] / [1] * [2] * [4]
		Length Non- Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0.00	60%	0.00 0.00
II	SHOULDERS AND EMBANMENTS	0.00	10%	0.00 0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00	15%	0.00 0.00
IV	SIGNAGE AND ROAD SAFETY	0.00	10%	0.00 0.00
V	VEGATAION	0.00	5%	0.00 0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				0.00 0.1981861ay

Date of inspection by E/I or his agent
Prepared by Contractor's self Control unit

Puneshwar Yadav
Name and Designation of person inspecting road

Date

Signature of person inspecting road

(Signature)

Certify by E/I [signature] Date:-

Markam

Name of Road : SHEOSAGAR RAYPUR CHOR ROAD SE MADKAJ GAW

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
25/5/22	10:11:5	80	0.1	330	10.1	3300	3881	G	24.931048	83.899225	Normal
25/5/22	10:11:40	80	0.1	310	20.2	3100	3654	G	24.931058	83.898265	Normal
25/5/22	10:12:0	80	0.1	340	10.1	3400	3994	G	24.931588	83.897575	Normal
25/5/22	10:12:17	80	0.1	300	20.2	3000	3540	G	24.931998	83.897053	Normal
25/5/22	10:13:28	80	0.1	260	20.2	2600	3086	G	24.931922	83.896278	Normal
Average IRI							3631				

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 3000$$

$$Y = 3540$$

(R) RURAL ROAD

Good

<4000

Average Poor
4001-5000 >5001

Executive Engineer
Rural Work's Department
Work Division, Sasaram-1

26/05/22
21-
05/07/22
AC


Name of Customer : BHOLE SHANKAR CONSTRUCTION
Name of Work / Road : SHEOSAGAR RAYPUR CHOR
Lab Job number : 80
Date : 25-05-2022
Section No. : 80

Test Date : 25-05-2022
Road Name : SHEOSAGAR RAYPUR CHOR
Machine No. : 391
Road Type : (R) RURAL ROAD
Start S No. : 920
Side : SHEOSAGAR
Start E No. : 924
Weather : NORMAL
UV Range : 2086 To 5000 Interval 1000 mm/km
Start Location : 24.931048
Dist Range : 0 To 0.168
End Location : 24.931922
Equation : test

Print Generate Report and Graph

Redraw Graph

Map View

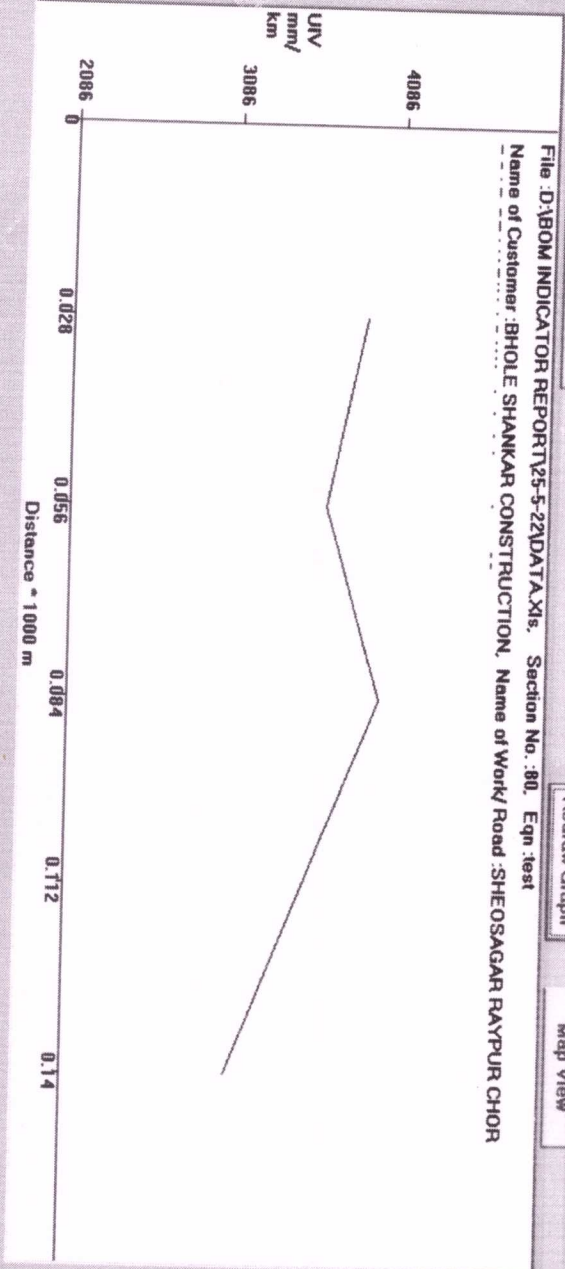

Shy
26.05.22
JC

Shy
26.05.22
JC

26/5/22

Accumulated
0.11.07.22
EE
