

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, महनार।

पत्रांक.....1099..... महनार/दिनांक.....28/07/22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, महनार

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :- नई अनुरक्षण नीति-2018MR (3054) Maintenance योजना के अंतर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054)- Maintenance योजना के अंतर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :- यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, महनार।

4/4/22
28/7/22

FORM GFR -19 -A

(see Govt. of India's decision (i) below rule 150)
Form of Utilisation Certificate upto 27.07.2022

05 year Routine Maintenance of Rural Road Maintenance policy-2018

PIU:- R.W.D. Works, Division , Mahnar

Sl. No.	Name of Scheme	Sanction No.& Date with amount (in Rs. Lakh)	Amount Received (in Rs. Lakh)	Particulars
1	2	3	4	5
1	Construction of Road Under 05 year Routine Maintenance of Rural Road Maintenance policy-2018	28.01780	28.01780	Certified that out of Rs.28.01780 Lakh received till date in favour of Ex-Engineer, R.W.D. Works Division, Mahnar a sum of Rs.15.59263 Lakh has been utilized for the purpose of 05 year Routine Maintenance of Rural Road Maintenance policy-2018 Scheme as given in the margin for which it was sanctioned and that the balance of Rs.12.42517 Lakh remaining unutilized at the end of the period under the time of completion.
		28.01780	28.01780	


- 2 Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the propose for which it was sanctioned.


Kind of Checks Exercised :-


- Workers have been supervised by Executive Engineer/ Superintending Engineer
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer
- Construction materials have been tested.
- Measurments have been recorded in the MB's and test check conducted by the Assistant
- All other codal formalities have overserved

3 Physical Progress Achieved.

- Construction of Bridge Works
- Construction of Piling Works.


28/7/22
Divisional Account Officer
Rural works Department
Works Division, mahnar


28/7/22
Executive Engineer
Rural works Department
Works Division, mahnar


28/7/22

Name of Works Division:- Mahanar

Maintenance Requisition Formate for Scheme Mead-MR (3054) U

NIDHI OF WORKS DEVELOPMENT																
Road Details				Agreement												
Sl. No.	Name of Raods	Batch No.	Project ID	Actual Date of Completion	AA Details										Total Maintenance	Length (in KM)
					Main Work Amount (in Lakh	Maintenance Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5				
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15		
1	Vill. Pirapur (Sri Tej Narayan Sharma's house) of	RM/VA/MA H/19/000 8	31507708020	27-05-2021	45.774	14.806	41.168	0.95395	1.92007	2.54803	2.32419	5.55458	13.30082	1.5		
2	Construction of road from Jandaha block main gate to Suresh chowk.(Jandaha)	RM/VA/MA H/19/000 8	31507601049	27-05-2021	51.813	17.439	46.598	1.10279	2.25177	3.01856	2.73404	6.58747	15.69463	2.3		
3	NH-103 Andharawar to Dhadhuhia Chowk	RM/VA/MA H/19/000 8	31507501013	05-12-2020	19.97	6.71	17.954	0.42245	0.86109	1.18185	1.04611	2.52188	6.03338	0.9		
4	Basantpur Gorla - Dailit Tola Kadilpur	RM/VA/MA H/19/000 8	NEA220002223	01-06-2021	28.496	11.533	22.608	0.72861	1.48686	2.00403	1.80468	4.34633	10.37051	1.55		
Total					146.05300	50.48800	128.32800	3.20780	6.51979	8.75247	7.90902	19.01026	45.39934	6.25		

Order

Bihar Rural Road Maintenance Policy-2018

Actual Maintenance Expenditure						Length as per Bump Report	IRI As per bump Report	Current Maintenance Demand							Remarks	
1st Year Maintenance	2nd Year Maintenance	3rd Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintenance Expenditure			1st QTR Maintenance	2nd QTR Maintenance	3rd QTR Maintenance	4th QTR Maintenance	5th QTR Maintenance	6th QTR Maintenance	7th QTR Maintenance		Total
16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32
0.000	0.000	0.000	0.000	0.000	0.000	1.5	2459.000	0.66504	0.66504	0.00000	0.000	0.000	0.000	0.000	1.33008	
0.000	0.000	0.000	0.000	0.000	0.000	2.3	2400.000	0.78473	0.78473	0.00000	0.000	0.000	0.000	0.000	1.56946	
0.000	0.000	0.000	0.000	0.000	0.000	0.9	3222.000	0.30167	0.30167	0.30167	0.30167	0.000	0.000	0.000	1.20668	
0.000	0.000	0.000	0.000	0.000	0.000	1.55	2925.00	0.51853	0.51853	0.00000	0.000	0.000	0.000	0.000	1.03706	
0.000	0.000	0.000	0.000	0.000	0.000			2.26997	2.26997	0.30167	0.30167	0.00000	0.00000	0.00000	5.14328	

Executive Engineer
R.W.D. Works Division
Mishnah

28/12/12

28/12/12

28/12/12

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	Vill. Pirapur (Sri Tej Narayan Sharma's house) of		
2	Batch No.	RM/VA/MAH/19/0008		
3	Project ID	31507708020		
4	Total Length of Road (in Km)	1.97		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	1.5		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	13.30082		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	0.66504		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.66504

Date of inspection by E/I or his agent Prepared by
Contractor's self Control unit

Date

Signature of person inspecting road

Name and Designation of person inspecting road
(Signature)

Certify by E/I (signature) Date

15/6/22

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Mahnar

Government of Bihar

OM01

Rural works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

To: Executive Engineer

RWD Works Division Mahnar

Date:

Road From-Vill. Pirapur (Sri Tej Narayan Sharma's house) of

Length of Road: 1.97 KM

Period : From.....

Inspector: A.E RWD Sub Division, Jandaha

Position: A.E

Standard Work item		Work	Units of work required in each kilometre										Comments
S No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM100 Sealed Pavement													
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No. Pothole found.
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Crack Sealing found
OM104 Surface Treatment													
	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Crocodile Cracking found
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Edge Repair Required
OM106	Digouts	m2	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	
OM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	
	Other activities	Lm											
OM1200 Shoulder													
	Unsealed Shoulder	No											
	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Edge Drop off Required
OM1201	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Holding water found
OM1202	Embankment Repair	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Embankment Repair Required
	Other Activities (Raincut)		1%	1%	1%	1%	1%	1%	1%	1%	1%	1%	Nil

24/11/18

24/11/18

24/11/18

OM 300 Drainage including culverts major									
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A				Not Required
OM302	Culvert Cleaning	Lm							Culvert maintain within stipulated time
OM303	Culvert and Pit repair	m2	Nil	Nil	Nil				Not Required
	Other activities (White Washing)	m2	Nil	Nil	Nil				Not Required
OM 400 Vegetation									
Grass Contorol									
OM401	a) Roadside-General Tidy	Ha	Nil	Nil	Nil				Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil				Not Required
OM402	Tree and shrub management	No	Nil	Nil	Nil				Not Required
	Cutting trees	No	Nil	Nil	Nil				Not Required
	Cutting Shrubs	No	Nil	Nil	Nil				Not Required
	Other activities (Trimming of Grass)	M2	Nil	Nil	Nil				Not Required
	Safety Signage and Road Signs Maintenance	No	Nil	Nil	Nil				Not Required
OM500	Guard Stones	Lm	N/A	N/A	N/A				Not Applicable
OM501	Distance Stones	No	N/A	N/A	N/A				Not Applicable
OM502	Road Marking	m2	Nil	Nil	Nil				Not Required
OM503	Other activities								
OM504									

Bidder

Appendix
11/11/12

Executive Engineer, Rural Work Department, Work Division, Mahabub

13/11/12

Name of the work: Vill. Pirapur (Sri Tej Narayan Sharma's house) of

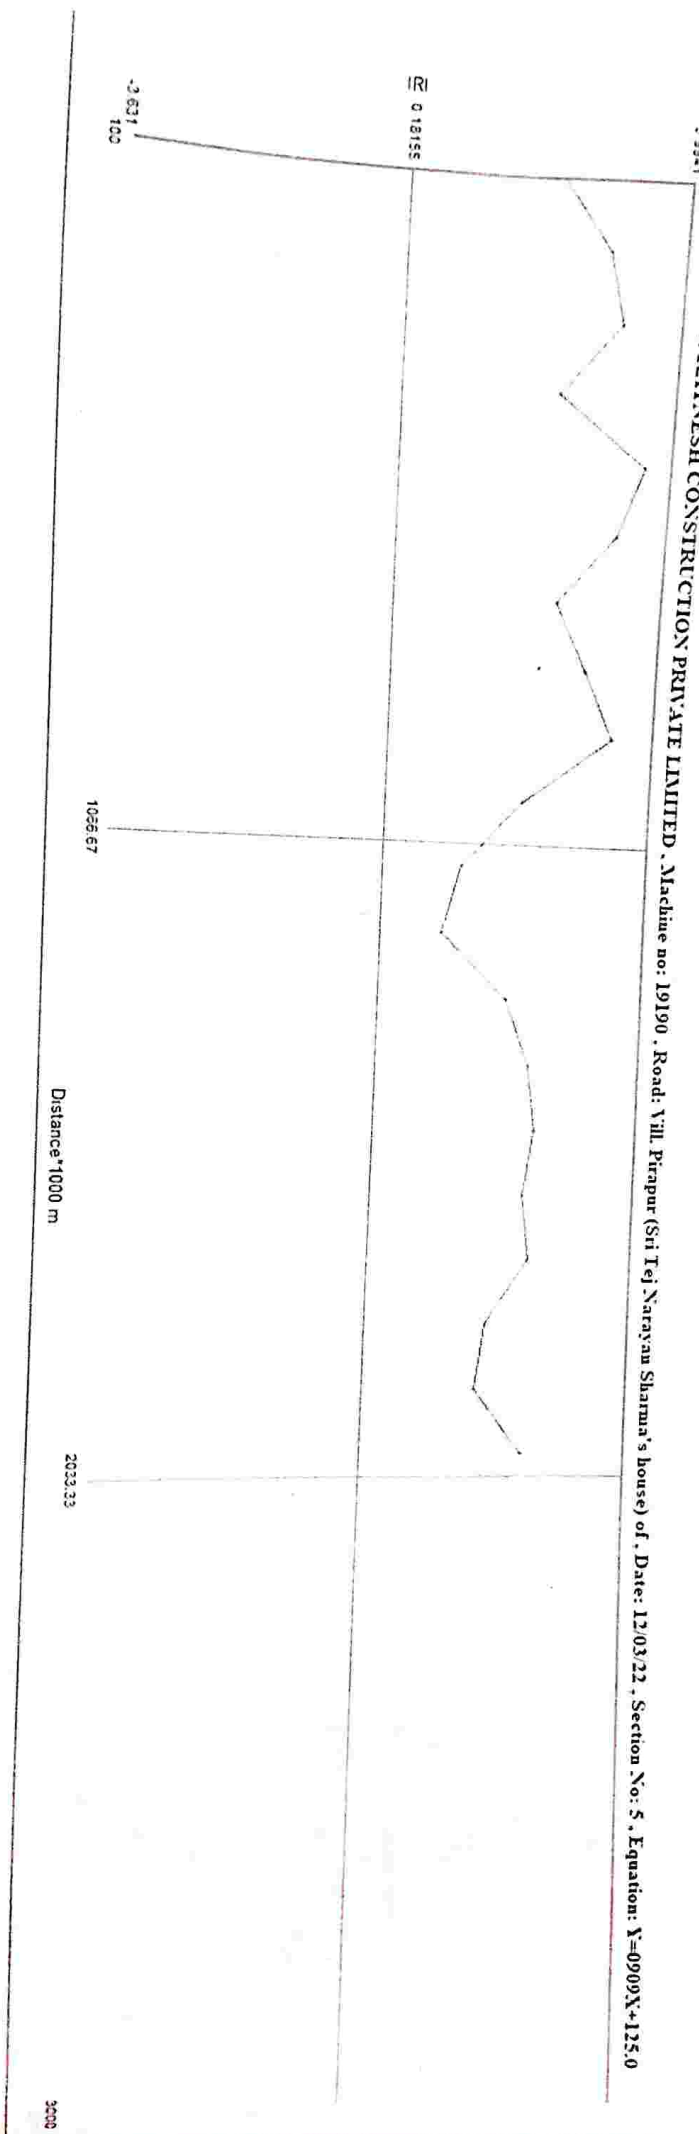
Date	Time	Test No	Distance (meter)	Total Distance (meter)	BUMP (cm)	Speed (km/h)	U (mm/Km)	Corrected U (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
03-12-2022	15:18:49	5	100	100	16.0 cm	4.2 Km/Hr	1600.0 mm/Km	1579.4	2.272	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:19:14	5	100	200	22.0 cm	14.2 Km/Hr	2200.0 mm/Km	2124.8	2.961	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:19:34	5	100	300	24.0 cm	17.6 Km/Hr	2400.0 mm/Km	2306.6	3.186	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:20:04	5	100	400	17.0 cm	12.1 Km/Hr	1700.0 mm/Km	1670.3	2.388	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:20:25	5	100	500	28.0 cm	17.1 Km/Hr	2800.0 mm/Km	2670.2	3.631	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:20:47	5	100	600	25.0 cm	16.2 Km/Hr	2500.0 mm/Km	2397.5	3.298	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:21:11	5	100	700	18.0 cm	15.1 Km/Hr	1800.0 mm/Km	1761.2	2.504	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:22:08	5	100	800	22.0 cm	6.4 Km/Hr	2200.0 mm/Km	2124.8	2.961	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:23:11	5	100	900	26.0 cm	5.6 Km/Hr	2600.0 mm/Km	2488.4	3.409	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:24:02	5	100	1000	15.0 cm	6.9 Km/Hr	1500.0 mm/Km	1488.5	2.155	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:24:27	5	100	1100	8.0 cm	13.9 Km/Hr	800.0 mm/Km	852.2	1.31	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:24:48	5	100	1200	6.0 cm	17.8 Km/Hr	600.0 mm/Km	670.4	1.057	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:25:10	5	100	1300	14.0 cm	16.2 Km/Hr	1400.0 mm/Km	1397.6	2.037	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:25:35	5	100	1400	17.0 cm	14.4 Km/Hr	1700.0 mm/Km	1670.3	2.388	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:26:08	5	100	1500	18.0 cm	10.8 Km/Hr	1800.0 mm/Km	1761.2	2.504	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:26:39	5	100	1600	17.0 cm	11.8 Km/Hr	1700.0 mm/Km	1670.3	2.388	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:27:20	5	100	1700	18.0 cm	8.8 Km/Hr	1800.0 mm/Km	1761.2	2.504	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:30:10	5	100	1800	13.0 cm	2.1 Km/Hr	1300.0 mm/Km	1306.7	1.918	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:31:03	5	100	1900	12.0 cm	6.7 Km/Hr	1200.0 mm/Km	1215.8	1.799	Good	25.7337828	N	85.5534983	E	Normal
03-12-2022	15:31:55	5	100	2000	18.0 cm	6.8 Km/Hr	1800.0 mm/Km	1761.2	2.504	Good	25.7337828	N	85.5534983	E	Normal

IRI Value 2459
Machine ID 19190

15/09/22
15/09/22
15/09/22

15/09/22
15/09/22

Name of Customer: RAJNESH CONSTRUCTION PRIVATE LIMITED, Machine no: 19190, Road: Vill Pirapur (Sri Tej Narayan Sharma's house) of, Date: 12/03/22, Section No: 5, Equation: $Y=0.909X+125.0$



[Signature]
15/07/22

[Signature]
15/07/22

[Signature]
15/07/22
